		<h1>Job Summary</h1>		Ticket Number TN# Bco-1812-0005		Ticket Date 12/2/2018	
COUNTY		COMPANY		API Number			
Weld		HIGHPOINT OPERATING		05-123-48494			
WELL NAME		RIG		JOB TYPE			
Wetco 4-63-5-4033B		Cartel 7		Surface Casing			
SURFACE WELL LOCATION		CJES Field Supervisor		CUSTOMER REP			
40.339926 104.449714		Derek Scott		Dustin Davis			
EMPLOYEES							
WELL PROFILE							
Max Treating Pressure (psi):				Bottom Hole Static Temperature (°F):			
Bottom Hole Circulating Temperature (°F):				Well Type:			

Open Hole

1	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
	13.5	0	851		

2	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)

Casing/Tubing/Drill Pipe

Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Surface	9.625	36	J-55	0	851		

Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)

Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)

CEMENT DATA							
Stage 1:		From Depth (ft):		0	To Depth (ft):		851
Type: Lead		Volume (sacks):		260	Volume (bbls):		89.3
Cement & Additives:				Density (ppg)	Yield (ft³/sk)	Water Req.	
100% CSC +0.25pps Poly Flake				13	1.93	10.54	
Stage 2:		From Depth (ft):			To Depth (ft):		
Type:		Volume (sacks):			Volume (bbls):		
Cement & Additives:				Density (ppg)	Yield (ft³/sk)	Water Req.	
Stage 3:		From Depth (ft):			To Depth (ft):		
Type:		Volume (sacks):			Volume (bbls):		
Cement & Additives:				Density (ppg)	Yield (ft³/sk)	Water Req.	
Stage 4:		From Depth (ft):			To Depth (ft):		
Type:		Volume (sacks):			Volume (bbls):		
Cement & Additives:				Density (ppg)	Yield (ft³/sk)	Water Req.	

SUMMARY							
Preflushes:		23 bbls of	Fresh Water	Calculated Displacement (bbl):	62.6	Stage 1	
		10 bbls of	Dye	Actual Displacement (bbl):	62.6	Stage 2	
Total Preflush/Spacer Volume (bbl):		33		Plug Bump (Y/N):	Yes	Bump Pressure (psi):	770
Total Slurry Volume (bbl):		89.3		Lost Returns (Y/N):	No	(if Y, when)	
Total Fluid Pumped		184.9					
Returns to Surface:		Cement	18 bbls				
Job Notes (fluids pumped / procedures / tools / etc.):							
Job went well. We bumped on time and there were no circulation issues.							
Thank You For Using							
CJES O-TEX Cementing							
Customer Representative Signature: _____							


Cement Job Log

[illegible]




Client	High Point	Client Rep	Dustin Davis	Supervisor	Derek Scott
Ticket No.	18120005	Well Name	Wetco 4-63-5-4033B	Unit No.	445067
Location	NWSW 4-4N-63W	Job Type	Surface Casing	Service District	Brighton, CO
Comments	260sx CSC @ 13.0ppg 1.93yield			Job Date	12/2/2018


Unit 445067 Rate Total

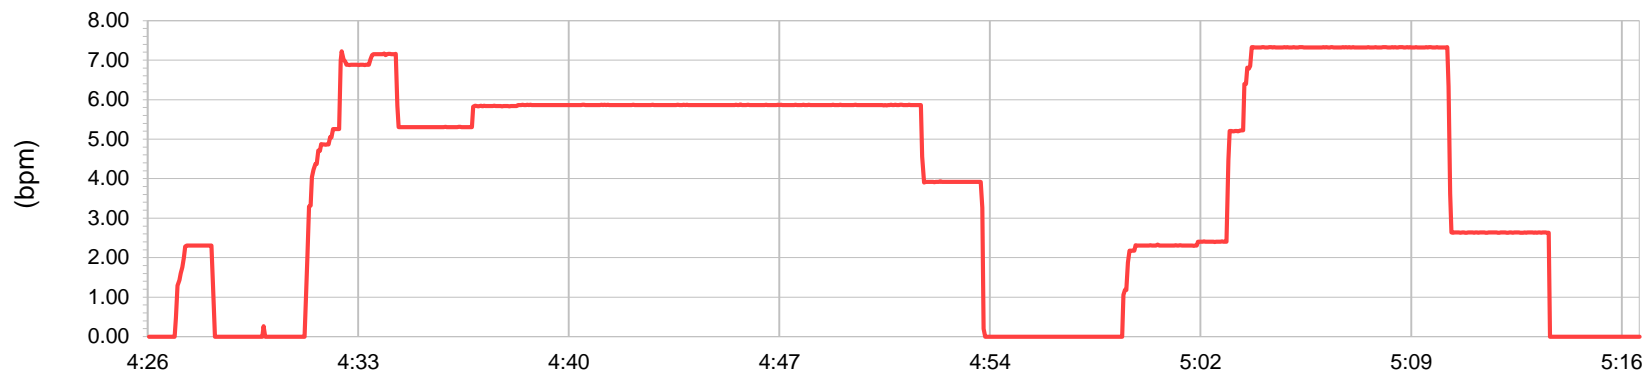


Unit 445067 Pump Pressure

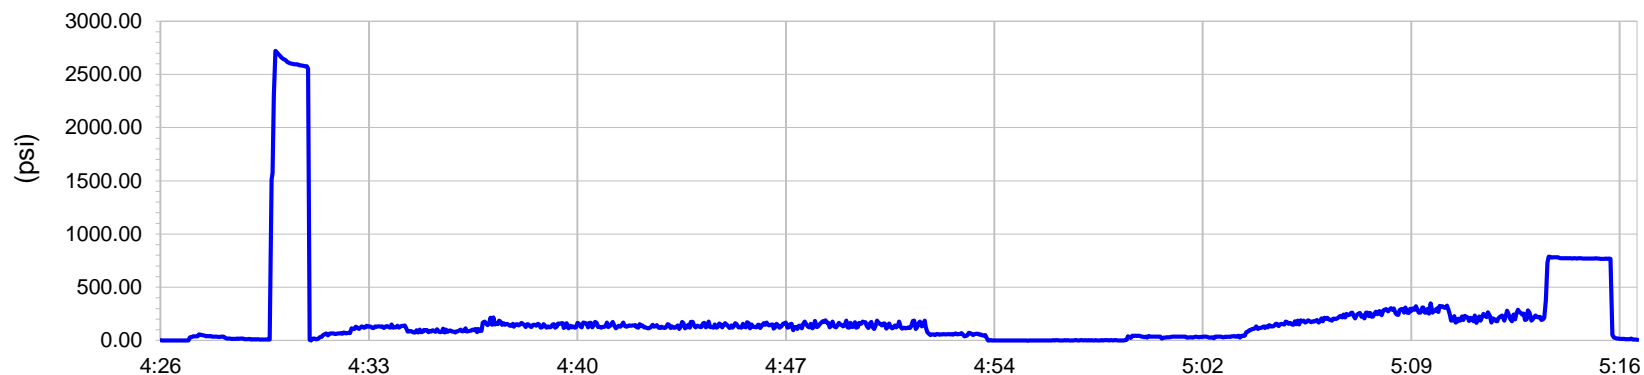

Unit 445067 Density

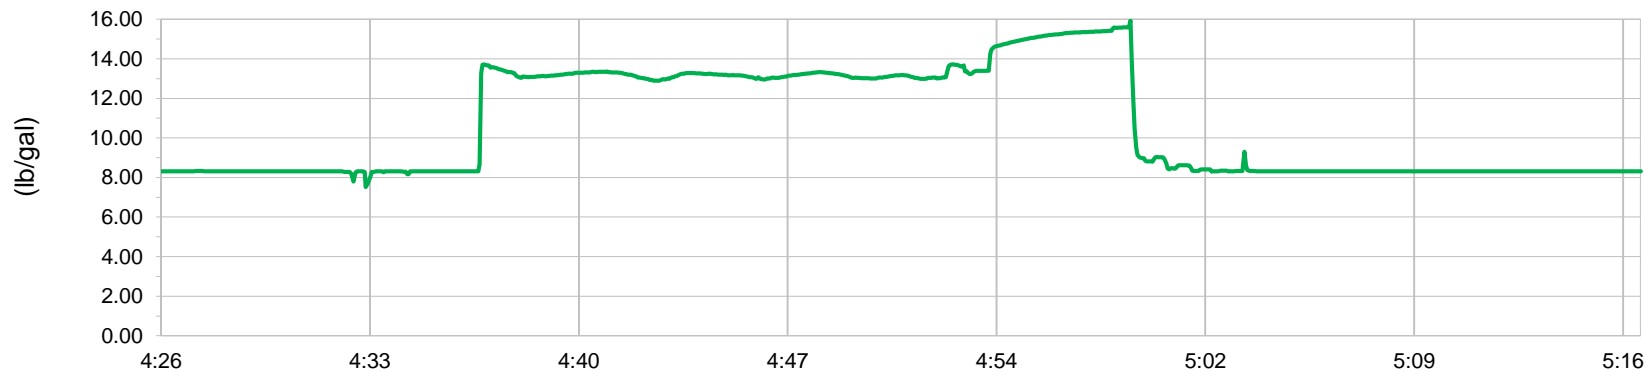



TICKET	Bco-1812-0005
DATE	12/2/2018
CREW INFORMATION	
SUPERVISOR	Derek Scott
PUMP UNIT	445067
NUMBERS	
ARRIVAL (D&T)	12/2/18 2:15 AM
DEPARTURE (D&T)	12/2/18 5:45 AM

[illegible][illegible]

Customer Name Printed _____

Customer Signature _____

Date Signed _____
