



PO Box 329
Ft. Lupton, CO 80621
(303) 654-9202

"Here Safety Meets Quality at the Axis of Efficiency"

Date of Service	Job Type	Customer	Consultant	Well Name	Last Tckt	Ticket #
9/13/2025	Surface	Bison	DAVE DONOHO	FREEMAN 1	Yes	5690
State	County	API	Rig	Operator		
Colorado	Weld	05-123-07087	Axis 2724			

Well Information						Water	
	Work String	Prod CSG	Surface	OH (I.D.)	Annular	Temp	76 °F
OD & Weight	2 7/8" 6.5#			7.875		PH	7
Factor	0.00579	0	0	0.0602		Chloride	1
Length	7265			119		Well Description	
Capacity	42.06	0.00	0.00	7.17	0.00	Toc Plug 1	7146'
OD & Weight	2 7/8" 6.5#			7.875		EOT	7265'
Factor	0.00579	0	0	0.0602		Toc Plug 2	6240'
Length	6580			340		EOT	6580'
Capacity	38.10	0.00	0.00	20.48	0.00	Toc Plug 3	1008'
OD & Weight	2 7/8" 6.5#		8 5/8" 24#	7.875		EOT	1632'
bbl/ft	0.00579	0	0.0678	0.0602		Toc Plug 4	110'
Length	608		189	419		EOT	608'
Capacity	3.52	0.00	12.81	25.22	0.00	Shoe	189'
Buoyancy	0.76	Buoyancy	0.76	Buoyancy	0.76	Toc Plug 5	0'
Lift Pressure	PRV	Lift Pressure	PRV	Lift Pressure	PRV	EOT	110'
5528	3750	1000	750	463	250		

Drivers, Crew and Equipment Allocation							
Driver and Heavy Duty Equipment				Crew and Light Duty Equipment			Misc. Tools or Equipment
Driver	Tractor	Trailer	Mileage	Crew	Equipment	Mileage	Required or Requested
Total Heavy Duty Mileage			0	Total Light Duty Mileage		0	

G Neat	135	G Neat	75	G Neat	270		
Desc	Qty	Rate	Total	Desc	Qty	Rate	Total
G Neat			\$0.00	Sugar			\$0.00
G Neat			\$0.00	Lq Retarder			\$0.00
G Neat			\$0.00	Calcium Chloride			\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00
		\$0.00	\$0.00			\$0.00	\$0.00

Ticket total \$0.00

Print Sign Date

See page 2 for job log and any necessary remarks



PO Box 329
 Ft. Lupton, CO 80621
 (303) 654-9202

"Here Safety meets Quality at the Axis of Efficiency"

Date of Service	Customer	Consultant	Well Name	Last Tckt	Ticket #
9/13/2025	Bison	DAVE DONOHO	FREEMAN 1	Yes	5690
State	County	API	Rig	Mileage	Operator
Colorado	Weld	05-123-07087	AXIS 2724	130	0

Job Specific Remarks

--	--	--	--	--	--


Time	Injection		Pressure	Slurry		Job Log
	Rate	BBL	PSI	Weight	Yield	
17:15						Left Axis yard 9/12/25
18:30						Arrived on location 9/12/25
18:45						JSA Spot and rig up 9/12/25
20:07						JSA Pump schedule w Rig Crew 9/12/25
20:15			4300			Pressure test 9/12/25
20:20	2	5	700	8.34	0	Break Circulation Fresh water 9/12/25
20:23	2	7.1	560	15.8	1.15	Mix and pump Cement 35 Sks+ Retarde 9/12/25
20:27	3.7	41.4	1000	8.34	0	Displace fresh water 9/12/25
20:38		120				Shutdown and release pressure 9/12/25
20:40						Standby for rig crew 9/12/25
21:30						JSA Pump schedule w Rig Crew 9/12/25
21:38	2	5	800	8.34	0	Break Circulation Fresh water 9/12/25
21:41	2.6	20.4	600	15.8	1.15	Mix and pump Cement 100 Sks+ Retarde 9/12/25
21:49	3.4	36.1	330	8.34	0	Displace fresh water 9/12/25
21:59		50				Shutdown and release pressure 9/12/25
22:00						Standby RIG CREW 9/12/25
0:30						JSA Pump schedule w Rig Crew 9/13/25
0:37	2	5	200	8.34	0	Break Circulation Fresh water 9/13/25
0:40	2.2	15.3	150	15.8	1.15	Mix and pump Cement 75 sks 2% CC 9/13/25
0:47	2.7	7.9	100	8.34	0	Displace fresh water 9/13/25
0:50			20			Shutdown and release pressure 9/13/25
0:55						Standby To Tag Cmt plug 3 9/13/25
7:30						JSA Pump schedule w Rig Crew 9/13/25
7:35	2	5	120	8.34	0	Break Circulation Fresh water 9/13/25
7:38	2.7	45	200	15.8	1.15	Mix and pump Cement 220 Sks 2%CC 9/13/25
7:55			30			Shutdown and release pressure 9/13/25
8:00						Standby To Tag Plug 4 9/13/25
12:30	2	5	120	8.34	0	Break Circulation Fresh water 9/13/25
12:33	2.1	8.2	170	15.8	1.15	Mix and pump Cement 40 sks 9/13/25
12:38			30			Shutdown and release pressure 9/13/25
12:45						Standby for rig crew 9/13/25
13:15	0.5	2	0	15.8	1.15	Top Off Well 10 Sks 9/13/25
13:20						Shutdown 9/13/25
13:25						Wash Pumps & Lines 9/13/25
13:35						JSA Rig down Cement equipment 9/13/25
14:00						Leave location 9/13/25
15:30						Arrive back at Axis yard 9/13/25

--	--	--	--	--	--

Customer Name (print)	(sign)	(Date)	Date of Service	9/13/2025
			Ticket total	\$0.00


FREEMAN 1 PLUG #1

CEMENTING

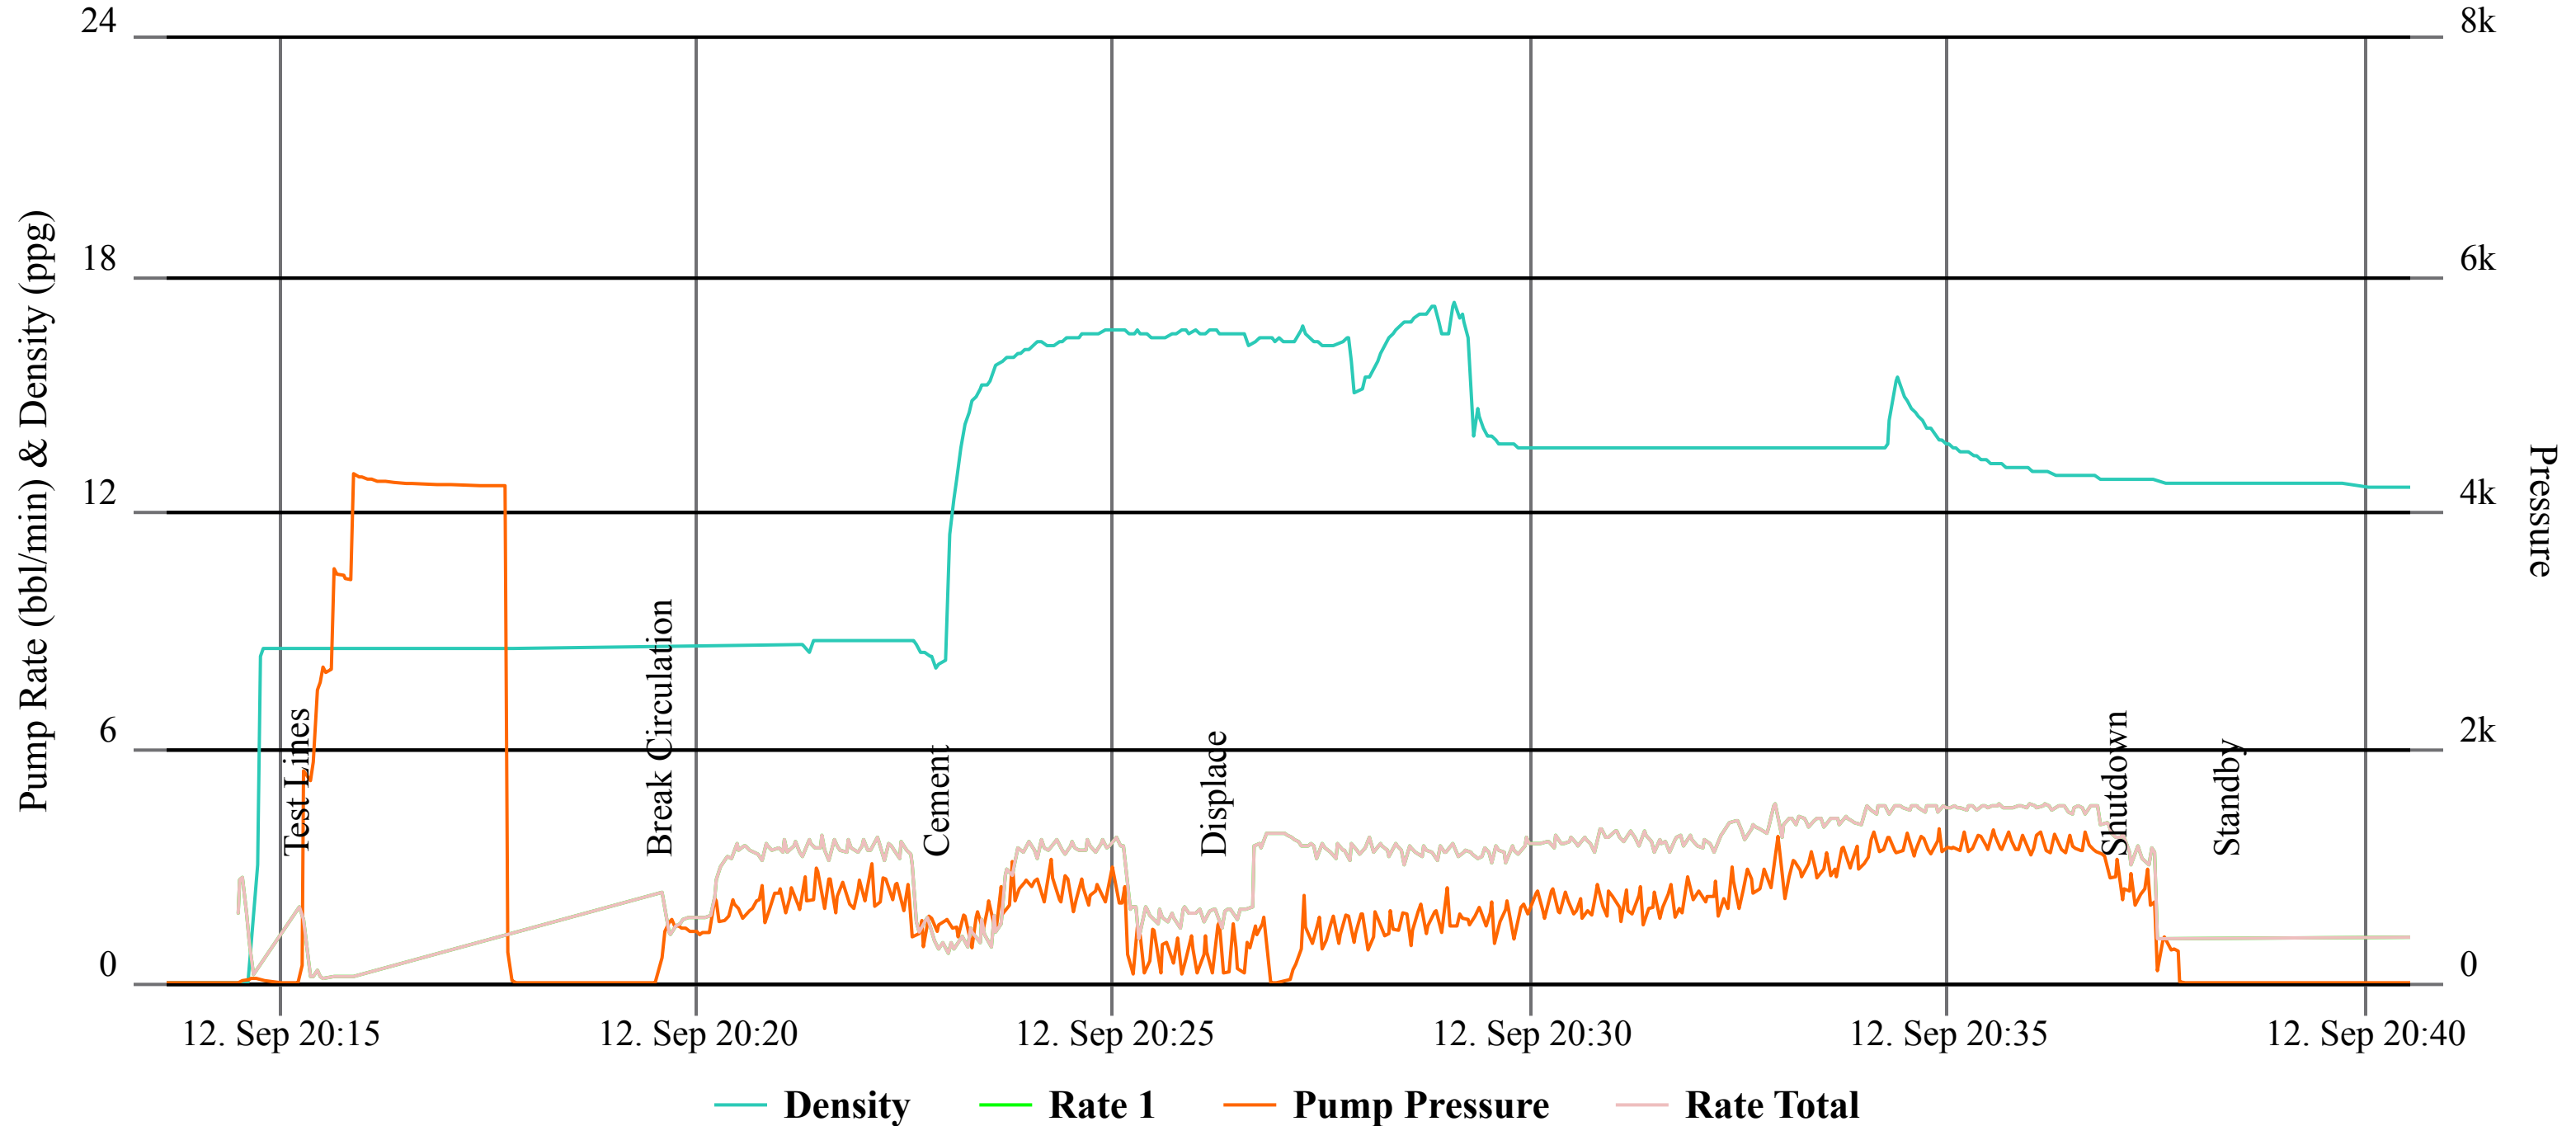


FREEMAN 1 PLUG #2

CEMENTING

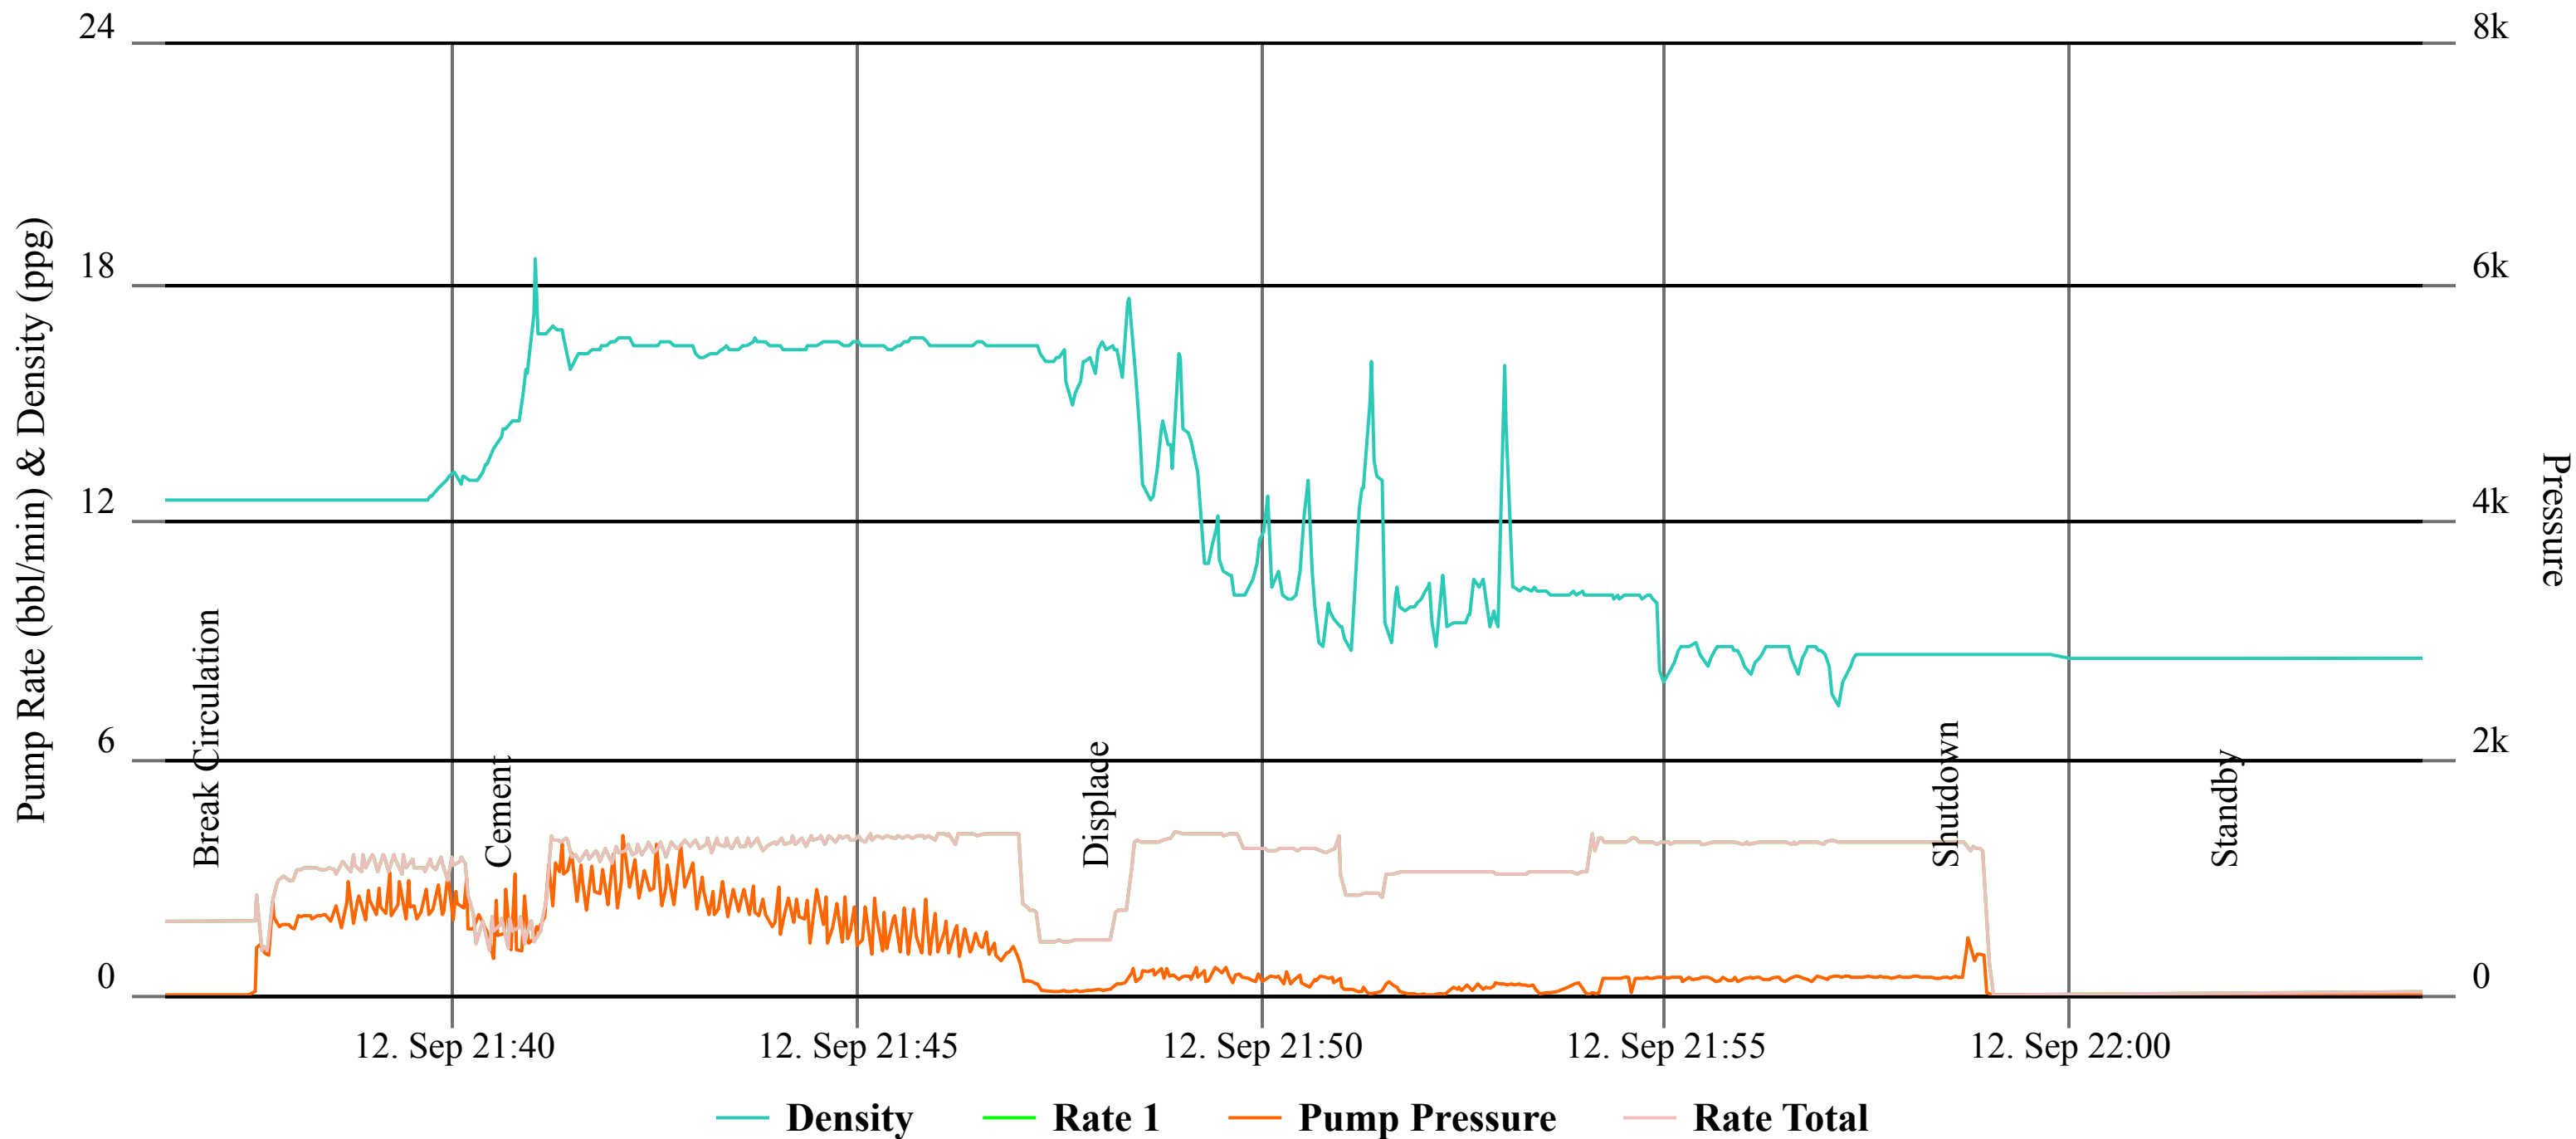


FREEMAN 1 PLUG #3

CEMENTING

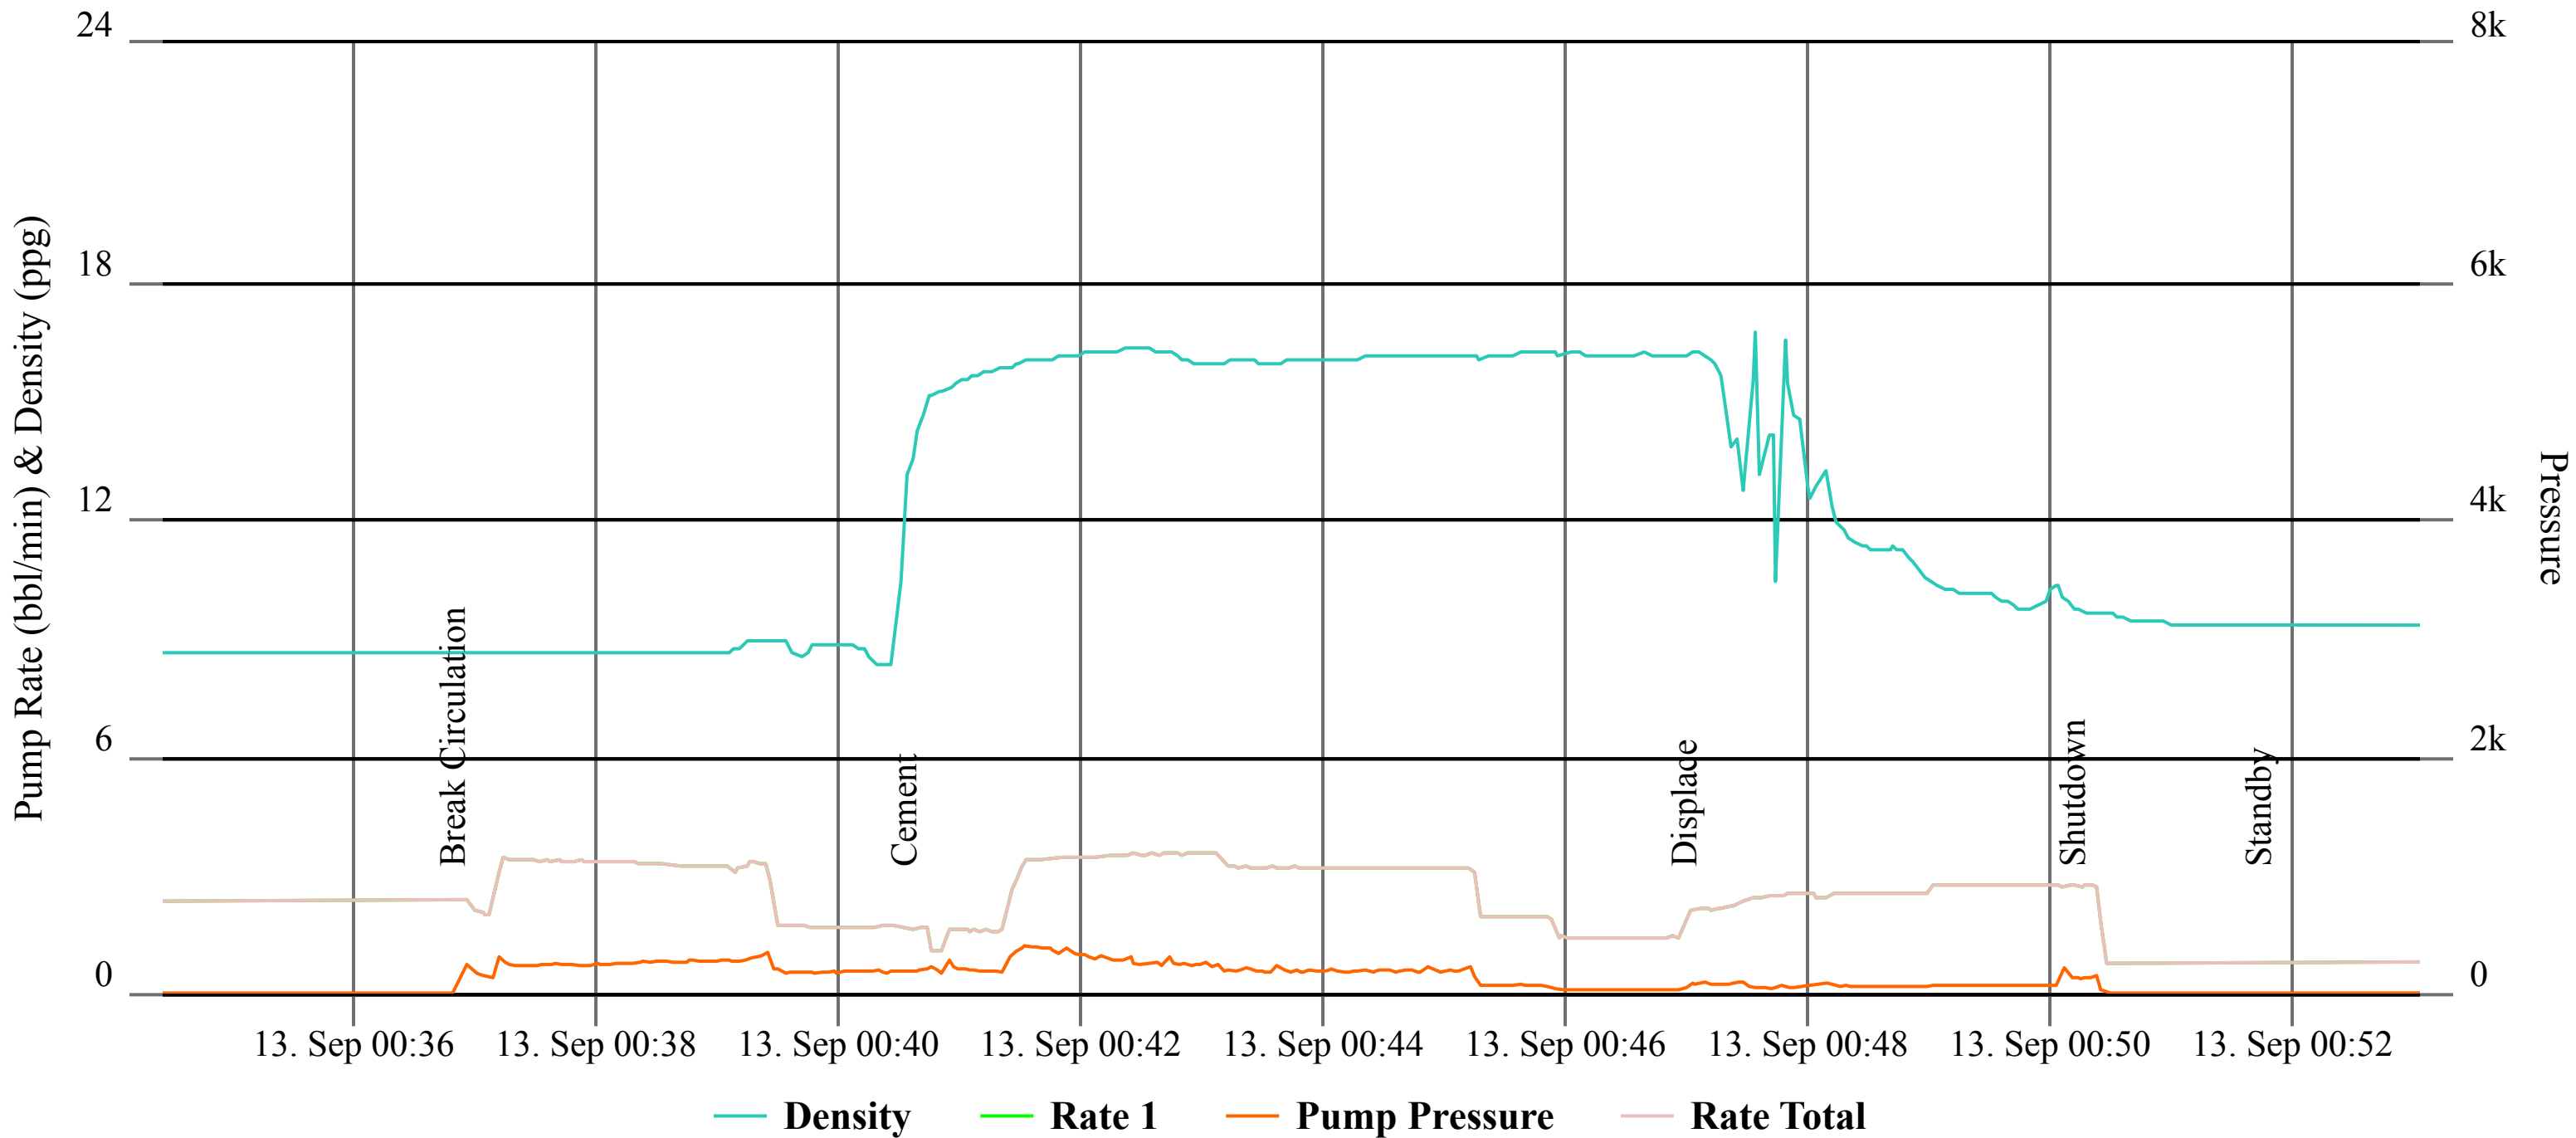

FREEMAN 1 PLUG #4

CEMENTING

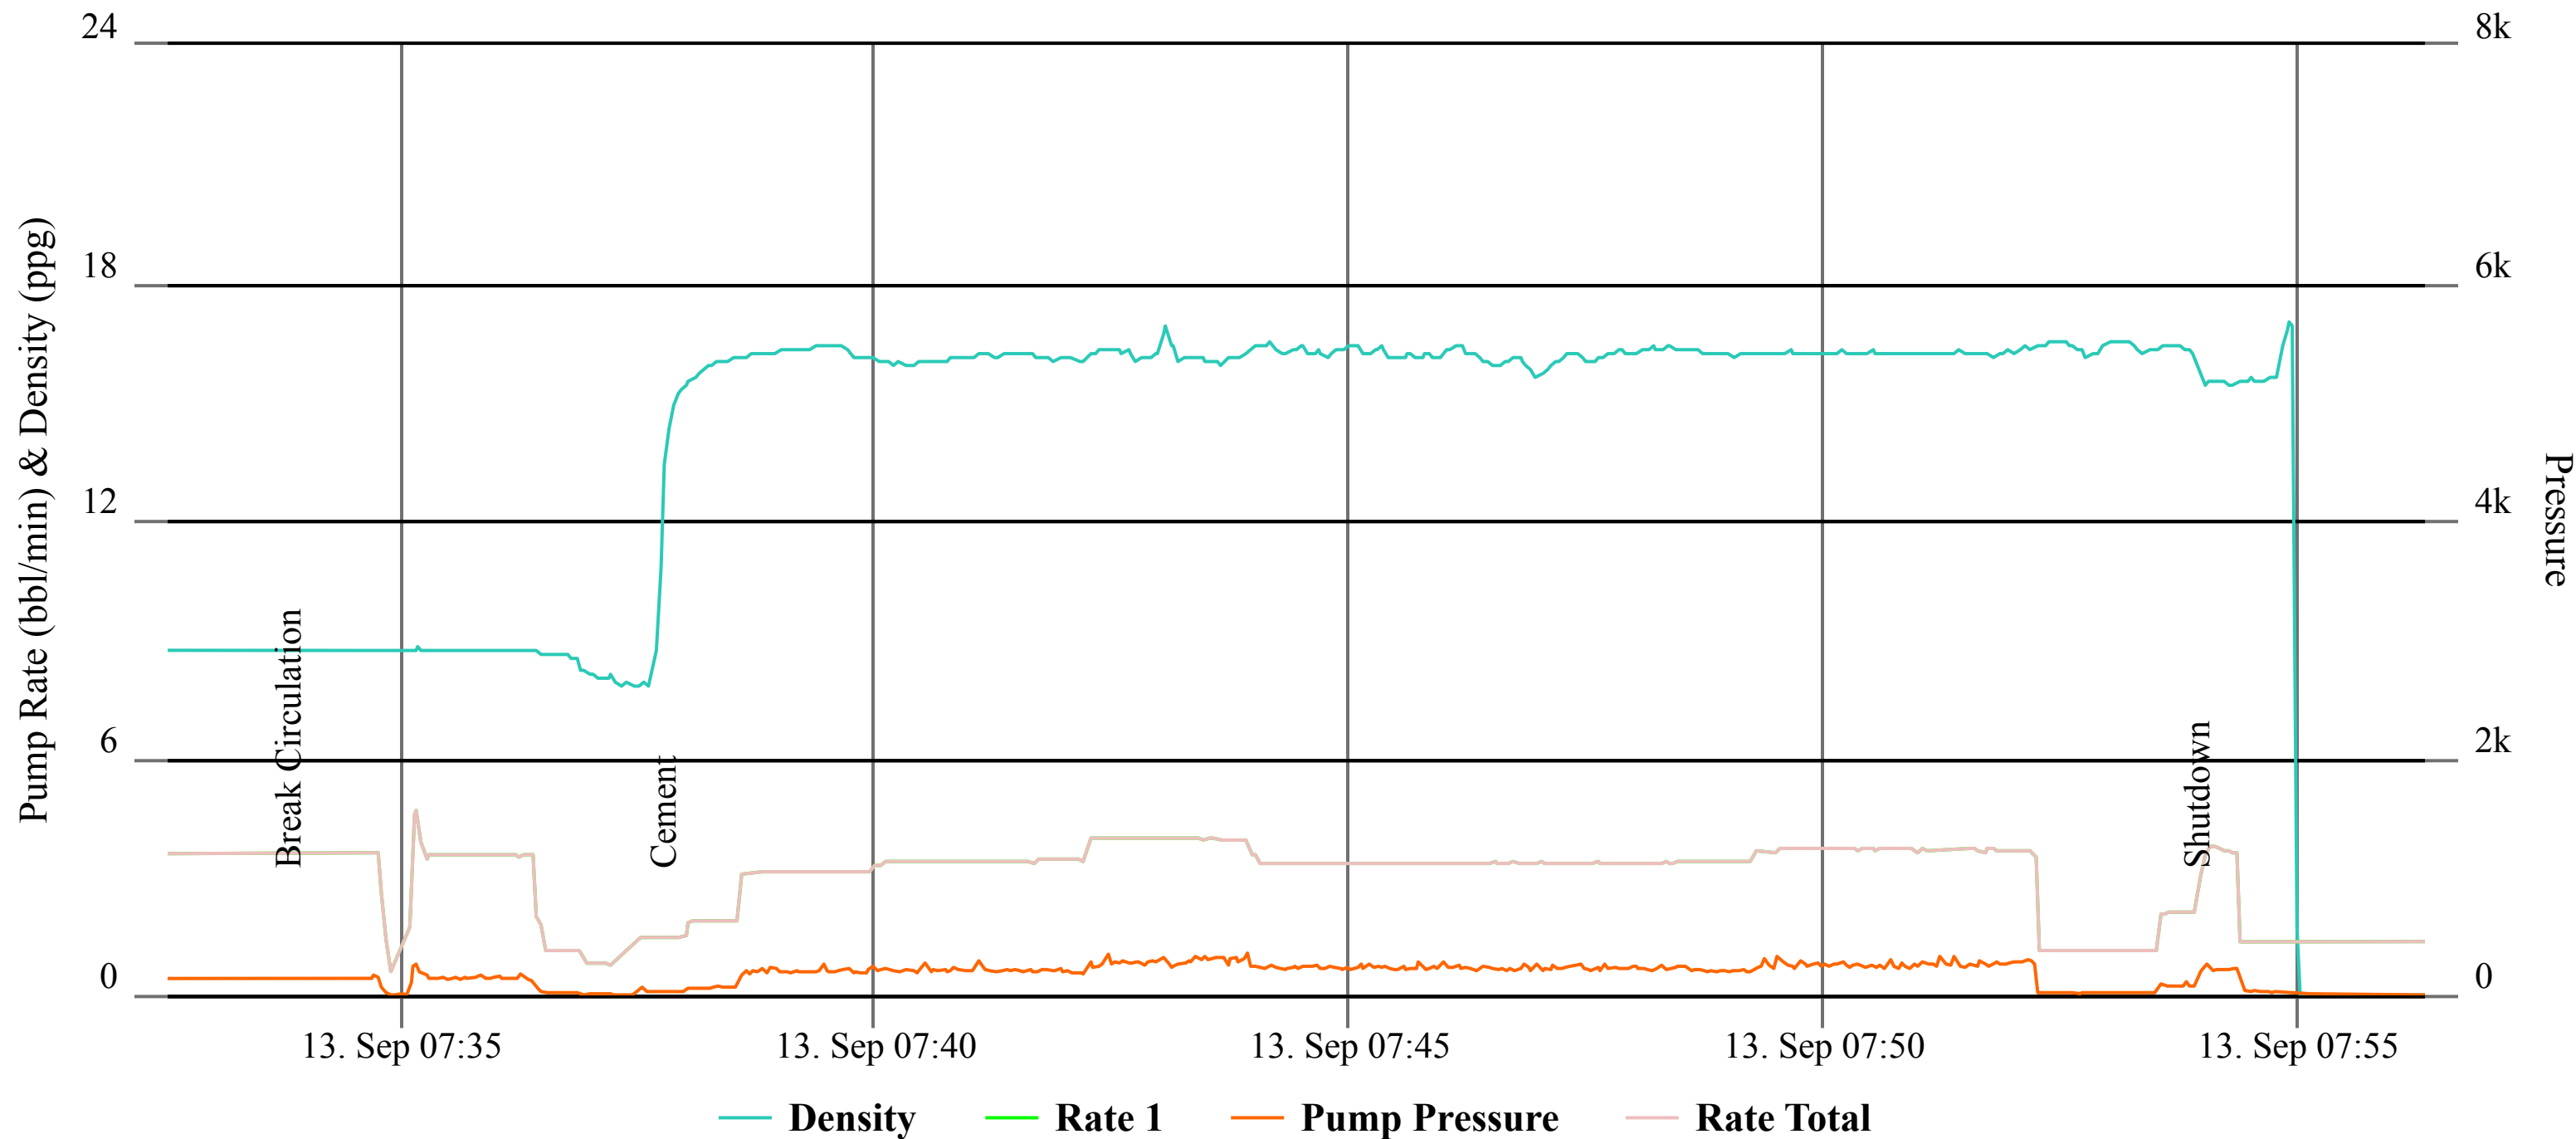

FREEMAN 1 PLUG #5

CEMENTING

