
WILLIAMS PRODUCTION RMT INC - EBUS

**GM 313-27
GRAND VALLEY
Garfield County , Colorado**

Cement Surface Casing
20-May-2011

Post Job Report

HALLIBURTON

Cementing Job Log

The Road to Excellence Starts with Safety

Sold To #: 300721	Ship To #: 2853371	Quote #:	Sales Order #: 8170994
Customer: WILLIAMS PRODUCTION RMT INC - EBUS		Customer Rep: Oaks, Rick	
Well Name: GM	Well #: 313-27	API/UWI #:	
Field: GRANDVALLEY	City (SAP):	County/Parish: Garfield	State: Colorado
Legal Description:			
Lat:		Long:	
Contractor: H&P 278		Rig/Platform Name/Num: H&P 278	
Job Purpose: Cement Surface Casing		Ticket Amount:	
Well Type: Development Well		Job Type: Cement Surface Casing	
Sales Person: KOHL, KYLE		Srv Supervisor: HUGENTOBLE, LOGAN	MBU ID Emp #: 447333

Activity Description	Date/Time	Cht #	Rate bbl/min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Call Out	05/20/2011 08:00							
Pre-Convoy Safety Meeting	05/20/2011 08:55							ALL HES EMPLOYEES
Arrive At Loc	05/20/2011 11:00							RIG STILL RUNNING CASING
Assessment Of Location Safety Meeting	05/20/2011 11:15							ALL HES EMPLOYEES
Rig-Up Equipment	05/20/2011 11:20							1 HT-400 PUMP TRUCK, 1 660 BULK TRUCK, 1 F-450 P/U, 1 QUICK LATCH PLUG CONTAINER
Pre-Job Safety Meeting	05/20/2011 14:10							ALL HES EMPLOYEES, RIG CREW, CO REP AND ANY 3RD PARTY VENDORS
Start Job	05/20/2011 14:26							TP 1223.1 FT, TD 1240 FT, FC 1180.4 FT, HOLE 13.5", MUD WT 10.1 PPG, RATE WILL BE 8-10-2, WILL BUMP 500 PSI OVER LAND PSI, RIG CIRCULATED HOLE FOR 1 HRS
Pump Water	05/20/2011 14:28		2	2			68.0	FILL LINES PRIOR TO PRESSURE TESTING LINES
Pressure Test	05/20/2011 14:31							NO LEAKS, KICK OUTS SET TO 3000 PSI FOR TEST.
Pump Spacer 1	05/20/2011 14:35		6	20			98.0	FRESH WATER
Activity Description	Date/Time	Cht	Rate bbl/min	Volume bbl		Pressure psig		Comments

Sold To #: 300721

Ship To #: 2853371

Quote #:

Sales Order #: 8170994

SUMMIT Version: 7.20.130

Friday, May 20, 2011 04:42:00

HALLIBURTON

Cementing Job Log

		#		Stage	Total	Tubing	Casing	
Pump Lead Cement	05/20/2011 14:44		6	67			246.0	160 SKS VERSACEM CMT TO BE MIXED AT 12.3 PPG, 2.38 YIELD, 13.75 GAL/SK, CMT TO BE WEIGHED VIA PRESSURE BALANCED MUD SCALES WET AND DRY SAMPLES SUBMITTED.
Pump Tail Cement	05/20/2011 14:54		6	60			267.0	160 SKS VERSACEM CMT TO BE MIXED AT 12.8 PPG, 2.38 YIELD, 11.75 GAL/SK, CMT TO BE WEIGHED VIA PRESSURE BALANCED MUD SCALES, WET AND DRY SAMPLES SUBMITTED.
Shutdown	05/20/2011 15:05							
Drop Plug	05/20/2011 15:09							PLUG LAUNCHED
Pump Displacement	05/20/2011 15:10		10	92			572.0	FRESH WATER 20BBLs CEMENT TO SURFACE
Slow Rate	05/20/2011 15:20		2				291.0	10 BBLs PRIOR TO CALCULATED DISPLACEMENT
Bump Plug	05/20/2011 15:25						799.0	PLUG LANDED
Check Floats	05/20/2011 15:27							FLOATS HOLDING
End Job	05/20/2011 15:28							THANK YOU FOR USING HES LOGAN HUGENTOBLE AND CREW
Post-Job Safety Meeting (Pre Rig-Down)	05/20/2011 15:30							ALL HES EMPLOYEES
Rig-Down Equipment	05/20/2011 15:40							
Pre-Convoy Safety Meeting	05/20/2011 17:30							ALL HES EMPLOYEES
Crew Leave Location	05/20/2011 17:35							LOCATION CLEAN

Sold To #: 300721

Ship To #: 2853371


Quote #:

Sales Order #: 8170994

SUMMIT Version: 7.20.130

Friday, May 20, 2011 04:42:00

WILLIAMS 9.625 SURFACE

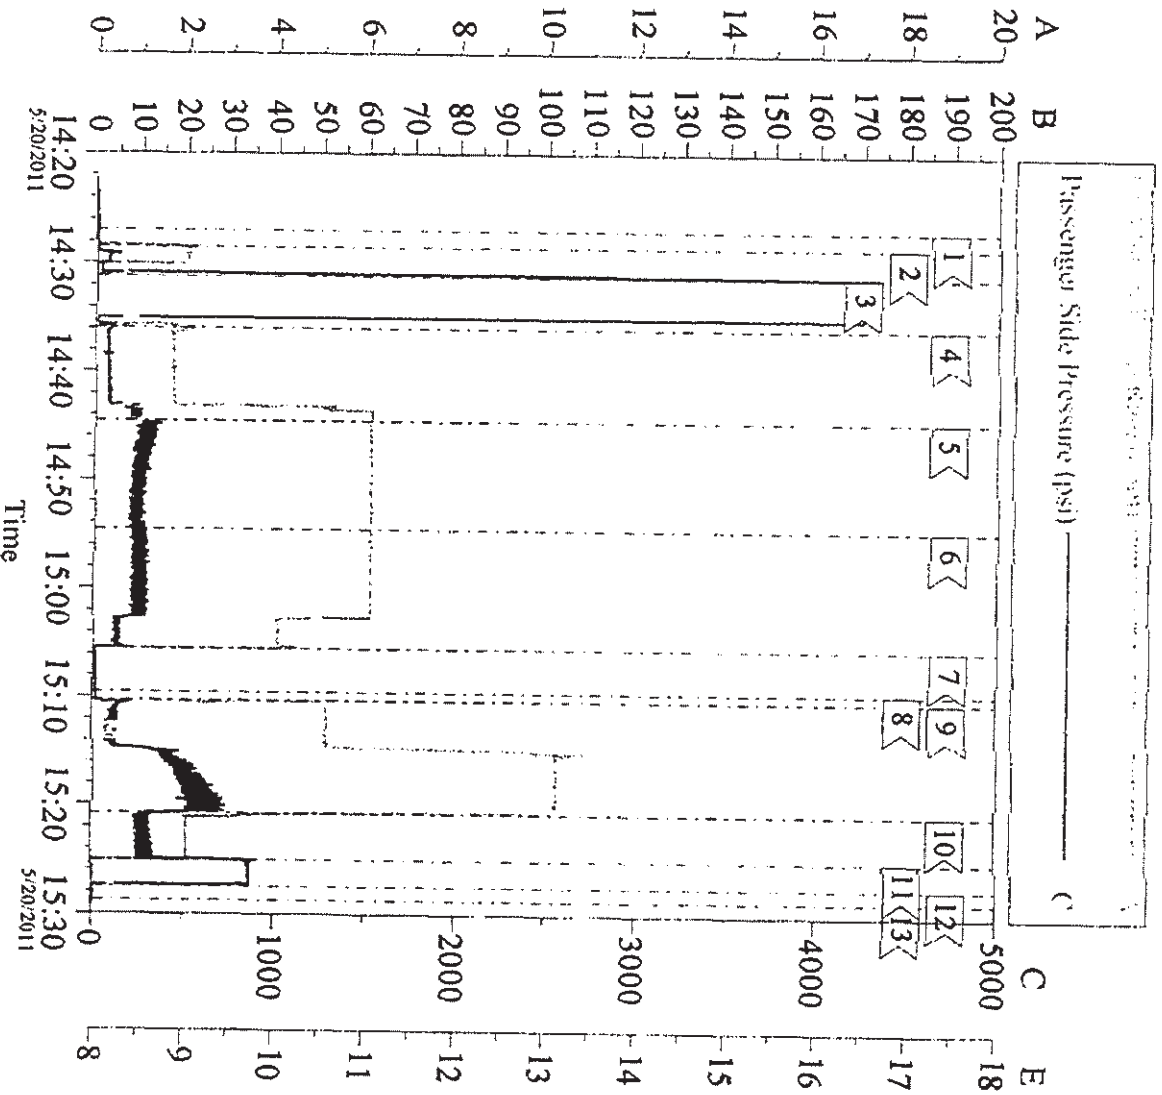

Local Event Log		
1	START JOB	14:26:58
2	PRIME LINES	14:28:32
3	PRESSURE TEST	14:31:10
4	PUMP H2O SPACER	14:35:59
5	PUMP LEAD CEMENT	14:44:34
6	PUMP TAIL CEMENT	14:54:37
7	SHUTDOWN	15:05:28
8	DROP PLUG	15:09:30
9	PUMP DISPLACEMENT	15:10:17
10	SLOW RATE	15:20:48
11	BUMP PLUG	15:25:05
12	CHECK FLOATS	15:27:33
13	END JOB	15:28:46
