


Downhole Schematic for Federal Savage 11-3C (RD11)

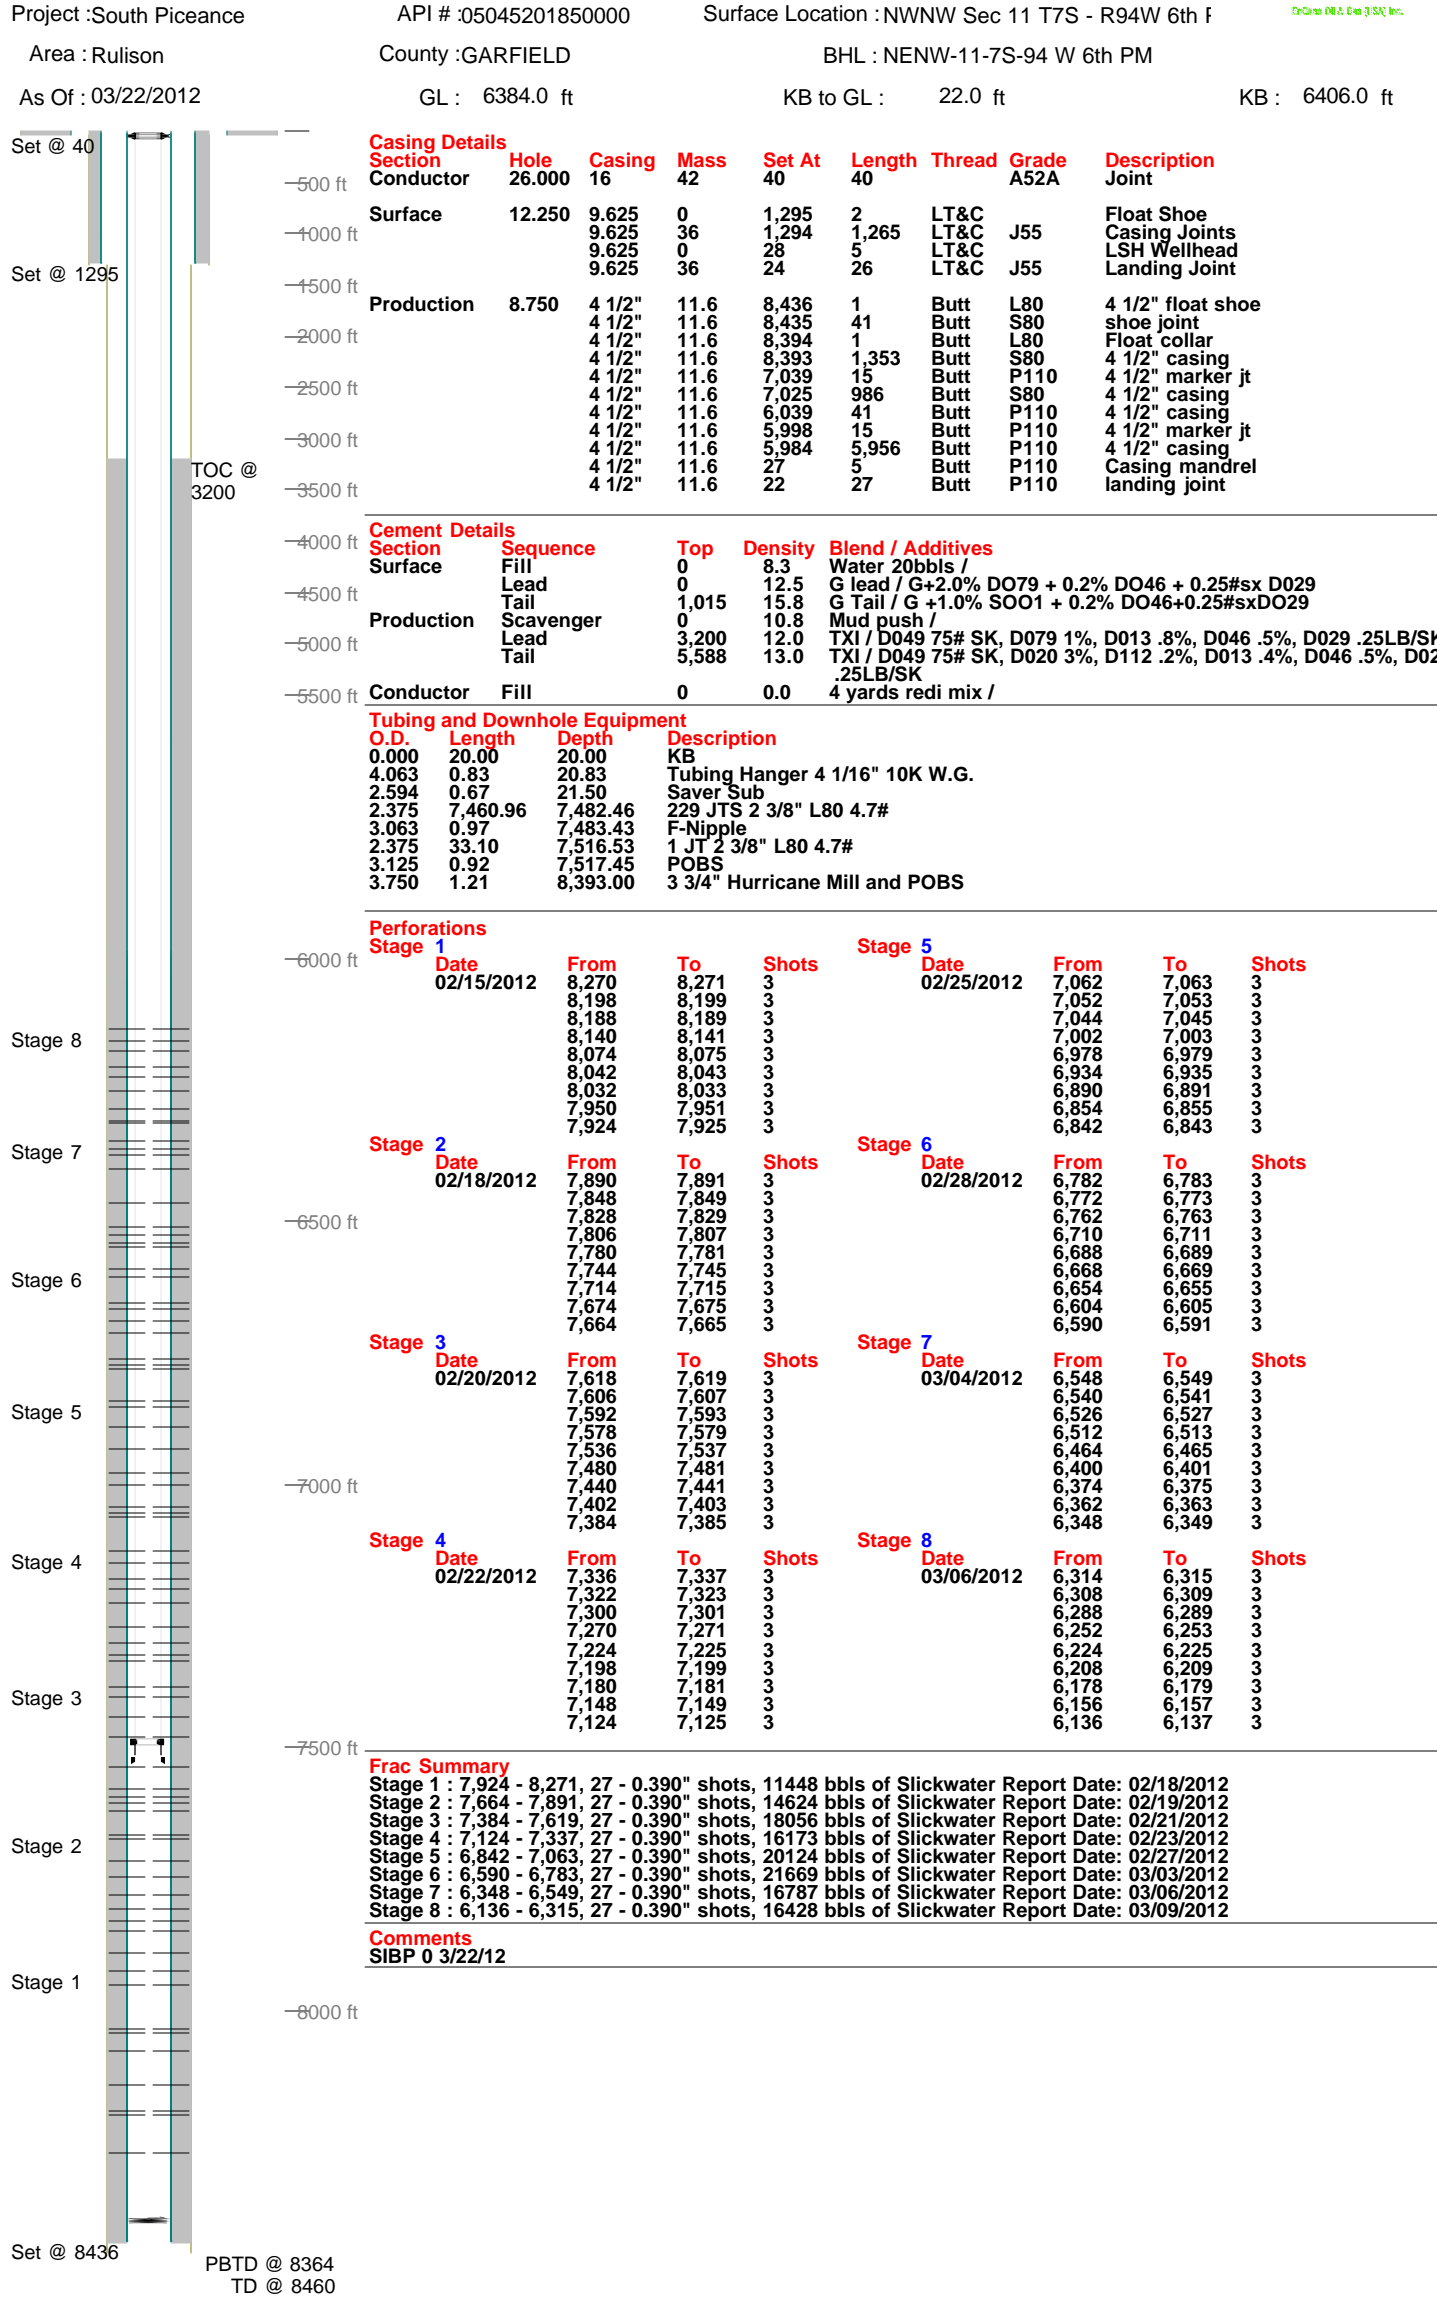

Frac Summary

Stage 1 : 7,924 - 8,271, 27 - 0.390" shots, 11448 bbls of Slickwater Report Date: 02/18/2012

Stage 2 : 7,664 - 7,891, 27 - 0.390" shots, 14624 bbls of Slickwater Report Date: 02/19/2012

Stage 3 : 7,384 - 7,619, 27 - 0.390" shots, 18056 bbls of Slickwater Report Date: 02/21/2012

Stage 4 : 7,124 - 7,337, 27 - 0.390" shots, 16173 bbls of Slickwater Report Date: 02/23/2012

Stage 5 : 6,842 - 7,063, 27 - 0.390" shots, 20124 bbls of Slickwater Report Date: 02/27/2012

Stage 6 : 6,590 - 6,783, 27 - 0.390" shots, 21669 bbls of Slickwater Report Date: 03/03/2012

Stage 7 : 6,348 - 6,549, 27 - 0.390" shots, 16787 bbls of Slickwater Report Date: 03/06/2012

Stage 8 : 6,136 - 6,315, 27 - 0.390" shots, 16428 bbls of Slickwater Report Date: 03/09/2012

Comments

SIBP 0 3/22/12

PBTD @ 8364

TD @ 8460
