


Spud Date: 03-04-12

Log Tops

Sussex	4253'
Niobrara	7331'
Codell	7590'
J Sand	7999'

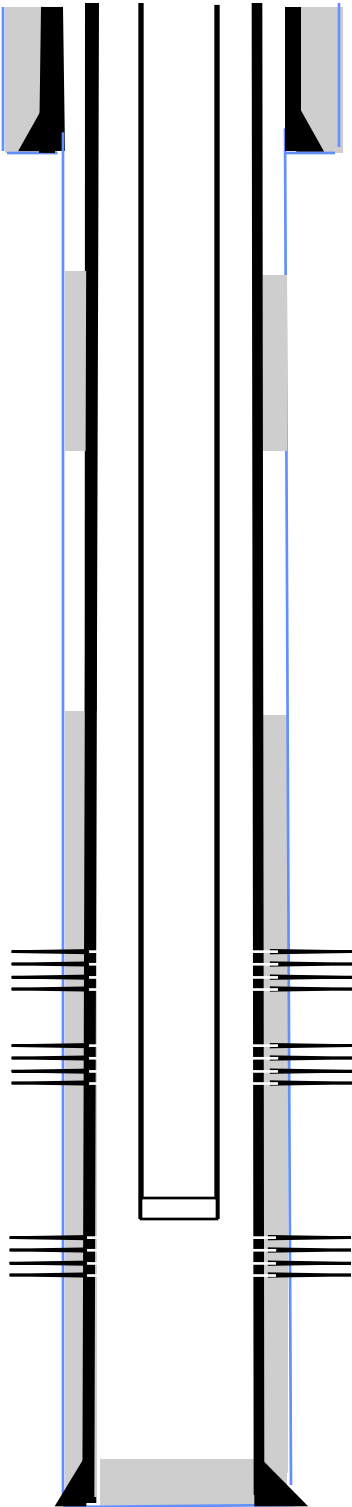

Surface Casing and Cement
8 5/8" , landed @ 1007',cemented with 510 sxs

Main Hole
7-7/8" to TD

Production Casing and Cement
4-1/2" , landed @ 8170',cemented with 680 sxs

CBP
Set @ 7160'. 04-11-13
Drilled out on 04-12-13

Perf'd the Niobrara 7394-7406' @ 4 spf
Frac'd the Niobrara 7394-7406' , (48 holes), w/ 98,238 gals 18 # Vistar Hybrid cross linked gel containing 250,320 # 30/50 sand. 09-25-12

RBP
Set @ 7440'. 09-25-12
Drilled out on 04-13-13

Perf'd the Codell from 7,592-7606' @ 3 spf
Frac'd the Codell 7,592-7606' (42 holes) w/ 87,570 gal 22# Vistar Hybrid cross linked gel containing 250,880 # 30/50 sand. 09-25-12

RBP
Set @ 7650'. 09-25-12
Drilled out on 04-13-13

Perf'd the J Sand from 7869-7893' @ 2 spf
Frac'd the J-Sand 7869-7893' , (48 holes)w/ 63,378gal 18 # Vistar Hybrid cross linked gel containing 250,460 # 20/40 Sand. 09-25-12

Production Tubing
2-3/8" , Set @ 7850.48'
