

New Frontier Energy

Battle Mountain 13-5

Black/Grey items are existing as of the last report in 2008

kws

Current 11-21-2008


WI/NRI:

KB: 11.0'

Spud: 01-Dec-07

GL:

Comp:

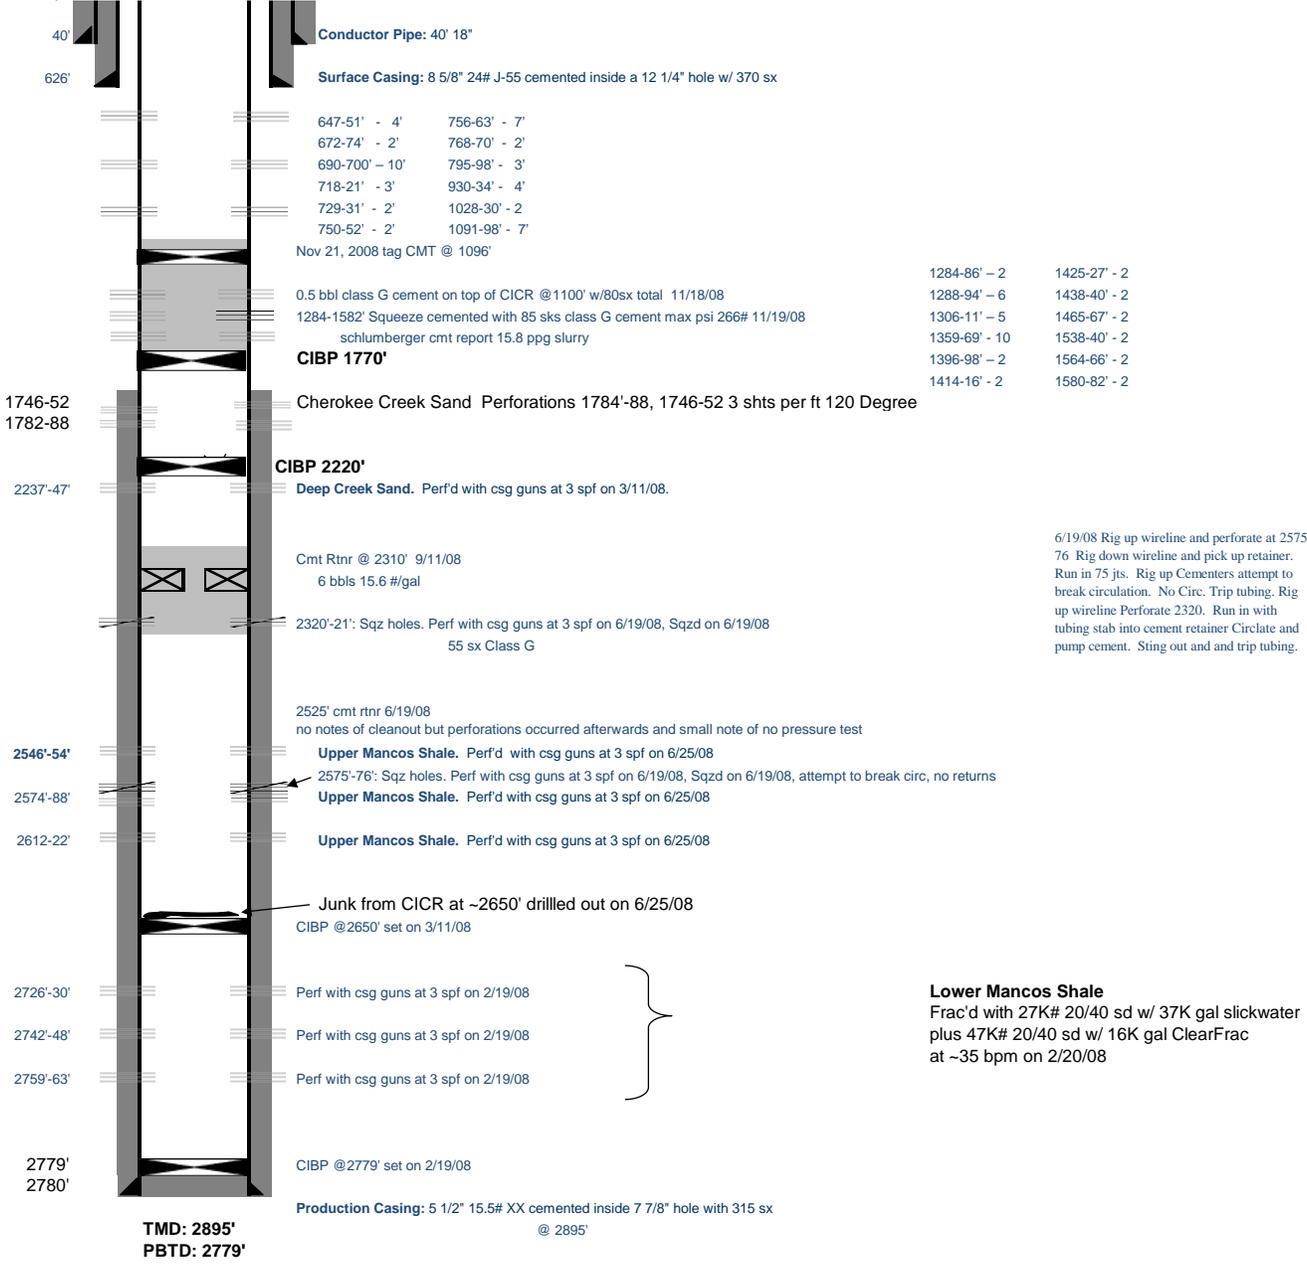

1284-86' - 2	1425-27' - 2
1288-94' - 6	1438-40' - 2
1306-11' - 5	1465-67' - 2
1359-69' - 10	1538-40' - 2
1396-98' - 2	1564-66' - 2
1414-16' - 2	1580-82' - 2

6/19/08 Rig up wireline and perforate at 2575-76 Rig down wireline and pick up retainer. Run in 75 jts. Rig up Cementers attempt to break circulation. No Circ. Trip tubing. Rig up wireline Perforate 2320. Run in with tubing stab into cement retainer Circulate and pump cement. Sting out and and trip tubing.

Lower Mancos Shale
Frac'd with 27K# 20/40 sd w/ 37K gal slickwater plus 47K# 20/40 sd w/ 16K gal ClearFrac at ~35 bpm on 2/20/08

Entek GRB LLC

Battle Mountain 13-5

Black/Grey items are existing as of the last report in 2008
 Red items are proposed for P&A purposes.

kws
Proposed ks 2013

WI/NRI:
 Spud: 01-Dec-07
 Comp:

KB: 11.0'
 GL:

