


HALLIBURTON

CONOCO/PHILLIPS COMPANY EBUSINESS

**Cline 4-64 2-1H
WILDCAT
Arapahoe County , Colorado**

**Cement Surface Casing
15-Oct-2013**

Job Site Documents

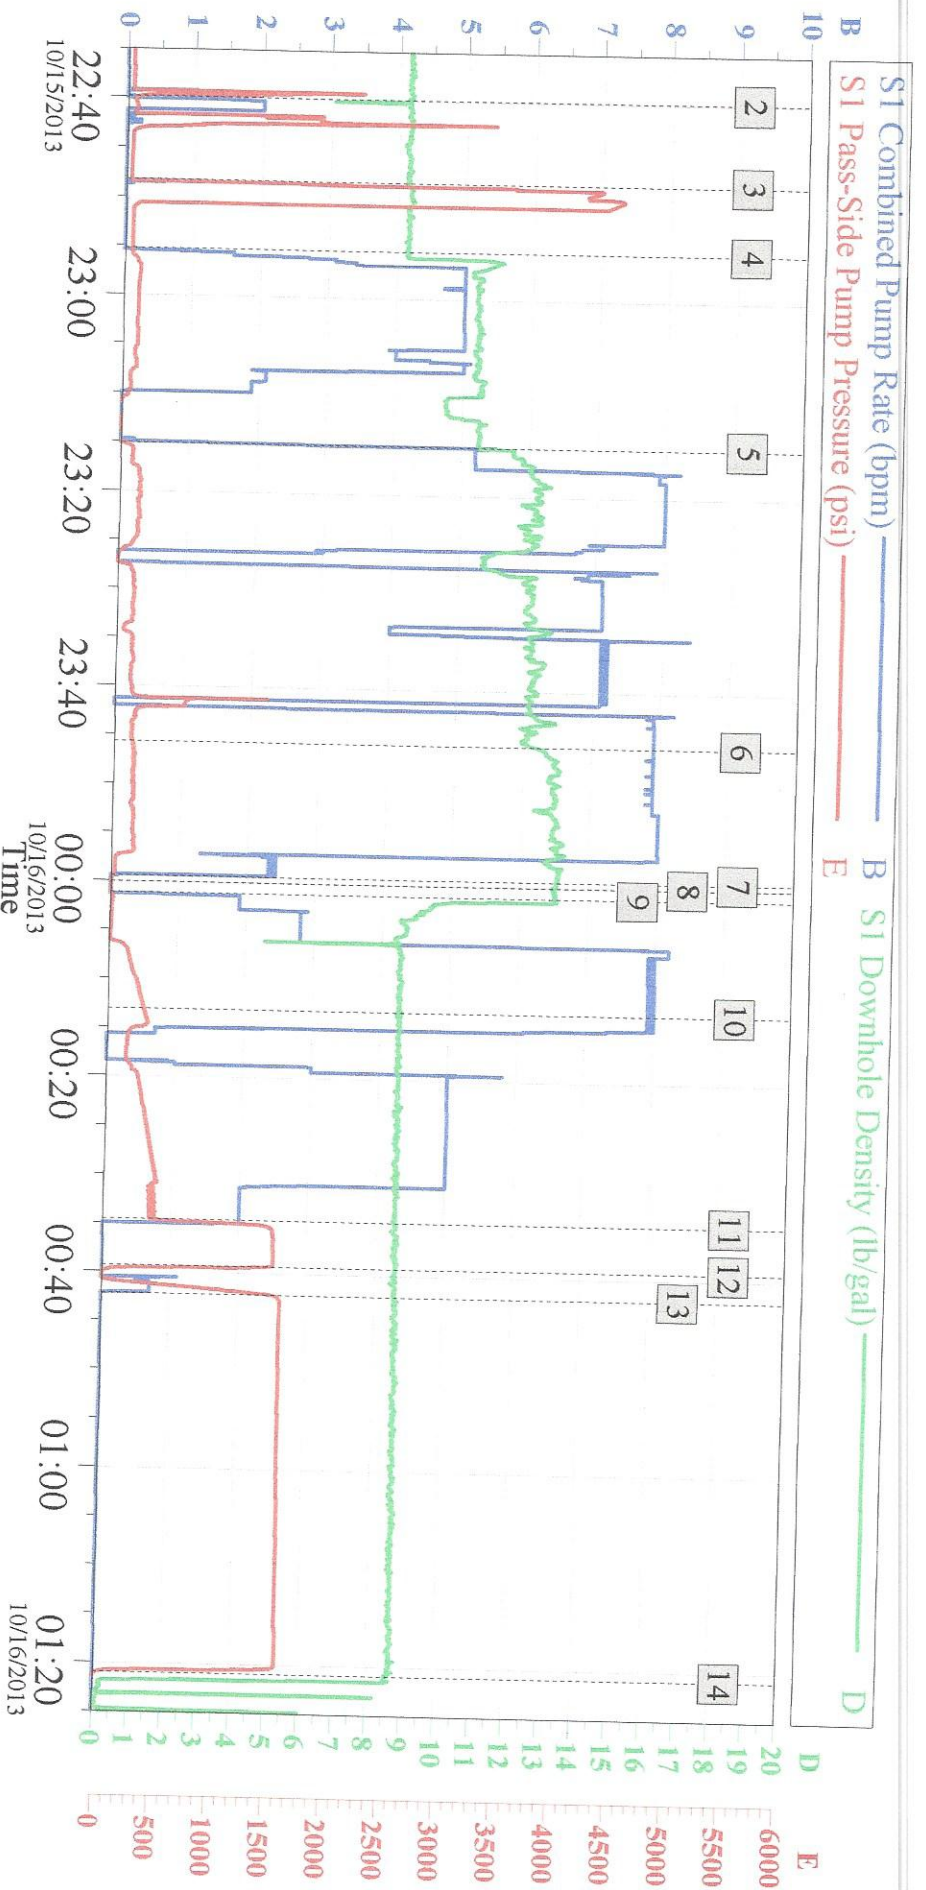

Customer: Conoco Phillips
 Well Description: Cline 4-64 2-1H

Job Date: 15-Oct-2013
 Job Type: Surface

Sales Order #: 900820018
 Supervisor: McBride

The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900820018
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Tolman, Ben	
Well Name: Cline	Well #: 4-64 2-1H	API/UWI #: 05-005-07212	
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Job Purpose: Cement Surface Casing			
Well Type: Development Well		Job Type: Cement Surface Casing	
Sales Person: GROFF, THEODORE		Srv Supervisor: MCBRIDE, NATHAN MBU ID Emp #: 313810	

Job Personnel

HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #
MARKOVICH, STEVEN Michael	8.2	502964	MCBRIDE, NATHAN Charles	8.2	313810			

Equipment

HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way
10025030	50 mile	11036295C	50 mile	11562562	50 mile	11645063	50 mile
12010170	50 mile						

Job Hours

Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours
TOTAL								

Total is the sum of each column separately

Job

Formation Name	Formation Depth (MD)	Top	Bottom	Form Type	Job depth MD	Job Depth TVD	Water Depth	Wk Ht Above Floor	Perforation Depth (MD)	From	To	Called Out	Date	Time	Time Zone
				BHST	1890. ft	1890. ft		5. ft					15 - Oct - 2013	14:00	MST
												On Location	15 - Oct - 2013	18:20	MST
												Job Started	15 - Oct - 2013	22:38	MST
												Job Completed	15 - Oct - 2013	01:21	MST
												Departed Loc	15 - Oct - 2013	02:30	MST

Well Data

Description	New / Used	Max pressure psig	Size in	ID in	Weight lbm/ft	Thread	Grade	Top MD ft	Bottom MD ft	Top TVD ft	Bottom TVD ft
13-1/2" Open Hole				13.5				100.	1890.		
16" Casing	Unknown		16.	15.5					100.		
9-5/8" Casing	Mixed		9.625	8.921	36.	STC	J-55		1890.		

Sales/Rental/3rd Party (HES)

Description	Qty	Qty uom	Depth	Supplier
CMT SURFACE CASING BOM	0	JOB		
SHOE,FLT,9-5/8 8RD,2-3/4 SUPER SEAL	1	EA		
CLR,FLT,9-5/8 8RD 29.3-40PPF,2-3/4	1	EA		
CENTRALIZER-9-5/8"-CSG-12 1/4"-HINGED	25	EA		
COLLAR-STOP-9 5/8"-FRICTION-HINGED	1	EA		
KIT,HALL WELD-A	1	EA		
MILEAGE FOR CEMENTING CREW,ZI	100	MI		

Tools and Accessories

Type	Size	Qty	Make	Depth	Type	Size	Qty	Make	Depth	Type	Size	Qty	Make
Guide Shoe					Packer					Top Plug			
Float Shoe					Bridge Plug					Bottom Plug			
Float Collar					Retainer					SSR plug set			
Insert Float										Plug Container			
Stage Tool										Centralizers			

The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900820018
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Tolman, Ben	
Well Name: Cline	Well #: 4-64 2-1H	API/UWI #: 05-005-07212	
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Contractor:	Rig/Platform Name/Num: H&P 280		
Job Purpose: Cement Surface Casing	Ticket Amount:		
Well Type: Development Well	Job Type: Cement Surface Casing		
Sales Person: GROFF, THEODORE	Srvc Supervisor: MCBRIDE, NATHAN	MBU ID Emp #: 313810	

Activity Description	Date/Time	Cht #	Rate bbl/min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Arrive at Location from Service Center	10/15/2013 18:20							All equipment and materials on location Rig Running Casing
Assessment Of Location Safety Meeting	10/15/2013 18:45							Hazard Hunt and review fluid location, wash up and truck layout
Pre-Rig Up Safety Meeting	10/15/2013 19:10							Review JSA
Rig-Up Equipment	10/15/2013 19:40							
Casing on Bottom	10/15/2013 19:45							
Circulate Well	10/15/2013 19:50							
Rig-Up Completed	10/15/2013 20:30							
Pre-Job Safety Meeting	10/15/2013 21:00							Safety Meeting end at 2130. Unload head and pick up to rig floor. 2120. Wait on rig to finish circulating, rig down casing running tool, and blow down system.
Start Job	10/15/2013 22:38							
Pump Water	10/15/2013 22:39		2	2			120.0	Fill Lines
Test Lines	10/15/2013 22:48						4218.0	
Pump Spacer	10/15/2013 22:55		5	50			128.0	Clean Spacer III @ 10.5ppg 3.86yield, 24.21gal/sk
Drop Bottom Plug	10/15/2013 23:12							
Pump Lead Cement	10/15/2013 23:15		7	184.7			240.0	405sks @ 12.0ppg, 2.56yield, 15.09gal/sk

Sold To #: 352431

Ship To #: 3108240

Quote #:

Sales Order #: 900820018

Cementing Job Log

Activity Description	Date/Time	Cht #	Rate bbl/ min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Pump Tail Cement	10/15/2013 23:45		7	69.8			190.0	195sks @ 13.0ppg, 2.01yield, 10.99gal/sk
Drop Top Plug	10/16/2013 00:00							
Pump Displacement	10/16/2013 00:01		5	142.9				Fresh Water
Spacer Returns to Surface	10/16/2013 00:05							8bbls into Displacement
Cement Returns to Surface	10/16/2013 00:13							58bbls Displaced 85bbls to Surface
Comment	10/16/2013 00:16							Shut down due to rig pump pinching off and not being able to move cement out of cellar.
Bump Plug	10/16/2013 00:34						600.0	500psi Over 1475 Final bump Pressure
Check Floats	10/16/2013 00:39							Floats Good
Pressure Test	10/16/2013 00:42							Test Casing 1500pis/ 30 Minutes 1560 Start Pressure 1600 End Pressure
End Job	10/16/2013 01:21							Thanks McBride and Crew

Sold To #: 352431

Ship To #: 3108240

Quote #:

Sales Order #: 900820018

HALLIBURTON


CONOCO/PHILLIPS COMPANY EBUSINESS

Cline 4-64 2-1H
WILDCAT
Arapahoe County , Colorado

Cement Intermediate Casing
22-Oct-2013

Job Site Documents

ConocoPhillips Cline 4-64 2-1H Intermediate

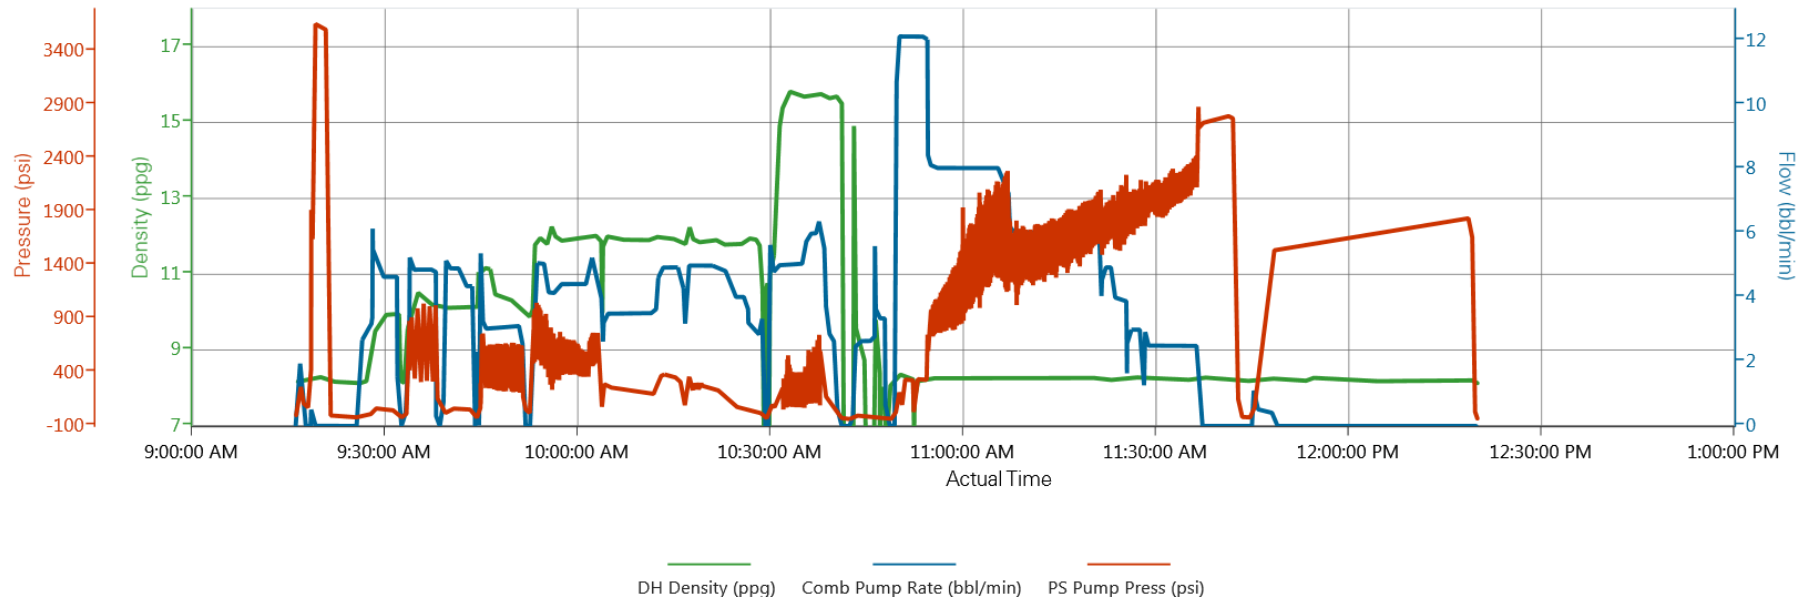

Cementing Job Log

The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900834442
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Tolman, Ben	
Well Name: Cline	Well #: 4-64 2-1H	API/UWI #: 05-005-07212	
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Contractor:		Rig/Platform Name/Num: H&P 280	
Job Purpose: Cement Intermediate Casing		Ticket Amount:	
Well Type: Development Well		Job Type: Cement Intermediate Casing	
Sales Person: GROFF, THEODORE		Srv Supervisor: SMITH, AARON	MBU ID Emp #: 518187

Activity Description	Date/Time	Cht #	Rate bbl/ min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Arrive at Location from Service Center	10/21/2013 12:30							
Assessment Of Location Safety Meeting	10/21/2013 13:00							
Casing on Bottom	10/21/2013 13:20							WITH ALL EQUIPMENT AND MATERIALS,
Circulate Well	10/21/2013 13:20							
Pre-Rig Up Safety Meeting	10/21/2013 13:20							RIG UP JSA WITH CREW AND SAFETY REP.
Rig-Up Equipment	10/21/2013 13:30							
Rig-Up Completed	10/21/2013 14:10							
Clean Lines	10/21/2013 14:19							WASH PUMPS AND LINES TO PIT
Pre-Job Safety Meeting	10/21/2013 15:00							WITH CUSTOMER REPS AND RIG CREW.
Start Job	10/21/2013 16:24							
Test Lines	10/21/2013 16:28						3500.0	PSI
Pump Spacer 1	10/21/2013 16:54		4	40	40			@10.5 PPG, 3.86 YIELD, 24.21 GAL/SK WITH 20 GAL MUSOL, 20 GAL SEM 7, 20 GAL DE-AIR.
Drop Bottom Plug	10/21/2013 17:09							PRE-LOADED WEATHERFORD BOTTOM PLUG IN PLUG CONTAINER VERIFIED BY CUSTOMER REP
Activity Description	Date/Time	Cht	Rate bbl/ min	Volume bbl		Pressure psig		Comments

Sold To #: 352431

Ship To #: 3108240

Quote # :

Sales Order #: 900834442

SUMMIT Version: 7.3.0106

Tuesday, October 22, 2013 02:24:00

The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900834442
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Tolman, Ben	
Well Name: Cline		Well #: 4-64 2-1H	API/UWI #: 05-005-07212
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Job Purpose: Cement Intermediate Casing			
Well Type: Development Well		Job Type: Cement Intermediate Casing	
Sales Person: GROFF, THEODORE		Srv Supervisor: SMITH, AARON	MBU ID Emp #: 518187

Job Personnel

HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #
CHISLUM, DENNIS	26.0	512130	DA COSTA, CHARLES Angelo	26.0	551308	GRIFFITHS, ZACHARY Sakae	26.0	551430
JOHNSON, BRANDON Matthew	26.0	545534	SMITH, AARON David	26.0	518187	WILSON, RANDY Wayne	26.0	314399

Equipment

HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way
10866493C	50 mile	11398319	50 mile	11488570C	50 mile	11518546	50 mile
11645065	50 mile	11764739	50 mile	12010173	50 mile	53301	50 mile

Job Hours

Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours
TOTAL								

Total is the sum of each column separately

Job

Formation Name	Formation Depth (MD)	Top	Bottom	Form Type	Job depth MD	Job Depth TVD	Water Depth	Perforation Depth (MD)	From	To
				BHST	7703. ft	7703. ft				

Job Times

	Date	Time	Time Zone
Called Out	21 - Oct - 2013	08:00	MST
On Location	21 - Oct - 2013	12:30	MST
Job Started	21 - Oct - 2013	16:24	MST
Job Completed	22 - Oct - 2013	12:32	MST
Departed Loc	21 - Oct - 2013	14:30	MST

Well Data

Description	New / Used	Max pressure psig	Size in	ID in	Weight lbf/ft	Thread	Grade	Top MD ft	Bottom MD ft	Top TVD ft	Bottom TVD ft
8-3/4" Open Hole				8.75							
7" Casing	Unknown		7.	6.094	32.	BTC	P-110	1890.	7684.		
9-5/8" Casing	Mixed		9.625	8.921	36.	STC	J-55		1890.		

Sales/Rental/3rd Party (HES)

Description	Qty	Qty uom	Depth	Supplier
CMT CASING EQUIPMENT BOM	0	JOB		
SHOE,FLT,7 8RD,2-3/4 SS II VLV	1	EA		
CLR,FLT,7 LG 8RD 23-26PPF,2-3/4	1	EA		
CENTRALISER SLIDER II,#0700-0834S	80	EA		
CLAMP - LIMIT - 7 - HINGED -	1	EA		
KIT,HALL WELD-A	1	EA		
MILEAGE FOR CEMENTING CREW,ZI	100	MI		
ZI FUEL SURCHG-CARS/PICKUPS<1 1/2TON	100	MI		

Tools and Accessories

Type	Size	Qty	Make	Depth	Type	Size	Qty	Make	Depth	Type	Size	Qty	Make
Guide Shoe					Packer					Top Plug			
Float Shoe					Bridge Plug					Bottom Plug			

Cementing Job Log

		#		Stage	Total	Tubing	Casing	
Pump Lead Cement	10/21/2013 17:10		5	155	195			440 SKS EXTENDACEM B2, @ 12 PPG, 1.99 YIELD, 10.64 GAL/SK
Pump Tail Cement	10/21/2013 17:53		4	36	231			135 SKS, HALCEM @ 15.8 PPG, 1.52 YIELD, 6.19 GAL/SK, DIDNT PUMP WRONG CEMENT WAS SENT FOR TAIL CEMENT AND LAST POD OF LEAD CEMENT
Shutdown	10/21/2013 17:54							HAD WRONG CEMENT SENT TO TRUCK FOR LAST POD OF LEAD, DID NOT CATCH IT, REALIZED WHEN WEIGHING UP WHAT WAS SUPPOSED TO BE TAIL CEMENT, SHUT JOB DOWN
Clean Hole	10/21/2013 18:10							HAD TO ROLL THE HOLE
Pre-Job Safety Meeting	10/22/2013 08:30							WITH CUSTOMER REP AND RIG CREW
Start Job	10/22/2013 09:38							
Test Lines	10/22/2013 09:42						3500. 0	FRESH WATER WITH NO ADDITIVES
Pump Spacer 1	10/22/2013 09:54		4	40	40		500.0	@10.5 PPG, 3.86 YIELD, 24.21 GAL/SK WITH 20 GAL MUSOL, 20 GAL SEM 7, 20 GAL DE-AIR.
Drop Bottom Plug	10/22/2013 10:24							PRE-LOADED WEATHERFORD BOTTOM PLUG IN PLUG CONTAINER VERIFIED BY CUSTOMER REP
Pump Lead Cement	10/22/2013 10:25		5	155	195		350.0	440 SKS EXTENDACEM B2, @ 12 PPG, 1.99 YIELD, 10.64 GAL/SK
Pump Tail Cement	10/22/2013 10:56		4	36	231		125.0	135 SKS, HALCEM @ 15.8 PPG, 1.52 YIELD, 6.19 GAL/SK,
Shutdown	10/22/2013 11:00							
Clean Lines	10/22/2013 11:03							

Sold To #: 352431

Ship To #: 3108240

Quote #:

Sales Order #: 900834442

SUMMIT Version: 7.3.0106

Tuesday, October 22, 2013 02:24:00

Float Collar					Retainer					SSR plug set			
Insert Float										Plug Container			
Stage Tool										Centralizers			

Miscellaneous Materials

Gelling Agt		Conc		Surfactant		Conc		Acid Type		Qty		Conc	%
Treatment Fld		Conc		Inhibitor		Conc		Sand Type		Size		Qty	

Fluid Data

Stage/Plug #: 1

Fluid #	Stage Type	Fluid Name	Qty	Qty uom	Mixing Density lbm/gal	Yield ft ³ /sk	Mix Fluid Gal/sk	Rate bbl/min	Total Mix Fluid Gal/sk
1	Clean Spacer III		80.00	bbl	10.5	.0	.0	.0	
	0.5 gal/bbl	SEM-7, 55 GAL DRUM (100001626)							
	0.5 gal/bbl	MUSOL(R) A, BULK (100003696)							
2	EXTENDACEM B1	EXTENDACEM (TM) SYSTEM (452981)	880.0	sacks	12.	1.99	10.64		10.64
	10.64 Gal	FRESH WATER							
3	HalCem	HALCEM (TM) SYSTEM (452986)	270.0	sacks	15.8	1.52	6.19		6.19
	6.19 Gal	FRESH WATER							

Calculated Values

Pressures

Volumes

Displacement	274	Shut In: Instant	2730	Lost Returns	0	Cement Slurry	191	Pad	
Top Of Cement	0	5 Min	2800	Cement Returns	21	Actual Displacement	274	Treatment	
Frac Gradient		15 Min		Spacers	40	Load and Breakdown		Total Job	505

Rates

Circulating		Mixing		Displacement		Avg. Job	
Cement Left In Pipe	Amount 80 ft	Reason	Shoe Joint				
Frac Ring # 1 @	ID	Frac ring # 2 @	ID	Frac Ring # 3 @	ID	Frac Ring # 4 @	ID

The Information Stated Herein Is Correct

Customer Representative Signature

Cementing Job Log

Activity Description	Date/Time	Cht #	Rate bbl/ min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Drop Top Plug	10/22/2013 11:10							PRE-LOADED WEATHERFORD TOP PLUG IN PLUG CONTAINER, VERIFIED BY CUSTOMER REP
Pump Displacement	10/22/2013 11:12		8	274	505		2000. 0	FRESH WATER
Spacer Returns to Surface	10/22/2013 11:35							@ 213 BBLS DISPLACEMENT, 40 BBLS TO THE PIT
Cement Returns to Surface	10/22/2013 11:45							
Bump Plug	10/22/2013 11:52		2.5	274	505		2730. 0	@ 500 OVER FINAL CIRCULATING PRESSURE 1273,
Check Floats	10/22/2013 11:57							FLOATS HELD, 3 BBLS BACK
Other	10/22/2013 11:59						1800. 0	CASING TEST @ 1500 PSI FOR 30 MIN
End Job	10/22/2013 12:32							RIG DOWN JSA, JOURNEY MANANGMENT MEETING, THANKS AARON SMITH AND CREW

CONOCO/PHILLIPS COMPANY EBUSINESS

**Cline 4-64 2-1H
WILDCAT
Arapahoe County , Colorado**

Cement Production Liner
29-Oct-2013

Job Site Documents

The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900855165
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Evans, Wes	
Well Name: Cline	Well #: 4-64 2-1H	API/UWI #: 05-005-07212	
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Contractor: H&P		Rig/Platform Name/Num: H&P 280	
Job Purpose: Cement Production Liner			
Well Type: Development Well		Job Type: Cement Production Liner	
Sales Person: GROFF, THEODORE	Srvc Supervisor: OTERI, VAUGHN	MBU ID Emp #: 443828	

Job Personnel

HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #	HES Emp Name	Exp Hrs	Emp #
DEY, JERRY A	10.0	505015	HARRAH, THADDEUS Gregory	10.0	552592	OTERI, VAUGHN Steeves	10.0	443828
WHIPPLE, WESLEY Morgan	10.0	518611						

Equipment

HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way	HES Unit #	Distance-1 way
10679720C	45 mile	10829457	45 mile	11036295	45 mile	11338223	45 mile
11410470C	45 mile						

Job Hours

Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours	Date	On Location Hours	Operating Hours

TOTAL Total is the sum of each column separately

Job				Job Times			
Formation Name				Date	Time	Time Zone	
Formation Depth (MD)	Top	Bottom		Called Out	29 - Oct - 2013	03:00	MST
Form Type	BHST			On Location	29 - Oct - 2013	06:45	MST
Job depth MD	11660. ft	Job Depth TVD	7500. ft	Job Started	29 - Oct - 2013	13:13	MST
Water Depth		Wk Ht Above Floor	30. ft	Job Completed	29 - Oct - 2013	15:18	MST
Perforation Depth (MD)	From	To		Departed Loc			

Well Data

Description	New / Used	Max pressure psig	Size in	ID in	Weight lbm/ft	Thread	Grade	Top MD ft	Bottom MD ft	Top TVD ft	Bottom TVD ft
6" Open Hole				6.25				7684.	11660.		
4-1/2" Liner	New		4.5	3.92	13.5		P-110	6682.	11660.		
7" Casing	Unknown		7.	6.094	32.	BTC	P-110	.	7684.		
4" Drill Pipe	Unknown		4.	3.34	14.			.	6682.		

Sales/Rental/3rd Party (HES)

Description	Qty	Qty uom	Depth	Supplier
CENTRALIZER SLIDER II 4 1/2" x 6"	185	EA		
SOLID STOP COLLAR 4-1/2", #0412-00SO	370	EA		
MILEAGE FOR CEMENTING CREW,ZI	50	MI		

Tools and Accessories

Type	Size	Qty	Make	Depth	Type	Size	Qty	Make	Depth	Type	Size	Qty	Make
Guide Shoe					Packer					Top Plug			
Float Shoe					Bridge Plug					Bottom Plug			
Float Collar					Retainer					SSR plug set			
Insert Float										Plug Container			
Stage Tool										Centralizers			

Miscellaneous Materials											
Gelling Agt	Conc		Surfactant		Conc		Acid Type		Qty	Conc %	
Treatment Fld	Conc		Inhibitor		Conc		Sand Type		Size	Qty	
Fluid Data											
Stage/Plug #: 1											
Fluid #	Stage Type	Fluid Name			Qty	Qty uom	Mixing Density lbm/gal	Yield ft ³ /sk	Mix Fluid Gal/sk	Rate bbl/min	Total Mix Fluid Gal/sk
1	Clean Spacer III				30.00	bbl	10.5	.0	.0	.0	
2	EXPANDACEM B2	EXPANDACEM (TM) SYSTEM (452979)			295.0	sacks	13.8	1.69	7.77		7.77
	0.5 %	HR-5, 50 LB SK (100005050)									
	7.774 Gal	FRESH WATER									
3	Clean Spacer III				12.00	bbl	10.5	.0	.0	.0	
	145.4583 lbm/bbl	SAND-SSA-1 - SILICA FLOUR - 200 MESH, BULK (100003691)									
4	Displacement with MMCR				66.00	bbl	8.34	.0	.0	.0	
	0.1 gal/bbl	MICRO MATRIX CEMENT RETARDER, 5 GAL PAIL (100003781)									
5	Displacement				52.00	bbl	.	.0	.0	.0	
Calculated Values		Pressures		Volumes							
Displacement		Shut In: Instant		Lost Returns		0	Cement Slurry			Pad	
Top Of Cement		5 Min		Cement Returns		20	Actual Displacement		130	Treatment	
Frac Gradient		15 Min		Spacers		42	Load and Breakdown			Total Job	
Rates											
Circulating		Mixing		Displacement			Avg. Job				
Cement Left In Pipe	Amount	90 ft	Reason	Shoe Joint							
Frac Ring # 1 @	ID		Frac ring # 2 @	ID		Frac Ring # 3 @	ID		Frac Ring # 4 @	ID	
The Information Stated Herein Is Correct				Customer Representative Signature							


The Road to Excellence Starts with Safety

Sold To #: 352431	Ship To #: 3108240	Quote #:	Sales Order #: 900855165
Customer: CONOCO/PHILLIPS COMPANY EBUSINESS		Customer Rep: Evans, Wes	
Well Name: Cline	Well #: 4-64 2-1H	API/UWI #: 05-005-07212	
Field: WILDCAT	City (SAP): WATKINS	County/Parish: Arapahoe	State: Colorado
Legal Description: Section 2 Township 4S Range 64W			
Lat: N 39.733 deg. OR N 39 deg. 43 min. 58.152 secs.		Long: W 104.509 deg. OR W -105 deg. 29 min. 28.68 secs.	
Contractor: H&P		Rig/Platform Name/Num: H&P 280	
Job Purpose: Cement Production Liner			Ticket Amount:
Well Type: Development Well		Job Type: Cement Production Liner	
Sales Person: GROFF, THEODORE	Srv Supervisor: OTERI, VAUGHN	MBU ID Emp #: 443828	

Activity Description	Date/Time	Cht #	Rate bbl/min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Call Out	10/29/2013 03:00							CALL FROM ARS OFFICE
Arrive At Loc	10/29/2013 06:45							ARRIVE ON LOCATION MET WITH COMPANY REP (WES & CLINT) DISCUSSED JOB PROCESS AND COCERNS
Rig-Up Equipment	10/29/2013 07:00							STARTED RIGGING UP ALL IRON AND HOSES
Safety Meeting	10/29/2013 12:00							HELD SAFETY MEETING IN DOG HOUSE WITH ALL HANDS ON LOCATION TO DISCUSS JOB PROCESS AND ANY HAZARDS
Start Job	10/29/2013 13:13							
Test Lines	10/29/2013 13:15						4293.0	PRESSURE TESTED PUMPS AND LINES FOUND NO LEAKS AND PRESSURE HELD GOOD
Pump Spacer 1	10/29/2013 13:25		4.5	30			830.0	MIXED 10.5PPG CLEAN SPACER WITH FRESH WATER
Pump Cement	10/29/2013 13:34		5	88			250.0	MIXED 13.8PPG EXPANDACEM WITH FRESH WATER
Shutdown	10/29/2013 14:01							
Clean Lines	10/29/2013 14:07							WASHED PUMPS AND LINES TILL FRESH WATER CAME OUT AT PIT

Activity Description	Date/Time	Cht #	Rate bbl/ min	Volume bbl		Pressure psig		Comments
				Stage	Total	Tubing	Casing	
Drop Top Plug	10/29/2013 14:10							RIG HAND RELEASED DART WITNESSED BY COMPANY REP AND BAKER HANDS
Pump Displacement	10/29/2013 14:13		4	130			1900. 0	PUMPED 66.55 BBLS OF MMCR WATER THEN MIXED 12 BBLS OF 10.5PPG CLEAN SPACER THEN PUMPED 51.94BBLS OF WATER BASED DRILLING MUD
Bump Plug	10/29/2013 14:52						1520. 0	BUMPED PLUG 500PSI OVER FINAL PUMP PRESSURE
Check Floats	10/29/2013 14:55			1.5			2345. 0	RELEASED PRESSURE BACK TO PUMP TRUCK FLOATS HELD GOOD
Reverse Circ Well	10/29/2013 15:18							LINED OUT ALL VAVLES SO THAT RIG COULD REVERSE OUT
End Job	10/29/2013 15:19							

ConocoPhillips Cline 4-64 2-1H Production Liner

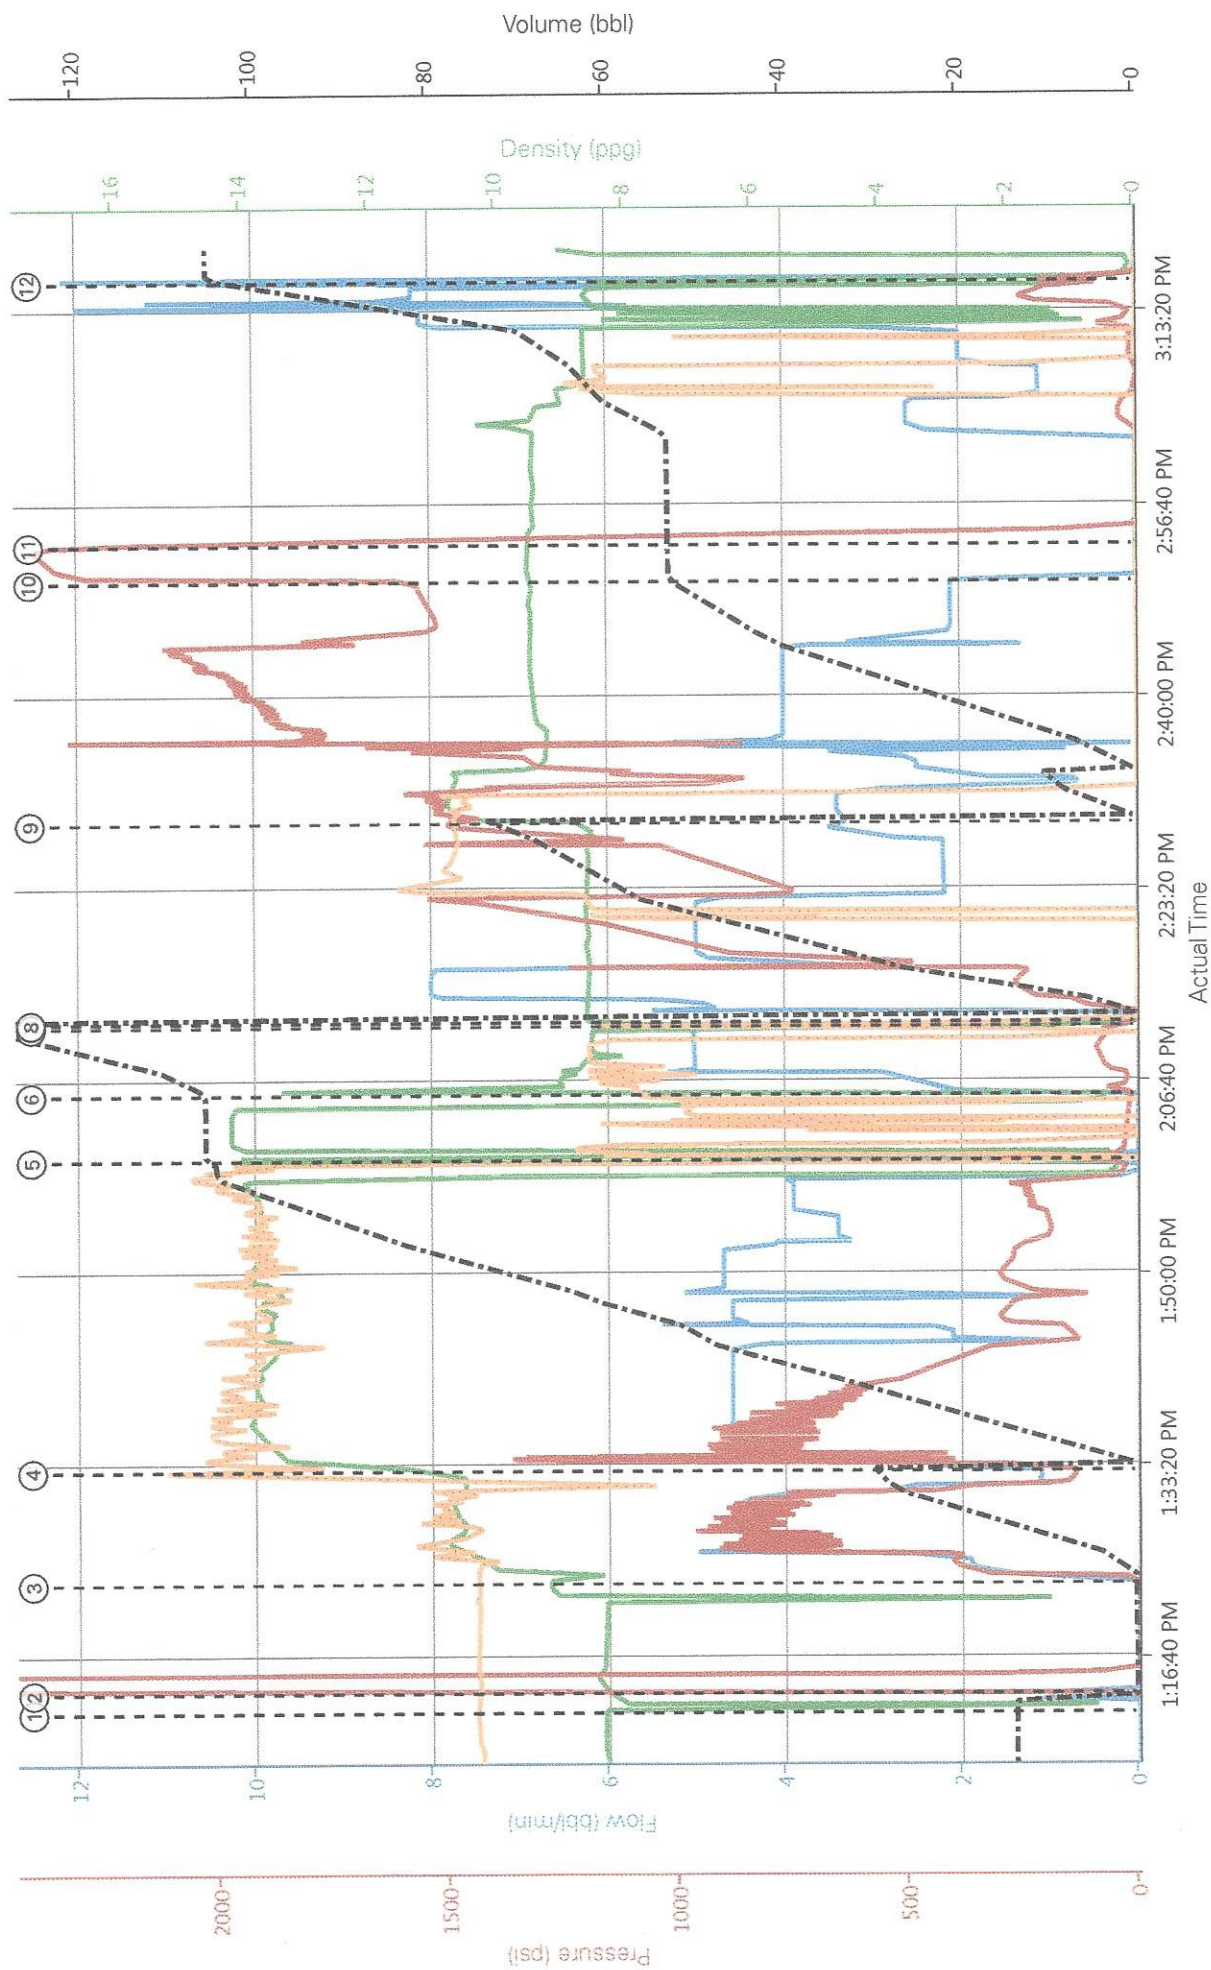

	Comb Pump Rate (bbl/min)	DH Density (ppg)	PS Pump Press (psi)	Recirc Density (ppg)	Pump Stg Tot (bbl)
① Start Job	0.8,35.6;10.37;13.9				
② Test Lines	0.8,42.32;12;10.42;0.4				
③ Pump Spacer 1	0.9,2.7;10.33;0				
④ Pump Cement	2.3;12.27;270;13.41;30.4				
⑤ Shutdown	0.1,1.11;52.6;93;105.6				
⑥ Clean Lines	2.2;10.46;80;7.87;106.1				
⑦ Drop Top Plug	0.8,67.2;0.129.3				
⑧ Pump Displacement	0.8,66;1;0.0				
⑨ Pump Spacer 1	3.3;10.69;1433;10.75;0				
⑩ Bump Plug	n/a;n/a;n/a;n/a;n/a				
⑪ Other	0.9,48;1321;0.53				
⑫ End Job	n/a;n/a;n/a;n/a;n/a				

Water Analysis For Cement Mixing Water

Company: CONOCO/PHILLIP S COMPANY
 Lease: Cline
 Well Name, Nbr: Cline, 4-64 2-1H
 Rig Name/Nbr: H&P 280
 API No. /UWI: 05-005-07212
 County: Arapahoe
 State: Colorado
 Country: United States of America

FIELD TEST KIT

NOTE: These tests are an indication of POTENTIAL contamination and are not conclusive.

For more comprehensive results, a sample should be submitted to the Local Area Lab

Date 29-Oct-2013 Ticket Number 900855165
 Service Supervisor OTERI, VAUGHN Water Source _____

Temperature _____ [*<80 F*]
 pH. _____ [*between 6-8 pH*]
 Specific Gravity _____ [*1.000 - 1.005 see Chart*]
 Chart in Kit shows comparisons of: Chlorides [*<3,000 ppm @ 1.004 S.G.*]
 Calcium [*<500 ppm @ 1.004 S.G.*]

PASS	FAIL	<u>Nessler's Nitrogen</u>	[<i>Passing Parameters</i>]
<input type="checkbox"/>	<input type="checkbox"/>	Color of Yellow _____	[<i><4.5 ppm (mg/L)</i>]
		<u>Tannin-Lignin</u>	
<input type="checkbox"/>	<input type="checkbox"/>	Color of Blue _____	[<i><25.0 ppm</i>]
		<u>Sulfate</u>	
		Degree of Clarity _____	[<i>200 ppm</i>]
<input type="checkbox"/>	<input type="checkbox"/>	Black X Visible _____	[<i>if NO >200 ppm = FAIL</i>]
		<u>Iron (Fe)</u>	
<input type="checkbox"/>	<input type="checkbox"/>	Degree of Orange _____	[<i><20.0 ppm</i>]

Material Roll UpCrew: CEMENT
Requested Job Start Date: _____Sales Order #:
AFE #:
WO #:
PO #:

Colorado Oil and Gas Commission Wellsite Form

Customer: CONOCO PHILLIPS

UWI / API Number

Well Name: CLINE

Well No: : 4-64-2-1H

Stage / Zone:

Formation:

Field: Wattenburg

County/Parish: ARAPAHOE

State: COLORADO

Latitude:

Longitude:

Sect / Twn / Rng: / /

Job Type: CEMENT LINER

Service Supervisor: VAUGHN OTERI

Cust Rep

Name:

Cust Rep

Phone #: (

Do Not leave the yard without the proper MSDS documentation for All chemicals.

Colorado Oil and Gas Commission					
Material	Delivered to Location	UOM	Specific Gravity	Weight (lbs)	Comment
CLEAN SPACER		BBL		42	
EXPANDACEM		LB		32098	
		LB			
		LB			
		Gal			
		LB			

☒Operator provided all Material Safety Data Sheets (MSDS) related to material listed above.
Operator representative will check box to designate he/she has received all MSDS documentation._____
Operator Representative Signature
