


Well Name: ANACAPA 32-31

VERTICAL - ORIGINAL HOLE, 7/31/2015 9:28:31 AM

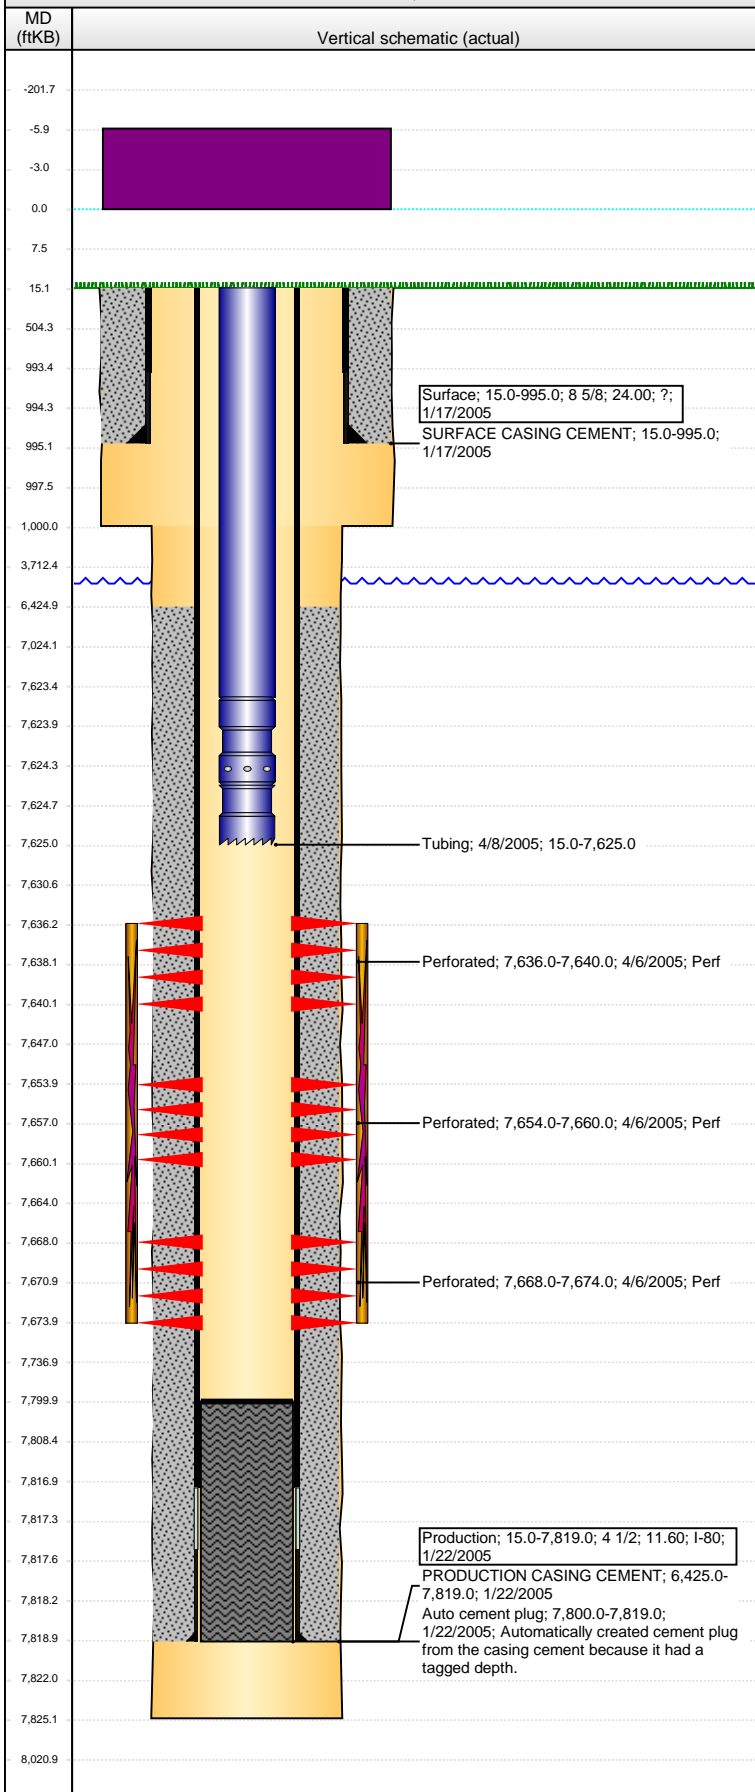

Well Header

API	Business Unit	District	Well Config
05-123-22116	DJ BASIN	15	VERTICAL
Original KB Elevation (ft)	KB - GL / MSL (ftKB)	Spud Date	P & A Date
4,987.00	15.00	1/16/2005	
Comment			
Directions To Well			

Congressional Location

Quarter 1	Quarter 2	Quarter 3	Quarter 4	Section	Township	Twnshp N...	Range	Rng E/W Dir
		SW	NE	31	2	N	64	W

Bottom Hole Location

North-South Distance (ft)	From N or S Line	East-West Distance (ft)	From E or W Line

Plug Back Total Depths

Date	Depth (ftKB)	Method	Com
2/11/2005	7,800.0	CASED HOLE LOG	DEPTH LOGGER ON CBL
4/8/2005	7,800.0	TAG	CLEAN OUT TO LAND TUBING

Wellbore Sections

Section Des	Size (in)	Act Top, MD (ftKB)	Act Btm, MD (ftKB)
SURFACE	12 1/4	15.0	1,000.0
PRODUCTION	7 7/8	1,000.0	7,825.0

Zone Statuses

Zone Name	Status Date	Status	Fluid Type	Job	Prod Method
J SAND	5/13/2005	PR		DRILLING/CO...	

Casing Strings

Surface, 995.0ftKB

Casing Description	Run Date	OD (in)	Wt/Len (l...)	Grade	Top, MD (ft...)	MD (ftKB)
Surface	1/17/2005	8 5/8	24.00	?	15.0	995.0

Production, 7,819.0ftKB

Casing Description	Run Date	OD (in)	Wt/Len (l...)	Grade	Top, MD (ft...)	MD (ftKB)
Production	1/22/2005	4 1/2	11.60	1-80	15.0	7,819.0

Cement

Description	Top Depth (ftKB)	Bottom Depth (ftKB)
SURFACE CASING CEMENT	15.0	995.0
PRODUCTION CASING CEMENT	6,425.0	7,819.0

Tubing Strings

Tubing Description	Run Date	String...	ID (in)	Wt (lb/ft)	Grade	Len (ft)	Set De...
Tubing	4/8/2005	2 3/8				7,610.00	

Tubing Components

Item Des	OD (in)	Wt (lb/ft)	Grade	Jts	Len (ft)	Btm (ftKB)	Btm (TVD) (ftKB)
Tubing	2 3/8			244	7,608.50	7,623.5	
Seal Nipple	2 3/8				1.00	7,624.5	
Notched collar	2 3/8			1	0.50	7,625.0	

Perforation Data

Zone	Bnch/St g	Entered Shot Total	Top (ftKB)	Btm (ftKB)	Date
J SAND, ORIGINAL HOLE		16	7,636.00	7,640.00	4/6/2005
J SAND, ORIGINAL HOLE		24	7,654.00	7,660.00	4/6/2005
J SAND, ORIGINAL HOLE		24	7,668.00	7,674.00	4/6/2005

Stimulations & Treatments

Date	Zone	Primary Job Type
4/7/2005	J SAND, ORIGINAL HOLE	DRILLING/COMPLETION - ORIGINAL
Technical Result		Tech Result Details
		Tech Result Note
Comment		

Other In Hole

Run Date	Des	OD (in)	Top (ftKB)	Btm (ftKB)

Logs

Date	Type	Top, MD (ftKB)	Btm, MD (ftKB)
1/21/2005	TRIPLE COMBO	995.0	7,825.0
2/11/2005	CBL/CCL/GR	6,165.0	7,795.0
