


Well Name: BOEDECKER 40

VERTICAL - ORIGINAL HOLE, 8/20/2015 11:45:06 AM

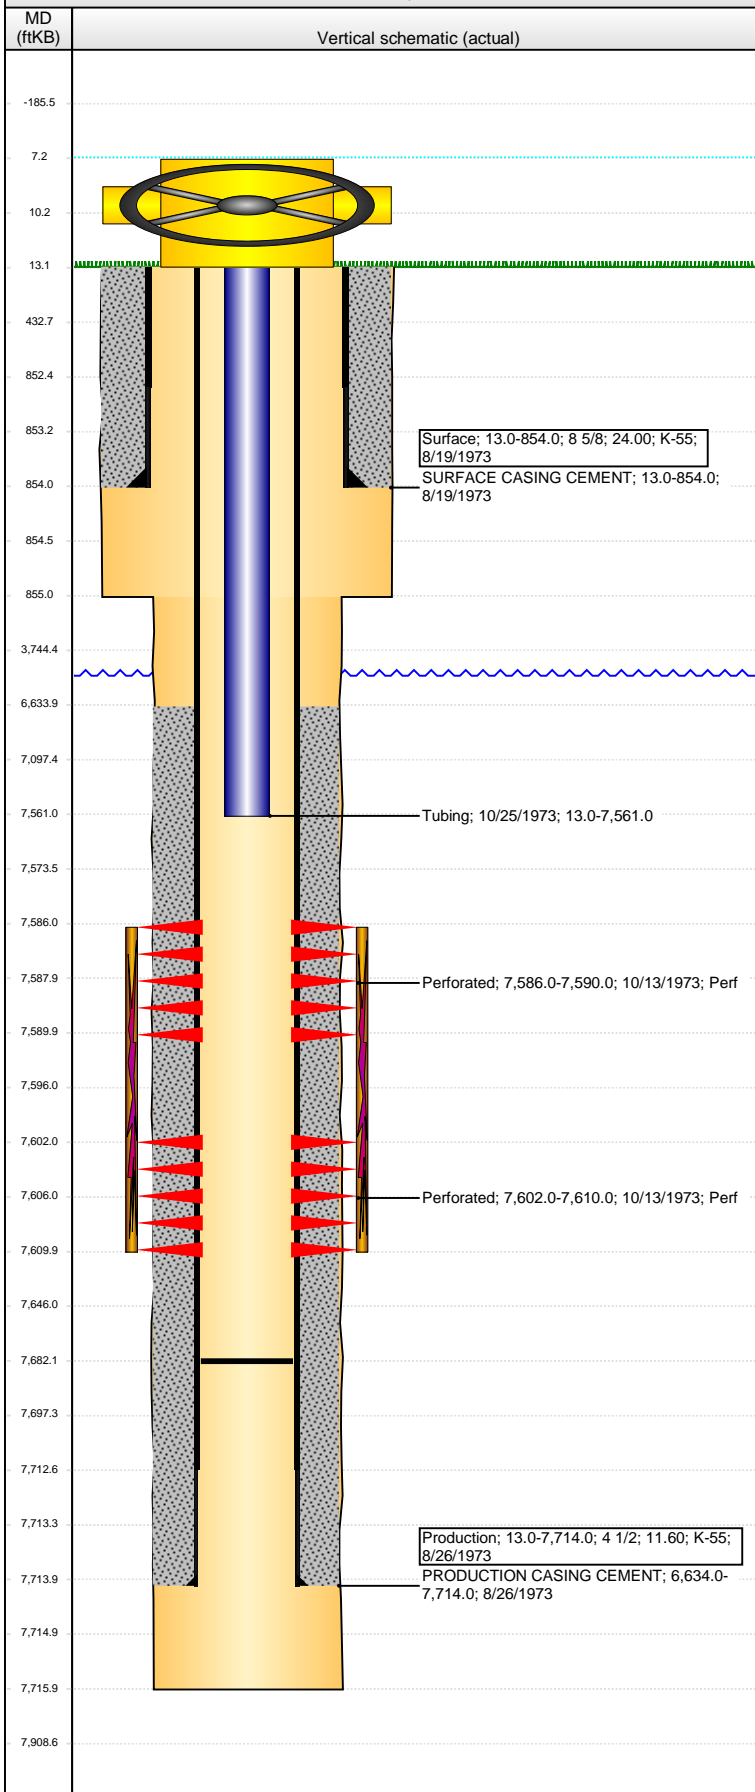

Well Header

API 05-123-07818	Business Unit DJ BASIN	District 15	Well Config VERTICAL
Original KB Elevation (ft) 5,006.00	KB - GL / MSL (ftKB) 13.00	Spud Date 8/18/1973	P & A Date

Comment
DISCREPANCY: DR RPT TD/TD DATE 7716, 8/26/1973; ST RPT TD/TD DATE 7710, 8/27/1973

SKETCHY DRILLING INFORMATION

Directions To Well

Congressional Location

Quarter 1	Quarter 2	Quarter 3	Quarter 4	Section	Township	Twnshp N...	Range	Rng E/W Dir
			SW	22	2	N	64	W

Bottom Hole Location

North-South Distance (ft)	From N or S Line	East-West Distance (ft)	From E or W Line

Plug Back Total Depths

Date	Depth (ftKB)	Method	Com
10/2/1973	7,623.0	CASED HOLE LOG	DEPTH LOGGER ON CBL
10/25/1973	7,682.0	TAG	TAG TO LAND TUBING

Wellbore Sections

Section Des	Size (in)	Act Top, MD (ftKB)	Act Btm, MD (ftKB)
SURFACE	12 1/4	13.0	855.0
PRODUCTION	7 7/8	855.0	7,716.0

Zone Statuses

Zone Name	Status Date	Status	Fluid Type	Job	Prod Method
J SAND	10/27/1973	PR		DRILLING/CO...	

Casing Strings

Surface, 854.0ftKB

Casing Description	Run Date	OD (in)	Wt/Len (l...)	Grade	Top, MD (ft...)	MD (ftKB)
Surface	8/19/1973	8 5/8	24.00	K-55	13.0	854.0

Production, 7,714.0ftKB

Casing Description	Run Date	OD (in)	Wt/Len (l...)	Grade	Top, MD (ft...)	MD (ftKB)
Production	8/26/1973	4 1/2	11.60	K-55	13.0	7,714.0

Cement

Description	Top Depth (ftKB)	Bottom Depth (ftKB)
SURFACE CASING CEMENT	13.0	854.0
PRODUCTION CASING CEMENT	6,634.0	7,714.0

Tubing Strings

Tubing Description	Run Date	String...	ID (in)	Wt (lb/ft)	Grade	Len (ft)	Set De...
Tubing	10/25/1973	3	1.9	1.610	2.90 WPCW-55	7,548.00	

Tubing Components

Item Des	OD (in)	Wt (lb/ft)	Grade	Jts	Len (ft)	Btm (ftKB)	Btm (TVD) (ftKB)
Tubing	1.9	2.90	WPC W-55	230	7,548.00	7,561.0	

Perforation Data

Zone	Bnch/St g	Entered Shot Total	Top (ftKB)	Btm (ftKB)	Date
J SAND, ORIGINAL HOLE		12	7,586.00	7,590.00	10/13/1973
J SAND, ORIGINAL HOLE		16	7,602.00	7,610.00	10/13/1973

Stimulations & Treatments

Date	Zone	Primary Job Type
10/22/1973	J SAND, ORIGINAL HOLE	DRILLING/COMPLETION - ORIGINAL
Technical Result	Tech Result Details	Tech Result Note
Comment		

Other In Hole

Run Date	Des	OD (in)	Top (ftKB)	Btm (ftKB)

Logs

Date	Type	Top, MD (ftKB)	Btm, MD (ftKB)
8/26/1973	INDUCTION	854.0	7,701.0
8/27/1973	COMPENSATED DENSITY	4,400.0	7,704.0
10/2/1973	CEMENT BOND	6,570.0	7,620.0
