

Foundation Energy Management, LLC
Drilling - Completion - Workover - Facilities
WBD

| | | | | | |
|-------------------------|---------------|-------------------|-----------------|---------------|----------|
| AFE No.: | | AFE Amount | | Original: | \$0 |
| AFE Type: | | Plug & Abandon | | Supplemental: | |
| AFE Category: | | CAPEX | | Total: | \$45,483 |
| WI: | NRI: | AFE Date: | 11/19/2014 | Budget Year: | 2014 |
| | | | | | |
| Well / Battery | Prospect Name | Total Depth | Est. Start Date | | |
| Mitchem 2-26X | Paladin | 7,614' | | | |
| Location | Sec-Twa-Rng | Producing Horizon | County & State | | |
| NE NE | 26-3S-63W | JSND | Adams, CO | | |
| AFE Description | | | | | |
| P&A | | | | | |
| | | | | | |
| WELLBORE DIAGRAM BEFORE | | | | | |

Prepared Date: 11-19-2014
Prepared By: Dalton Reazin

General Info

API #: 05-001-07685

KB Elevation: 5,409'
GL Elevation: 5,397'

Spud Date: 09-18-1980
Completion Date: 10-09-1980

TVD: 7,614'
MD: 7,614'
Last PBTD: 7,492' (03-08-2013)

Tubing Detail

inch(OD)
(weight)
grade

Cmnt Basket @ 1,350'

Tubing Tally

| | Length | Depth |
|-----------|--------|-------|
| No Tubing | | |

Rod Design

| | length | depth |
|---------|--------|-------|
| NO RODS | | |

Surface Casing

8-5/8" inch (OD)
24 # (weight)
J-55 grade
233' depth from KB
Surface cement top
230 sacks of cement
12-1/4" inch (OD) HOLE SIZE

Visual Returns

Production Casing

4-1/2" inch (OD)
12 # (weight)
J-55 grade
6,878' depth from KB
6,512' cement top
200 sacks of cement
7-7/8" inch (OD) HOLE SIZE

Calculated


Open Perforations

7520'-7550' - 61 holes
JSND

Pump Details:
none

Pumping Unit Details:
none

Well Notes:
CIBP @ 7,492' from TA
Cement basket @ 1,350'

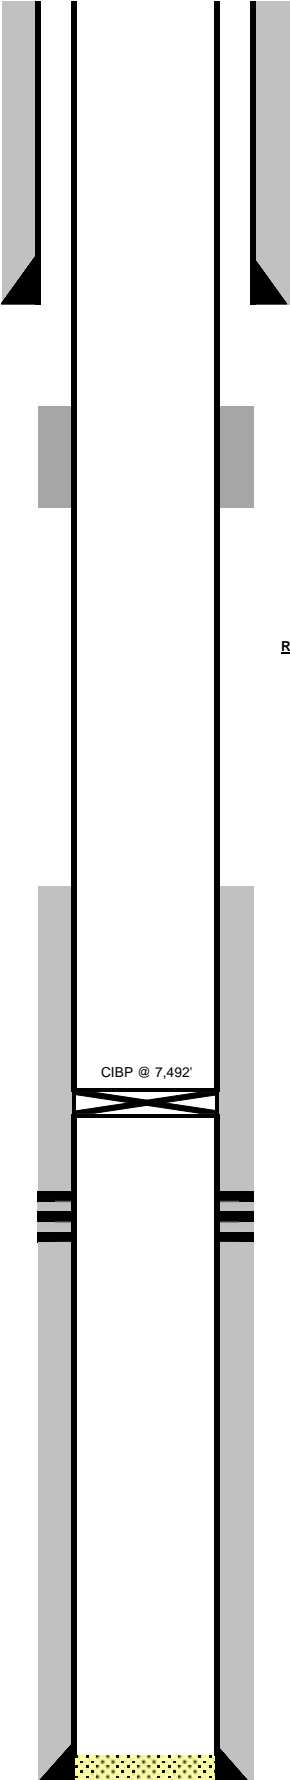

Original PBTD: 7,612'
