

CEMENT JOB REPORT



CUSTOMER BAYSWATER EXPLORATION ;			DATE 02-FEB-16		F.R. # 10011191198			SERV. SUPV. JOHN R WUDARCZYK						
LEASE & WELL NAME Albrighton L-10HN - API 05123425040000			LOCATION 10-6N-64W			COUNTY-PARISH-BLOCK Weld Colorado								
DISTRICT Brighton			DRILLING CONTRACTOR RIG # Frontier 8			TYPE OF JOB Surface								
SIZE & TYPE OF PLUGS		LIST-CSG-HARDWARE			MECHANICAL BARRIERS		MD	TVD	HANGER TYPES		MD	TVD		
Cement Plug, Rubber, Top 9-5/8 in		Float Shoe 9-5/8 - 8rd												
		Float Collar, Pop Valve, 9-5/8 - 8rd												
		Centralizer, with Pins, 9-5/8 in												
MATERIALS FURNISHED BY BJ				LAB REPORT NO.		PHYSICAL SLURRY PROPERTIES								
						SACKS OF CEMENT	SLURRY WGT PPG	SLURRY YLD FT₃	WATER GPS	PUMP TIME HR:MIN	Bbl SLURRY	Bbl MIX WATER		
Fresh Water						0	8.34	0	0	00:00	20			
Type III Cement + Addis						700	14.5	1.40	6.79		174	113.06		
Fresh Water						0	8.34	0	0	00:00	112.87			
Available Mix Water 500 Bbl.			Available Displ. Fluid 500 Bbl.			TOTAL			306.87			113.06		
HOLE			TBG-CSG-D.P.						COLLAR DEPTHS					
SIZE	% EXCESS	DEPTH	ID	OD	WGT.	TYPE	MD	TVD	GRADE	SHOE	FLOAT	STAGE		
13.5	30	1555	8.921	9.625	36	CSG	1541	1541	J-55	1541	1537	0		
LAST CASING			PKR-CMT RET-BR PL-LINER			PERF. DEPTH		TOP CONN		WELL FLUID				
ID	OD	WGT	TYPE	MD	TVD	BRAND & TYPE		DEPTH	TOP	BTM	SIZE	THREAD	TYPE	WGT.
						NO PACKER		0			9.625	8RND	FRESH WATER	8.34
DISPL. VOLUME		DISPL. FLUID		CAL. PSI	CAL. MAX PSI	OP. MAX	MAX TBG PSI		MAX CSG PSI		MIX WATER			
VOLUME	UOM	TYPE		WGT.	BUMP PLUG	TO REV.	SQ. PSI	RATED	Operator	RATED	Operator			
115.6	BBLS	Fresh Water		8.34	478	0	0	0	0	2816	2000	RIG		
Circulation Prior to Job														
Circulated Well: Rig <input checked="" type="checkbox"/> BJ <input type="checkbox"/>				Circulation Time: 1				Circulation Rate: 5 BPM						
Mud Density In: 8.34 LBS/G				Mud Density Out: 8.34 LBS/GAL				PV & YP Mud In: 0		PV & YP Mud Out: 0				
Gas Present: NO <input checked="" type="checkbox"/> YES <input type="checkbox"/>				Units:				Solids Present at End of Circulation: NO <input checked="" type="checkbox"/> YES <input type="checkbox"/>						
Displacement And Mud Removal														
Displaced By: Rig <input type="checkbox"/> BJ <input checked="" type="checkbox"/>				Amount Bled Back After Job: .5 BBLS										
Returns During Job: <input type="checkbox"/> NONE <input type="checkbox"/> PARTIAL <input checked="" type="checkbox"/> FULL				Method Used to Verify Returns: VISUAL										
Cement Returns at Surface: <input checked="" type="checkbox"/> YES <input type="checkbox"/> NO				Were Returns Planned at Surface: <input type="checkbox"/> NO <input checked="" type="checkbox"/> YES										
Pipe Movement: <input type="checkbox"/> ROTATION <input type="checkbox"/> RECIPROICATION <input checked="" type="checkbox"/> NONE <input type="checkbox"/> UNABLE DUE TO STUCK PIPE														
Centralizers: <input type="checkbox"/> NO <input checked="" type="checkbox"/> YES				Quantity: 15				Type: <input type="checkbox"/> BOW <input type="checkbox"/> RIGID						
Job Pumped Through: <input type="checkbox"/> CHOKE MANIFOLD <input type="checkbox"/> SQUEEZE MANIFOLD <input checked="" type="checkbox"/> MANIFOLD <input type="checkbox"/> NO MANIFOLD														
Plugs														
Number of Attempts by BJ: 0				Competition: 0				Wiper Balls Used: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES Quantity:						
Plug Catcher Used: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES				Parabow Used: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES										
Was There a Bottom: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES				Top of Plug: 0 FT				Bottom of Plug: 0 FT						
Squeezes (Update Original Treatment Report for Primary Job)														
BLOCK SQUEEZE <input type="checkbox"/>				SHOE SQUEEZE <input type="checkbox"/>				TOP OF LINER SQUEEZE <input type="checkbox"/>				PLANNED <input type="checkbox"/>	UNPLANNED <input type="checkbox"/>	
Liner Packer: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES				Bond Log: <input checked="" type="checkbox"/> NO <input type="checkbox"/> YES				PSI Applied: 0		Fluid Weight: 0 LBS/GAL				
Casing Test (Update Original Treatment Report for Primary Job)														
Casing Test Pressure: 0 PSI				With 0 LBS/GAL Mud				Time Held: 00 Hours 00 Minutes						
EXPLANATION: TROUBLE SETTING TOOL, RUNNING CSG, ETC. PRIOR TO CEMENTING: NONE														
PRESSURE/RATE DETAIL						EXPLANATION								

CEMENT JOB REPORT



Shoe Test (Update Original Treatment Report for Primary Job)

Depth Drilled out of Shoe: 0 FT	Target EMW: 0 LBS/GAL	Actual EMW: 0 LBS/GAL
Number of Times Tests Conducted: 0	Mud Weight When Test was Conducted: 0 LBS/GAL	


Problems Before Job (I.E. Running Casing, Circulating Well, ETC)
NONE

Problems During Job (I.E. Lost Returns, Equipment Failure, Bulk Delivery, Foaming, ETC)
NONE

Problems After Job (I.E. Gas at Surface, Float Equipment Failed, ETC)
NONE

PRESSURE/RATE DETAIL						EXPLANATION	
TIME HR:MIN.	PRESSURE - PSI		RATE BPM	Bbl. FLUID PUMPED	FLUID TYPE	SAFETY MEETING: BJ CREW <input checked="" type="checkbox"/> CO. REP. <input checked="" type="checkbox"/>	
	PIPE	ANNULUS				TEST LINES	3140 PSI
						CIRCULATING WELL - RIG <input checked="" type="checkbox"/> BJ <input type="checkbox"/>	
20:00	0	0	0	0	0	ARRIVE ON LOCATION (ARRIVED EARLY DUE TO WEATHER CONDITIONS)	
08:30	0	0	0	0	0	SPOT TRUCKS	
09:00	0	0	0	0	0	PRE RIG UP SAFETY MEETING	
10:15	0	0	0	0	0	PRE JOB MEETING	
10:55	3140	0	0	0	H2O	PRESSURE TEST PUMPS AND LINES	
11:00	187	0	5	20	H2O	FRESH WATER SPACER	
11:15	269	0	4	171	CMR	BATCH NUP AND PUMP 700 SKS CMT @ 14.5#	
12:10	0	0	0	0	H2O	DROP PLUG	
12:11	684	0	5.6	100	H2O	START DISPLACEMENT	
12:32	624	0	3.5	16	H2O	SLOW RATE	
12:36	1330	0	0	0	H2O	BUMP PLUG @ 116 BBLs	
12:38	0	0	0	0	H2O	CHECK FLOATS 1/2 BBL BACK	
12:40	0	0	0	0	0	POST JOB RIG DOWN SAFETY MEETING	

BUMPED PLUG	PSI TO BUMP PLUG	TEST FLOAT EQUIP.	BBL.CMT RETURNS/ REVERSED	TOTAL BBL. PUMPED	PSI LEFT ON CSG	SPOT TOP OUT CEMENT	Service Supervisor Signature: _____
<input type="checkbox"/> Y <input checked="" type="checkbox"/> N	1330	<input type="checkbox"/> Y <input checked="" type="checkbox"/> N	35	307	0	Y <input type="checkbox"/> N	

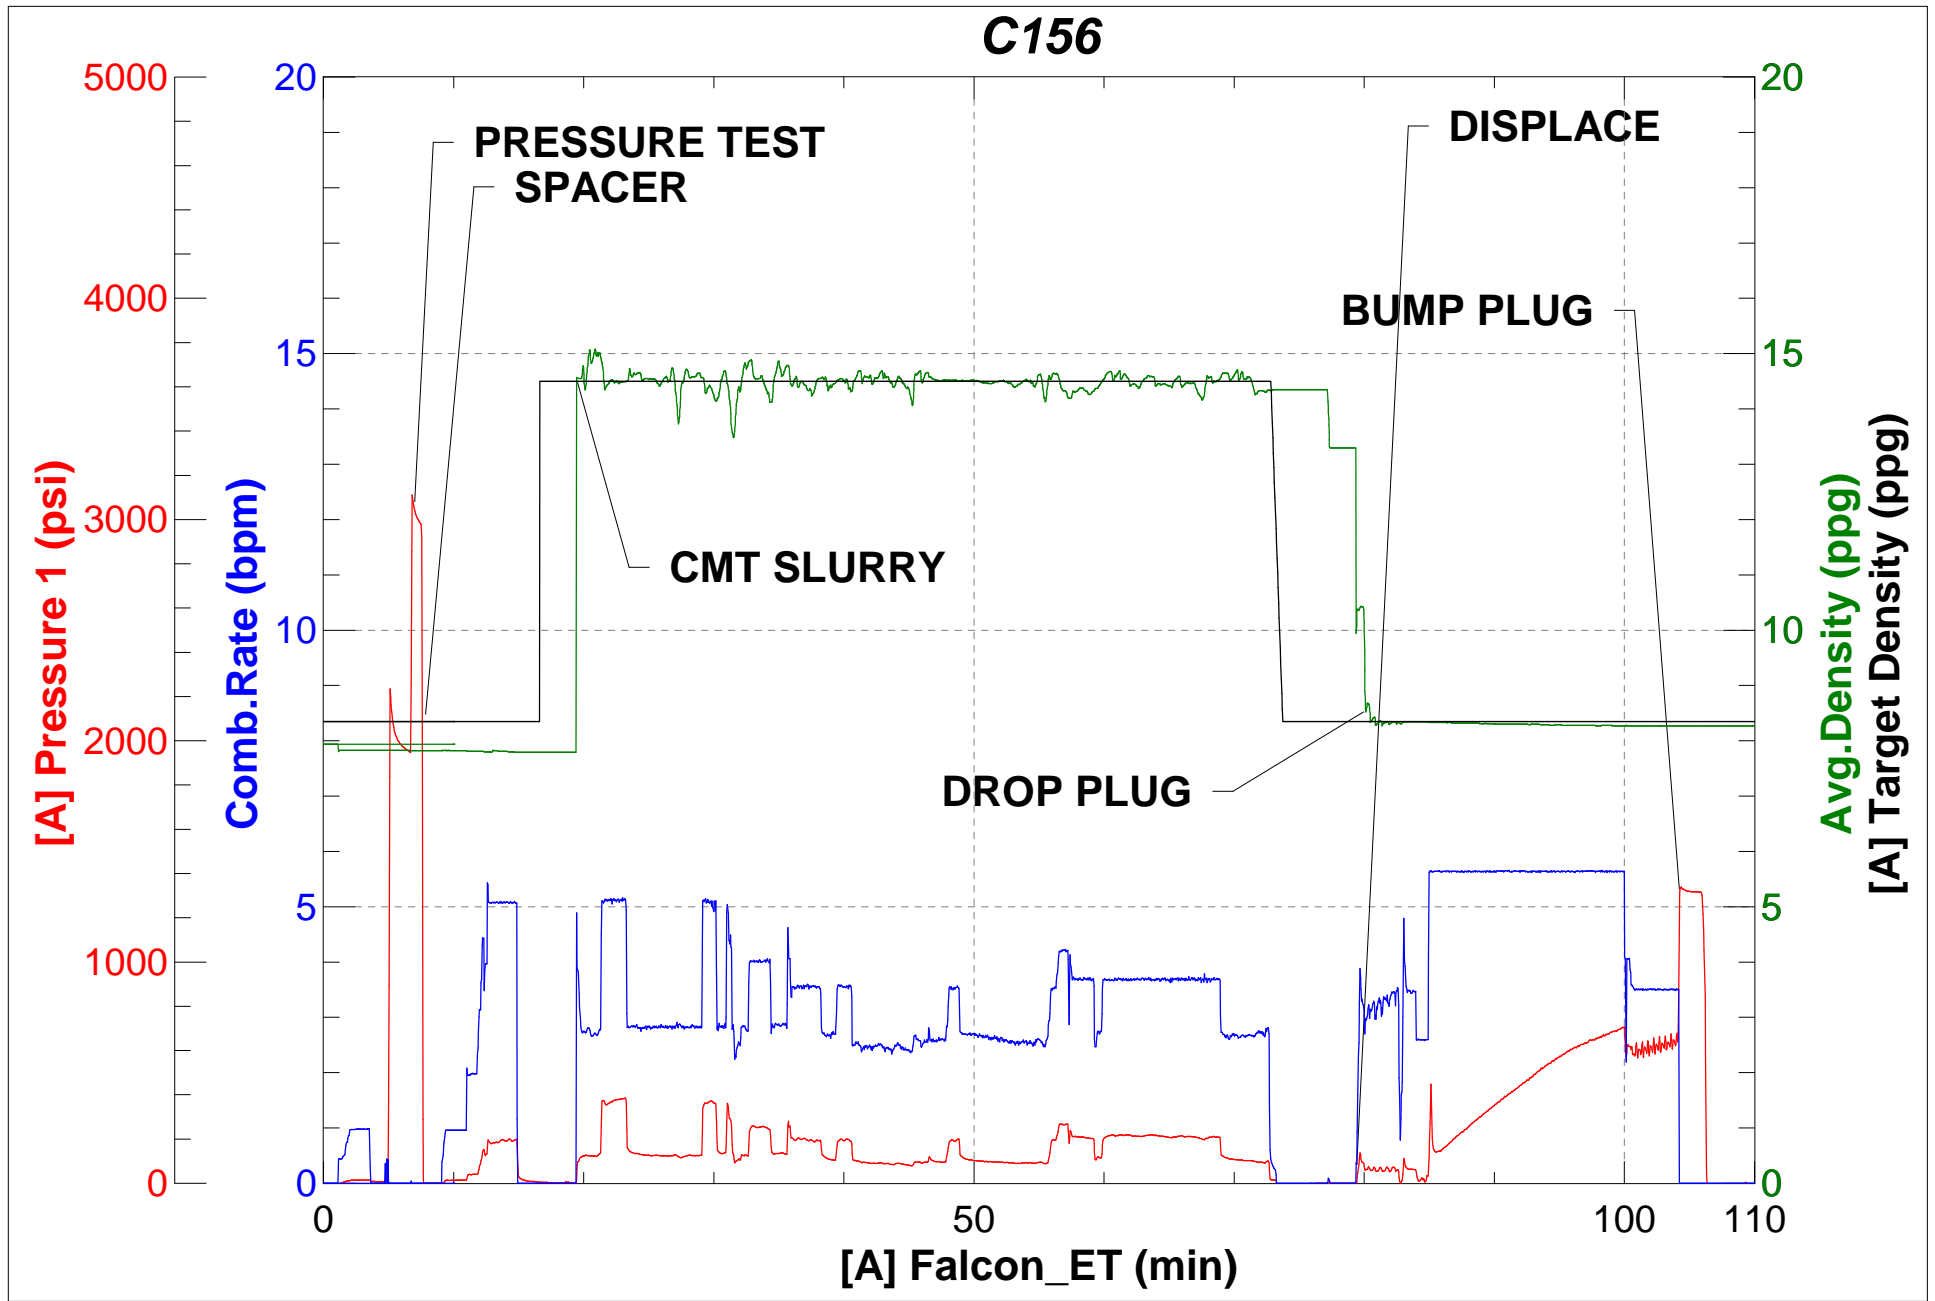



FIELD RECEIPT NO. 1001191198

CUSTOMER BAYSWATER EXPLORATION & PRODUCTION					CREDIT APPROVAL NO.	PURCHASE ORDER NO.	CUSTOMER NUMBER 20007918 - 00244714	INVOICE NUMBER		
MAIL INVOICE TO		STREET OR BOX NUMBER 730 17TH ST, STE 610			CITY DENVER		STATE Colorado	ZIP CODE 80202		
DATE WORK COMPLETED	MO. 02	DAY 02	YEAR 2016	BHI REPRESENTATIVE JOHN R WUDARCZYK	WELL API NO: 05123425040000	WELL TYPE : New Well				
DISTRICT PP, BRIGHTON					JOB DEPTH (ft) 1,540	WELL CLASS : Oil				
WELL NAME AND NUMBER Albrighton L-10HN					TD WELL DEPTH (ft) 1,555	GAS USED ON JOB : No Gas				
WELL LOCATION :		LEGAL DESCRIPTION 10-6N-64W			COUNTY/PARISH Weld	STATE Colorado	JOB TYPE CODE : Surface			
PRODUCT CODE	DESCRIPTION				UNIT OF MEASURE	QUANTITY	LIST PRICE UNIT	GROSS AMOUNT	% DISC.	NET AMOUNT
100112	Calcium Chloride				lbs	629	1.290	811.41	76%	194.74
100295	Cello Flake				lbs	175	5.100	892.50	76%	214.20
100404	Sodium Chloride				lbs	100	0.520	52.00	76%	12.48
488019	FP-6L				gals	10	104.250	1,042.50	76%	250.20
499632	Granulated Sugar				lbs	50	3.840	192.00	76%	46.08
499680	Static Free				lbs	56	40.700	2,279.20	76%	547.01
499703	Type III Cement				sacks	700	31.700	22,190.00	76%	5,325.60
	SUB-TOTAL FOR Product Material							27,459.61	76.00%	6,590.31
VP001	Cement Svcs Surf Equip 50 miles or less				ea	1	7,250.000	7,250.00	0%	7,250.00
	SUB-TOTAL FOR Equipment							7,250.00	0%	7,250.00
	FIELD ESTIMATE							34,709.61	60.13%	13,840.31
ARRIVE LOCATION :	MO. 02	DAY 01	YEAR 2016	TIME 20:00	SERVICE ORDER: I AUTHORIZE WORK TO BEGIN PER SERVICE INSTRUCTIONS IN ACCORDANCE WITH THE TERMS AND CONDITIONS PRINTED ON THE LAST PAGE OF THIS FORM AND REPRESENT THAT I HAVE AUTHORITY TO ACCEPT AND SIGN THIS ORDER.				SERVICE RECEIPT: I CERTIFY THAT THE MATERIALS AND SERVICES LISTED WERE RECEIVED AND ALL SERVICES PERFORMED IN A WORKMANLIKE MANNER.	
CUSTOMER REP. SCOTT OSBORNE					CUSTOMER AUTHORIZED AGENT				X	
SEE LAST PAGE FOR GENERAL TERMS AND CONDITIONS									CUSTOMER AUTHORIZED AGENT	
