


**Well Name: WILHITE 30-31**

VERTICAL - ORIGINAL HOLE, 10/24/2016 2:53:31 PM

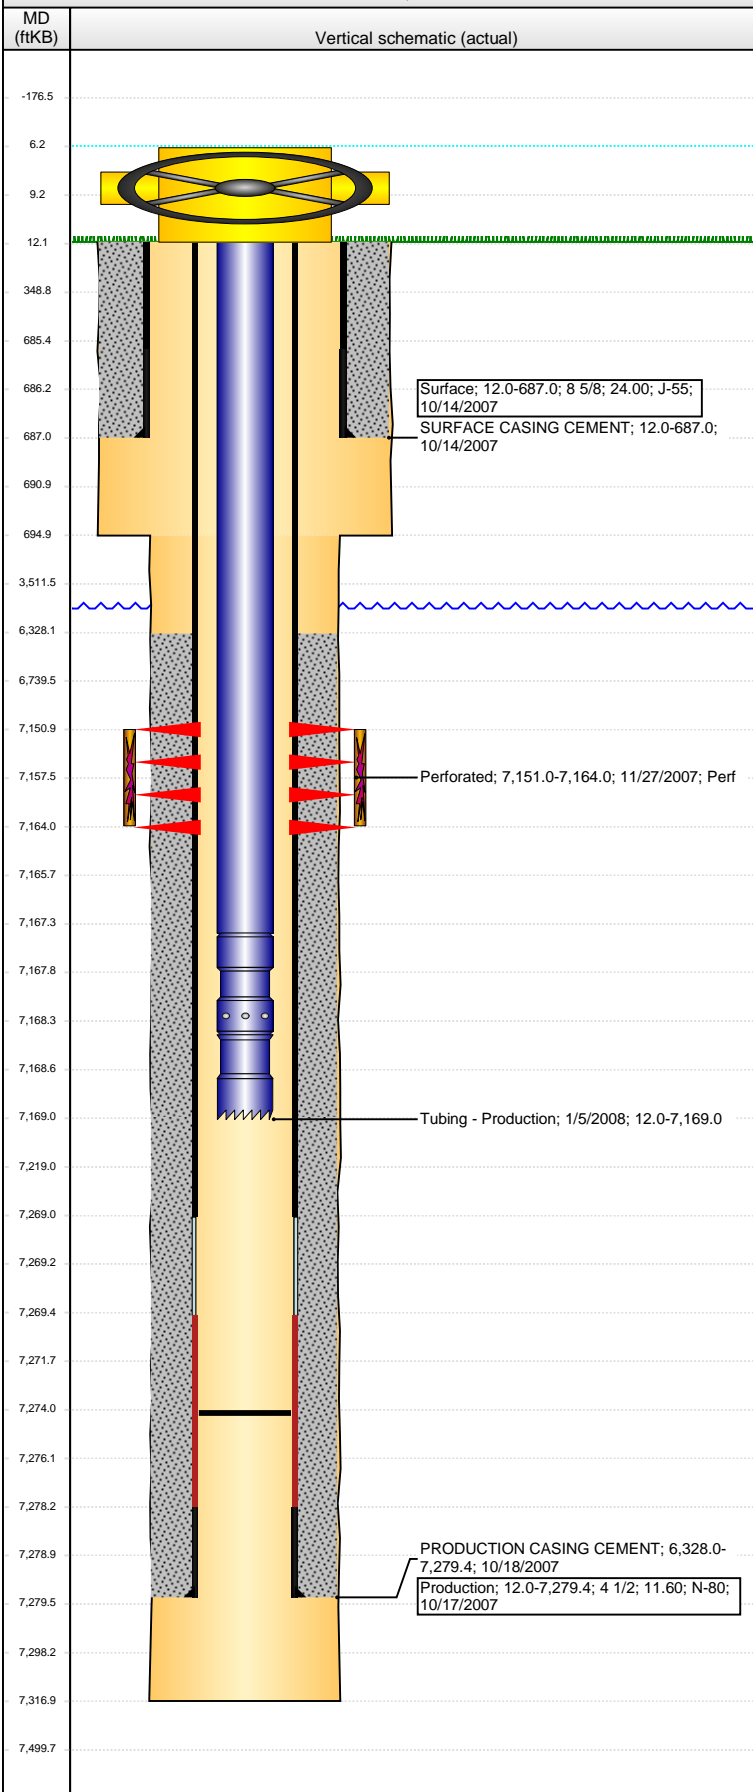

Well Header								
API 05-123-24806		Business Unit DJ BASIN		District 15		Well Config VERTICAL		
Original KB Elevation (ft) 4,873		KB - GL / MSL (ftKB) 12.00		Spud Date 10/13/2007		P & A Date		
Comment								
Directions To Well								
Congressional Location								
Quarter 3 NE		Quarter 4 SW	Section 30	Township 7	Twntshp N/S Dir N	Range 64		Range E/W Dir W
Bottom Hole Location								
North-South Distance (ft)			From N or S Line		East-West Distance (ft)		From E or W Line	
Plug Back Total Depths								
Date		Depth (ftKB)	Method		Com			
10/18/2007		7,269.0	CASING TALLY		TOP OF BAFFLE PLATE			
11/27/2007		7,245.0	TAG		CBL DEPTH LOGGER			
1/5/2008		7,274.0	TAG		MOST RECENT C/O			
Wellbore Sections								
Section Des			Size (in)		Act Top, MD (ftKB)		Act Btm, MD (ftKB)	
SURFACE			12 1/4		12		695	
PRODUCTION			7 7/8		695		7,317	
Zone Statuses								
Zone Name		Status Date	Status	Fluid Type	Job	Prod Method		
CODELL		12/5/2007	PR	Oil	DRILLING/CO...			
Casing Strings								
Surface, 687.0ftKB								
Casing Description Surface		Run Date 10/14/2007	OD (in) 8 5/8	Wt/Len (l...) 24.00	Grade J-55	Top, MD (ft...) 12.0	MD (ftKB) 687.0	
Production, 7,279.4ftKB								
Casing Description Production		Run Date 10/17/2007	OD (in) 4 1/2	Wt/Len (l...) 11.60	Grade N-80	Top, MD (ft...) 12.0	MD (ftKB) 7,279.4	
Cement								
Description SURFACE CASING CEMENT					Top Depth (ftKB) 12.0		Bottom Depth (ftKB) 687.0	
Description PRODUCTION CASING CEMENT					Top Depth (ftKB) 6,328.0		Bottom Depth (ftKB) 7,279.4	
Tubing Strings								
Tubing Description Tubing - Production		Run Date 1/5/2008	String... 2 3/8	ID (in) 1.995	Wt (lb/ft) 4.70	Grade J-55	Len (ft) 7,157.00	Set De...
Tubing Components								
Item Des		OD (in)	Wt (lb/ft)	Grade	Jts	Len (ft)	Btm (ftKB)	Btm (TVD) (ftKB)
Tubing		2 3/8	4.70	J-55	224	7,155.40	7,167.4	
Pump Seating		2 3/8			1	1.00	7,168.4	
Nipple								
Notched collar		2 3/8			1	0.60	7,169.0	
Perforation Data								
Zone		Bnch/St g	Entered Shot Total	Top (ftKB)		Btm (ftKB)		Date
CODELL, ORIGINAL HOLE			52	7,151.00		7,164.00		11/27/2007
Stimulations & Treatments								
Date 12/1/2007		Zone CODELL, ORIGINAL HOLE			Primary Job Type DRILLING/COMPLETION - ORIGINAL			
Technical Result			Tech Result Details			Tech Result Note		
Comment								
Other In Hole								
Run Date		Des			OD (in)	Top (ftKB)	Btm (ftKB)	
Logs								
Date		Type				Top, MD (ftKB)		Btm, MD (ftKB)
10/17/2007		COMPENSATED DENSITY				3,750.0		7,293.0
10/17/2007		INDUCTION				675.0		7,313.0
11/27/2007		CBL/CCL/GR				6,200.0		7,243.0

**Well Name: WILHITE 30-31**

VERTICAL - ORIGINAL HOLE, 10/24/2016 2:53:33 PM

## Logs

