


**TEP Rocky Mtn
TR 334-27**

Sidetrack diagram

SHL Location:
200' FSL and 257' FEL
Sec 27, T5S, R97W
Garfield County, Colorado

API # 05-045-23333-00

NOTE: No cement plugs were set as hole bridged off

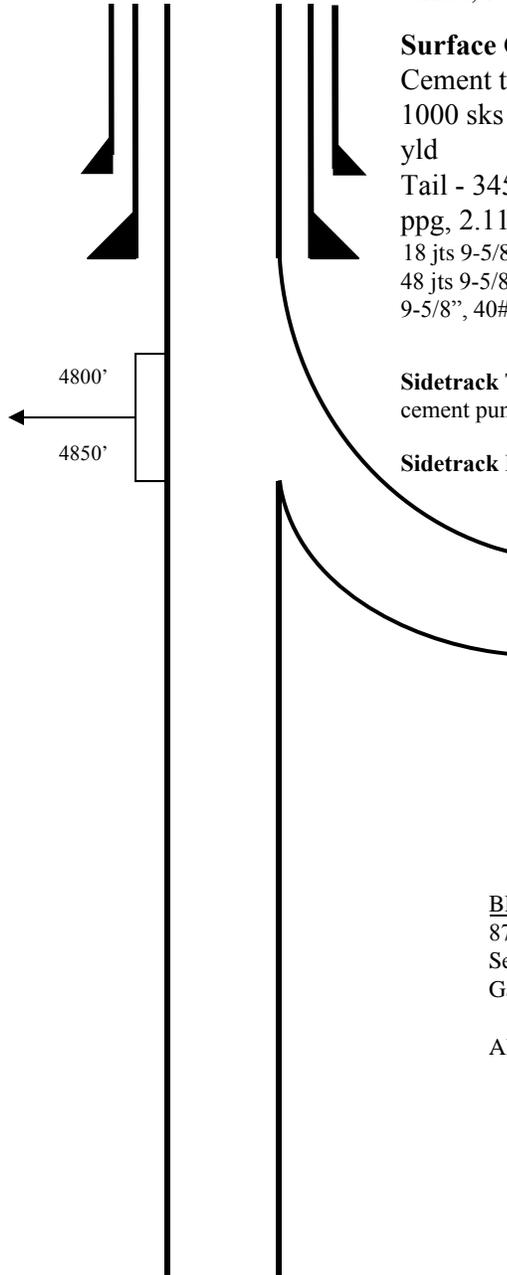

Conductor Casing @ 60',
26" hole, 3 jts, 18", 47#,
Welded,
.250 API5L X42, Cement to
surface, 100sks, ready mix

Surface Casing @ 2799'
Cement to surface -Lead
1000 sks 12.3 ppg, 2.38
yld
Tail - 345 sks of 12.8
ppg, 2.11 yld.
18 jts 9-5/8", 40#, J-55, LT&C
48 jts 9-5/8" 36#, J-55, LTC 1 jt
9-5/8", 40#, J-55, ST&C

**Sidetrack TOC - N/A as No
cement pumped**

Sidetrack KOP @ 4800'

Sidetrack: 8.75" hole
Well TD @ 9902'
Permitted depth 10.039'

BHL Location:
876' FSL and 2268' FEL
Sec 27, TS, R97W
Garfield County, Colorado

API # 05-045-23333-00

**TD @ 8899'
8.75" Hole**
