



New Day Set-Up

Well Name: Gibson Gulch Unit 13-28

Date: 9/30/2017, **Report #:** 1.0, **DFS:** 8,027.25

Job Type: Reconfigure Tubing/Components

Click on the 'New' button to start a new daily report.

Report Start Date 9/29/2017 06:00	Report End Date 9/30/2017 06:00
--------------------------------------	------------------------------------

Operations Summary
MIRU MWS #3 AND RELATED EQUIPMENT, PULL AND LD TBG, PU AND RIH W/KLINE RETRIEAVABLE BRIDGE PLUG, SET ABOVE PERF'S TO ISOLATE PRODUCTION ZONE FROM SURFACE. LAND WELL CIRCULATE PACKER FLUID, PRESSURE TEST RDMO

Operations Next Report Period
NO PRODUCTION

Daily Contacts

Job Contact

JOHN RANTS, <title>

Time Log

Start Date	End Date	Dur (hr)	Cum Dur (hr)	Code 1	Code 2	Unschd Type	Com
9/29/2017	9/29/2017	1.00	1.00	RMOV	Rig Move		MOVE RIG OVER FROM 16-29 WELL TO 13-28 WELL AND RIG UP
9/29/2017	9/29/2017	1.00	2.00	BOPI	Install BOP's		ND WELL HEAD, NU BOP'S
9/29/2017	9/29/2017	2.00	4.00	PULT	Pull Tubing		PULL AND LD 181 JTS 2 3/8 4.7# J-55 TBG
9/29/2017	9/29/2017	3.00	7.00	RUTB	Run Tubing		WITH MILLER PUMPS & PACKERS HAND MAKE UP 5 1/2" KLINE RETRIEABLE BRIDGE PLUG AND RETRIEVING HEAD, RIH W/ 158 JTS 2 3/8 4.7" J-55 TBG TO SET @ 4942.29 LET GO OF BP AND LD 1 JT TBG, CIRCULATE 96 BBLs PACKER FLUID
9/29/2017	9/29/2017	1.00	8.00	BOPR	Remove BOP's		ND BOP'S NU WELL HEAD
9/29/2017	9/29/2017	1.00	9.00	SRIG	Rig Up/Down		RDMO
9/29/2017	9/30/2017	15.00	24.00	inactive	inactive		



Tubing

Well Name: Gibson Gulch Unit 13-28

API/UWI 05-045-07018	Surface Legal Location SWSW-28-6S-91W-W6M	Field Name Gibson Gulch	License #	State/Province Colorado	Well Configuration Type
Original KB Elevation (ft)	KB-Tubing Head Distance (ft)	Spud Date 10/9/1995 00:00	Rig Release Date	PSTD (All) (ftKB)	Total Depth All (TVD) (ftKB)

Main Hole: 9/29/2017 6:00:00 AM

Vertical schematic (actual)

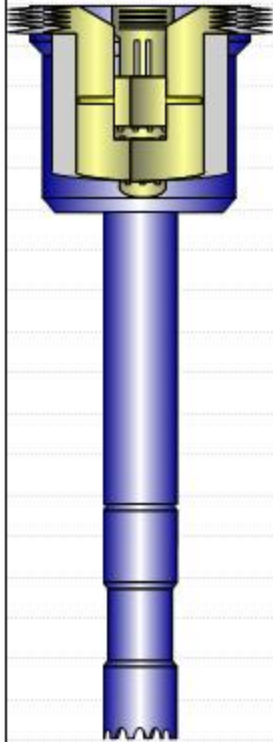

7-5; KLINE 5 1/2" RETRIEVABLE BRIDGE PLUG

Tubing															
Tubing Description						Set Depth (ftKB)		Run Date		Pull Date					
Tubing - Workstring										4,942.3		9/29/2017			
Jts	Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Len (ft)	Top (ftKB)	Bot (ftKB)						
1	Tubing Hanger	7	2.00			8-rd. e.u.e.	0.85	0.0	0.8						
157	Tubing	2 3/8	2.00	4.70	J-55	8-rd. e.u.e.	4,923.79	0.8	4,924.6						
	On-Off Tool	2 3/8	2.00			8-rd. e.u.e.	2.50	4,924.6	4,927.1						
1	Depth Correction					8-rd. e.u.e.	9.57	4,927.1	4,936.7						
1	KLINE 5 1/2" RETRIEVABLE BRIDGE PLUG	5	2.00			8-rd. e.u.e.	5.60	4,936.7	4,942.3						
	TOP PERF 5154	2 3/8				8-rd. e.u.e.		4,942.3	4,942.3						
	BOT PERF 7312	2 3/8				8-rd. e.u.e.		4,942.3	4,942.3						
