

P.O. Box 1751
Vernal, Utah 84078
(435) 823-3497

GREY ROCK CEMENTING

INVOICE
No 1151

Date 8-22/23/24/25, 2017
For PRE Resources Address 1888 Sherman Street #500 Denver CO
Lease Iles Dome #6 DOC-1 LLC Rig No. Stone 80203

CODE	DESCRIPTION	UNIT	AMOUNT	
1	Mileage Pump truck	290 mi	6 -	1740 -
	Mileage Crew truck	290 mi	3 50	1015 -
	Pump charge	3238 ft		4800 -
	Additional hours	3 hrs	725 -	2175 -
	Operator Expenses	3 men	450 -	1350 -
	Mileage Crew truck	40 mi	3 50	140 -
	Additional hours	9 hrs	725 -	6525 -
	Operator Expenses	3 men	450 -	1350 -
	Mileage Crew truck	40 mi	3 50	140 -
	Additional hours	8 hr	725 -	5800 -
	Mileage Crew truck	290 mi	3 50	1015 -
	Additional hours	4 hr	725 -	2900 -
2	Premium "G" Cement	400 sk	30 -	12000 -
	Calcium chloride	6 sk	157 -	942 -
	Sugar	200 lb	3 -	600 -
	Poly pipe + crossovers	100 ft	2 00	200 -
	CR-180	27 lb	5 20	140 40
	Blending charge	400 A3	3 40	1360 -
	Delivery charge <37,600 lbs>	2726 T/mi	2 15	5860 90
			2.10	5724 60
	Subtotal		49,917.00	50053 30
	Less Discount		27,454.35	22599 31
	Total		22,462.65	22599 31
	Tax			409 18
	TOTAL INVOICE			22871 83

Operator

Accepted and approved by

P.O. Box 1751
Vernal, Utah 84078
(435) 823-3497

GREY ROCK CEMENTING

JOB LOG
No 1150

Date 8-24 & 8-25, 2017

For PRE Resources DOC-1 LLC

Lease Iles Dome #6
Cont.

Rig No. Stone

TIME	DESCRIPTION	RATE	PSI	VOLUME
06:45	On location / Safety meeting			
	Run Tbg to tag cmt - tagged @ 1545'			
	POOH to 181' *3			
850	Start fresh	3	110	0
853	End			10
	Start cmt @ 15.8 lb/gal			0
855	End 33 SKS			6.7
	Start disp.			0
856	End	3	110	.3
905	POOH to 63' reverse well clean	3	80	15
	POOH WOC			
	Tag cmt ? with wireline			
	Didn't tag! ran with wireline did NOT tag!			
	Shoot holes @ 50' - EOT 304			
1333	Fresh Ahead	2	40	2
1334	Start cmt @ 15.8 lb/gal			20
1340	circ. outside 8 5/8 Ann. (up Dirt)			8
1351	cmt to surface			24
1354	End - No disp. (140 SKS)	2	40	28.6
	POOH			
	Wash up			
1500	Released from location			
8-25				
0630	On location			
08:00	Tag cmt @ 13'			
0900	Released from location			

Operator

[Signature]

Accepted and approved by

P.O. Box 1751
Vernal, Utah 84078
(435) 823-3497

GREY ROCK CEMENTING

JOB LOG
No 1149

Date 8-22-8-23, 2017

For Pre Resources

DOC - 1 LLC

Lease IKS Dome #6

Rig No. Stone

TIME	DESCRIPTION	RATE	PSI	VOLUME
10:30	On location			
	Safety meeting			
	Rig up			
	Safety Meeting - All personnel			
	EOT @ 3238' #1			
1206	Start fresh	3	240	0
1207	Catch circ.			2
1209	End			10
1209	Start cmt @ 15.8 ¹⁰ /gal		240	0
1221	End cmt. (140 sks .2% CR-180)		200	28.6
1221	Start disp.		40	0
1226	POOH End	3	40	15.8
	POOH - Wash up			
	WOC to tag / Tagged @ 2796'			
1710	POOH			
1730	Released from location			
0800	On location @ 08:00 8-23-17			
	Safety meeting			
830-845	PSI test Csg 15 mins. - HELD -			
1430	Perf @ 1800' & 166'			
	Trip in hole EOT @ 1805' #2			
1521	Start fresh (Circ. @ 2 gal)	3	210	0
1524	End			10
	Start cmt @ 15.8 ¹⁰ /gal			0
1530	End			18.4
	Start disp			0
1533	End	3	210	8.5
	POOH			
	Wash up			
1645	Released from location			

Operator

Russ Hall

Accepted and approved by

P.O. Box 1751
Vernal, Utah 84078
(435) 823-3497

GREY ROCK CEMENTING


JOB SUMMARY REPORT

No 1112


Customer PRE Resources DOC-1 LLC		Date 8-22-17		Ticket No. 8-23 + 8-24	
Lease & Well Name Iles Dome #6		Sec. 23	Twp. T4N	Range 92W	County Moffat Color
Job Type PTA		Drilling Contractor Stone			
Surface CSG Size CSG Not Here! 13" ?	Wt./Grade 50#	Thread No surface	Depth From ?	To 0	To 116'
Inter CSG Size	Wt./Grade	Thread	Depth From	To	
Prod. CSG Size 8 5/8	Wt./Grade 36#	Thread	Depth From 0	To 3314'	
Liner CSG Size	Wt./Grade	Thread	Depth From	To	
TBG or D.P. Size	Wt./Grade	Thread	Depth From	To	
SKS	Materials Furnished		Slurry Wt. P.P.G.	Slurry Yield FT³	Water Gal./Sk.
140	Premium "G" Cement, 2% CR-180		15.8	1.15	5
260	Premium "G" Cement		15.8	1.15	5
Float Equipment N/A - CR-180 low temp. retarder 27lbs in 1st 140sx Plug Calc to tag plugs					
Equipment & Personnel Gregg PerK 107-PT103 Pete 104-BT3					
Notes Plug #1 set @ 3238' - 2757' (481') tagged @ 2797' 140sx Plug #2 set @ 1805 - 1495' (310') tagged @ 1545' 90sx Plug #3 set @ 181' - 66' (115') tagged @ No tag 33sx Plug #4 set @ 304' - surface 137sx Tagged @ 13'					

PRE RESOURCES

AUG 22, 2017

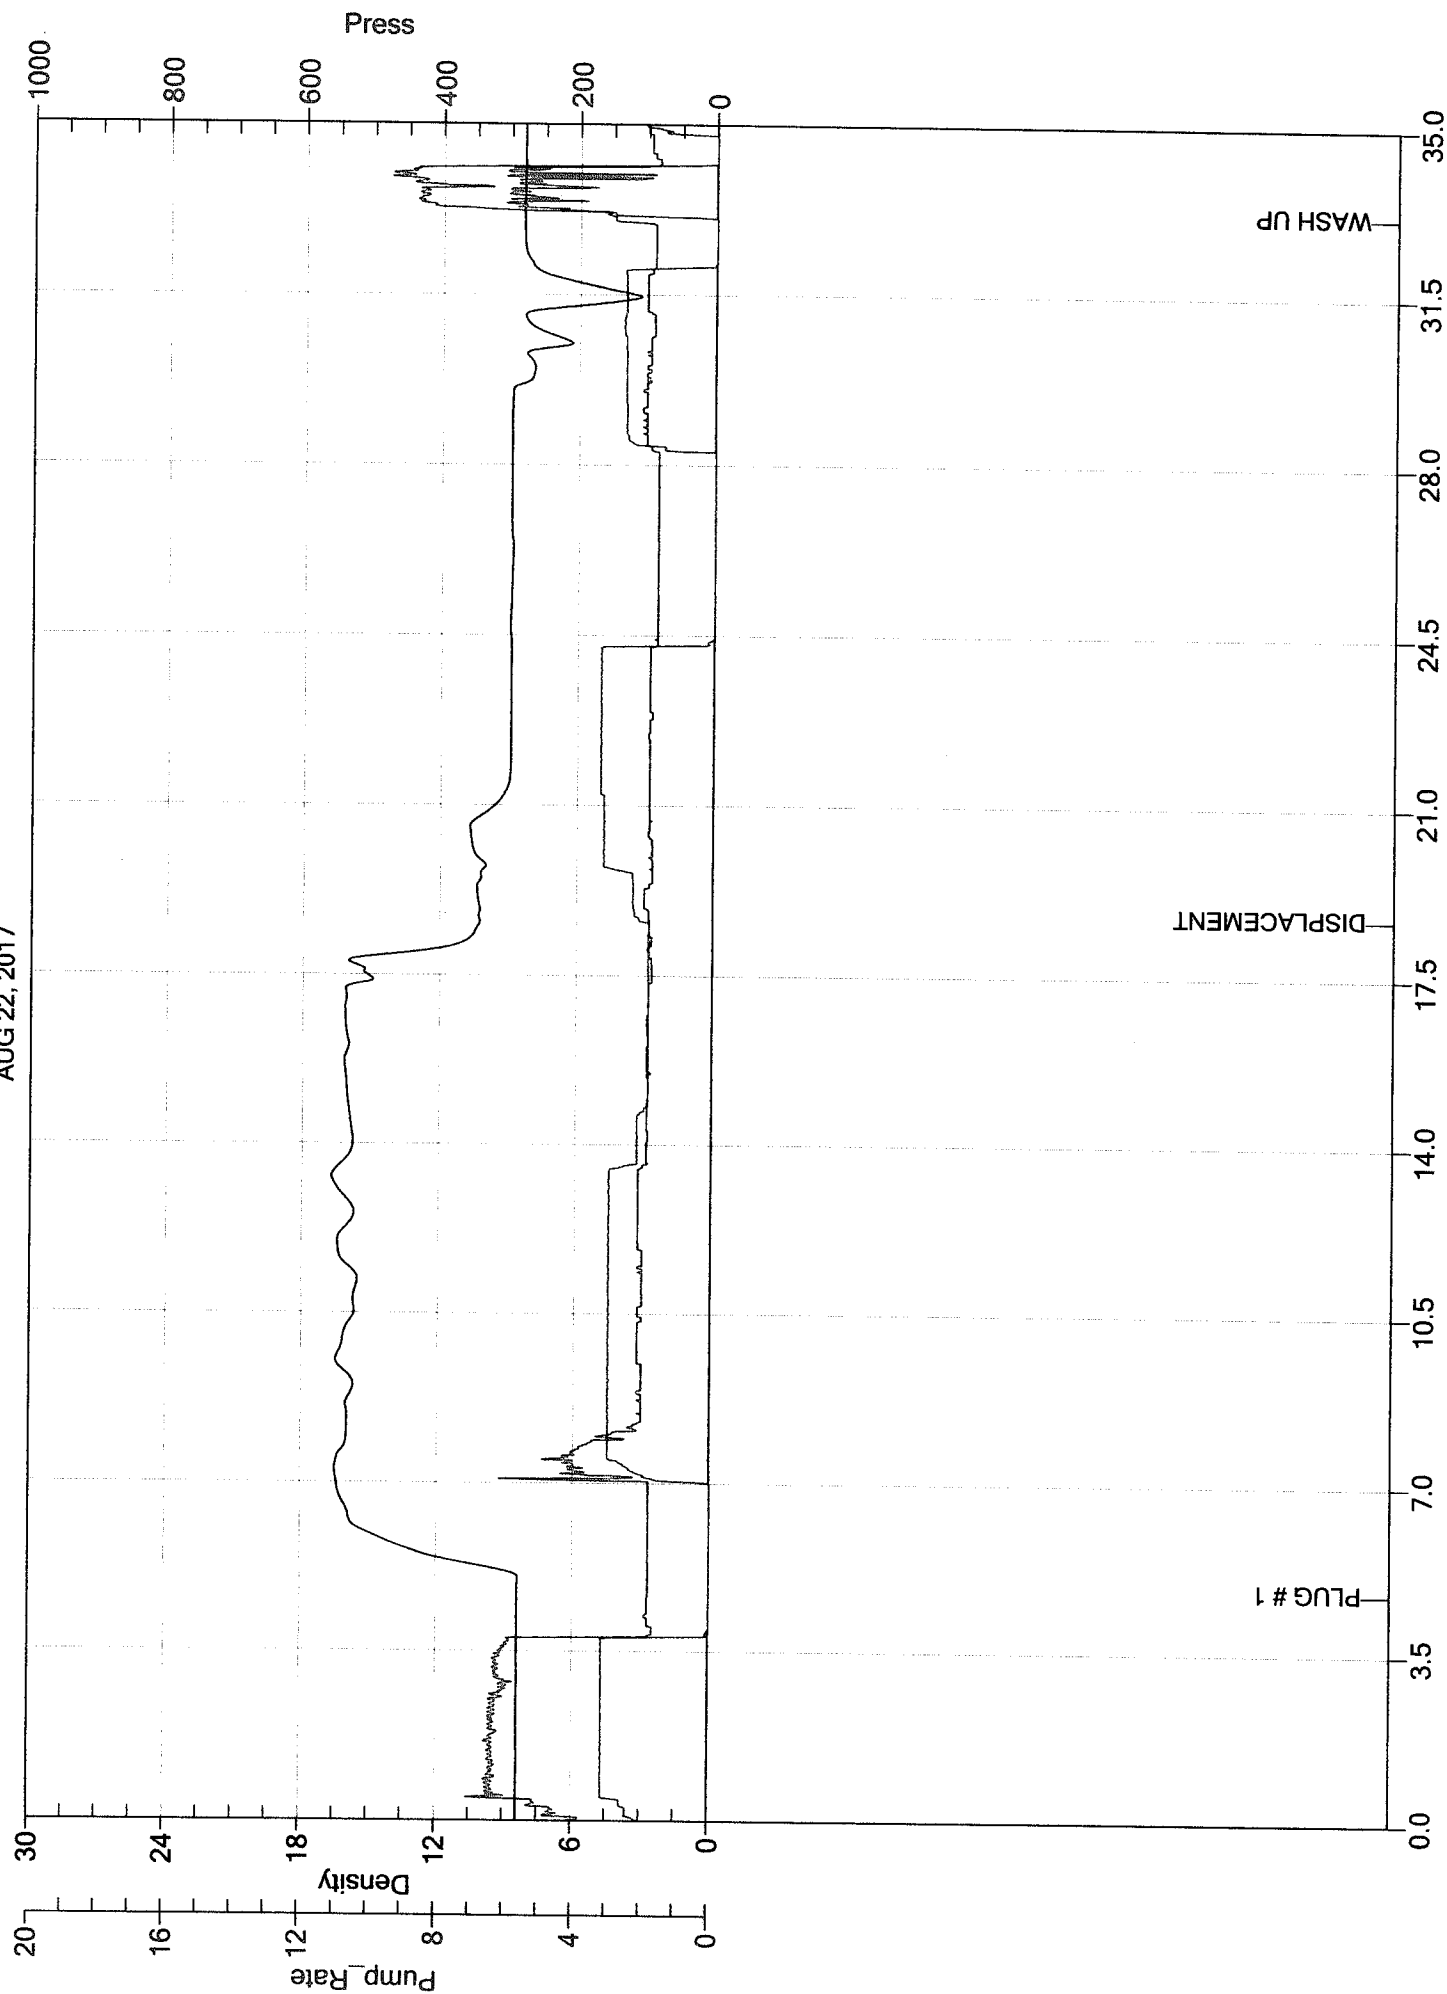

PRE RESOURCES
AUG 22, 2017

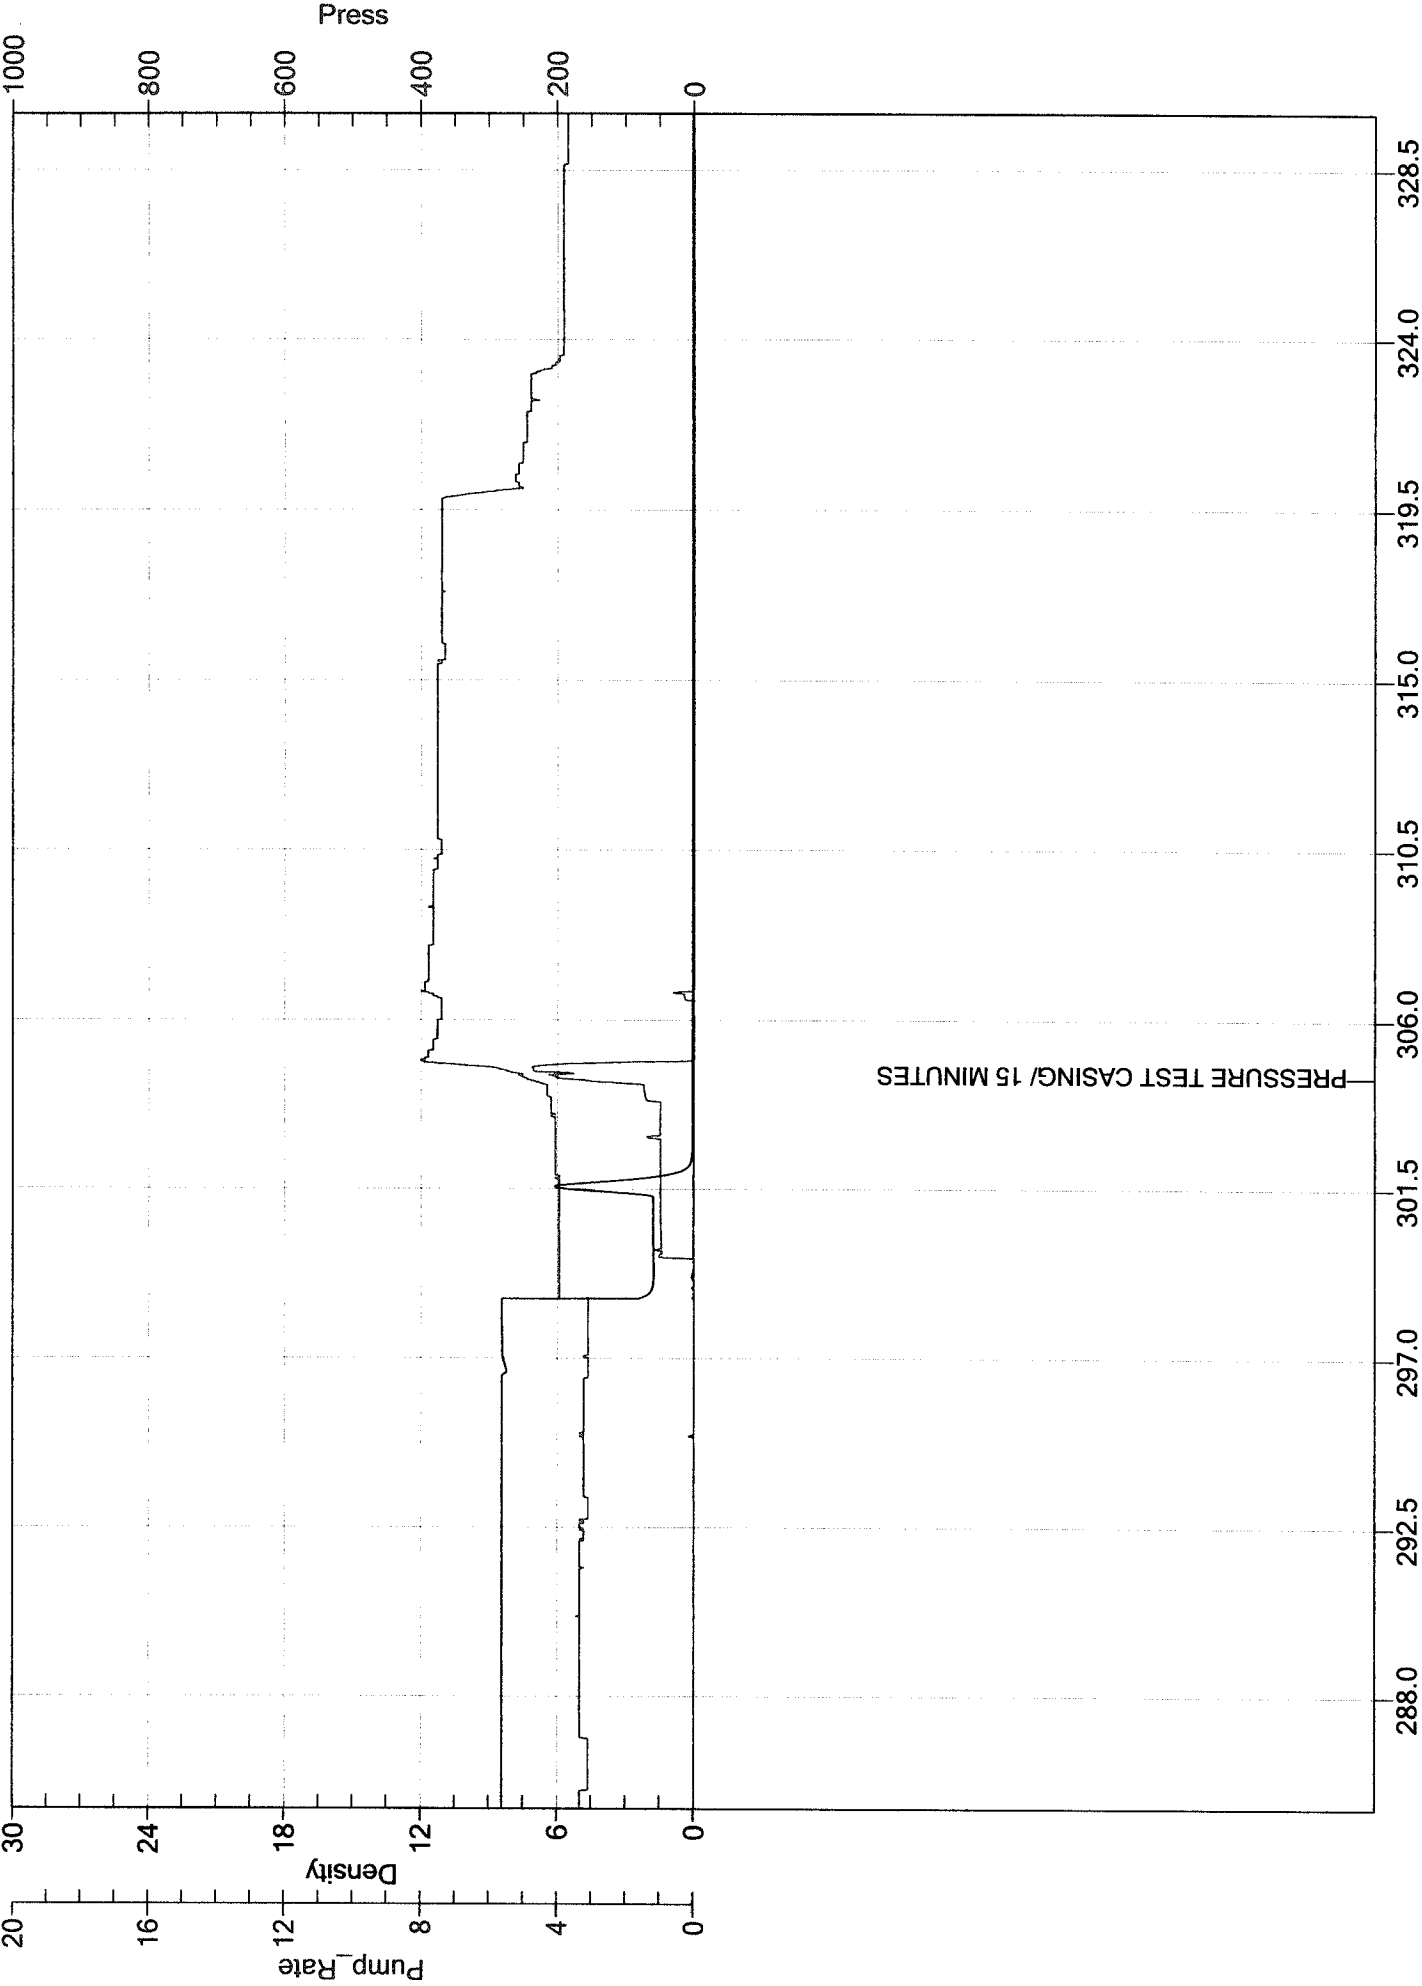

PRE RESOURCES

AUG 22, 2017

