



9.625" Deep Surface
Cement Post Job Report

Prepared For: Daniel Eldridge
Prepared Date: 7/31/2018
Job Date: 7/29/2018

HighPoint Operating
Lion Creek 23-0362B
Weld County, Colorado

Prepared By: Cody Michel
Phone: (303) 720-8081
Email: cody.michel@cjes.com

Job Summary

Ticket Number	Ticket Date
TN# FL4299	7/29/2018

COUNTY	COMPANY	API Number
Weld	HighPoint Operating	05-123-47399
WELL NAME	RIG	JOB TYPE
Lion Creek 23-0362B	WM 344	Deep Surface
SURFACE WELL LOCATION	O-TEX Field Supervisor	CUSTOMER REP
NENW 23-11N-64W	Scott, Derek	Daniel Eldridge

EMPLOYEES
<i>White, Cori</i>
<i>Lindsay, Kevin</i>

WELL PROFILE			
Max Treating Pressure (psi):	1500	Bottom Hole Static Temperature (°F):	0
Bottom Hole Circulating Temperature (°F):		Well Type:	Oil

Open Hole

1	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
	13.5	0	1538		
2	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)

Casing/Tubing/Drill Pipe

Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Surface	9.625	36	J-55	0	1538		
Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)

CEMENT DATA

Stage 1:	From Depth (ft):	0	To Depth (ft):	803
Type: Lead	Volume (sacks):	205	Volume (bbls):	90.5

Cement & Additives:	Density (ppg)	Yield (ft³/sk)	Water Req.
100% Control Set C+0.4% CF-41P+0.25#/sx Cello Flake	12	2.48	14.63

Stage 2:	From Depth (ft):	803	To Depth (ft):	1538
Type: Tail	Volume (sacks):	205	Volume (bbls):	63.9

Cement & Additives:	Density (ppg)	Yield (ft³/sk)	Water Req.
100% Control Set C+0.25#/sx Cello Flake	13.5	1.75	9.21

SUMMARY

		Stage 1	Stage 2
Preflushes:	22 bbls of Fresh Water	Calculated Displacement (bbl): 115.7	
	20 bbls of Dye	Actual Displacement (bbl): 117.7	
	bbls of		
Total Preflush/Spacer Volume (bbl):	42	Plug Bump (Y/N): N	Bump Pressure (psi): 330
Total Slurry Volume (bbl):	154.4	Lost Returns (Y/N): N (if Y, when)	
Total Fluid Pumped	314.1		
Returns to Surface:	Cement 15 bbls		

Job Notes (fluids pumped / procedures / tools / etc.): 41.17' of shoe joint, bump plug @1497' - 115.7bbls calculated. Pumped 2bbls over calculated displacement and did not bump.

Thank You For Using
O-TEX Cementing

Customer Representative Signature: _____


[illegible]




Client	High Point	Client Rep	Daniel Eldridge
Ticket No.	4299	Well Name	Lion Creek 23-0362B
Location	NENW 23-11N-64W	Job Type	Surface Casing
Comments	205sx Lead @ 12.0ppg 2.48yield and 205sx Tail @ 13.5ppg 1.75yield		

Supervisor	Derek Scott
Unit No.	445024
Service District	Brighton, CO
Job Date	07/29/2018


Unit 445024 Rate Total

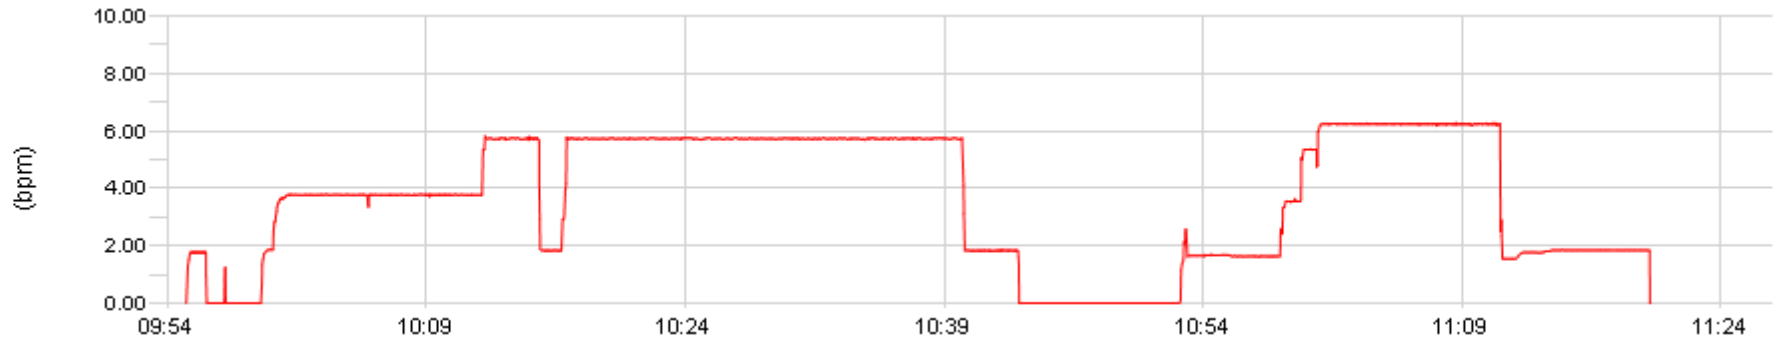

Unit 445024 Pump Pressure

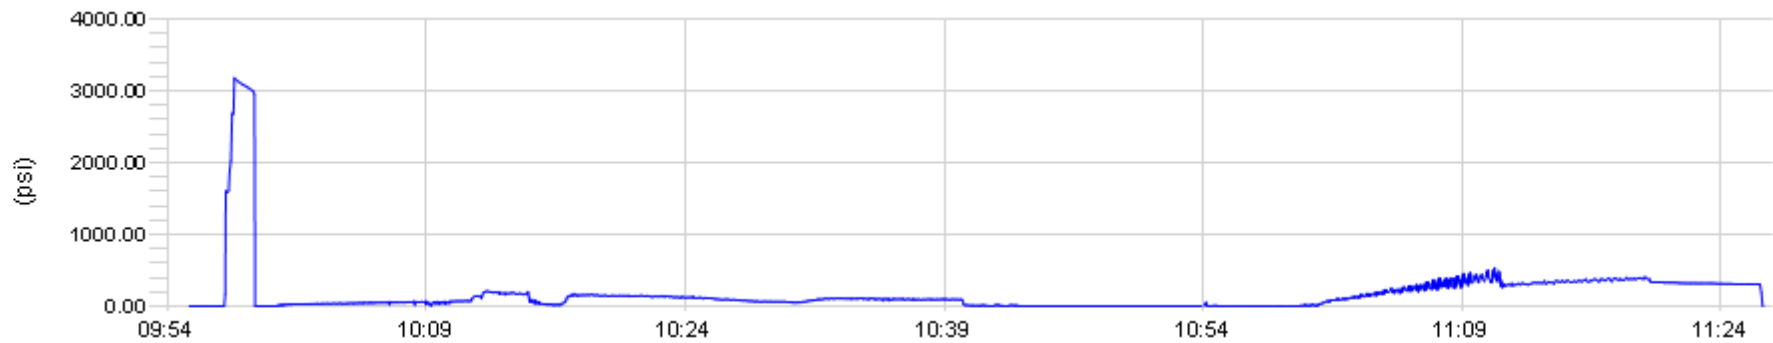

Unit 445024 Density

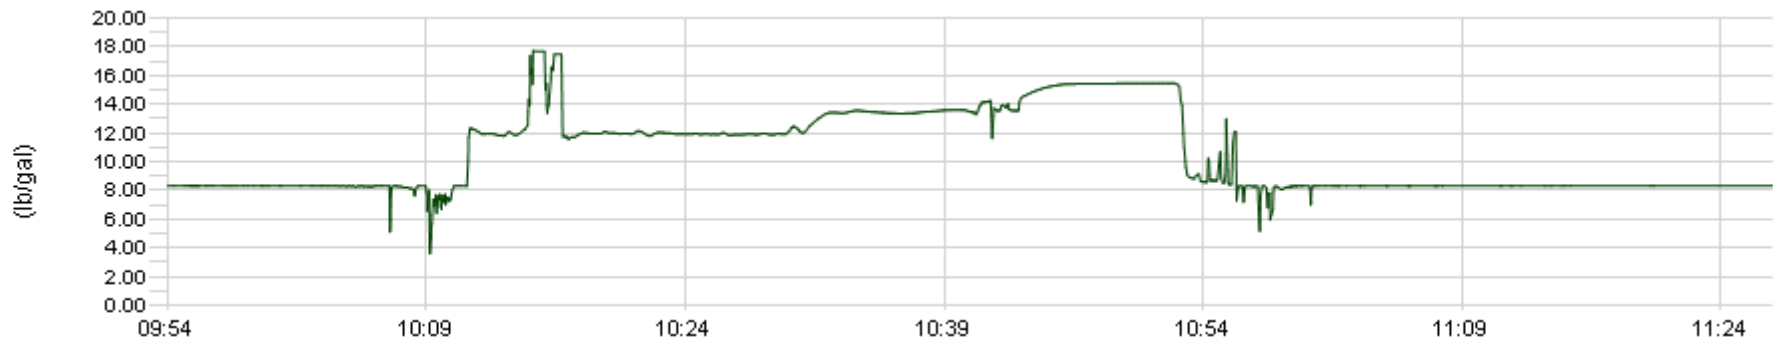



TN # FL4299

Service Date:	7/29/2018	Well Name:	Lion Creek 23-0362B	Job Type:	Deep Surface
Customer:	HighPoint Operating			Service Supervisor:	Scott, Derek
Address:	1099 18th Street, Suite 2300	County:	Weld		
City:	Denver	State:	Colorado		
St:	CO 80202	API #	05-123-47399		
Customer Rep:	Daniel Eldridge	AFE #	20242D	Pump #1	445024
				Pump #2	

[illegible]

I HAVE READ AND UNDERSTAND THIS CONTRACT AND REPRESENT THAT I AM AUTHORIZED TO SIGN THE SAME AS CUSTOMERS AGENT.

Customer Authorized Agent: _____

DISCLAIMER OF LIABILITY: With respect to this report, neither C&J Energy Services nor any of their employees, makes any warranty, express or implied, including the warranties of merchantability and fitness for a particular purpose, or assumes any legal liability or responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights.
