




00238816



OIL &amp; GAS

RECOMPLETION PROGNOSIS  
MOUNT HOPE WATER FLOOD  
UNIT 28-WI (Formerly Shell-Green A-11)

NWNE 30-9N-53W

Present Status:


DF: 4177

AFE: C-6416

DF-CHF: 11'

Proposed Work: (All depths refer to open-hole logs and are contingent on PDC log.)

1. Pull any production equipment in hole. Run sand pump, clean out to PBTD.
2. Run PDC from PBTD to 4700 if PDC log unavailable.
3. Perforate in water Muddy interval 4827-4838 w/4 jets/ft.
4. Install injection equipment and begin injecting down casing. Consult w/Division. (If unable to establish satisfactory rate, consider acidizing or fracture treating.)

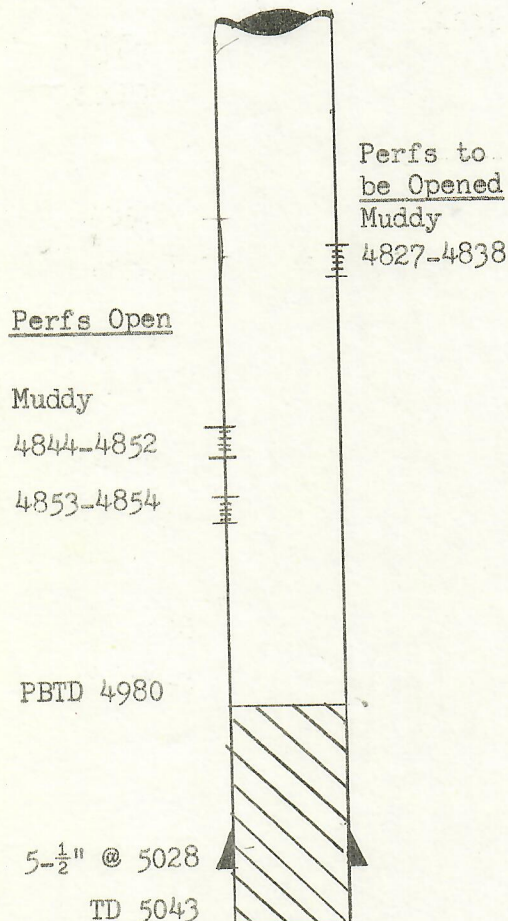

*J. D. Sweet*  
J. D. Sweet

*E. E. Saye*

for J. E. Saye

*A. T. Rylands*  
A. T. Rylands

9/21  
RGM/kw  
Billings, Montana  
November 20, 1962
