

# Inspection Photos

Operator: Enduring Resources  
API#: 067-07864  
Date: 4/14/2020



Photo 1. View of the project area from the northeastern corner facing center.





Photo 2. View of the eastern fill slope from the northeastern corner facing southward. Revegetation is progressing here with grasses and shrubs such as western wheatgrass, and rubber rabbitbrush.



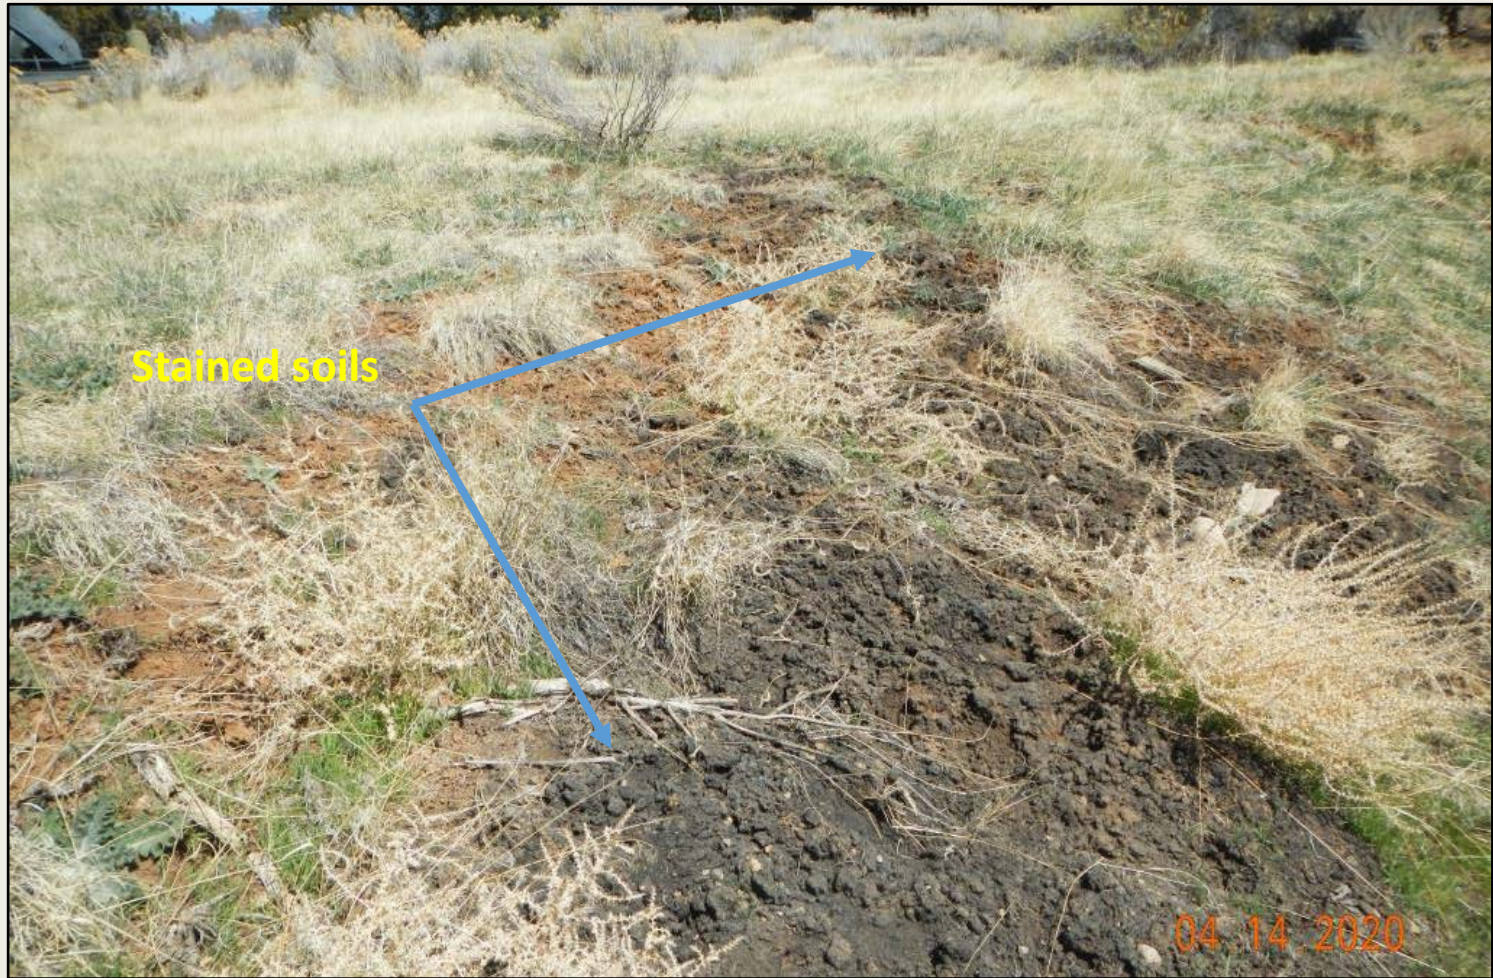


Photo 3. View of stained soils approximately 20 feet long and 6 feet wide, placed within the eastern portion of the interim reclamation area.





Photo 4. View of unmarked rig anchor on the well pad.





Photo 5. View of erosional rilling and channeling, approximately 2 feet wide and deep, occurring along the access road. Hard hat in place for scale reference.





Photo 6. View of area downstream from photo 5 where erosional channeling is occurring from diverted stormwater flowing off of the access road.





Photo 7. View of rutting on the access road, approximately 1.5 feet deep.





Photo 8. View of roadside ditch along access, that is not stabilized. Significant downcutting is observed, as ditch is approximately 4 feet wide and deep.





Photos 9/10. View of Scotch thistles within the project area, also observed along access. Approximately 300 individuals observed.





Photo 11. View of reference area, comprised of pinyon-juniper woodland with understory of gambel oak and mountain mahogany with grasses such as Arizona fescue.
