


Well Name: BOOTH USX EE25-25

VERTICAL, ORIGINAL HOLE, 8/5/2020 8:49:24 AM

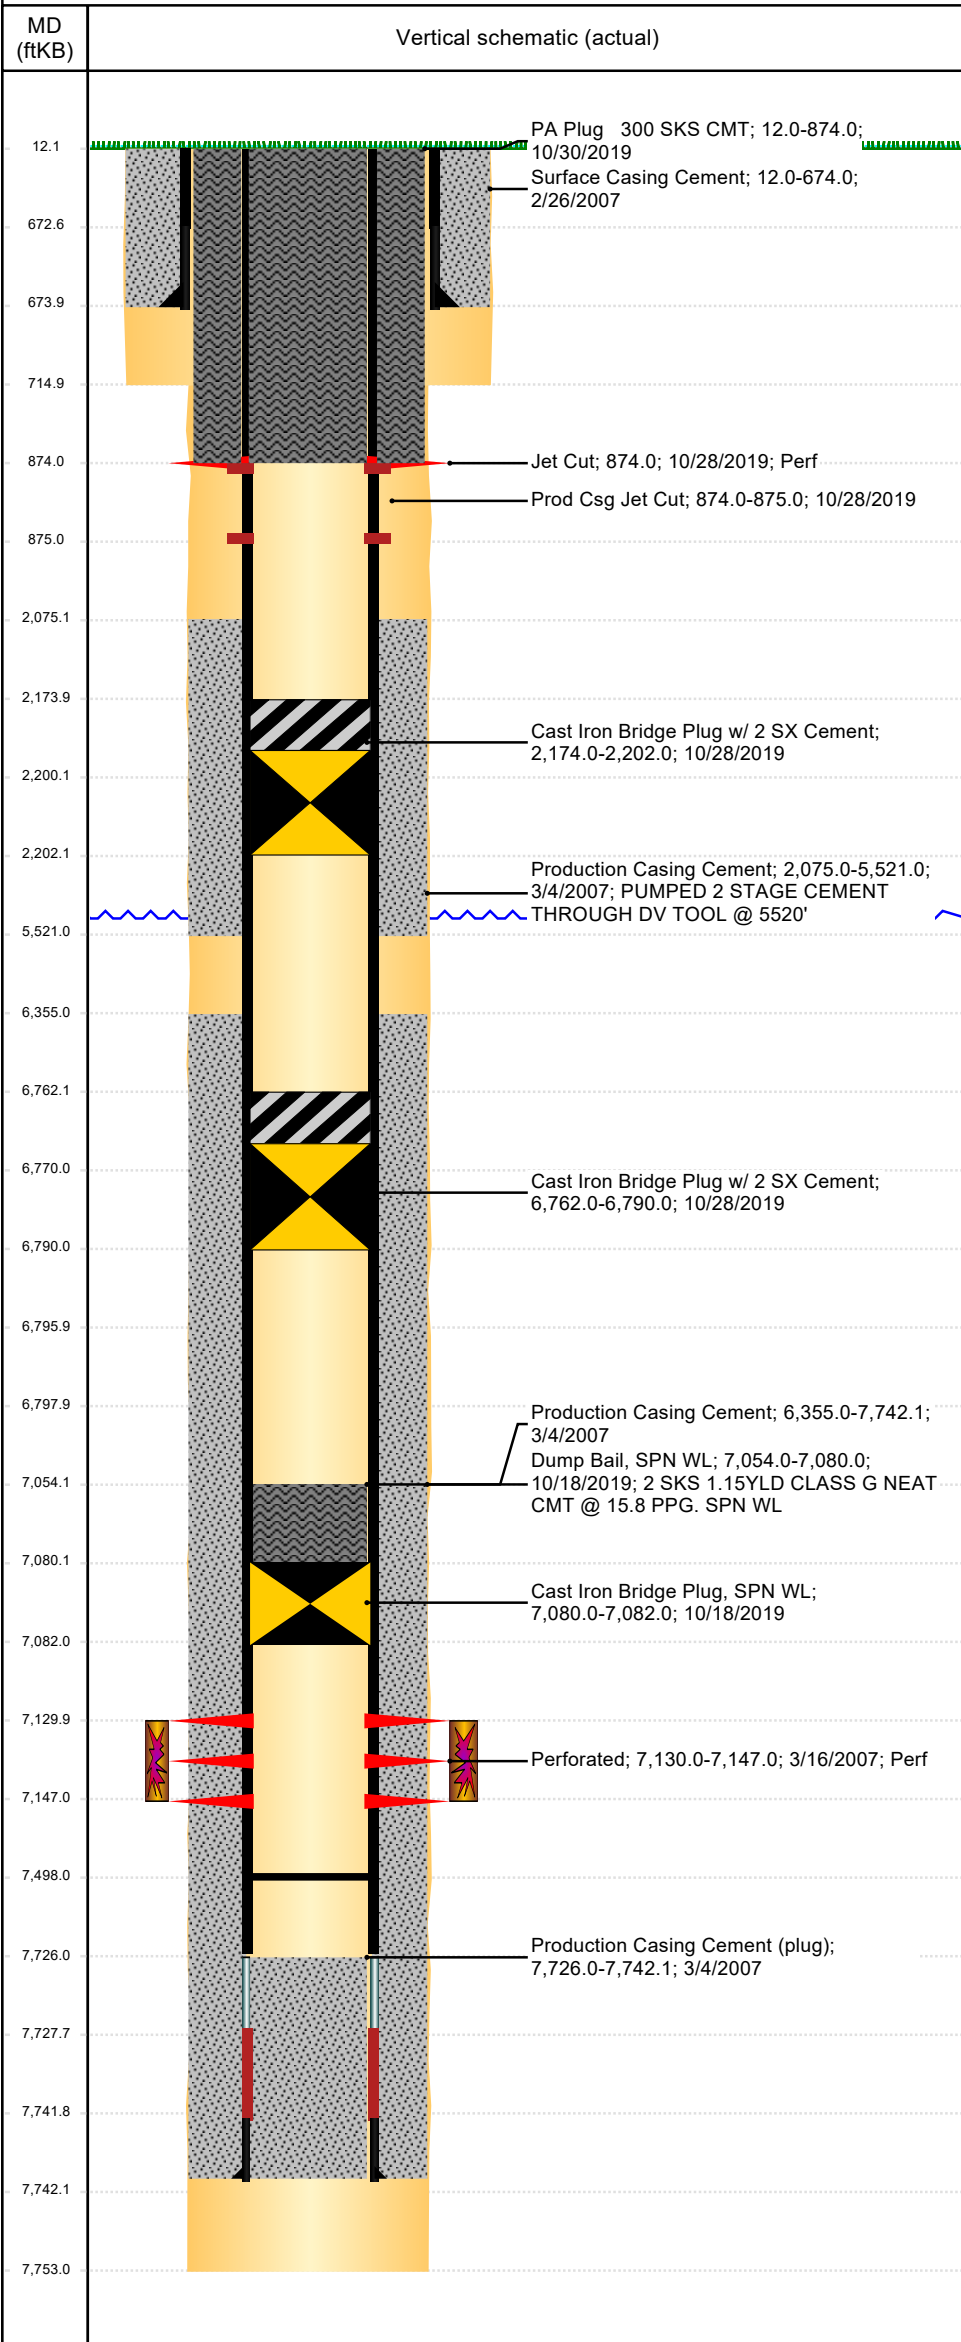

Well Header				
API	Business Unit	District	Well Configuration Type	
05-123-24717	DJ BASIN	15	VERTICAL	
KB - GL / MSL (ftKB)	Spud Date	P & A Date	Well Production Status	SoRT
12.00	2/25/2007	1/7/2020	PA	Yes

Comment
 DV TOOL +/- 5520', DRILLED OUT 03/13/07. 03/15/07 DV TOOL REPORTED LEAKING @ 5517', 10/17/2019: MOVE IN SERVICE UNIT, LD TBG, SET CIBP @ 7,080.0', DUMP BAIL 2 SKS CMT. TEST 500 PSI, GOOD TEST.

Surface Location (Congressional)								
Quarter 3	Quarter 4	Section	Township	Twnshp N	Range	Rng E/W	Actual Latitude (°)	Actual Longitude (°)
SE	SW	25	7	N	65	W	40.54088509	-104.61557821

Wellbore Sections			
Section Des	Size (in)	Act Top, MD (ftKB)	Act Btm, MD (ftKB)
SURFACE	12 1/4	12	715
PRODUCTION	7 7/8	715	7,753

Casing Strings						
Csg Des	Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top, MD (ftKB)	MD (ftKB)
Surface	2/26/2007	8 5/8	24.00	J-55	12.0	674.0
Production	3/3/2007	4 1/2	11.60	M-80	12.0	7,742.1

Cement			
Des	Start Date	Top (ftKB)	Btm (ftKB)
Surface Casing Cement	2/26/2007	12.0	674.0
Production Casing Cement	3/4/2007	2,075.0	5,521.0
Production Casing Cement	3/4/2007	6,355.0	7,742.1
Dump Bail, SPN WL	10/18/2019	7,054.0	7,080.0
PA Plug 300 SKS CMT	10/30/2019	12.0	874.0

Zone Statuses					
Zone Name	Status Date	Status	Fluid Type	Job	Prod Method
CODELL	10/18/2019	TA		PLUG AND ABANDON, 10/15/2019 07:00	
CODELL	10/30/2019	P&A		PLUG AND ABANDON, 10/15/2019 07:00	

Perforation Data					
Linked Zone	Bnch/Stg	Entered Shot Total	Top (ftKB)	Btm (ftKB)	Date
CODELL, ORIGINAL HOLE		68	874.00	874.00	10/28/2019
CODELL, ORIGINAL HOLE			7,130.00	7,147.00	3/16/2007

Stimulation Intervals			
Zone	Start Date	Top (ftKB)	Btm (ftKB)
CODELL, ORIGINAL HOLE	3/26/2007	7,130.0	7,147.0
CODELL, ORIGINAL HOLE	3/26/2007		

Other In Hole					
Run Date	Des	Make	OD (in)	Top (ftKB)	Btm (ftKB)
10/18/2019	Cast Iron Bridge Plug, SPN WL		4	7,080.0	7,082.0
10/28/2019	Cast Iron Bridge Plug w/ 2 SX Cement		3.99	6,762.0	6,790.0
10/28/2019	Cast Iron Bridge Plug w/ 2 SX Cement		3.99	2,174.0	2,202.0
10/28/2019	Prod Csg Jet Cut		5 1/2	874.0	875.0

Logs			
Date	Type	Top, MD (ftKB)	Btm, MD (ftKB)
3/1/2007	COMPENSATED DENSITY	7,530.0	7,728.0
3/1/2007	INDUCTION	674.0	7,748.0
3/15/2007	CBL/CCL/GR	1,900.0	7,715.0

Plug Back Total Depths			
Date	Type	Com	Depth (ftKB)
3/30/2007	FILL	NO TAG	7,297.0
10/15/2019	FILL	FISHED ALL TOOLS AND TAG FILL FOR P&A PREP	7,498.0
