


**Well Name: MONFORT GILCREST K16-01**

VERTICAL, ORIGINAL HOLE, 11/13/2021 6:09:01 AM

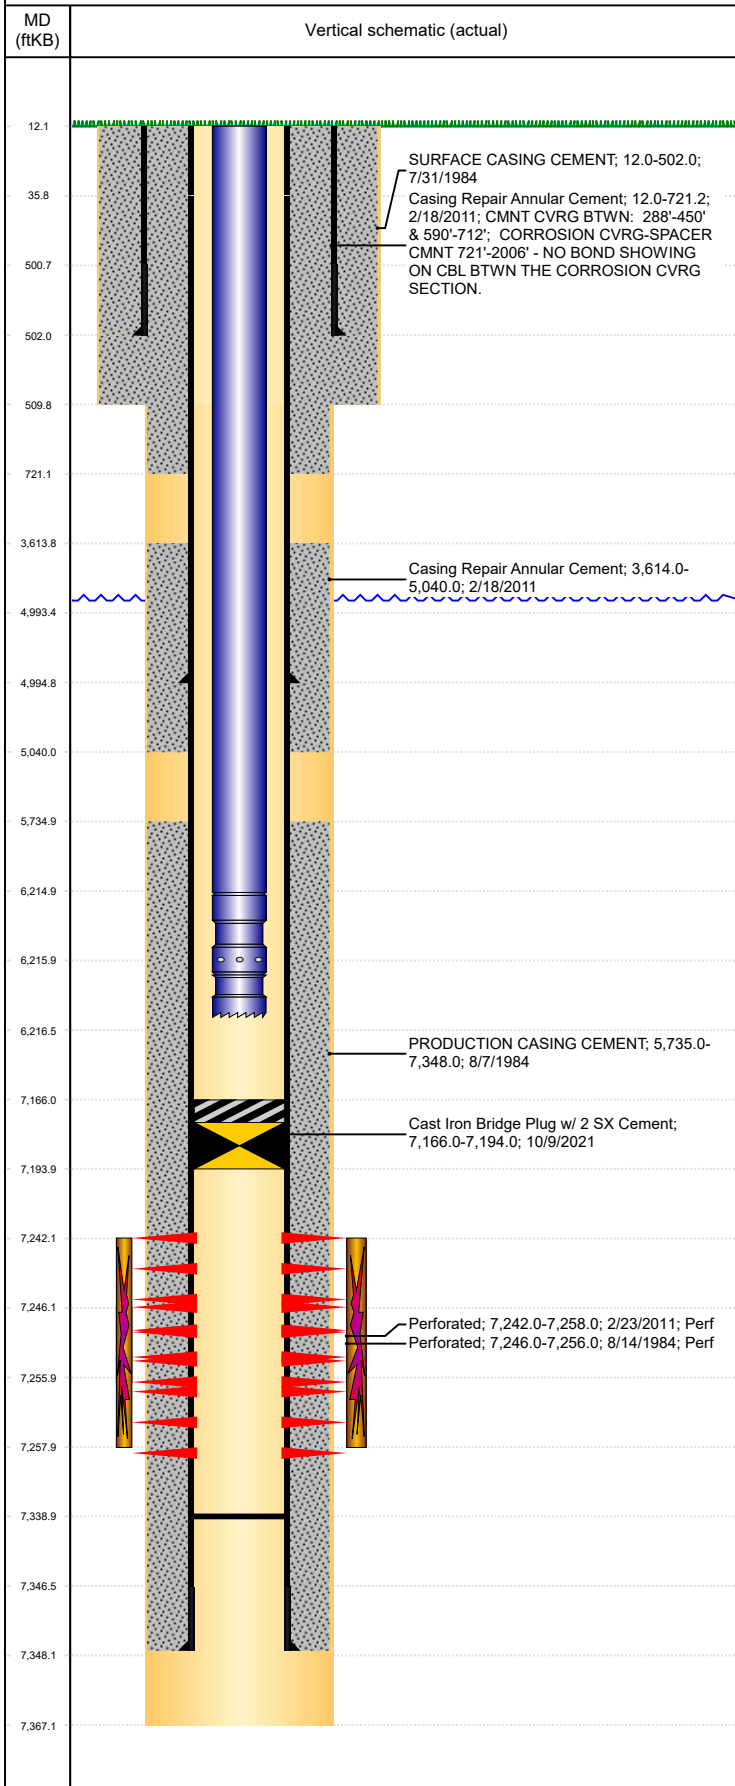

Well Header									
API 05-123-11511		Business Unit DJ BASIN			District 15		Well Config VERTICAL		
KB - GL / MSL (ft... 12.00		Spud Date 7/30/1984		P & A Date		Well Production Status TA			SoRT Yes
Comment NO WELLFILE INFO FROM ACQUISITION; SPUD TO 2010 DATA FROM COGCC WEBSITE.									
Surface Location (Congressional)									
Qtr 3 NE	Qtr 4 NE	Section 16	Twnshp 4	Twnsh... N	Range 66	Rng E/... W	Actual Latitude (°) 40.31709928	Actual Longitude (°) -104.77560637	
Wellbore Sections									
Section Des			Size (in)			Act Top, MD (ftKB)		Act Btm, MD (ftKB)	
SURFACE			12 1/4			12		510	
PRODUCTION			7 7/8			510		7,367	
Casing Strings									
Csg Des			Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top, MD (ftKB)	MD (ftKB)	
Surface			7/31/1984	8 5/8	24.00		12.0	502.0	
Production			2/15/2011	4 1/2	11.60	N-80	12.0	4,994.8	
Production			8/7/1984	4 1/2	11.60	?	4,994.8	7,348.0	
Cement									
Des				Start Date		Top (ftKB)		Btm (ftKB)	
SURFACE CASING CEMENT				7/31/1984		12.0		502.0	
PRODUCTION CASING CEMENT				8/7/1984		5,735.0		7,348.0	
Casing Repair Annular Cement				2/18/2011		12.0		721.2	
Casing Repair Annular Cement				2/18/2011		3,614.0		5,040.0	
Zone Statuses									
Zone Name		Status Date	Status	Fluid Type	Job			Prod Method	
CODELL		3/5/2011	PR	Gas	RE-FRAC, 12/1/2010 06:30				
CODELL		10/11/2021	TA	Gas					
Perforation Data									
Linked Zone			Bnch/Stg	Entered Shot Total	Top (ftKB)		Btm (ftKB)		Date
CODELL, ORIGINAL HOLE				64	7,242.00		7,258.00		2/23/2011
CODELL, ORIGINAL HOLE				21	7,246.00		7,256.00		8/14/1984
Stimulation Intervals									
Zone				Start Date		Top (ftKB)		Btm (ftKB)	
CODELL, ORIGINAL HOLE				3/4/2011		7,242.0		7,258.0	
CODELL, ORIGINAL HOLE				8/25/1984		7,246.0		7,256.0	
Other In Hole									
Run Date		Des			Make		OD (in)	Top (ftKB)	Btm (ftKB)
10/9/2021		Cast Iron Bridge Plug w/ 2 SX Cement					3.99	7,166.0	7,194.0
Logs									
Date		Type				Top, MD (ftKB)		Btm, MD (ftKB)	
8/7/1984		COMPENSATED DENSITY				4,290.0		7,365.0	
8/7/1984		INDUCTION				500.0		7,365.0	
8/14/1984		CEMENT BOND				5,493.0		7,297.0	
2/22/2011		CBL/CCL/GR				12.0		7,297.0	
Plug Back Total Depths									
Date		Type			Com				Depth (ftKB)
3/11/2011		FILL			FILL				7,334.5
2/13/2014		FILL			FILL				7,339.0
