

Brian Stanley


From: Jacobson - DNR, Eric <eric.jacobson@state.co.us>
Sent: Friday, December 24, 2021 7:17 AM
To: Brian Stanley
Cc: Jason Eisenach
Subject: [External]:Re: [External]:Re: Mile-Hi Duck Club Pascoe #1 CBL (05-001-06992)

Brian

Perfect!!

On Thu, Dec 23, 2021 at 10:01 PM Brian Stanley <BStanley@verdadresources.com> wrote:

Something like this? Full WBD attached as well.

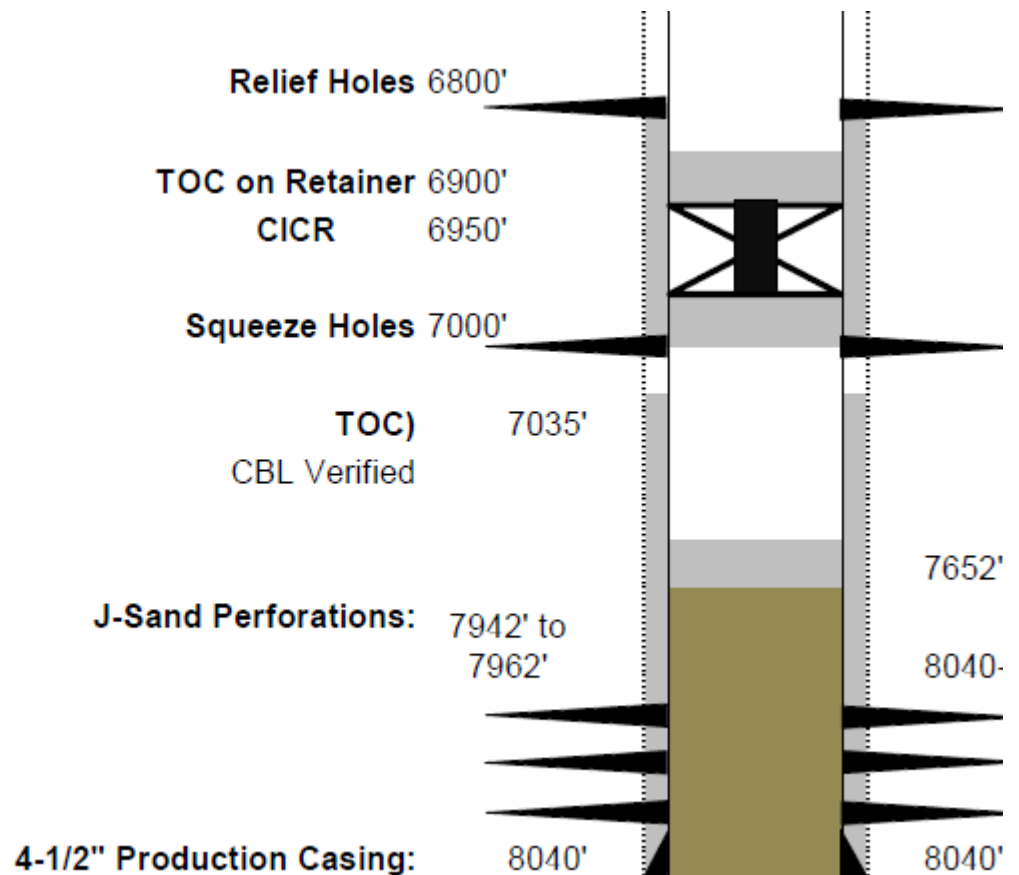

From: Jacobson - DNR, Eric <eric.jacobson@state.co.us>
Sent: Thursday, December 23, 2021 8:30 PM
To: Jason Eisenach <jeisenach@phxresources.com>

Cc: Brian Stanley <BStanley@VerdadResources.com>

Subject: [External]:Re: Mile-Hi Duck Club Pascoe #1 CBL (05-001-06992)

Brian

After reviewing the CBL, I would make one change on the lower plug.

Perforate at 7000' and pump 50 sacks of cement leaving 100' in the casing.

The rest of the plugs look good.

Eric

On Thu, Dec 23, 2021 at 5:47 PM Jason Eisenach <jeisenach@phxresources.com> wrote:

Jason Eisenach

O- 303.219.3362

M-970.301.0499

[5566 S. Sycamore ST](#)

[Littleton, CO 80120](#)



From: Brian Stanley <BStanley@VerdadResources.com>
Sent: Tuesday, December 21, 2021 4:48:32 PM
To: Jacobson - DNR, Eric <eric.jacobson@state.co.us>
Cc: Jason Eisenach <jeisenach@phxresources.com>
Subject: Mile-Hi Duck Club Pascoe #1 CBL (05-001-06992)

Eric,

Just wanted to give you a heads up. We're planning on pulling the CBL pass on this well tomorrow afternoon/Thursday morning. With CPW's guidance to get this done ASAP, we're going to try and cram as much in as possible as fast as we can, so I just wanted to let you know to keep an eye out for it in case we need to adjust.

Thanks,

Brian Stanley

Sr. Completions Engineer


435-640-6426



--

Eric Jacobson, PE

Engineer



[303-894-2100](tel:303-894-2100) (5265)

| [1120 N Lincoln St Ste 801, Denver, CO 80203](#)

--

Eric Jacobson, PE
Engineer



[303-894-2100](#) (5265)

[1120 N Lincoln St Ste 801, Denver, CO 80203](#)
