



9.625" Deep Surface
Cement Post Job Report

Prepared For:
Prepared Date: 7/31/2018
Job Date: 7/30/2018

HighPoint Operating
Lion Creek 23-0164B
Weld County, Colorado

Prepared By: Cody Michel
Phone: (303)720-8081
Email: cody.michel@cjes.com

Job Summary

Ticket Number		Ticket Date	
TN#	FL4311	7/30/2018	

COUNTY	COMPANY	API Number
Weld	HighPoint Operating	
WELL NAME	RIG	JOB TYPE
Lion Creek 23-0164B		Deep Surface
SURFACE WELL LOCATION	O-TEX Field Supervisor	CUSTOMER REP
	Cheal, Sam	Daniel

EMPLOYEES		
<i>White, Cori</i>		
<i>Roger, Peterson</i>		

WELL PROFILE			
Max Treating Pressure (psi):	1500	Bottom Hole Static Temperature (°F):	0
Bottom Hole Circulating Temperature (°F):		Well Type:	Oil

Open Hole

1	Size (in)	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
	13.5	0	1541	0	1541

Casing/Tubing/Drill Pipe

Type	Size (in)	Weight (lb/ft)	Grade	TMD From (ft)	TMD to (ft)	TVD From (Ft)	TVD to (Ft)
Surface	9.625	36	J-55	0	1541	0	1541

CEMENT DATA

Stage 1: From Depth (ft): To Depth (ft):

Type: **Lead** Volume (sacks): Volume (bbls):

Cement & Additives:	Density (ppg)	Yield (ft³/sk)	Water Req.
100% Control Set C+0.4% CF-41P+0.25#/sx Cello Flake	12	2.48	14.63

Stage 2: From Depth (ft): To Depth (ft):

Type: **Tail** Volume (sacks): Volume (bbls):

Cement & Additives:	Density (ppg)	Yield (ft³/sk)	Water Req.
100% Control Set C+0.25#/sx Cello Flake	13.5	1.75	9.21

SUMMARY

Preflushes:	20 bbls of Fresh Water	Calculated Displacement (bbl):	115.6
	10 bbls of Dye	Actual Displacement (bbl):	117
	2 bbls of Fresh Water		
Total Preflush/Spacer Volume (bbl):	32	Plug Bump (Y/N):	Yes
Total Slurry Volume (bbl):	154.3	Lost Returns (Y/N):	No (if Y, when)
Total Fluid Pumped	303.3	Bump Pressure (psi):	750
Returns to Surface:	Cement 10 bbls		

Job Notes (fluids pumped / procedures / tools / etc.): **Surface Casing** - Pumped 20bbls fresh water, 10bbls fresh water with **red dye**, 2bbls fresh water spacer, Mixed / Pumped 90.5bbls lead cement @ 12.0ppg, Mixed / Pumped 63.8bbls tail cement @ 13.5ppg, Displaced with fresh water to bump plug, Float collar @ **1,496ft**. Float Shoe @ **1,541ft**. Estimated cement coverage **0 - 1,541ft**. Pumped job as per customers request. Detailed discription of events in job log.

Thank You For Using
O-TEX Cementing

Customer Representative Signature: _____

[illegible]




Client HighPoint Operating
Ticket No. FL4311
Comments See job log for details


Client Rep Daniel
Well Name Lion Creek 23-0164B
Job Type Surface casing

Supervisor Sam Cheal
Unit No. 445024
Service District Brighton, CO
Job Date 07/30/2018

Unit 445024 Rate Total

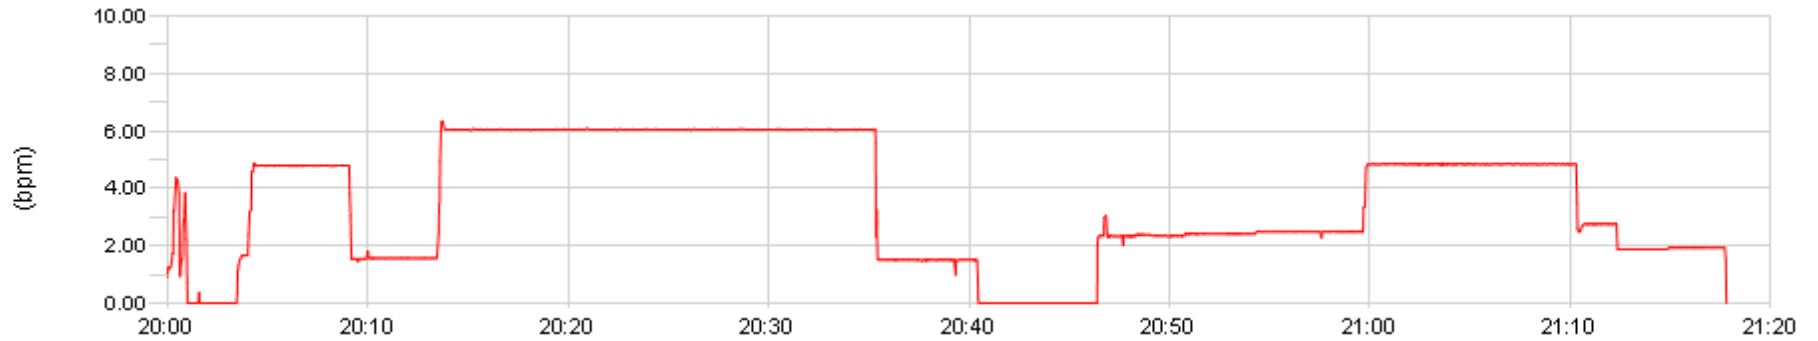

Unit 445024 Pump Pressure

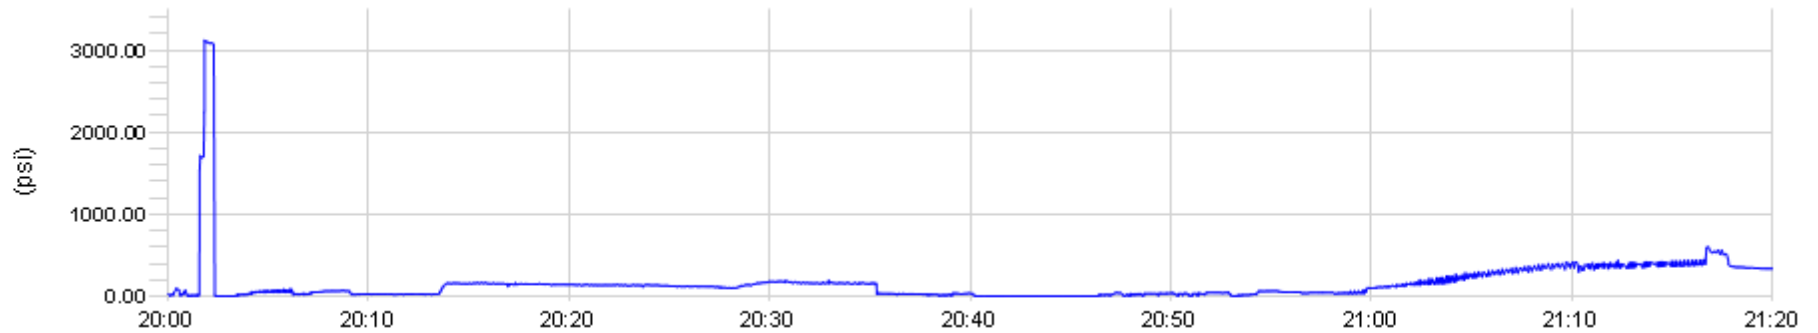

Unit 445024 Density






Client HighPoint Operating
Ticket No. FL4311
Comments See job log for details


Client Rep Daniel
Well Name Lion Creek 23-0164B
Job Type **BUMP**

Supervisor Sam Cheal
Unit No. 445024
Service District Brighton, CO
Job Date 07/30/2018

Unit 445024 Rate Total

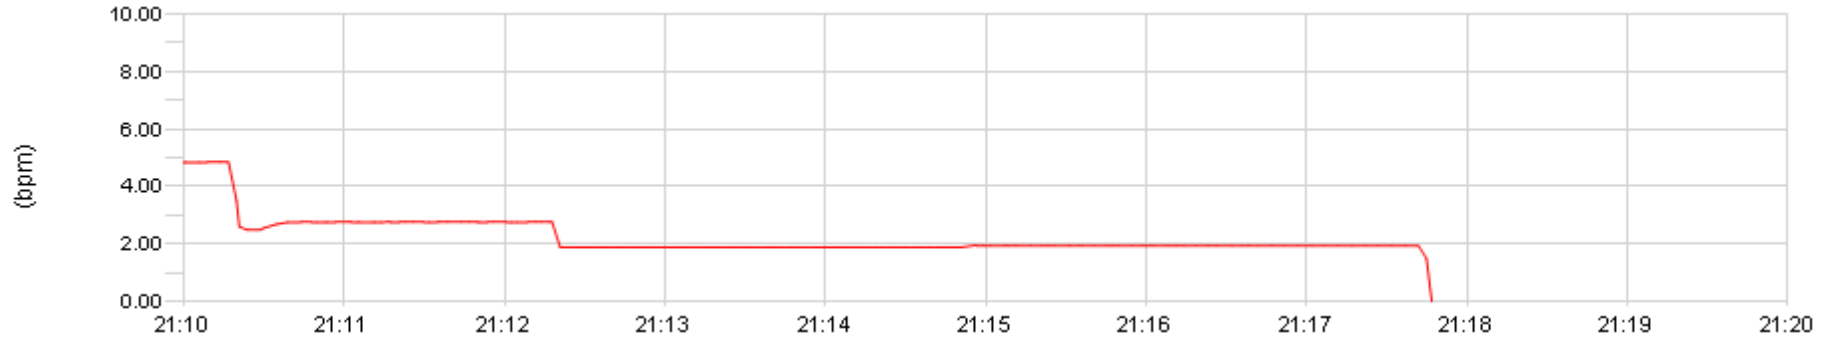

Unit 445024 Pump Pressure

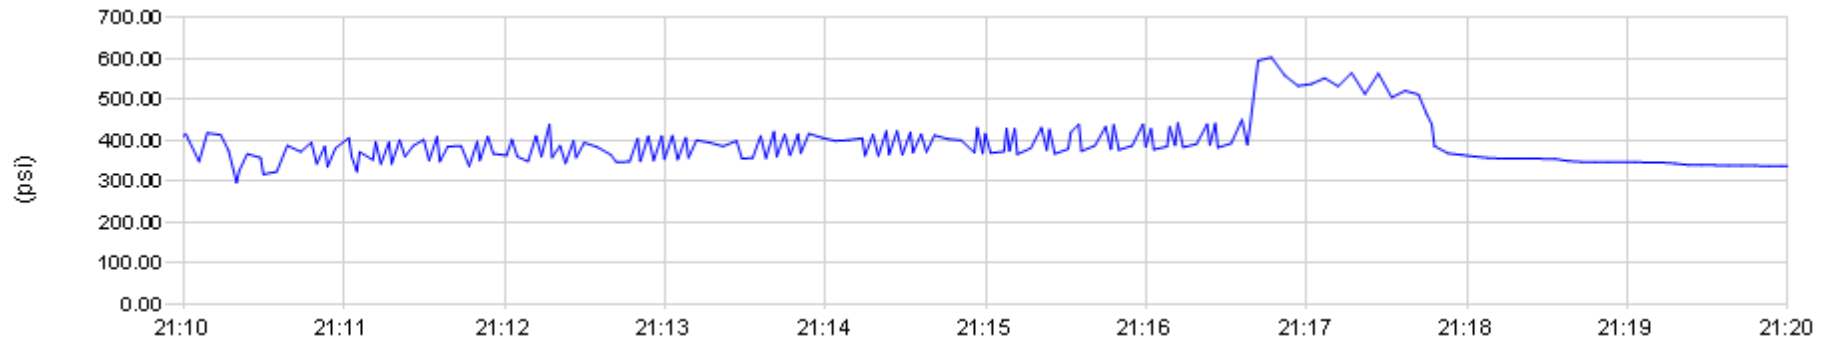

Unit 445024 Density

