

# WORK COMPLETE

## ANDERSON 1,2 & BATTERY



**Well Pad:** Anderson 1,2 & Battery

**Location ID #:** -

**Legal Description:** SESW SEC25 T5N R66W

**County:** Weld

**Date Work Completed:** March 30, 2023

**\*Reclamation Price:** \$5000.00

\*Reclamation Price includes cost of Reclamation/Baseline Plan.

### Activity Report

On March 30, 2023, H2 mobilized to location. The site was deep ripped to a depth of 18-inches, vibrashanked and disced to prep seedbed, then drilled in Dryland Grass seed mix with QuickGuard, one bale of certified weed free straw was blown across site and crimped into dirt. The site measured 0.5 acres.

### Photos



Photo 1. Photo point for the former Anderson 1,2 & Battery production facility before work was completed on March 30, 2023.



Photo 2. Photo point for the former Anderson 1,2 & Battery production facility after work was completed on March 30, 2023.

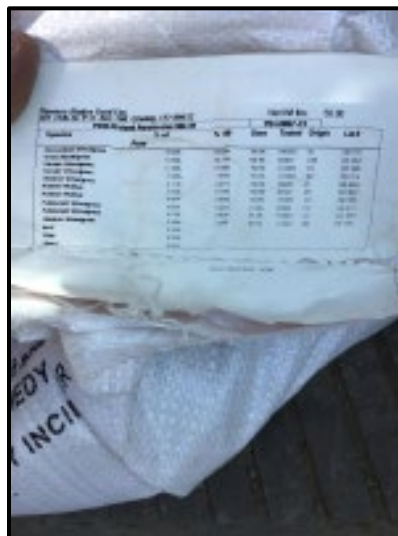


Photo 3. Seed mix used on Anderson 1,2 & Battery on March 30, 2023.
