




Wellbore Schematic Input Report

Well Name: GUTTERSEN STATE C36-775

Land, Original Hole, 5/10/2023 6:59:34 AM

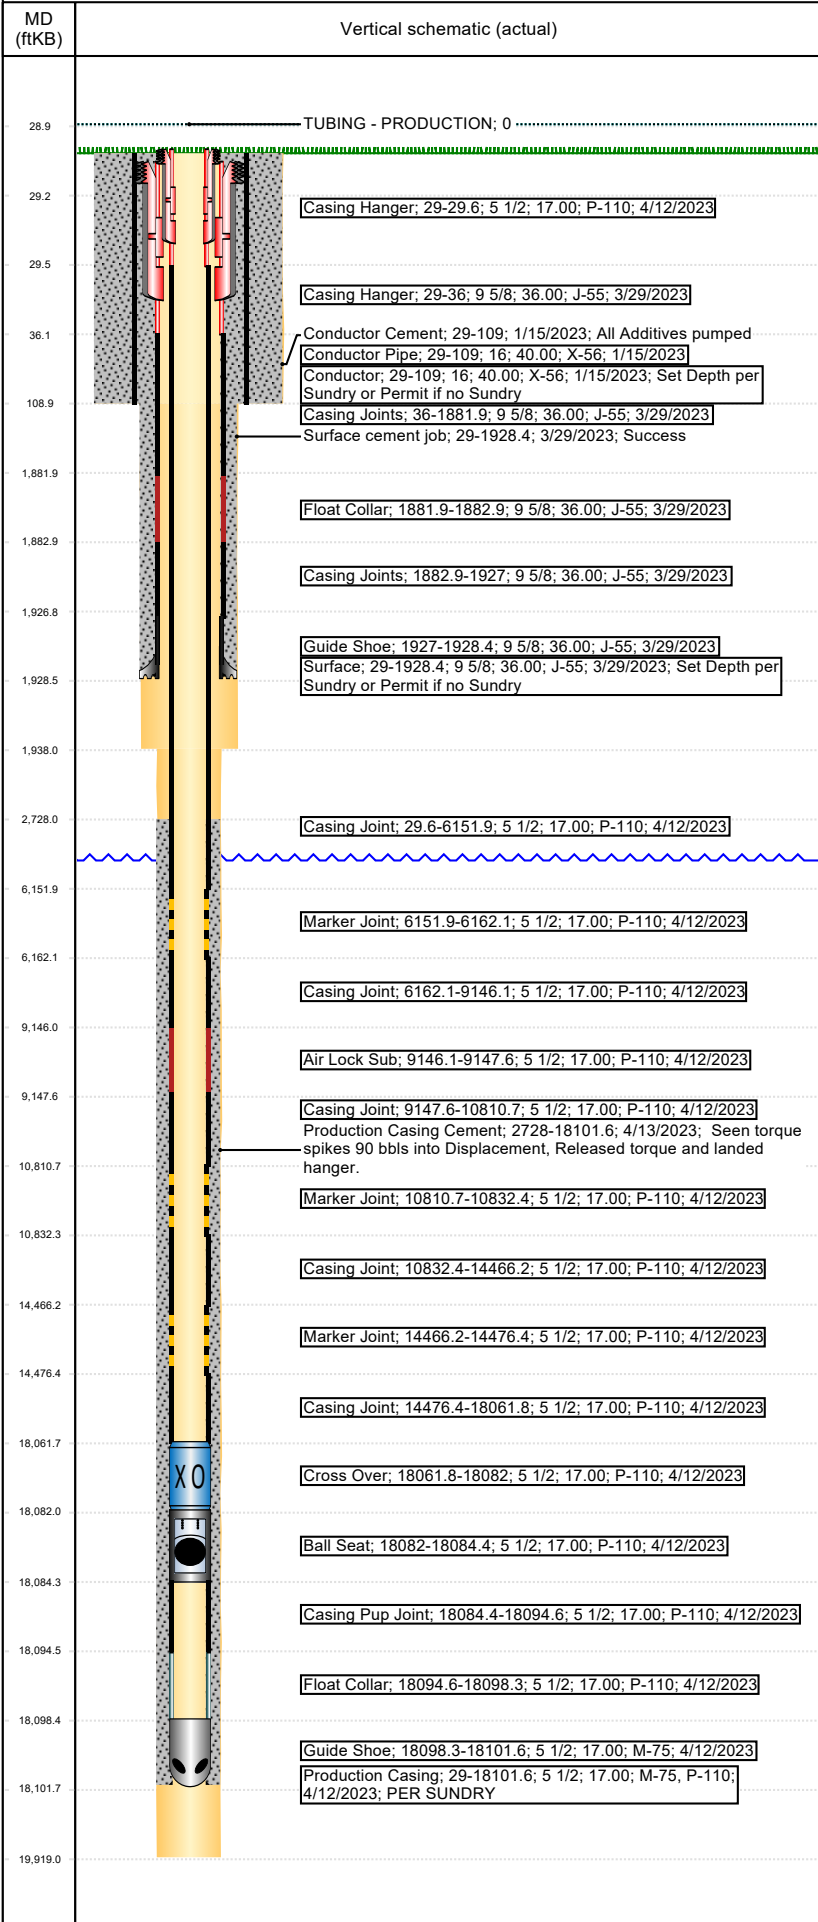

Well Header						
Surface UWI 0512349076		Asset Team		Production Tree Location Land		
Original RKB Elevation (ft) 4,775.00		Original KB to Ground (ft) 29.00		Original Spud Date 3/29/2023		Abandon Date
Range			Well Sub-Status PW		High Pressure N	
Directions To Well From intersection of CR53 & 34 (west/main gate) east 2.5 miles, north 1.5 miles, east 0.75 of a mile, northeast 0.4 of a mile, north into D01-03 Multi				Latitude (°) 40.260458604		Longitude (°) -104.502886211
Comment THERE IS AN EXCEPTION TO THE COGCC LOGGING REQUIREMENTS RULE 317.p. See Sundry Doc. # 402491254 dated 09/22/2020 for details. No special logging needed for D01-03-B Pad. The Gutteresen D12-755 API 05-123-49077 had a Cased Hole Neutron log run 5/17/2022 and it's part of the D01-03 Multi Pad.						
Congressional Location						
Quarter 3 NE	Quarter 4 NW	Section 1	Township 3	Township N/S Dir N	Range 64	Range E/W Dir W
Rig Operator						
Rig/Unit Supervisor						
Daily Cost Summary						
Sum of Field Est (Cost) 0						
Sum of Field Est (Cost) 0						
Plug Back Total Depths						
Date	PBTD (ftKB)	Method		Com		
4/12/2022	18,082	CSG TALLY		BALL SEAT SUB		
Wellbore Sections						
Section Des		Hole Size (in)		Act Top (ftKB)		Act Btm (ftKB)
CONDUCTOR		26		29.0		109.0
SURFACE		13 1/2		109.0		1,938.0
PRODUCTION		8 1/2		1,938.0		19,919.0
Zone Statuses						
Zone Name		Status Date		Status		
Casing Strings						
Conductor, Planned?-N, 109ftKB						
Casing Description	Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top Depth (M)	Set Depth (M)
Conductor	1/15/2023	16	40.00	X-56	29	109
Surface, Planned?-N, 1928.4ftKB						
Casing Description	Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top Depth (M)	Set Depth (M)
Surface	3/29/2023	9 5/8	36.00	J-55	29	1928.4
Production Casing, Planned?-N, 18101.6ftKB						
Casing Description	Run Date	OD (in)	Wt/Len (lb/ft)	Grade	Top Depth (M)	Set Depth (M)
Production Casing	4/12/2023	5 1/2	17.00	P-110	29	18101.6
Cement						
Des		Start Date		Top (ftKB)		Btm (ftKB)
Conductor Cement		1/15/2023		29.0		109.0
Surface cement job		3/29/2023		29.0		1,928.4
Production Casing Cement		4/13/2023		2,728.0		18,101.6
Proposed Cement						
Des				Top (ftKB)		Btm (ftKB)
Tubing Strings						
Tubing Description	Run Date	String Make	OD (in)	Wt (lb/ft)	Grade	Len (ft)
TUBING - PRODUCTION						
Other In Hole						
Run Date	Des		Make	OD (in)	Top (ftKB)	Btm (ftKB)
Proposed Other In Hole						
Des		Make		OD (in)	Top (ftKB)	Btm (ftKB)
Logs						
Date	Type			Depth Top (MD) (ftKB)		Btm (ftKB)
4/5/2023	Logging While Drilling (LWD)			1,925		19,911.0



Wellbore Schematic Input Report

Well Name: GUTTERSEN STATE C36-775

Land, Original Hole, 5/10/2023 6:59:34 AM

Job Supply Amounts

Supply Item Des	Job Supply Type	Unit L	Job Category	Total Req	Total Co	Total Re
-----------------	-----------------	--------	--------------	-----------	----------	----------

Daily Cost Breakdown by Category

Field Est (Cost)	Description	Note
------------------	-------------	------

