

DUCO INCORPORATED

Well Servicing Company
2403 1/2 E. Main - PO Box 416 (mailing)
Rangely, CO 81648
Phone (970)-629-1906 or (970)-675-8685

CMT Package

8/31/2023

INVOICE PDC #20.2023

COMMENTS

All CMT pumped by Duco in
will be 15.8lbs 1.15 yield class
g neat.

Hiring Company: PDC

CMT truck operator: Diego Cardona
CMT truck operator:
CMT truck operator:
Pod trailer operator: Kurtis Johnson
Pod trailer operator: Raudell Salazar
Labor Hand: Mike Birdow
Labor Hand: Jorge Gomez
Supervisor: Lane Griffin
Pump Unit: RCM-4

Fuel Used: 120 Gallons
Lease: Brighton Farms 1

PO:
Company Foreman: Bud Holman
Ensign Rig 313 (Matt McGraw)

Hour Work Started:
Hour Work Completed:

BREAKDOWN OF CHARGES	HOURS/QT.	RATE	AMOUNT
Day Rate for CMT truck	3.00	\$3,500.00	\$ 10,500.00
skts of cmt	1140.00	\$20.00	22,800.00
Calcium (50# Bag)	9.50	\$260.00	2,470.00
Clay Control (5 Gal Bucket)	3.00	\$200.00	600.00
Drilling Detergent (5 Gal Bucket)	4.00	\$200.00	800.00
LCM/3mm Radiclock Fiber (10# Bag)	0.00	\$1,200.00	
LCM Sawdust 50# Bag	1.00	\$100.00	100.00
SAPP	2.00	\$200.00	400.00
Standby (8-28-2023)	1.00	\$1,500.00	1,500.00
	0.00	\$0.00	
	0.00	\$0.00	
	0.00	\$0.00	
	0.00	\$0.00	

DESCRIPTION OF WORK PERFORMED:

Meet with company man and confirm numbers Daily. Safety meeting with duco crew and rig crew Daily. 8-28-2023 equipment and crew arrive on location. Job cancellation. standby charged. 8-29-2023 DAY ONE ON PUMP- First Pump: EOT 7349'. Mix and pump 250 sks/51.2 BBLS slurry 15.8# class G cement neat. 29 BBLS mix water used for slurry. 527' plug EST TOC 6822'. Displace 35.1 BBLS FW to balance. 8-30-2023 DAY TWO ON PUMP- Second Pump: EOT 2411'. Mix and pump 120 sks/24.6 BBLS slurry 15.8# class G cement with 2% calcium. 14.2 BBLS mix water used for slurry. 253' plug EST TOC 2158'. Displace 11.2 BBLS FW to balance. TAG. 8-31-2023 DAY THREE ON PUMP- Third Pump: EOT 1442'. Mix and pump 250 sks/51.2 BBLS slurry 15.8# class G cement with 2% calcium. 29 BBLS mix water used for slurry. 527' plug EST TOC 915'. Displace 4.7 BBLS FW to balance. 4 hour wait and TAG. Fourth Pump: EOT 695' surface job. Mix and pump 520 sks/104.4 BBLS slurry 15.8# class G cement neat. 62 BBLS mix water used for slurry. Good cement circulated to surface. TOH and secure wellhead cap. no top off necessary.

#

SUBTOTAL	\$ 39,170.00
TAX RATE	0.00%
SALES TAX	-
OTHER	
TOTAL	\$ 39,170.00

Bud Holman

9-11-23
PD-900073-0024
8030.013

All accounts net 30 days. 24% per annum interest plus cost of attorney's fees and collection fees

THANK YOU FOR YOUR BUSINESS!



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: PDC
Contact: Bud
Phone: 0

Email: 0



JOB DETAILS

Date: 8-29-2023
Start Time: 14:21:10
End Time: 14:45:59

Operator: Diego Cardano
Ticket #: 0
LSD #: Brighton Farms 1

Comments: 1st pump 250sks class G

SUMMARY GRAPHS

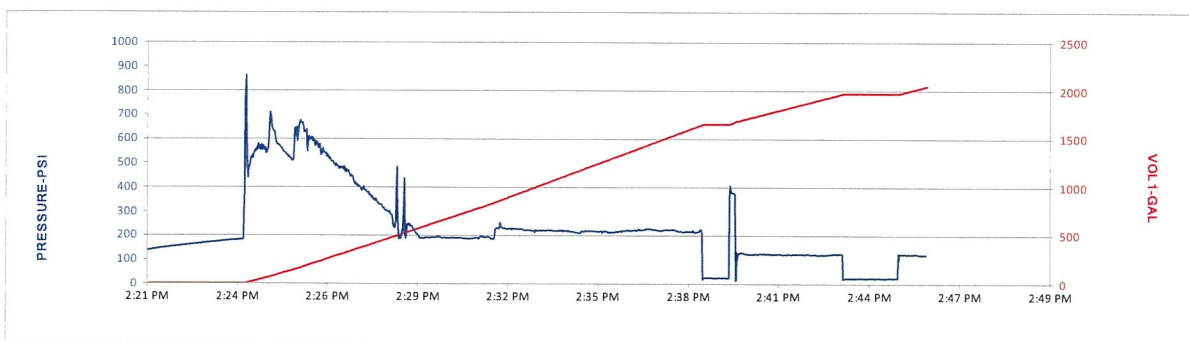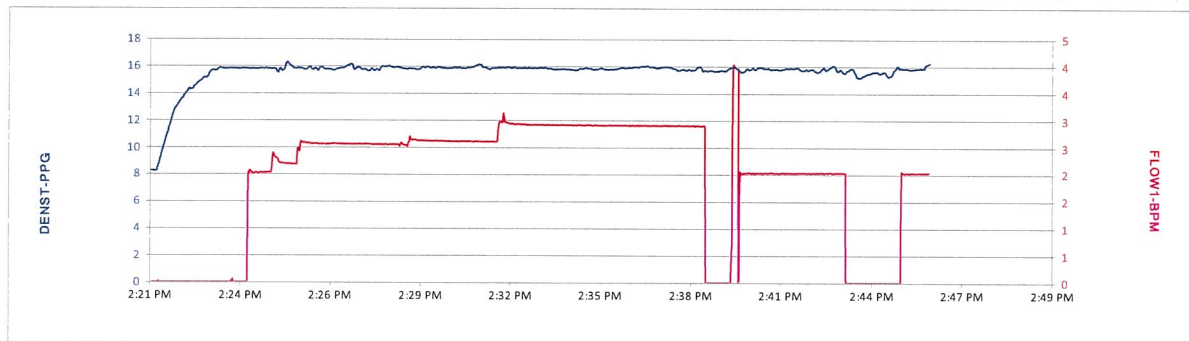

Report Created: 0



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: PDC

Email: 0

Contact: Bud

Phone: 0

JOB DETAILS

Date: 8-30-2023

Operator: Diego Cardona

Start Time: 14:42:49


Ticket #: 0

End Time: 14:55:59

LSD #: Brighton Farms 1

Comments: 2nd pump 120 sks class G

SUMMARY GRAPHS

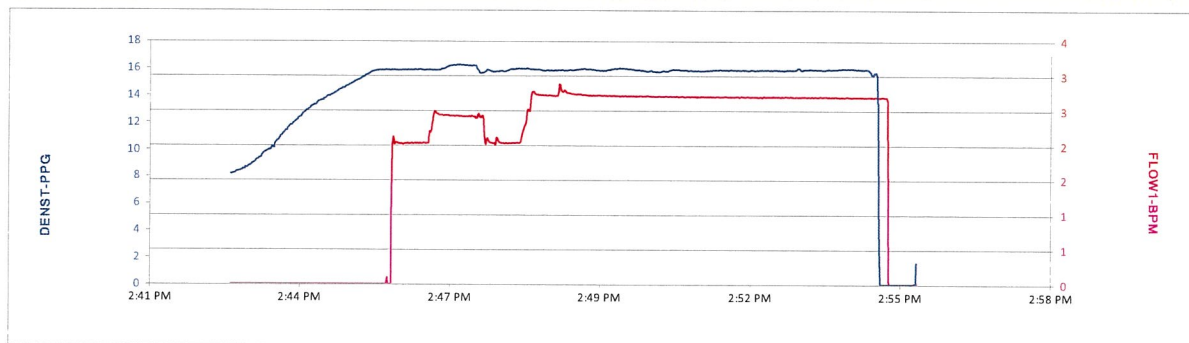

Report Created: 0



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: PDC
Contact: Bud
Phone: 0

Email: 0



JOB DETAILS

Date: 8-31-2023
Start Time: 09:42:28
End Time: 10:03:59

Operator: Diego Cardona
Ticket #: 0
LSD #: Brighton Farms 1

Comments: 3rd pump 250 sks class G 2% CC

SUMMARY GRAPHS

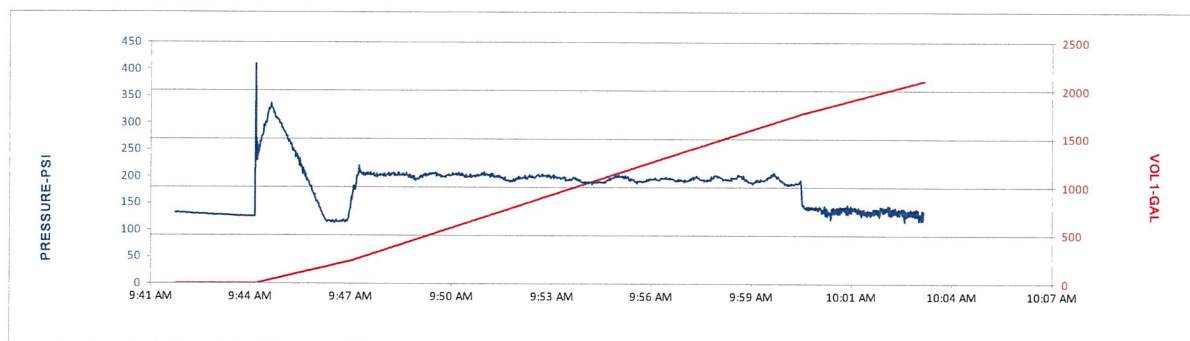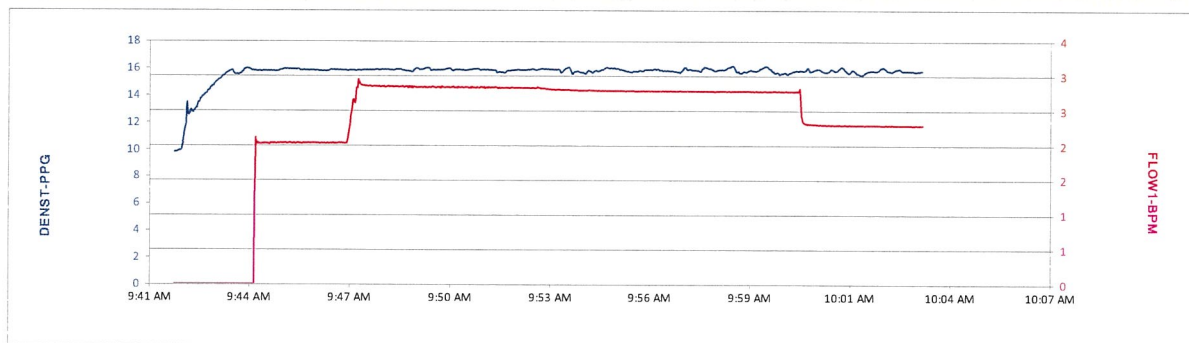

Report Created: 0



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: *PDC*

Email: *0*

Contact: *Bud*

Phone: *0*

JOB DETAILS

Date: *8-31-2023*

Operator: *Diego Cardona*

Start Time: *14:07:05*



Ticket #: *0*

End Time: *14:43:59*

LSD #: *Brighton Farms 1*

Comments: *4th pump to surface 510skts total class G*

SUMMARY GRAPHS

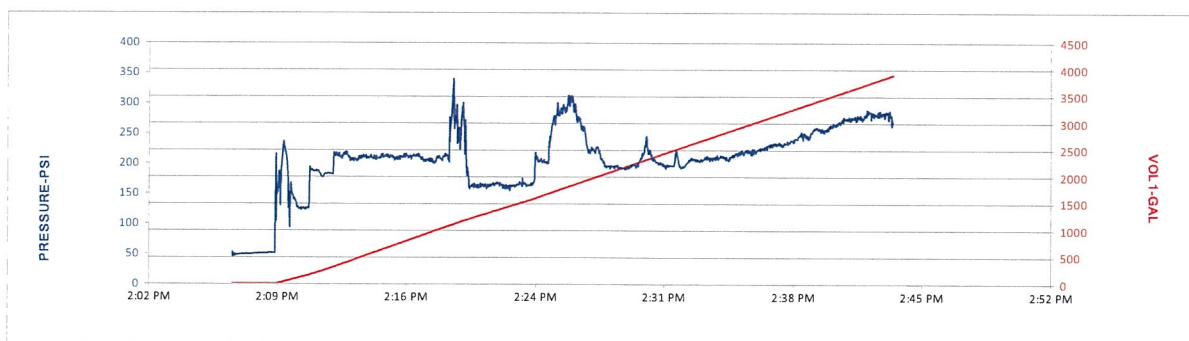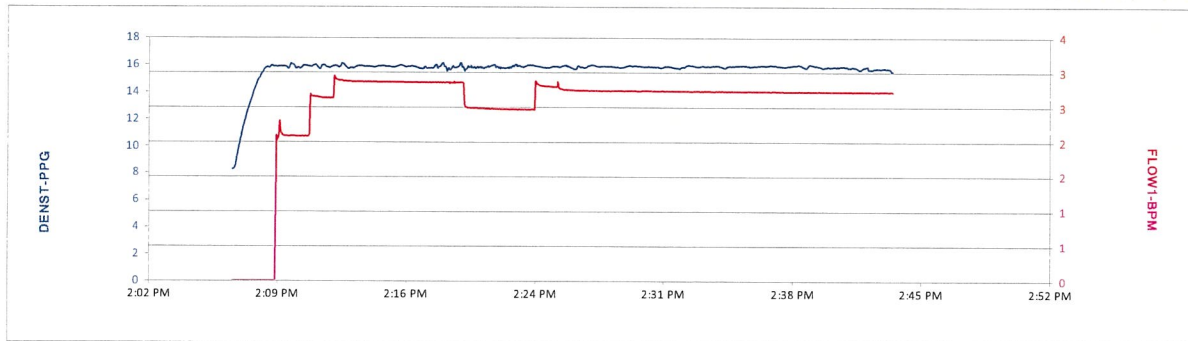

Report Created: *0*
