

From: [Katherine Feir](#)
To: [IKAV Energy Inc. SJN Inspections Mailbox](#)
Cc: [Matthew Baca](#)
Subject: RE: Koon 1 PxA ECMC Inspection #693904348 completion photos and update
Date: Tuesday, December 12, 2023 4:00:18 PM
Attachments: [Koon 1 Completion Photos 693904348 2023_12.pdf](#)

Matt,

The final work steps addressing the ECMC inspection #693904348 for the AMOCO Legacy P&A Koon 1 API No. 05-067-06050 were complete 12/08/2023.

Much of this work was complete in July 2023 but we needed to work through the on location flowline abandonment sampling and remediation steps. Once the samples passed the required ECMC threshold values, we backfilled and seeded the disturbances.

Please see the attached for the photo documentation associated with this work. This includes the same photos I sent in August with the seeding and backfilling ones at the end.

Please reference the following related ECMC documents in the FIRR to provide a connection/trail.

Location ID 385503 On location flowline abandonment notice #403190297

Location ID 385503 Form 27 Initial Site Investigation and Remediation Workplan # 403194155

Location ID 385503 Form 27 Supplementals #403366136, #403489563, and #403586242

Please review the inspection and these completion photos to see if there is anything missing.

Let me know any questions.

Thanks.

Kate

Kate Feir
IKAV Energy Inc.
1199 Main St. Ste 101 | Durango, CO 81301
Mobile: 970-394-4457
Telephone: 970-852-5162
Email: katherine.feir@ikavenergy.com

Confidentiality notice:

This e-mail communication (and any attachment/s) are confidential and are intended only for the individual(s) or entity named above and to others who have been specifically authorized to receive it. Any information in this email and attachments may be legally privileged. If you are not the intended recipient, any disclosure, copying, reading, distribution, or any action taken or omitted in reliance on it, is prohibited and may be unlawful. Any opinions or advice contained in this email are subject to confidentiality and any terms and conditions may be protected by an engagement letter or other agreement. Please notify the sender that you have received this e-mail in error by calling the phone number above or by e-mail, and delete the e-mail (including any attachment/s) subsequently. This information may be subject to professional confidentiality (e.g. auditors, tax, or legal advisors), other privilege, or may otherwise be protected by work product immunity or other legal rules. Thank you.

From: Katherine Feir
Sent: Tuesday, August 1, 2023 2:26 PM
To: IKAV Energy Inc. SJN Inspections Mailbox <sninspections@ikavenergy.com>
Cc: Steven Firestone <steven.firestone@ikavenergy.com>
Subject: Koon 1 PxA ECMC Inspection #693904348 completion photos and update

Attached are the completion photos for the Koon 1 PxA ECMC Inspection #693904348.

Activities completed 7/10/2023 include:

- Trash picked up – cable, sign, carsonite, white pvc tube, t-post
- Valve and riser shown in inspection photo #4 belongs to Harvest and is part of an active pipeline

system. Harvest took over from Williams; Williams is on the pipeline carsonite. Valve/riser is not SIMCOE's and not part of the plug and abandonment.

- Cut and capped remaining on location flowline risers. Removed above ground items.

As part of the riser abandonment, samples were taken at the on location flowline abandonment locations. One location did not meet all the ECMC Table 915-1 requirements. SIMCOE plans to treat this location and resample. SIMCOE is working with the ECMC via Form 27's on this remediation. Removal of netting, backfilling of flowline holes, and seeding will be performed once the remediation and sample results are approved. This is still in progress.

It's your choice to file a FIRR now, however, there is a risk the FIRR will not be approved since vegetating the disturbed areas still needs to be done. That is probably 60 days out.

Thanks.

Kate

Kate Feir

IKAV Energy Inc.

1199 Main St. Ste 101 | Durango, CO 81301

Mobile: 970-394-4457

Telephone: 970-852-5162

Email: katherine.feir@ikavenergy.com

Confidentiality notice:

This e-mail communication (and any attachment/s) are confidential and are intended only for the individual(s) or entity named above and to others who have been specifically authorized to receive it. Any information in this email and attachments may be legally privileged. If you are not the intended recipient, any disclosure, copying, reading, distribution, or any action taken or omitted in reliance on it, is prohibited and may be unlawful. Any opinions or advice contained in this email are subject to confidentiality and any terms and conditions may be protected by an engagement letter or other agreement. Please notify the sender that you have received this e-mail in error by calling the phone number above or by e-mail, and delete the e-mail (including any attachment/s) subsequently. This information may be subject to professional confidentiality (e.g. auditors, tax, or legal advisors), other privilege, or may otherwise be protected by work product immunity or other legal rules. Thank you.

Koon 1 PxA API No. 05-067-06050
ECMC Inspection 693904348


Date completed 7/10/2023



Before Sign removed. After



Before T-post removed After

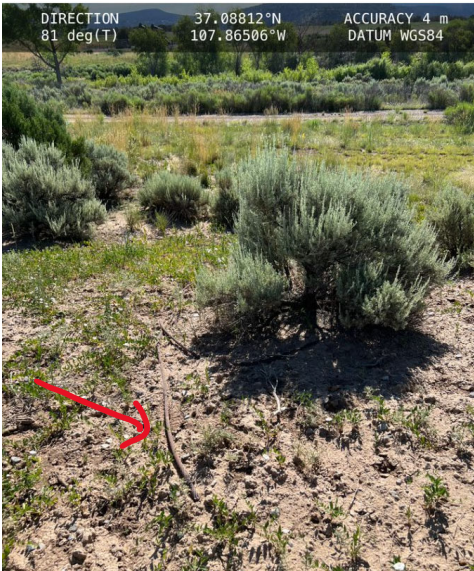

Before

Cable removed

After



Picture of existing above ground valve, belongs to Harvest (took over Williams' assets) as shown on carsonite. Valve is part of active pipeline and not part of PxA. Harvest notified that valve could use a blind flange. This equipment is not SIMCOE's.

Date completed 7/10/2023



On location above ground flowline stubs removed. Cut and capped below grade. Completed July 2023

Before



After



On location above ground flowline stub and trash near marker removed. Cut and capped below grade. White PVC is not flowline riser, just trash. Carsonite removed. Completed July 2023.

Before



After



Post sample results below thresholds, holes backfilled, and seeded. Completed 12/8/2023.

