		PO Box 329 Ft. Lupton, CO 80621 (303) 654-9202		"Here Safety Meets Quality at the Axis of Efficiency"						
Date of Service	Job Type	Customer	Consultant	Well Name		Last Tckt	Ticket #			
2/5/2024	P & A	OXY	Jeremy Caldwell	Ulrich 22-8L		No	2679			
State	County	API		Rig	Mileage	Operator				
Colorado	Weld	05-123-16730		Ensign 122	N/A	Jonathon Rhamy				
		Well Information		Unit #		Crew members				
		Work String	Prod CSG	Surface	OH (I.D.)	Annular	P 90530 Geoffrey Miller			
OD & Weight	DP 4 1/2" 16.6#			7.875			B 2250 Alexander Pomales			
bbl/ft Factor	0.01422	0	0	0.0602	0.0406		B 2321 Seth Campbell			
Length in ft	3526			3526	3536		B 8990 Cori Grauberger			
Capacity in bbls	50.14	0.00	0.00	212.42	143.46		B 8988			
OD & Weight	DP 4 1/2" 16.6#			7.875		Well Description				
bbl/ft Factor	0.01422	0	0	0.0602		EOT	Depth in Ft			
Length in ft	2400			2400		TOC	3,526			
Capacity in bbls	34.13	0.00	0.00	144.59	0.00		2,514			
OD & Weight	DP 4 1/2" 16.6#		8 5/8" 24#	7.875		EOT	2,400			
bbl/ft Factor	0.01422	0	0.0636	0.0602		TOC	1,388			
Length in ft	1370		513	857						
Capacity in bbls	19.48	0.00	32.63	51.63	0.00	EOT	1,370			
Buoyancy	0.76	Buoyancy	0.76	Buoyancy	0.76	TOC	115			
Lift Pressure	PRV	Lift Pressure	PRV	Lift Pressure	PRV	Shoe	513			
2797	2000	1904	1250	1087	750					
Remarks										
Lower AGM		285	Lower AGM		285	Upper AGM		360	Water	
Class G 94lb/sk	26,790.0	Class G 94lb/sk	26,790	Class G 94lb/sk	33,840	Temp	75 °F			
CaCL2	267.9	CaCL2	268	CaCL2	508	PH	7			
Gypsum	1,071.6	Gypsum	1,072	Gypsum	1,354	Chloride	1.5ppm			
RFL-1 (latex)	107.2	RFL-1 (latex)	107	RFL-1 (latex)	135					
Defoamer	80.4	Defoamer	80	Defoamer	102					
RFL-70X(Latex)	-	RFL-70X(Latex)	-	RFL-70X(Latex)	-					
RFL-9(Fluid Loss)	-	RFL-9(Fluid Loss)	-	RFL-9(Fluid Loss)	-					
RCD-3(Dispersant)	-	RCD-3(Dispersant)	-	RCD-3(Dispersant)	-					
RCR-201(Retarder)	-	RCR-201(Retarder)	-	RCR-201(Retarder)	-					
PreMag	-	PreMag	-	PreMag	-					
THIX-C2	-	THIX-C2	-	THIX-C2	-					
Silica Flour	-	Silica Flour	-	Silica Flour	-					
Desc	Qty	Rate	Total	Desc	Qty	Rate	Total			
Class G 94lb/sk	285									
CaCL2	268.00									
Gypsum	1072.0									
RFL-1 (latex)	108.0									
Defoamer	81.0									
Sugar	200.00									
Alpha	4.00									
ProFlush	70.00									
Add'l Bulk	2.00									
Data Recording	1.00									
Pump & Bulk/Hour	2.00									
Pump & Bulk/Hour	15.00									
Print		Sign		Date						

[illegible]

Print


Sign

Date

Date of service


ULRICH 22-8L LOWER AGM PLUG @ 3,526'

CEMENTING

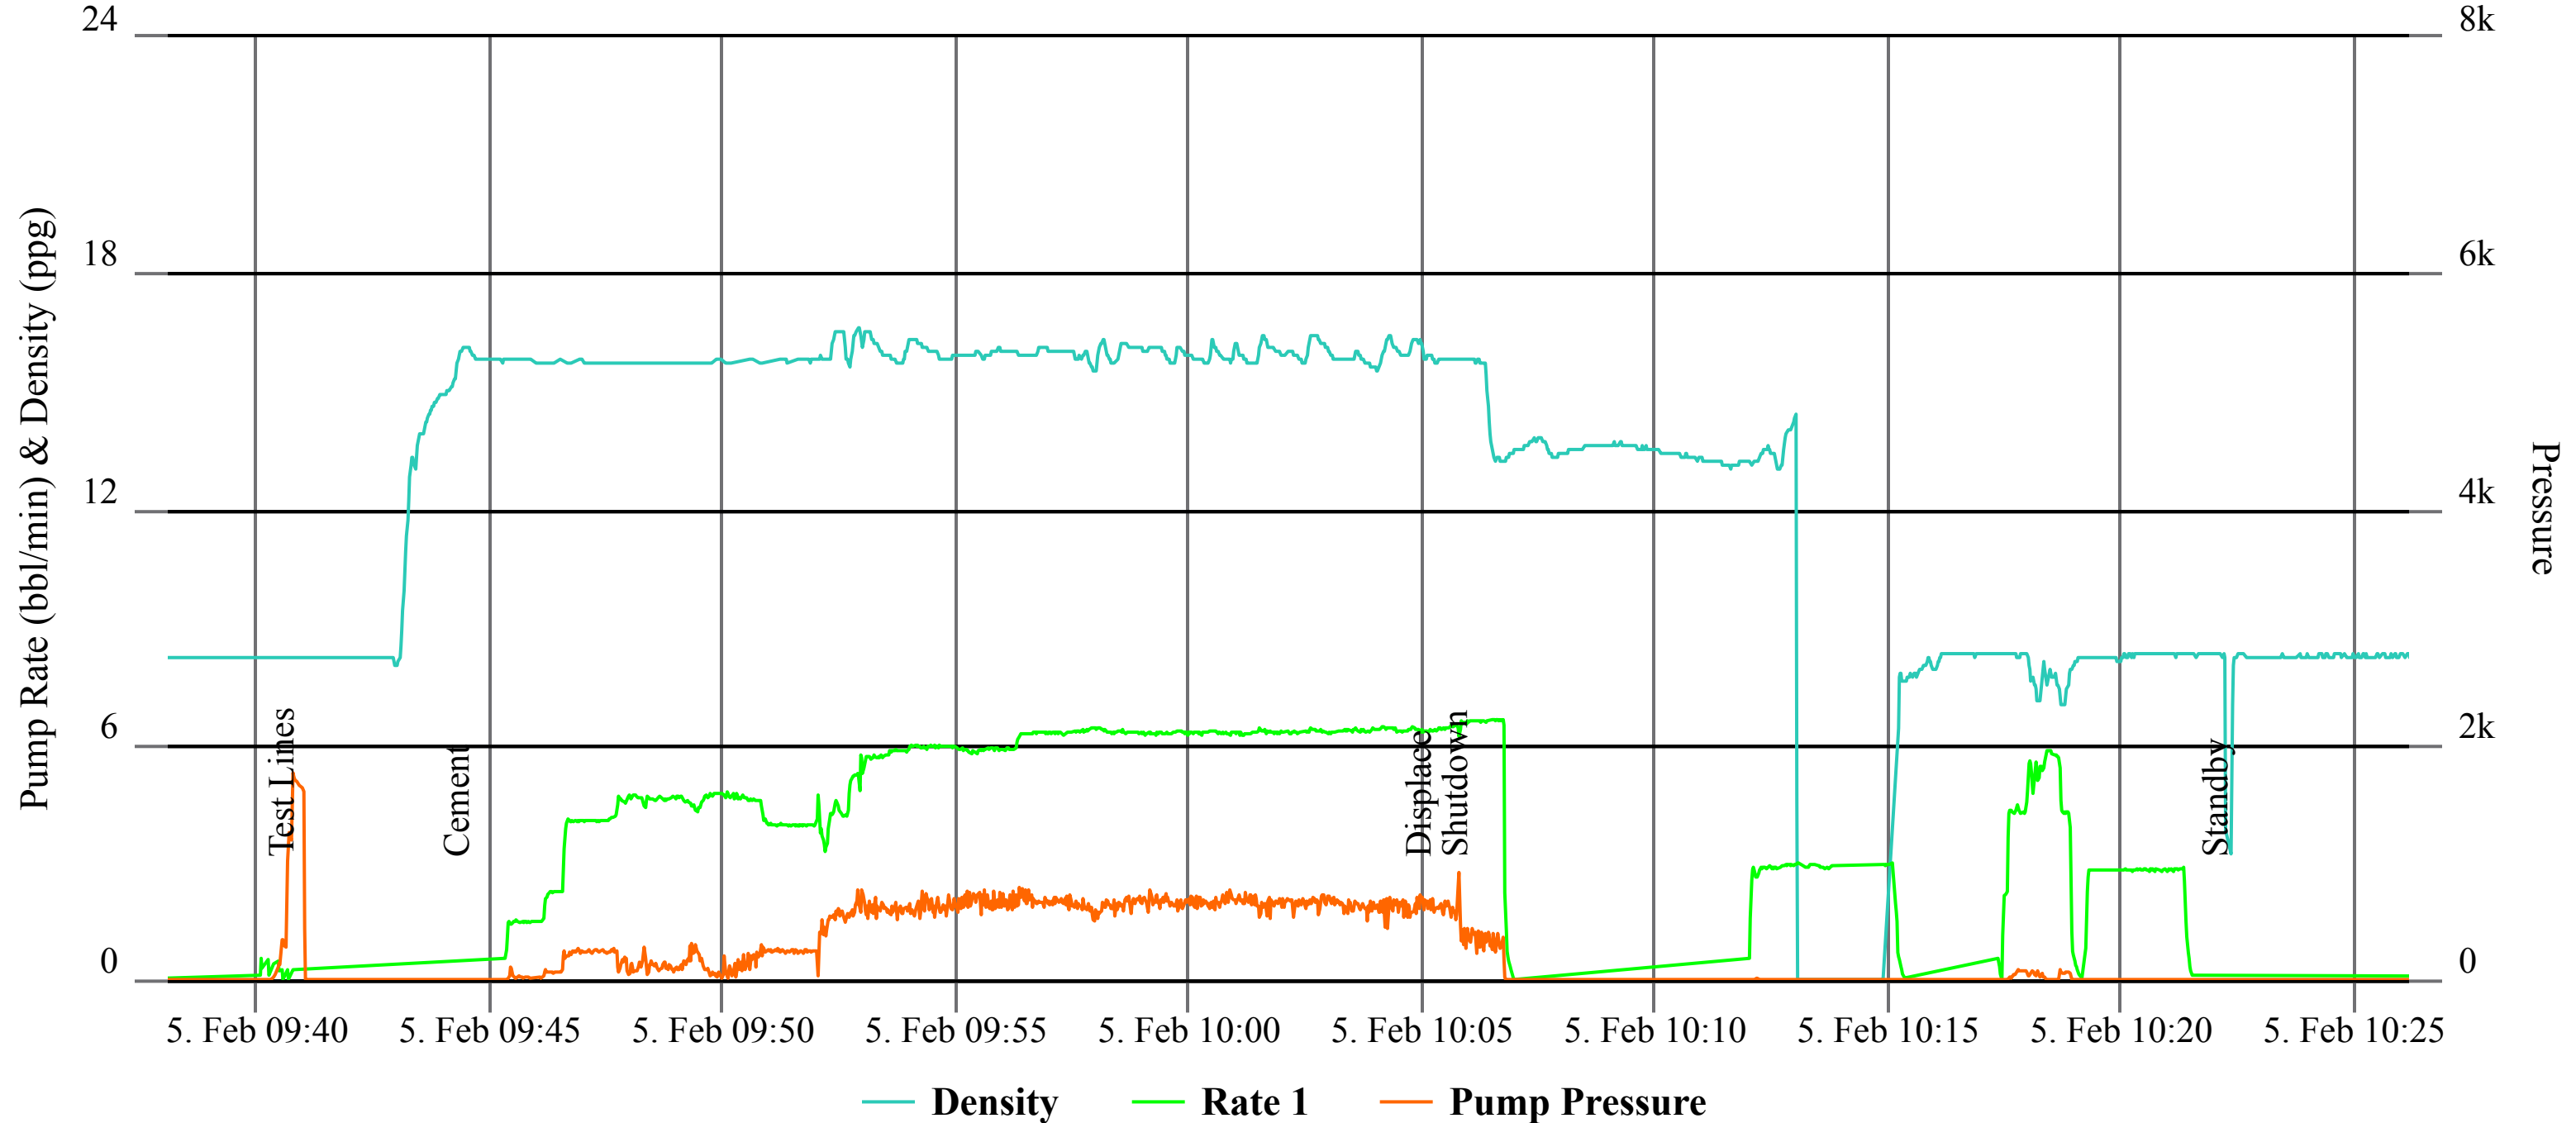


ULRICH 22-8L LOWER AGM PLUG @ 2,400'


CEMENTING

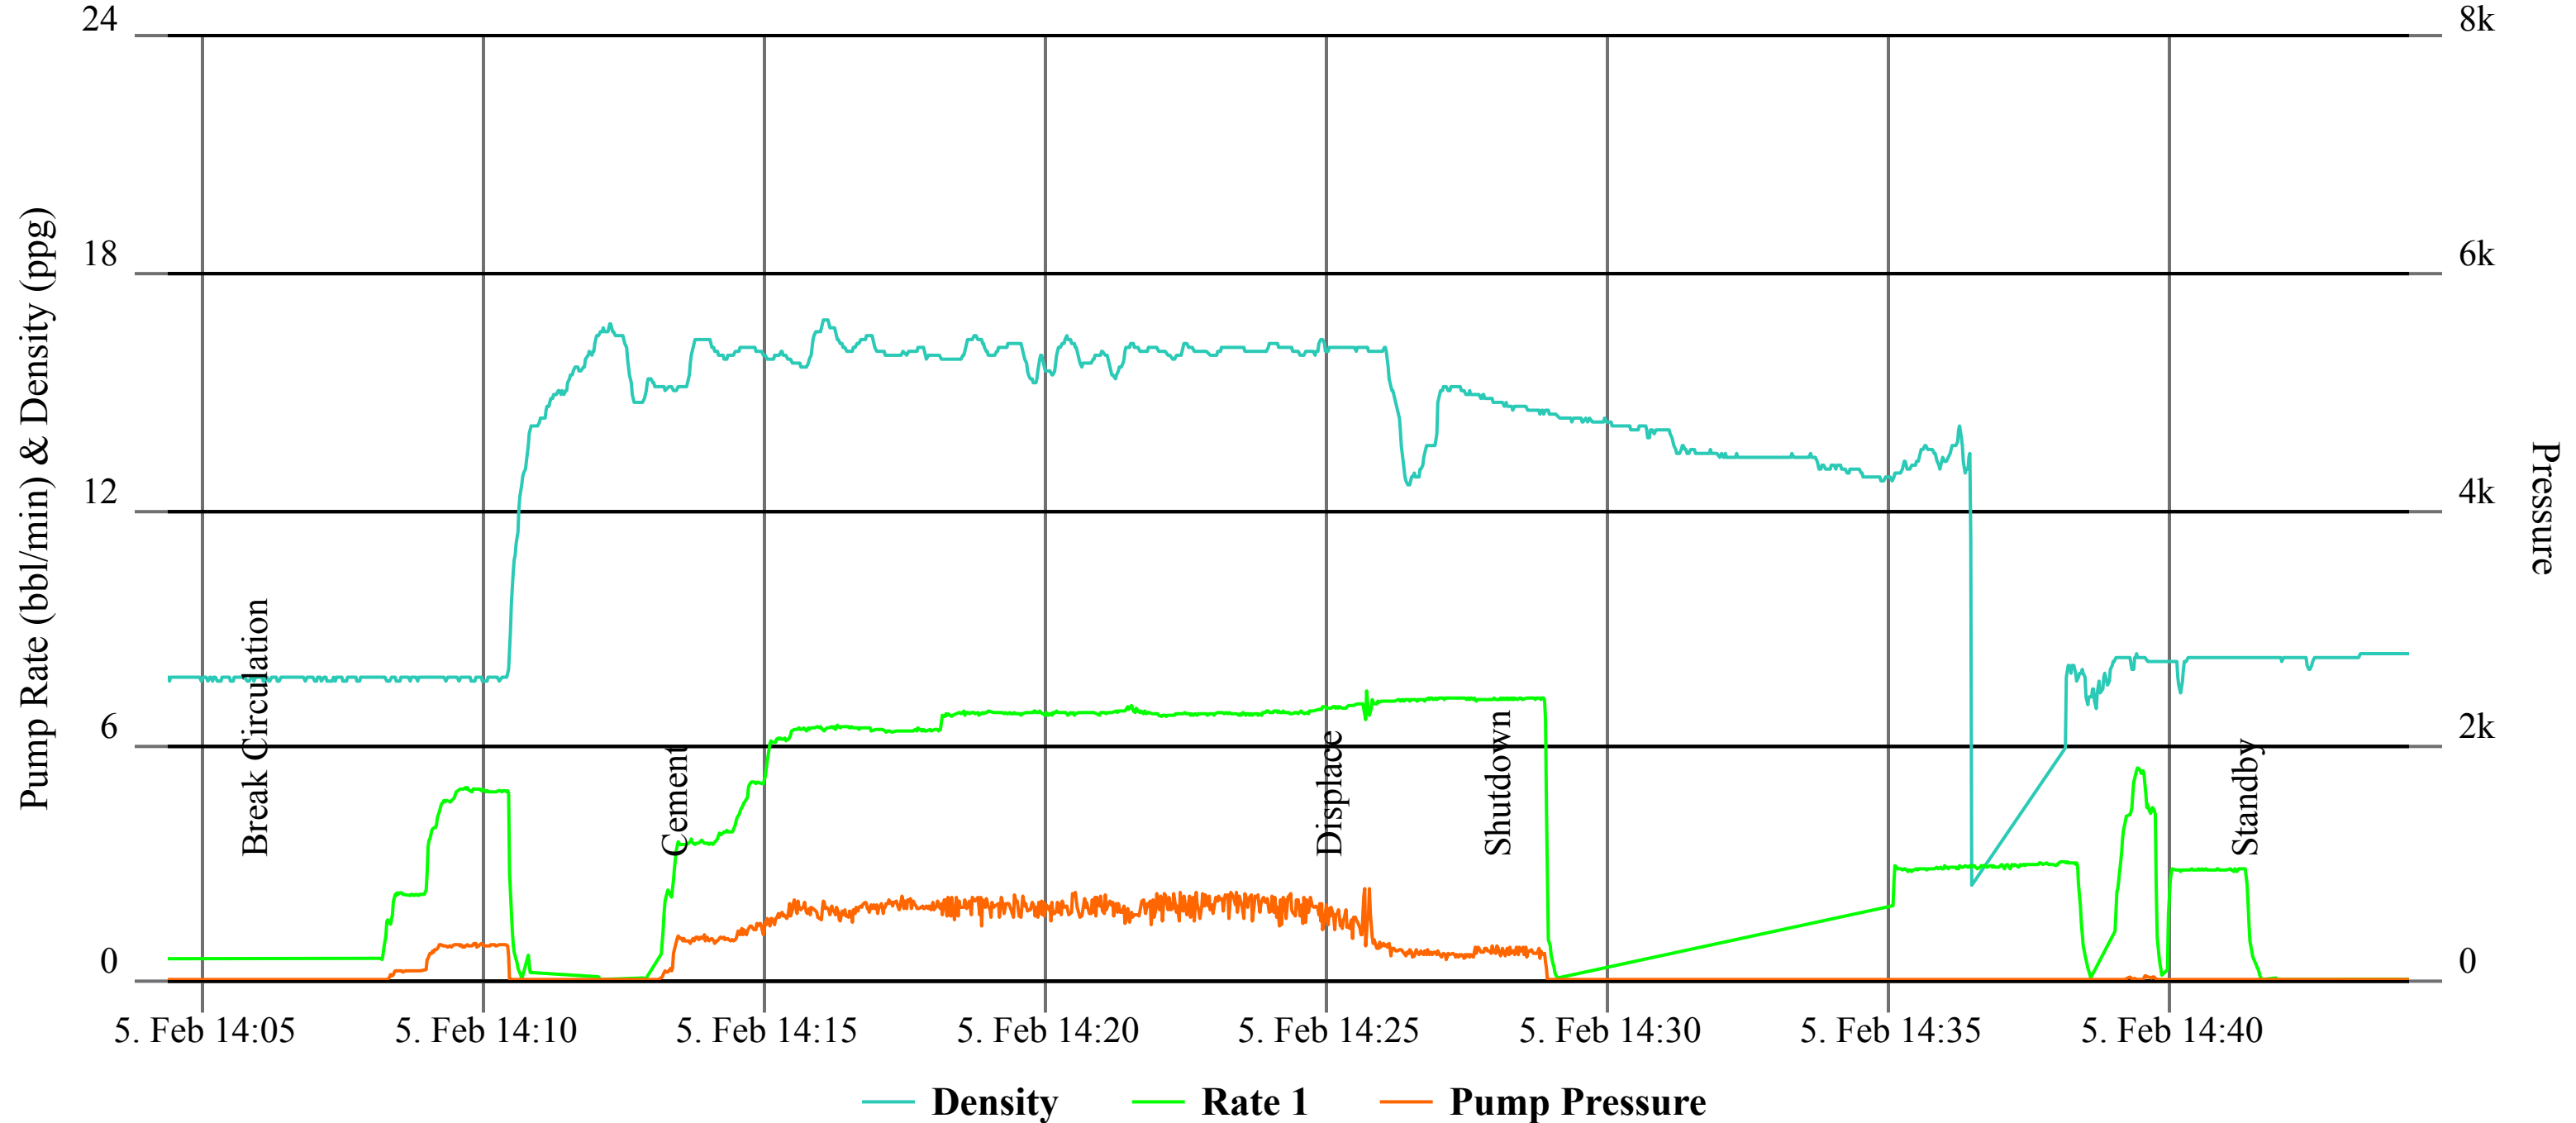

ULRICH 22-8L UPPER AGM PLUG @ 1,370'

CEMENTING

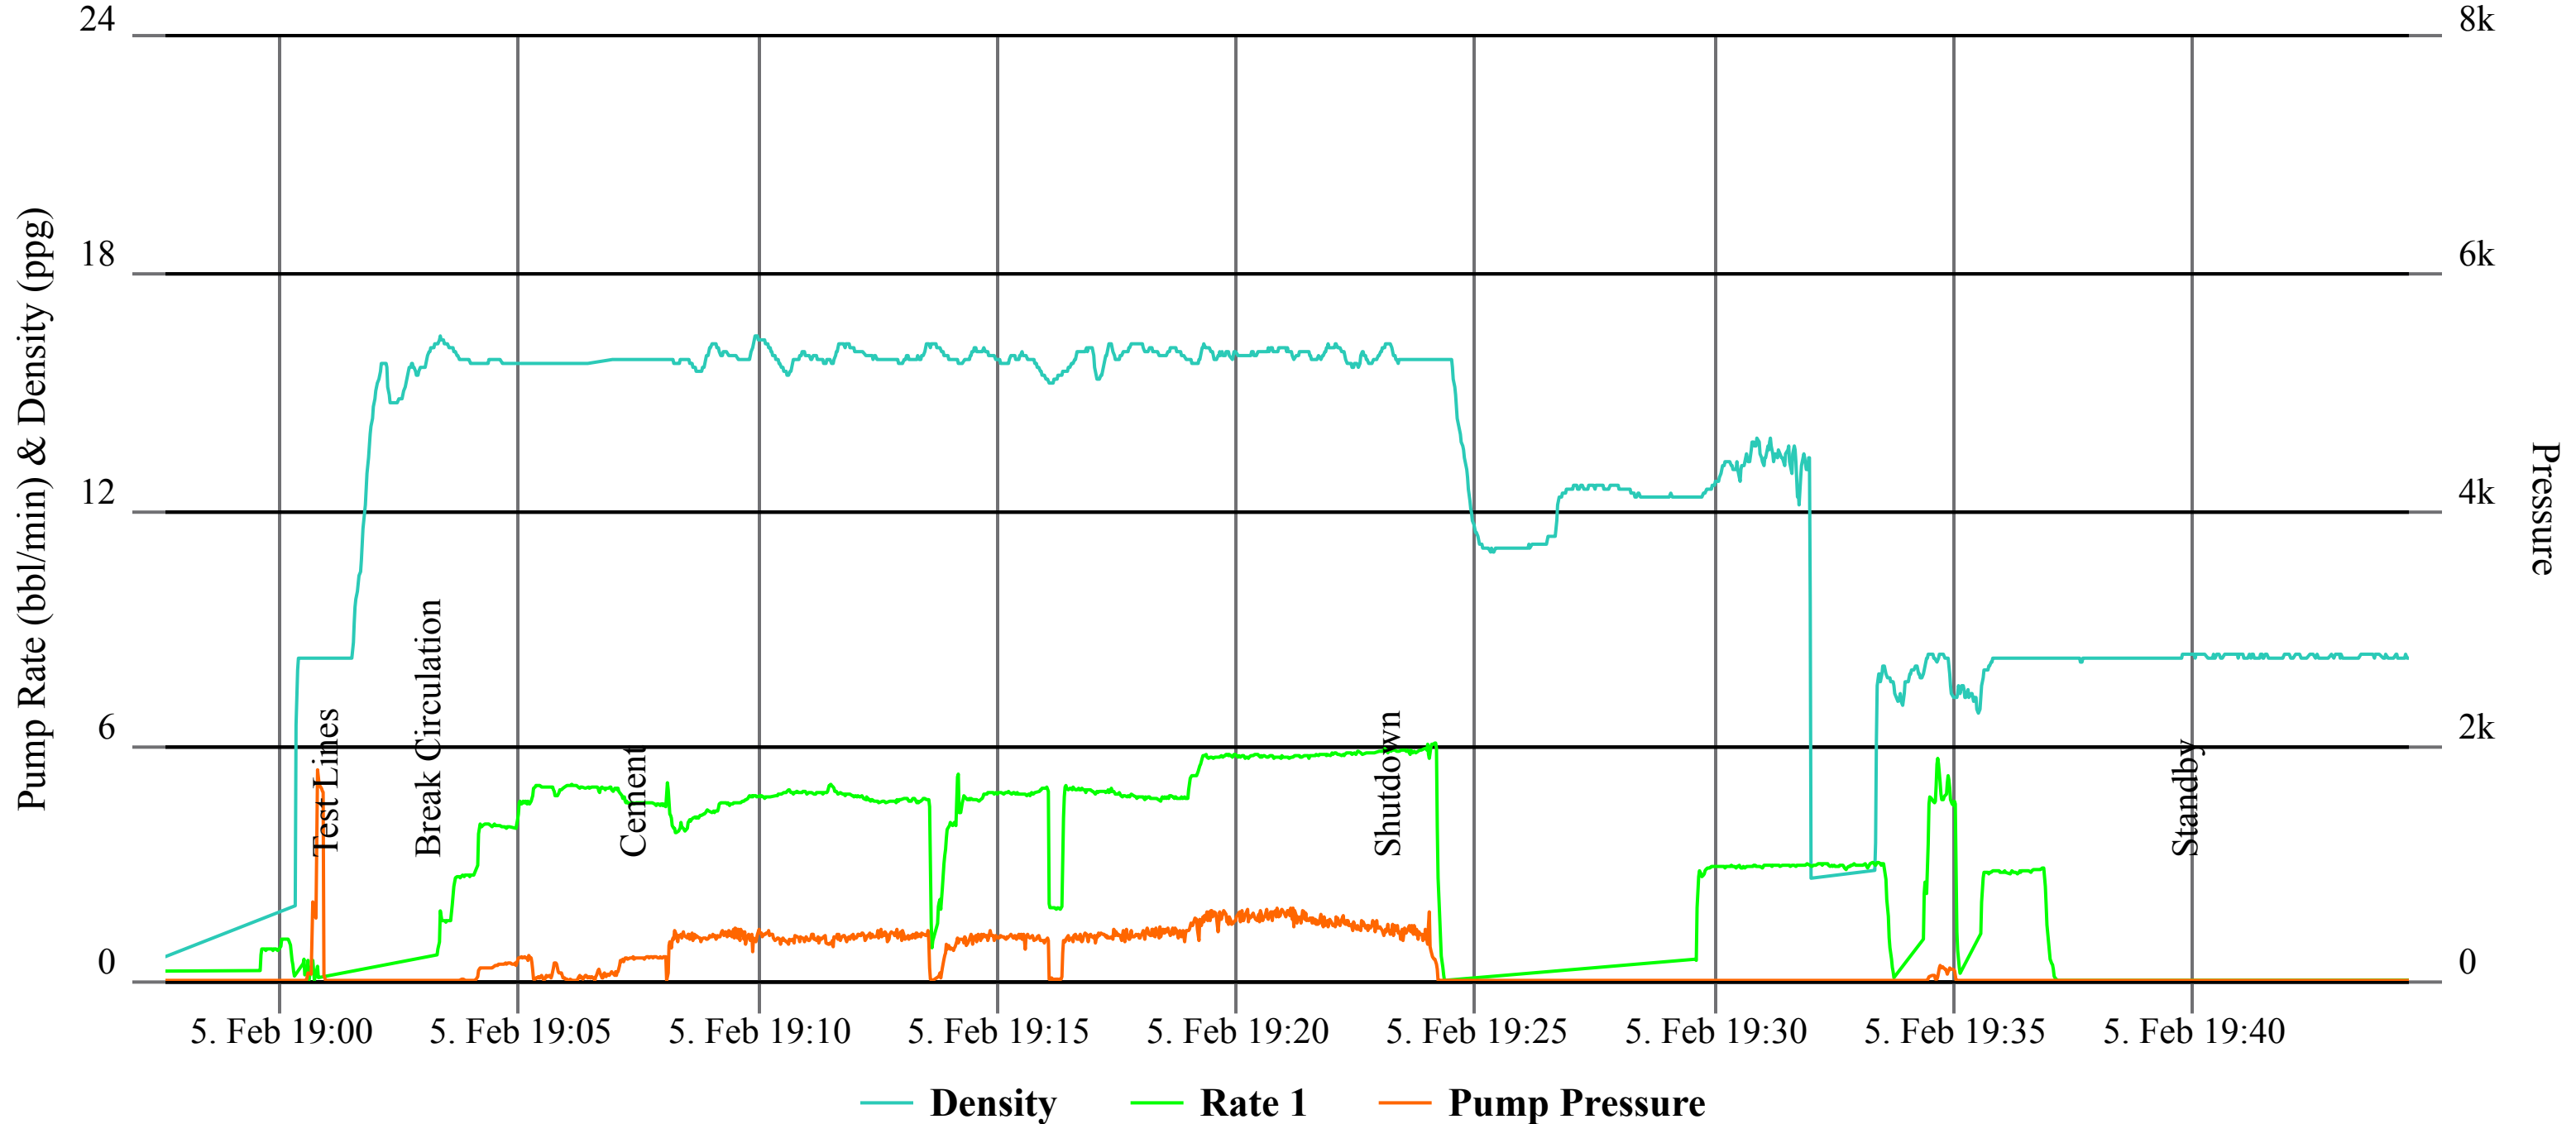

		PO Box 329 Ft. Lupton, CO 80621 (303) 654-9202		"Here Safety Meets Quality at the Axis of Efficiency"				
Date of Service	Job Type	Customer	Consultant	Well Name		Last Tckt	Ticket #	
2/6/2024	P & A	OXY	Isaac Rulla	Ulrich 22-8L		Yes	2681	
State	County	API		Rig	Mileage	Operator		
Colorado	Weld	05-123-16730		Ensign 122	N/A	Jonathon Rhamy		
Well Information				Unit #		Crew members		
	Work String	Prod CSG	Surface	OH (I.D.)	Annular	P 90530	Geoffrey Miller	
OD & Weight	DP 4 1/2" 16.6#		8 5/8" 24#	7.875	3.826	B 2884	Alexander Pomales	
bbl/ft Factor	0.01422	0	0.0636	0.0602		B 8990	Seth Campbell	
Length in ft	848		515	335				
Capacity in bbls	12.06	0.00	32.75	20.18	0.00			
OD & Weight	DP 4 1/2" 16.6#		8 5/8" 24#			Well Description		
bbl/ft Factor	0.01422	0	0.0636	0.0000		EOT	Depth in Ft	
Length in ft	260		260			TOC	848	
Capacity in bbls	3.70	0.00	16.54	0.00	0.00		266	
OD & Weight	DP 4 1/2" 16.6#					EOT	260	
bbl/ft Factor	0.01422	0	0	0.0000		TOC	0	
Length in ft								
Capacity in bbls	0.00	0.00	0.00	0.00	0.00			
Buoyancy	0.76	Buoyancy	0.76	Buoyancy	0.76			
Lift Pressure	PRV	Lift Pressure	PRV	Lift Pressure	PRV			
673	500	206	250	0	0			
Remarks								
Upper AGM		430	Surface AGM		90	Blend		0
Class G 94lb/sk		40,420.0	Class G 94lb/sk		8,460	Class G 94lb/sk		-
CaCL2		606.3	CaCL2		169	CaCL2		-
Gypsum		1,616.8	Gypsum		338	Gypsum		-
RFL-1 (latex)		161.7	RFL-1 (latex)		34	RFL-1 (latex)		-
Defoamer		121.3	Defoamer		25	Defoamer		-
RFL-70X(Latex)		-	RFL-70X(Latex)		-	RFL-70X(Latex)		-
RFL-9(Fluid Loss)		-	RFL-9(Fluid Loss)		-	RFL-9(Fluid Loss)		-
RCD-3(Dispersant)		-	RCD-3(Dispersant)		-	RCD-3(Dispersant)		-
RCR-201(Retarder)		-	RCR-201(Retarder)		-	RCR-201(Retarder)		-
PreMag		-	PreMag		-	PreMag		-
THIX-C2		-	THIX-C2		-	THIX-C2		-
Silica Flour		-	Silica Flour		-	Silica Flour		-
Desc	Qty	Rate	Total	Desc	Qty	Rate	Total	
Class G 94lb/sk	430							
CaCL2	607.00							
Gypsum	1617.0							
RFL-1 (latex)	162.0							
Defoamer	122.0							
Sugar	250.00							
Alpha	3.00							
Add'l Bulk	1.00							
Pump & Bulk/Hour	2.00							
Pump & Bulk/Hour	10.00							
Discount	10.00							
Print		Sign		Date				



PO Box 329


Ft. Lupton, CO 80621
(303) 654-9202

"Here Safety meets Quality at the Axis of Efficiency"

[illegible]

ULRICH 22-8L UPPER AGM PLUG @ 848'

CEMENTING

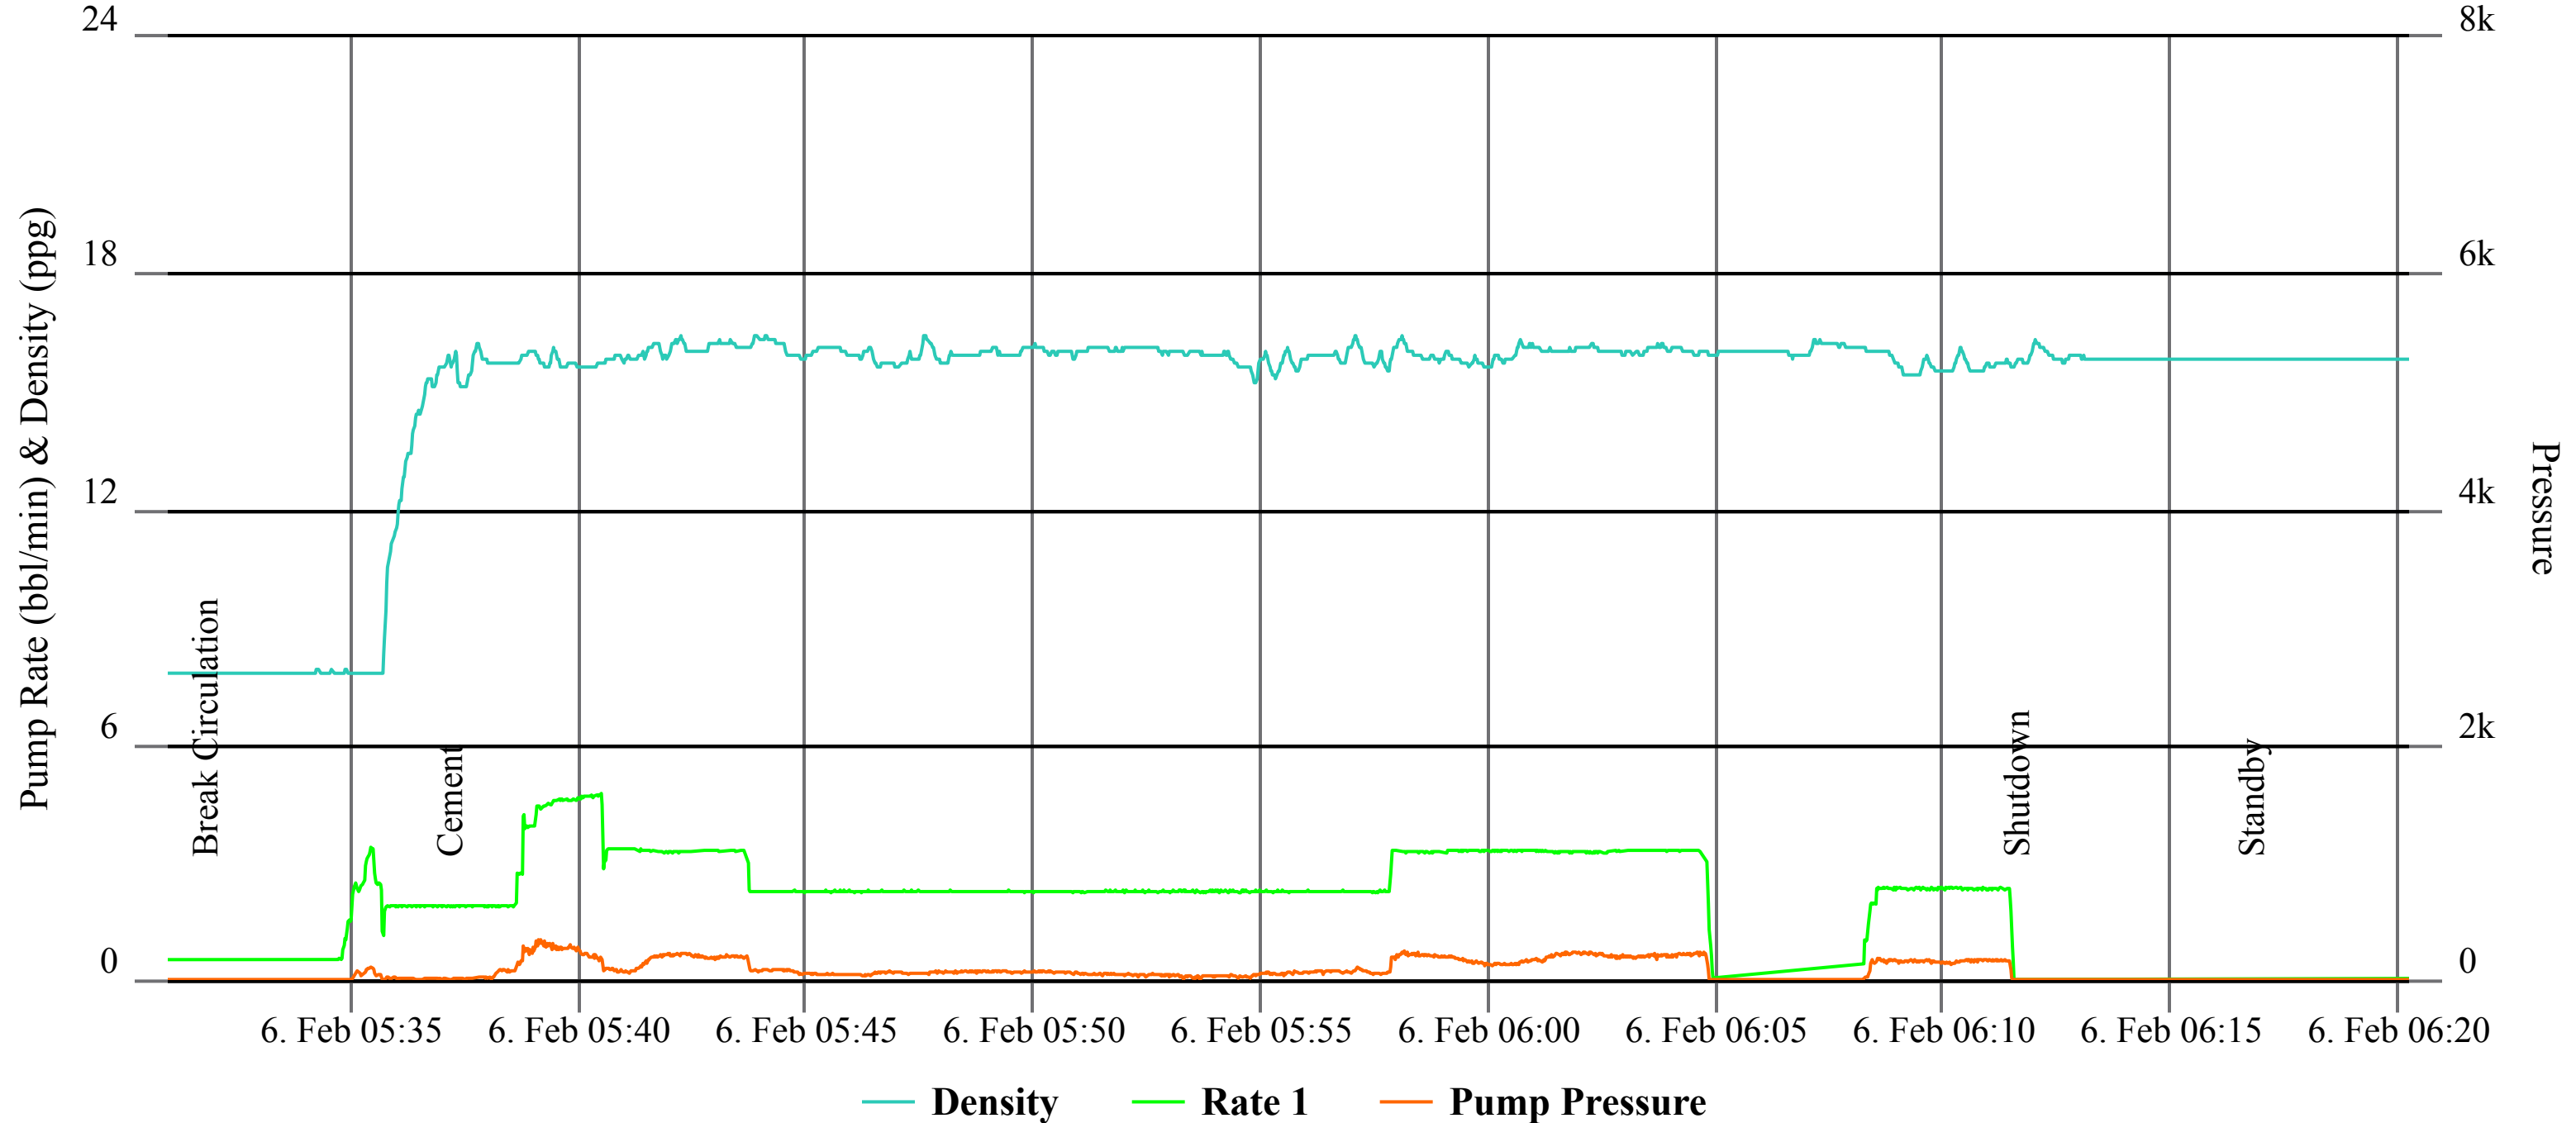

ULRICH 22-8L SURFACE AGM PLUG @ 260'

CEMENTING

