

DUCO INCORPORATED

Well Servicing Company
2403 1/2 E. Main - PO Box 416 (mailing)
Rangely, CO 81648
Phone (970-629-1906 or (970)-675-8685

CMT Package

12-19 & 12-20 (2024)
INVOICE #: E116.2024

Hiring Company: Ensign

Fuel Used: 30 Gallons
Lease: Sylvester 36-9H6

CMT truck operator: Jesus Hernandez
CMT Operator #2:
Pod trailer operator: Joel Martinez
Labor Hand: Louie
Labor Hand: Gilberto Verduzco
Supervisor: Lane Griffin
Pump Unit#: RCM-4

PO:
Company Foreman: Roger Jackson Rig 314
Chevron WSR: Shane Paris

COMMENTS

All CMT pumped by Duco in
will be 15.8lbs 1.15 yield class
g neat.

Hour Work Started: D1: 12:30PM D2: 8:00AM D3: D4: D5:
Hour Work Completed: D1: 2:30PM D2: 11:00AM D3: D4: D5:

BREAKDOWN OF CHARGES	HOURS/QTY.	RATE	AMOUNT
Initial 4 HRS: CMT truck and Pod trailer	2.00	\$0.00	\$ -
Additional Hours	0.00	\$0.00	
SKS of CMT	233.00	\$0.00	
Calcium (LBS)	0.00	\$0.00	
Standby Rate	0.00	\$0.00	
Mudflush Detergent (Gal)	0.00	\$0.00	
Clay Control (Gal)	0.00	\$0.00	
Defoamer (Gal)	0.00	\$0.00	
RCR-201 Retarder (LBS)	0.00	\$0.00	
RFL-70X Fluid Loss (LBS)	0.00	\$0.00	
Sodium Metasilicate (LBS)	0.00	\$0.00	
Radilock 3mm Fiber LCM (LBS)	0.00	\$0.00	
Pol-E-Flake (LBS)	0.00	\$0.00	
Cancellation	0.00	\$0.00	
Trucking Hours	0.00	\$0.00	
SKS of 2K THIXO CMT	0.00	\$0.00	
SKS of 1K THIXO CMT	0.00	\$0.00	
SKS of Upper AGM CMT	0.00	\$0.00	
DESCRIPTION OF WORK PERFORMED:			
Rig up and meet with company man and crew for procedure review and safety meeting. Pump Lines pressure tested to 3000PSI Daily. Day One (12-19-24): First Pump: EOT 2278'. Break circulation and lead with 5 BBLS FW. Mix and pump 10sks/2.04 BBLS slurry 15.8# class G cement neat. 1.19 BBLS mix water used for slurry. 219' plug EST TOC 2059'. Displace 6 BBLS FW to balance. Second Pump: EOT 898'. Break circulation and lead with 5 BBLS FW. Mix and pump 15sks/3 BBLS slurry 15.8# class G cement neat. 1.78 BBLS mix water used for slurry. 345' plug EST TOC 560'. Displace 1.7 BBLS FW to balance. Day Two (12-20-24): Third Pump: EOT 560'. Break circulation and lead with 5 BBLS FW. Mix and pump 188sks/38.4 BBLS slurry 15.8# class G cement neat. 22.38 BBLS mix water used for slurry. Circulate cement to surface. TOH. Top Off: Mix and pump 5sks/1 BBLS slurry 15.8# class G cement neat. Additional 15sks/3 BBLS slurry pumped to waste tank. Good cement at surface. Clean up and rig down cement equipment. Move off location.		SUBTOTAL	\$ -
		TAX RATE	0.00%
		SALES TAX	-
		OTHER	
		TOTAL	\$ -

#

All accounts net 30 days. 24% per annum interest plus cost of attorney's fees and collection fees

THANK YOU FOR YOUR BUSINESS!



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: *Chevron*
Contact: *Shane Paris*
Phone: *0*

Email: *0*



JOB DETAILS

Date: *12-19-24*
Start Time: *13:12:40*
End Time: *13:47:59*

Operator: *Jesus Hernandez*
Ticket #: *0*
LSD #: *1st pump 10sks class G 15.8#*

Comments: *Sylvester 36-9H6*

SUMMARY GRAPHS

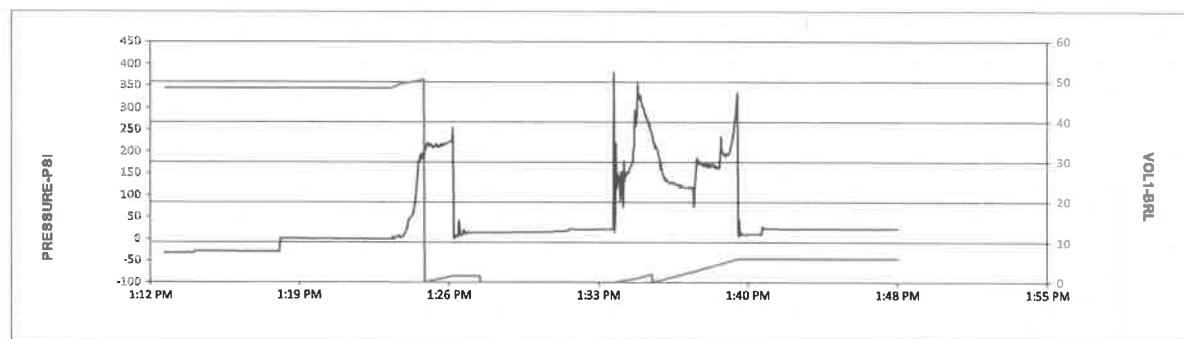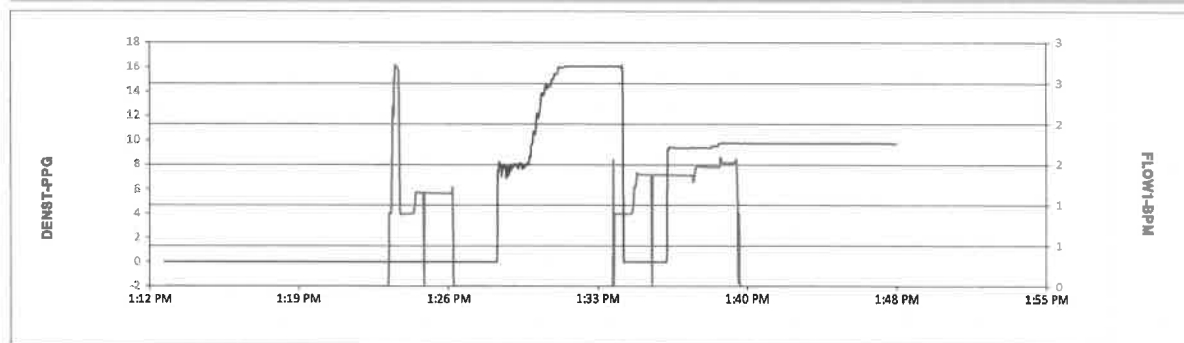

Report Created: *0*



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: *Chevron*
Contact: *Shane Paris*
Phone: *0*

Email: *0*



JOB DETAILS

Date: *12-19-24*
Start Time: *14:08:42*
End Time: *14:32:59*

Operator: *Jesus Hernandez*
Ticket #: *0*
LSD #: *2nd pump 15sks class G 15.8#*

Comments: *Sylvester 36-9H6*

SUMMARY GRAPHS

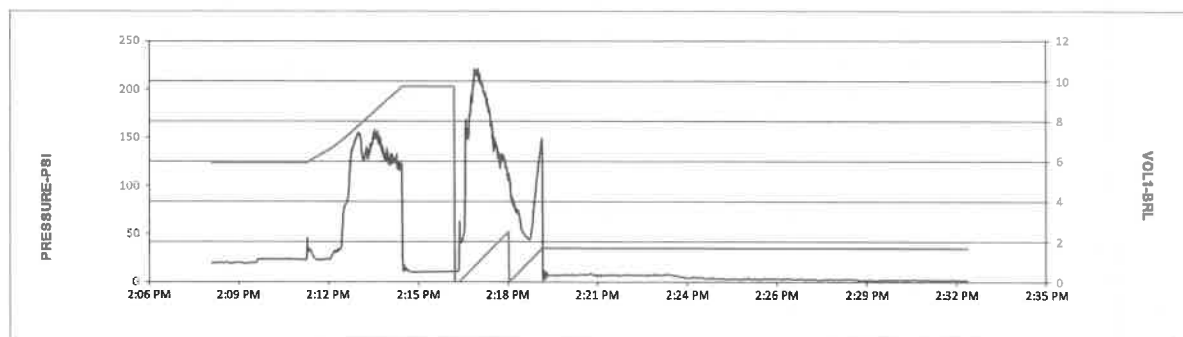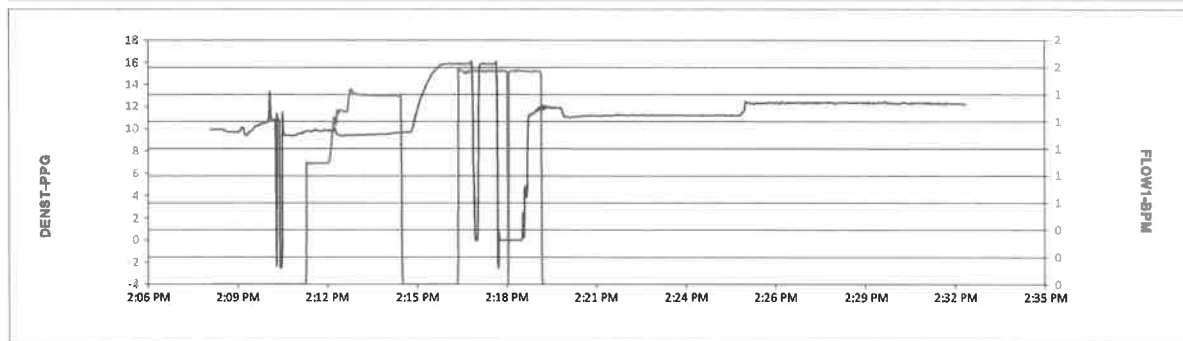

Report Created: *0*



JOB REPORT

DUCO INC.

COMPANY DETAILS

Company: *Chevron*
Contact: *Shane Paris*
Phone: *0*

Email: *0*



JOB DETAILS

Date: *12-20-24*
Start Time: *08:54:41*
End Time: *10:23:59*

Operator: *Jesus Hernandez*
Ticket #: *0*
LSD #: *3rd pump 188sks class G 15.8#*

Comments: *Sylvester 36-9H6*

SUMMARY GRAPHS

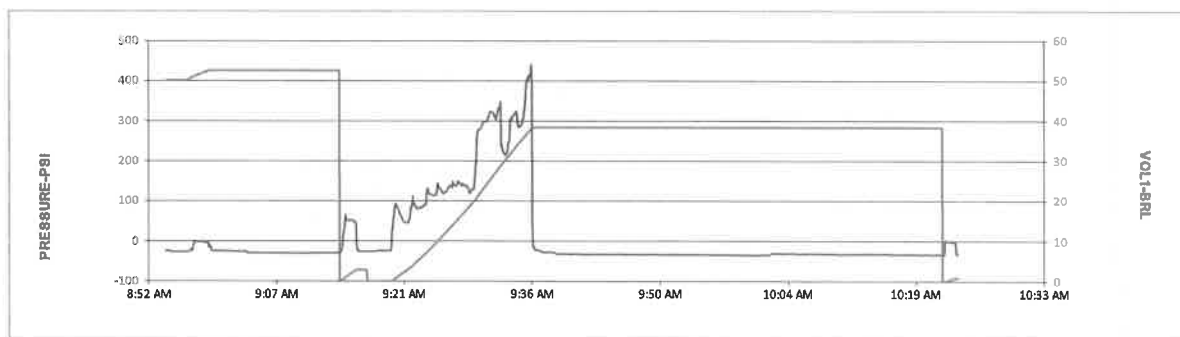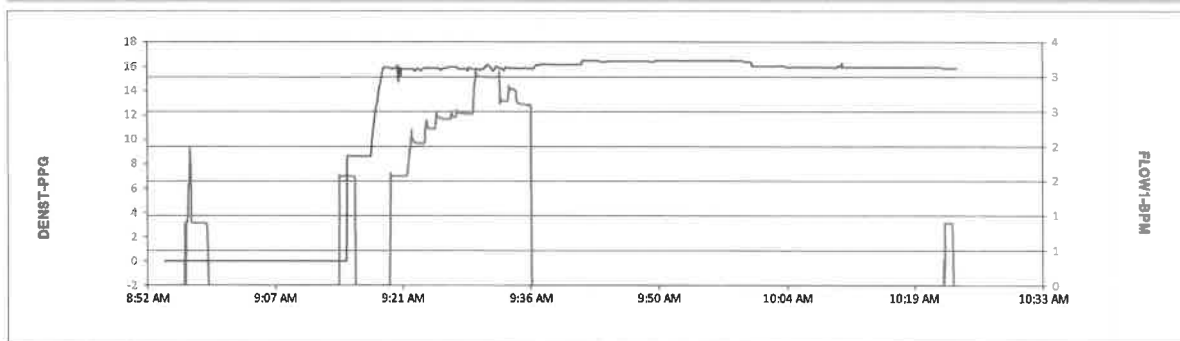

Report Created: *0*
