

PEAKVIEW OPERATING COMPANY

WELL: Kowach 1-9 FIELD: Buck Peak
 County: Moffat Co, CO
 Surface Loc: 300' FSL & 1,520' FWL (SE/SW) Sec. 9 T6N-R90W
 Bottom Hole Loc: 273' FSL & 2,152' FWL (SE/SW) Sec. 9 T6N-R90W


STATUS: Producer- Rod Pump

ELEVATIONS: 6,262' GL; 6,276' \diamond (14' KB) API NO: 05-081-6185

SPUD DATE: 1/6/1973 COMP DATE: 3/29/73

ROTARY TD: 7,481' (Sidetrack Hole) PBD: 7,420.53' (Junk in hole)

SURFACE CSG: 17 1/2" Hole with 13 3/8" 48# H-40 pipe landed @ 343'. Cemented with 450 sxs class G cement. Cement Circulated.
 INTERMEDIATE CSG: 12 1/4" Hole with 9 5/8" 36# K-55 pipe landed @ 2,002'. Cemented with 175 sxs class G cement. TOC ??
 INITIAL PRODUCTION CSG: 8 3/4" Hole with 7" 20# J-55 & 7" N-80 pipe landed @ 6,400'. Cemented with 175 sxs class G cement. TOC @ 5,383'.
 SIDE TRACK PRODUCTION CSG: 8 3/4" Hole with 7" 20# J-55 & 7" 23# N-80 pipe landed @ 5,104'. INITIAL PRODUCTION CSG cut @ 5,379'. 5 1/2" pipe pulled and landed @ 5,104'. Cemented with 200 sxs class G cement. TOC @ 4,026'
 LINER: 6 3/4" Hole with 5 1/2" 17# N-80 FJ pipe landed @ 7,481'. Top of Liner @ 4,937'. Liner run across OH section. Uncemented.

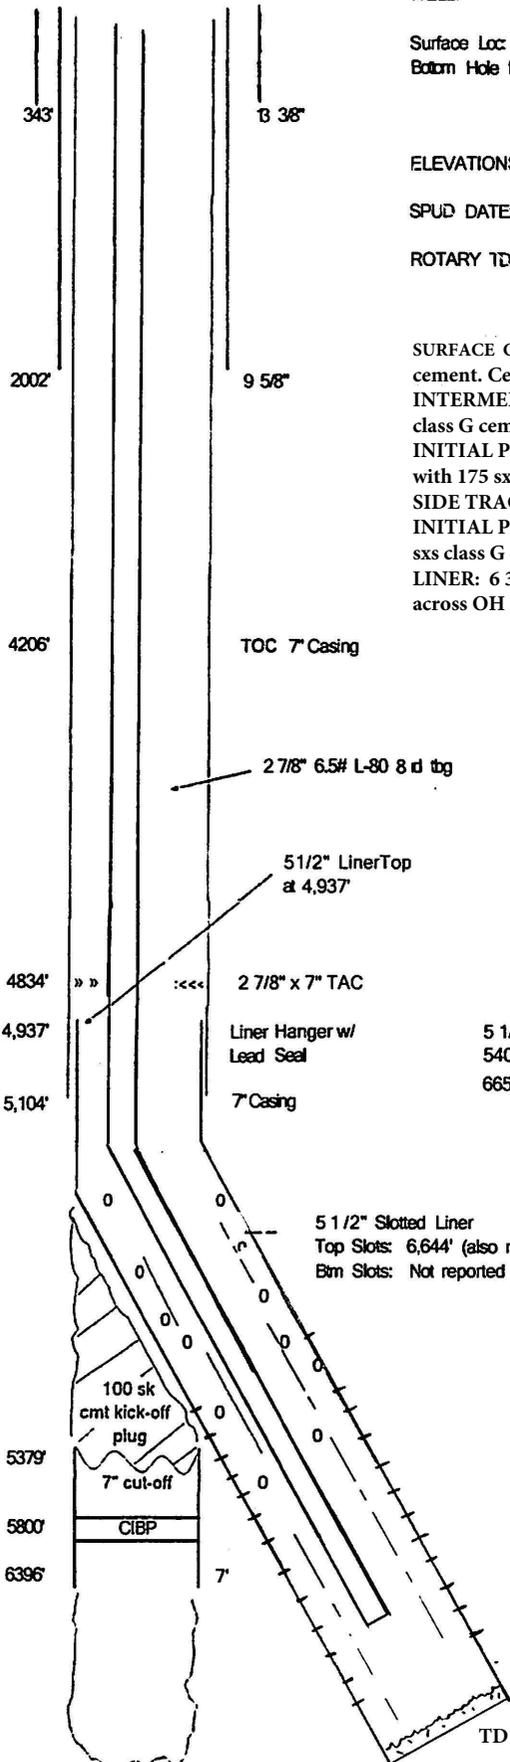

<u>7' Casing</u>	<u>Depth</u>
20# J-55 STC	5 104'-1,707'
23# J-55 STC	1 707'-405'
23# N-80 LTC	405'-0'
<u>5 1/2" Liner</u>	<u>Depth</u>
17# FJ PA 7 thrd	7,481'-4,937'

5 1/2" Liner Perforations:
 5400', 5600', 5800', 6000', 6200', 6300', 6400', 6500', 6600', 6700', 6800', 6850', 7000', & 7050' w/ 2 Jspf
 6652.5-62.5', 6852.5-62.5', 7052.5-62.5', 7263.5-73.5' w/ 4 jspf

5 1/2" Slotted Liner
 Top Slots: 6,644' (also reported as 6,683')
 Btm Slots: Not reported
