
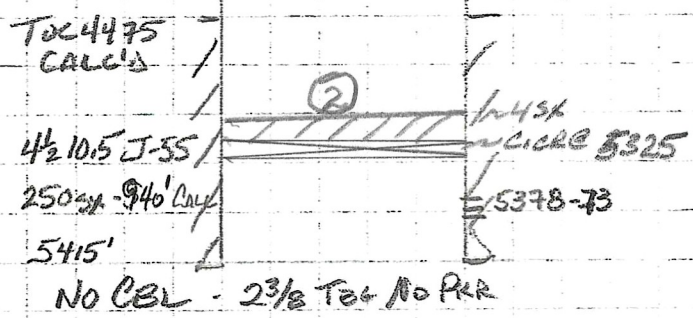




APPROVED W/ BDO PRA  
30 APR 26

STRACHAN EXPLORATION, INC  
STAVELY 1-26  
API 05-061-06394  
SPUD 5/06/74  
STR SESE 26-185-51N  
COUNTY KIOWA  
LOCID 324837  
FACILITY 213033  
LAT/LNG 38.456519/-103.082644  
FED LEASE  
MORROW 5373-78' DIESEL FRAC



PROPOSED PROCEDURE

- RUN BH TEST + REPORT TO SDR
- 1) MIRR Pull Rods, PUMP, TBG.
  - 2) PU CIRC - R/W, SET @ 5325' + 4SX CMT
  - 3) PRESSURE TEST (CSG 250 PSI 15 MIN)
  - 4) PERF @ 2640'  
1470'  
1000'  
357'
  - 5) PU CIRC (TBG) R/W, SET @ 2640'
  - 6) Mix & Pump 50SX, 40 THRU TOOL 10SX ON TOP
  - 7) PU CIRC (TBG) R/W, SET @ 1370'
  - 8) Mix & Pump 90SX, 75SX THRU + 15SX ON TOP
  - 9) PU CIRC (TBG) R/W, SET @ 950'
  - 10) Mix & Pump 50SX, 40 THRU + 10SX ON TOP
  - 11) CIRCULATE 1115X CMT LEAVE 4 1/2 CSG FULL  
 $257(.2471)/1.15 \rightarrow 55SX$   
 $100(.3313)/1.15 \rightarrow 29SX$   
 $357(.0872)/1.15 \rightarrow 27SX$

WAIT 5 DAYS MIN TO CUT & CAP  
PICS TO SDR.
