

Downhole Schematic for Federal 28-7 (PJ28)



Project :South Piceance

API # :05045110630000

Surface Location :

Area :Parachute

County :GARFIELD


BHL :

As Of : 10/08/2011

GL : ft

KB to GL : 13.0 ft

KB : ft

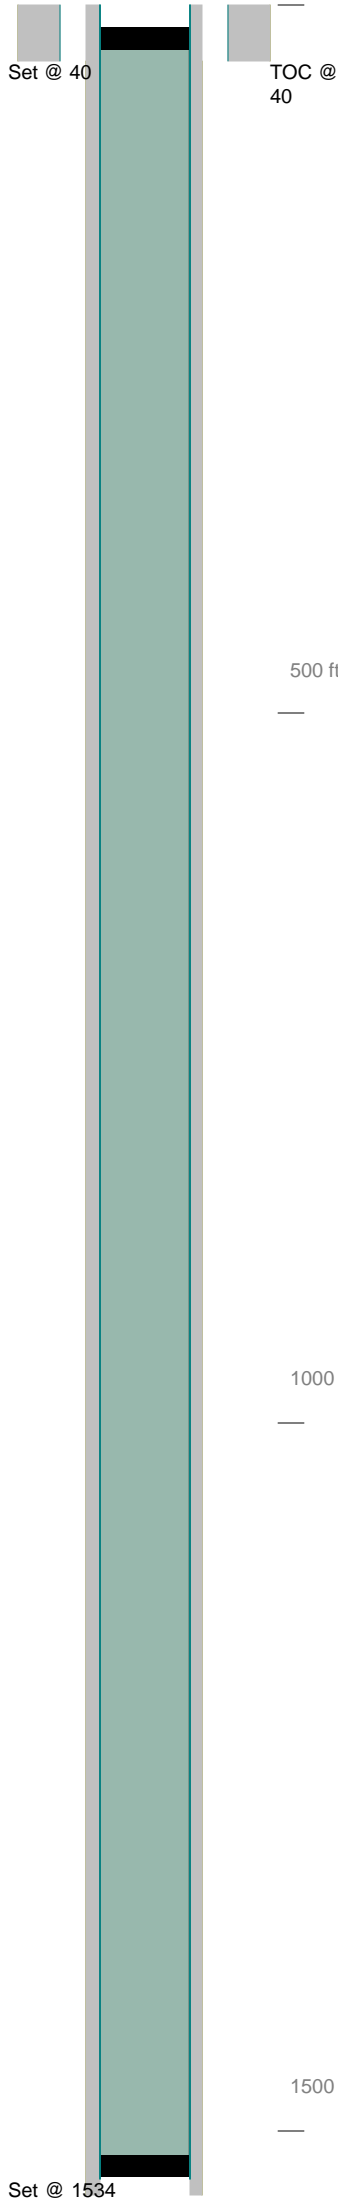

Casing Details

Section	Hole	Casing	Mass	Set At	Length	Thread	Grade	Description
Conductor	24.000	16	42	40	40			CONDUCTOR
Surface	11.000	8.625	24	1,534	1	ST&C	J55	Guide shoe
		8.625	24	1,533	42	ST&C	J55	Casing
		8.625	24	1,491	2	ST&C	J55	Float collar
		8.625	24	1,489	1,490	ST&C	J5	CASING

Cement Details

Section	Sequence	Top	Density	Blend / Additives
Conductor	Scavenger	0	15.8	5 YRDS OF READY MIX /
Surface	Tail	0	13.5	TXI TAIL / DO46 /DO29 /S001 /DO40

Tubing and Downhole Equipment

O.D.	Length	Depth	Description
8.625	1,534.00	1,534.00	500 sxs cement
