

NOBLE ENERGY INC.
DKW GREEN STATE BB18-01
NENE 18-5N-63W
802' FNL & 747' FEL
WELD COUNTY, CO
Wattenberg
CURRENT WELLBORE SCHEMATIC
with PROPOSED P&A
4/20/2015

API: 05-123-19277
COGCC #

GL Elev: 4657'
KB Elev: 4667'

Spud Date: 1/2/1997

Surface Casing :
8 5/8" 24# @ 368'
Cement: 260 sx
TOC: Surface


Annular Fill Cement from 3000' to 4294' (calc'd)

NEED FULL CBL RUN TO
CONFIRM CEMENT DEPTHS

Casing Repair Cement from 5180' to 5218' (calc'd)
Casing Patch @ 5213' (5/14/2001)

TOC @ 5870'

Production Casing :
3 1/2" 7.7# @ 6843'
Cement: 175 sx
TD: 1/6/1997

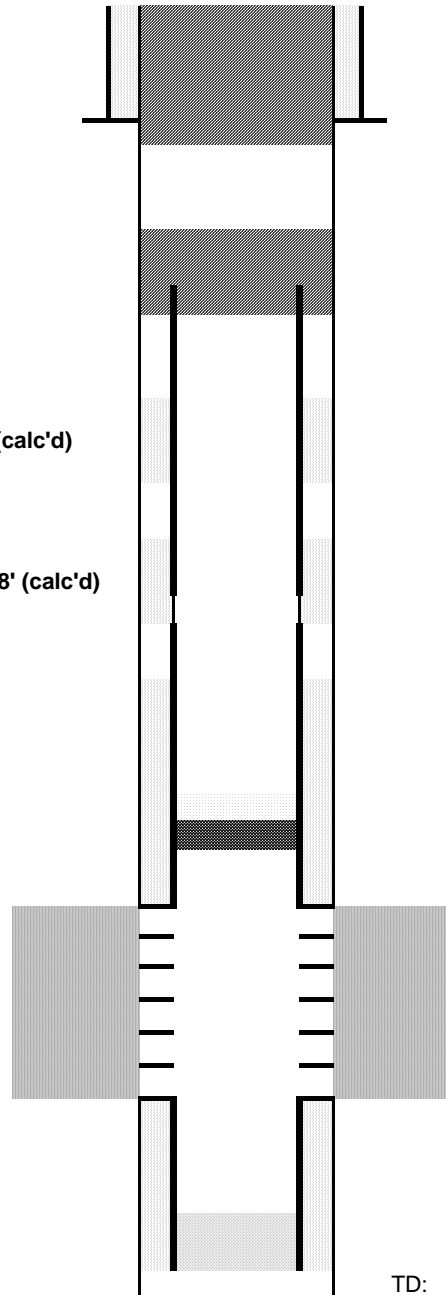

Cut surface casing off 6'-8' below surface.

Pump approx 175 sx shoe plug @ 470'
Will bring cement to surface.

Pump 100 sx stub plug where csg was pulled
Cut and pull csg @ 2500'

CIBP @ 6389' w/ 2 sx cement on top

Niobrara Perforations 6439' - 6532'

Codell Perforations 6686' - 6696'

TD: 6848'
