

Foundation Energy Management, LLC
Drilling - Completion - Workover - Facilities
WBD

AFE No.:		AFE Amount		Original:	\$0
AFE Type:		Plug & Abandon		Supplemental:	
AFE Category:		CAPEX		Total:	\$45,483
WI:	NRI:	AFE Date:	11/19/2014	Budget Year:	2014
Well / Battery	Prospect Name	Total Depth	Est. Start Date		
Mitchem 2-26X	Paladin	7,614'			
Location	Sec-Twa-Rng	Producing Horizon	County & State		
NE NE	26-3S-63W	JSND	Adams, CO		
AFE Description					
P&A					
WELLBORE DIAGRAM AFTER					

Prepared Date: 11-19-2014
Prepared By: Dalton Reazin

General Info

API #: 05-001-07685

KB Elevation: 5,409'
GL Elevation: 5,397'

Spud Date: 09-18-1980
Completion Date: 10-09-1980

TVD: 7,614'
MD: 7,614'
Last PBTD: 7,492' (03-08-2013)

Tubing Detail

inch(OD)
(weight)
grade

Tubing Tally

No Tubing

Length

Depth

Cmnt basket @ 1,350'


Niobrara 6,474'-6,674'

Perf @ 6,650'
TOC @ 6,812'

Pump Details:
none

Pumping Unit Details:
none

Well Notes:
CIBP @ 7,492' from TA
Cement basket @ 1,350'

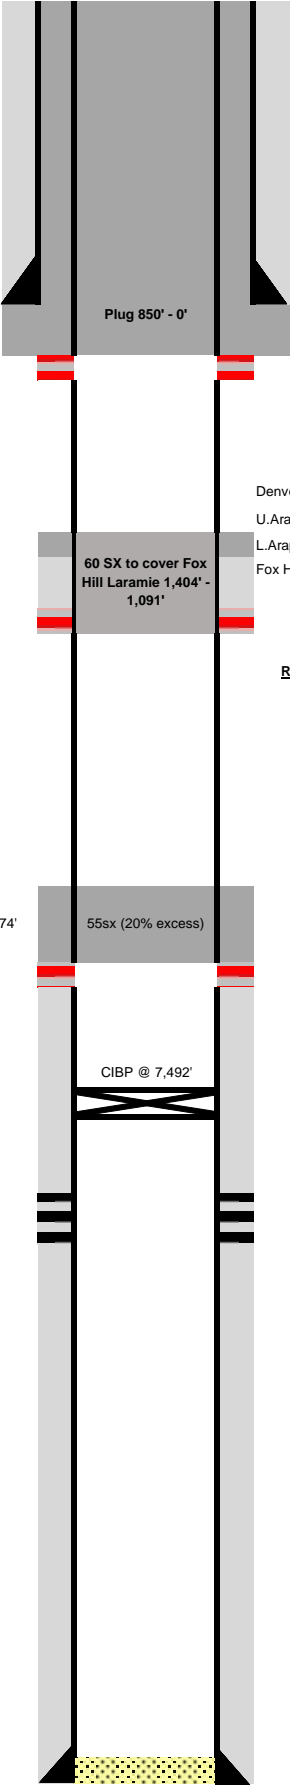

Surface Casing

8-5/8" inch (OD)
24 # (weight)
J-55 grade
233' depth from KB
Surface cement top
230 sacks of cement
12-1/4" inch (OD) HOLE SIZE

Aquifers

Denver 240-56'
U.Arapaho 557-312'
L.Arapahoe 816-632'
Fox Hills 1354-1141'

Visual Returns

Rod Design

NO RODS

length

depth

Production Casing

4-1/2" inch (OD)
12 # (weight)
J-55 grade
6,878' depth from KB
6,512' cement top
200 sacks of cement
7-7/8" inch (OD) HOLE SIZE

Calculated

Open Perforations

7520'-7550' - 61 holes
JSND

Original PBTD: 7,612'
