

Foundation Energy Management, LLC

WELLBORE DIAGRAM

Well / Battery	Prospect Name		Total Depth	Current Status
CSF 6-14	Baxter Pass		7098'	TA
Legal				
NESW 14 4S104W				

WELLBORE DIAGRAM

6/1/2021

General Info

API #: 05-103-10063

KB Elevation:

GL Elevation: 6294'

Spud Date: 12/21/2000

Completion Date: 2/19/2001

TVD: 7098'

MD: 7098'

Last PBTD: 7053'

Tubing Detail

inch(OD)
(weight)
depth

Rod Detail

Formation	Log Top	Log Bottom
CA	2757	3012
MA	3831	4250
FR	6281	6675
DA	6675	6813
MO	6906	

Stage Tool 4,970'

TOC: 440'

Surface Casing

8 5/8 inch (OD)
24 # (weight)
grade
588 depth from KB
0 cement top Calculated
428 sacks of cement
12 1/4 inch (OD) HOLE SIZE

Production Casing

4 1/2 inch (OD)
11.6 # (weight)
grade
7098 depth from KB
440 cement top CBL
1873 sacks of cement
7 7/8 inch (OD) HOLE SIZE

CIBP set @ 6660' (12/18/2018)

6712' - 6802' Dakota

Well Notes:

Foundation Energy Management, LLC

WELLBORE DIAGRAM

Well / Battery	Prospect Name		Total Depth	Current Status
CSF 6-14	Baxter Pass		7098'	TA
Legal				
NESW 14 4S104W				

Current WELLBORE DIAGRAM

6/1/2021

General Info

API #: 05-103-10063

KB Elevation:
GL Elevation: 6294'

Spud Date: 12/21/2000
Completion Date: 2/19/2001

TVD: 7098'
MD: 7098'
Last PBTD: 7053'


Tubing Detail

inch(OD)
(weight)
depth

Rod Detail

Formation	Log Top	Log Bottom
CASTLEGATE	2757	3012
MANCOS B	3831	4250
FRONTIER	6281	6675
DAKOTA	6675	6813
MORRISON	6906	

Stage Tool 4,970'

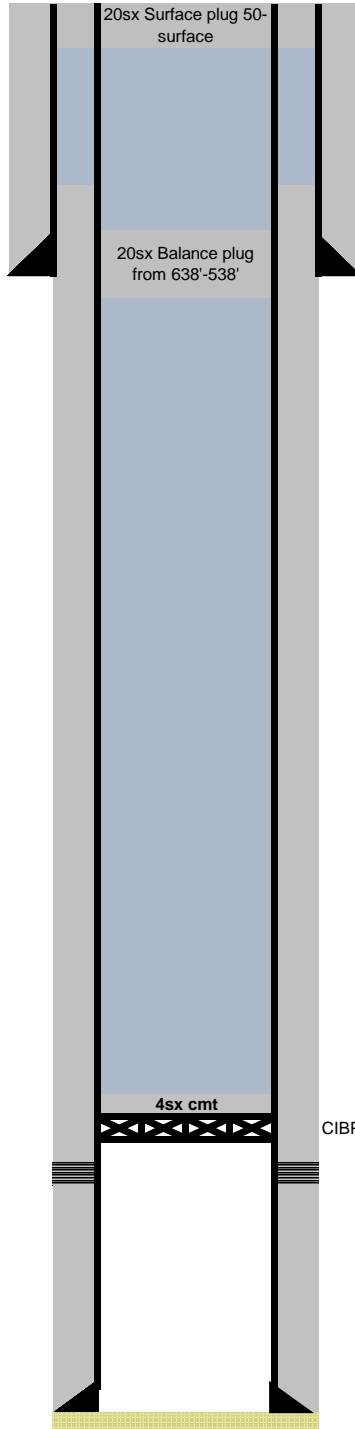

Surface Casing

8 5/8 inch (OD)
24 # (weight)
grade
588 depth from KB
0 cement top Calculated
428 sacks of cement
12 1/4 inch (OD) HOLE SIZE

Production Casing

4 1/2 inch (OD)
11.6 # (weight)
grade
7098 depth from KB
440 cement top CBL
1873 sacks of cement
7 7/8 inch (OD) HOLE SIZE

CIBP set @ 6660' (12/18/2018)

6712' - 6802' Dakota

Well Notes:
