

Alex Waner

From: Wolfe - DNR, Stephen <stephen.wolfe@state.co.us>
Sent: Monday, August 21, 2023 8:47 AM
To: Alex Waner
Cc: Jason Eisenach; Justin Pivik
Subject: [External]:Re: Verdad Hallet 1 Well

Approved.


On Thu, Aug 17, 2023 at 5:13 PM Alex Waner <AWaner@verdadresources.com> wrote:

Steve – Below is our agreed upon updated plan for the Hallet 1 (API 05-123-05736) that we are currently plugging.

1. TOOH with 5.5" casing
2. TIH w/ 2-7/8" tubing w/ notched collar to 1300'. If able to get into exiting 5.5" casing, TIH to 1300'. If unable to get into casing, TIH to maximum depth reached @ 1248', if conditions allow
3. Pump 60 sks, 1.15 Yield, 15.8 ppg cement inside 5-1/2" for lower hole isolation. 350' plug with 40% excess
4. POOH, WOC minimum 4 hours. TIH and tag cement
5. POOH to top of 5.5" casing @ 910'
6. Pump 320 sks, 1.15 Yield, 15.8 ppg cement in 7-7/8" open hole for Fox Hills isolation and surface casing isolation. Pump in 2 stages if necessary
7. Top off and RD

Please let me know if you approve. Thanks.

Hallet #1 Adjusted Plan WBD

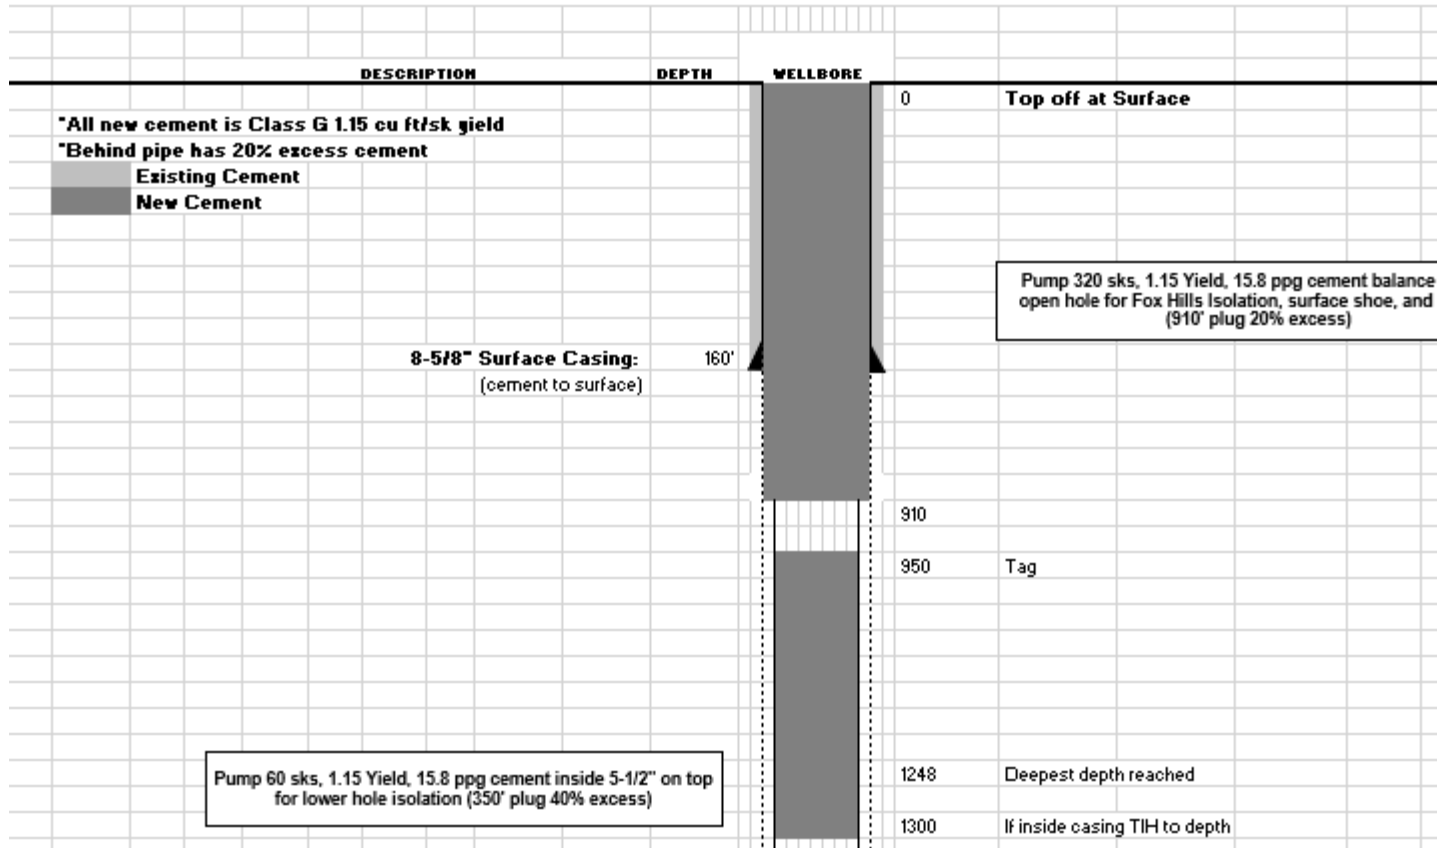

Alex Waner

awaner@verdadresources.com

C: 303-204-9636

1125 17th Street. Suite 550. Denver, CO 80202



|

--

Stephen Wolfe
303-894-2100 x5187 (o)
303-882-0224 (c)
