

WELL DETAILS: RG 524-13-298

+N/-S	+E/-W	Northing	Ground Level:	Easting	6667.00	Latitude	Longitude	Slot
0.00	0.00	1754857.810	2203514.060	2203514.060	39.871743	-108.338022	RG 524-13-298 B1	

DESIGN TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
VP	7647.00	-515.66	-2288.56	1754413.890	2201210.510	39.870327	-108.346176
BHL	1427.00	-515.66	-2288.56	1754413.890	2201210.510	39.870327	-108.346176

ANNOTATIONS

TVD	MD	Inc	Azi	+N/-S	+E/-W	VSect	Departure	Annotation
204.99	205.00	0.96	286.39	0.48	-1.65	1.50	1.72	First Survey @ 205 MD/ 204.9 TVD
11410.40	11793.00	5.62	225.19	-554.32	-2351.21	2415.55	2465.71	PTB @ 11793 MD/ 11410.4 TVD

SLOTS



Slot Name	+N/-S	+E/-W	Northing	Easting
RG 13-18-297 B5	20.95	21.47	1754878.080	2203536.170
RG 14-18-297 A5	13.80	28.45	1754870.710	2203542.930
RG 21-24-298 A3	3.31	17.72	1754860.570	2203531.870
RG 312-18-297 B7	31.42	32.20	1754888.210	2203547.230
RG 313-18-297 A8	29.50	44.55	1754885.900	2203559.510
RG 314-18-297 B4	15.72	16.11	1754873.020	2203530.650
RG 321-24-298 A2	-1.92	12.35	1754855.510	2203526.340
RG 324-13-298 B3	10.47	10.74	1754867.940	2203525.120
RG 412-18-297 B8	36.65	37.57	1754893.270	2203552.760
RG 413-18-297 A7	24.27	39.18	1754880.840	2203553.980
RG 414-18-297 A4	8.56	23.08	1754865.640	2203537.400
RG 421-24-298 A1	-7.16	6.99	1754850.440	2203520.820
RG 424-13-298 B2	5.24	5.37	1754862.880	2203519.590
RG 512-18-297 B6	26.18	26.84	1754883.140	2203541.700
RG 514-18-297 A6	19.03	33.81	1754875.770	2203548.450
RG 524-13-298 B1	0.00	0.00	1754857.810	2203514.060

FORMATION TOP DETAILS

TVDPath	MDPath	Formation
30.00	30.00	Uinta
880.00	889.21	GRRV
1030.00	1046.04	GRRV A Grove
1220.00	1248.16	GRRV B Groove
1530.00	1578.78	GRRV Dissolution Surf
2220.00	2314.67	Garden Gulch
2400.00	2506.64	GRRV Orange
2480.00	2591.96	U WSCH
4600.00	4852.97	G Dand
5015.00	5295.57	FRUN
5800.00	6132.78	L WSCH
6127.00	6481.53	OCRK
6847.00	7236.65	U MVRD
7647.00	8042.62	Top Gas
9217.00	9612.62	CMEO
9947.00	10342.62	RLNS
10097.00	10492.62	CZT
10422.00	10817.62	CRCN
10682.00	11077.62	Sego
10927.00	11322.62	Sego Lower


CASING DETAILS

TVD	MD	Name	Size
1330.00	1365.48	13 3/8"	13-3/8
2980.00	3125.22	9 5/8"	9-5/8

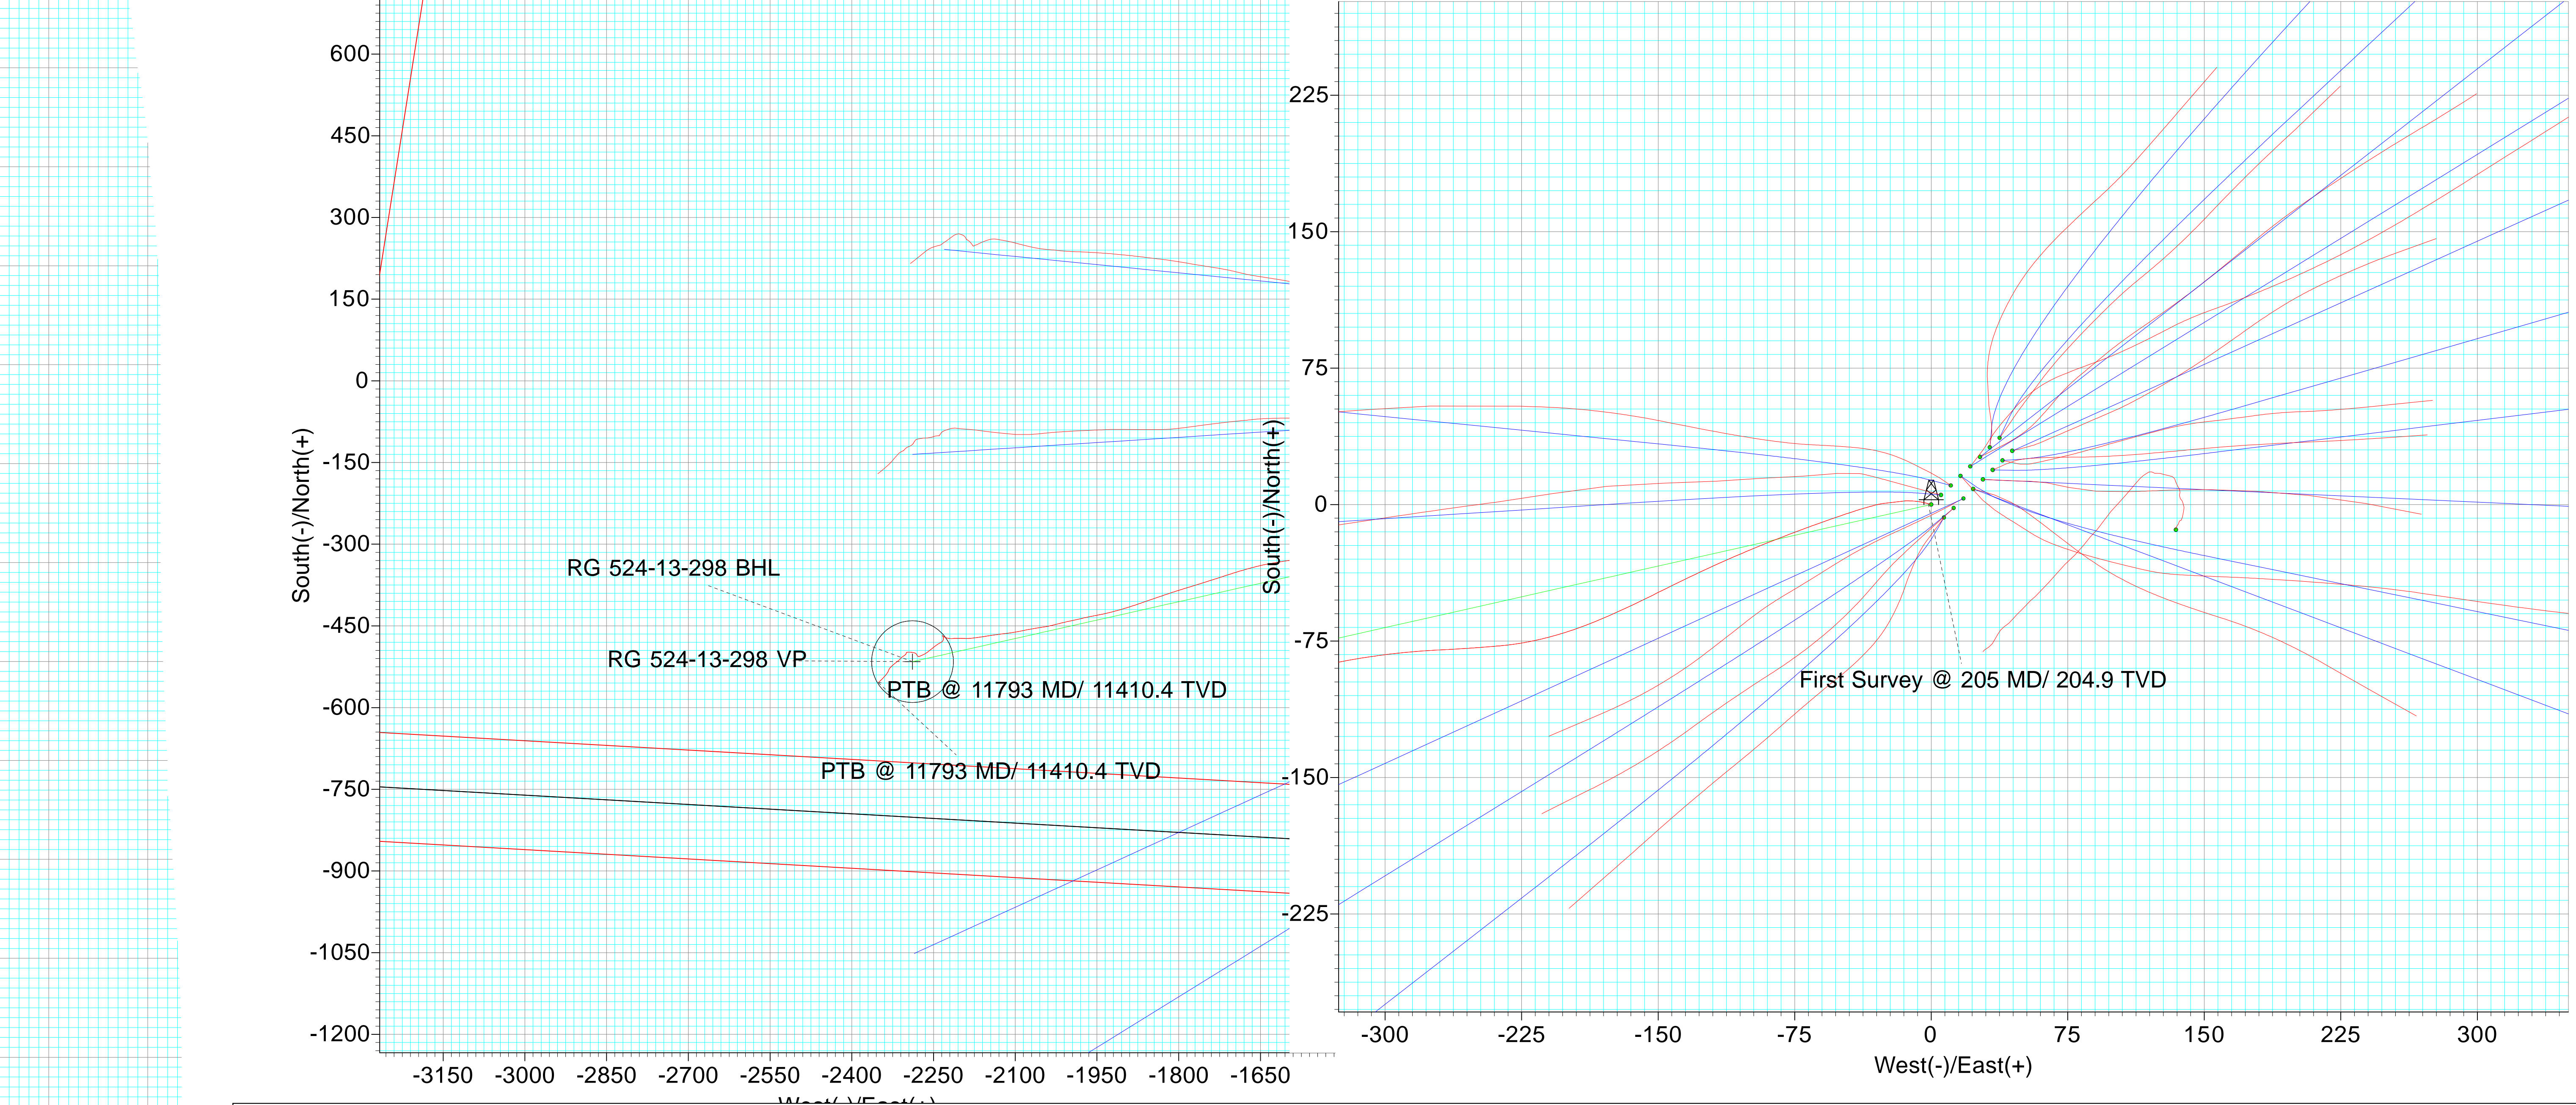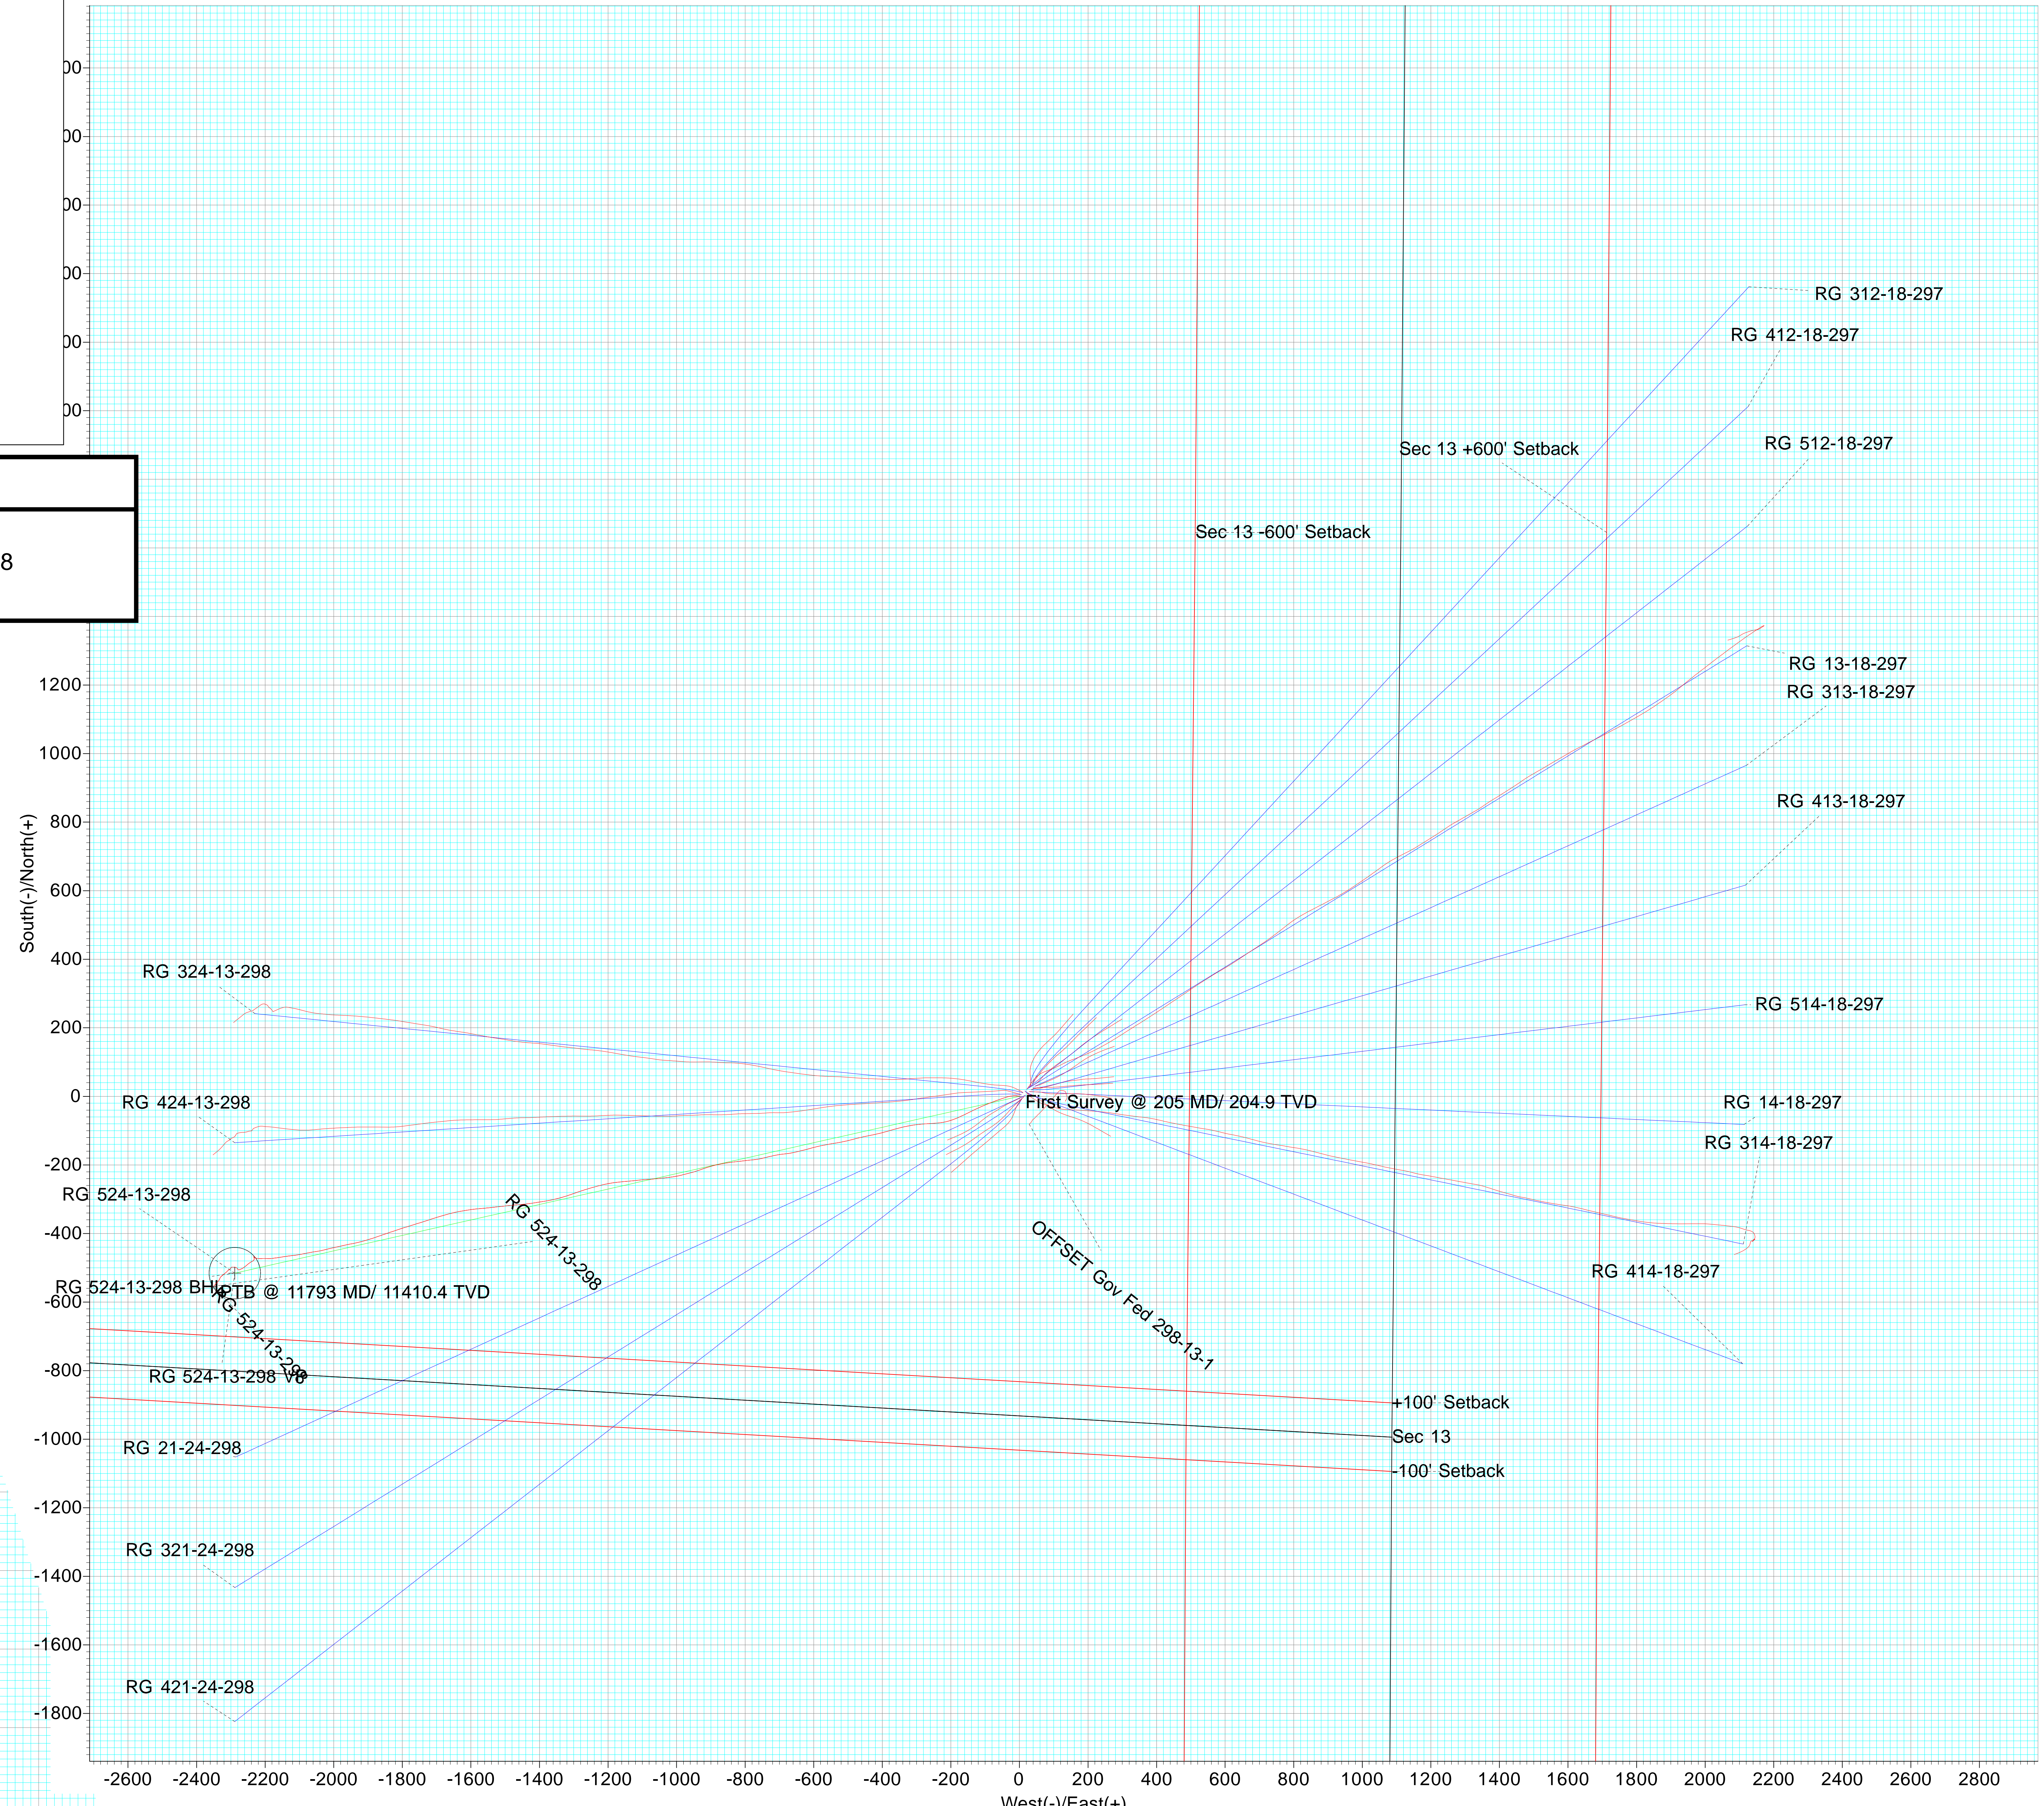

ANNOTATIONS

TVD	MD	Inc	Azi	+N/-S	+E/-W	VSect	Departure	Annotation
204.99	205.00	0.96	286.39	0.48	-1.65	1.50	1.72	First Survey @ 205 MD/ 204.9 TVD
11410.40	11793.00	5.62	225.19	-554.32	-2351.21	2415.55	2465.71	PTB @ 11793 MD/ 11410.4 TVD

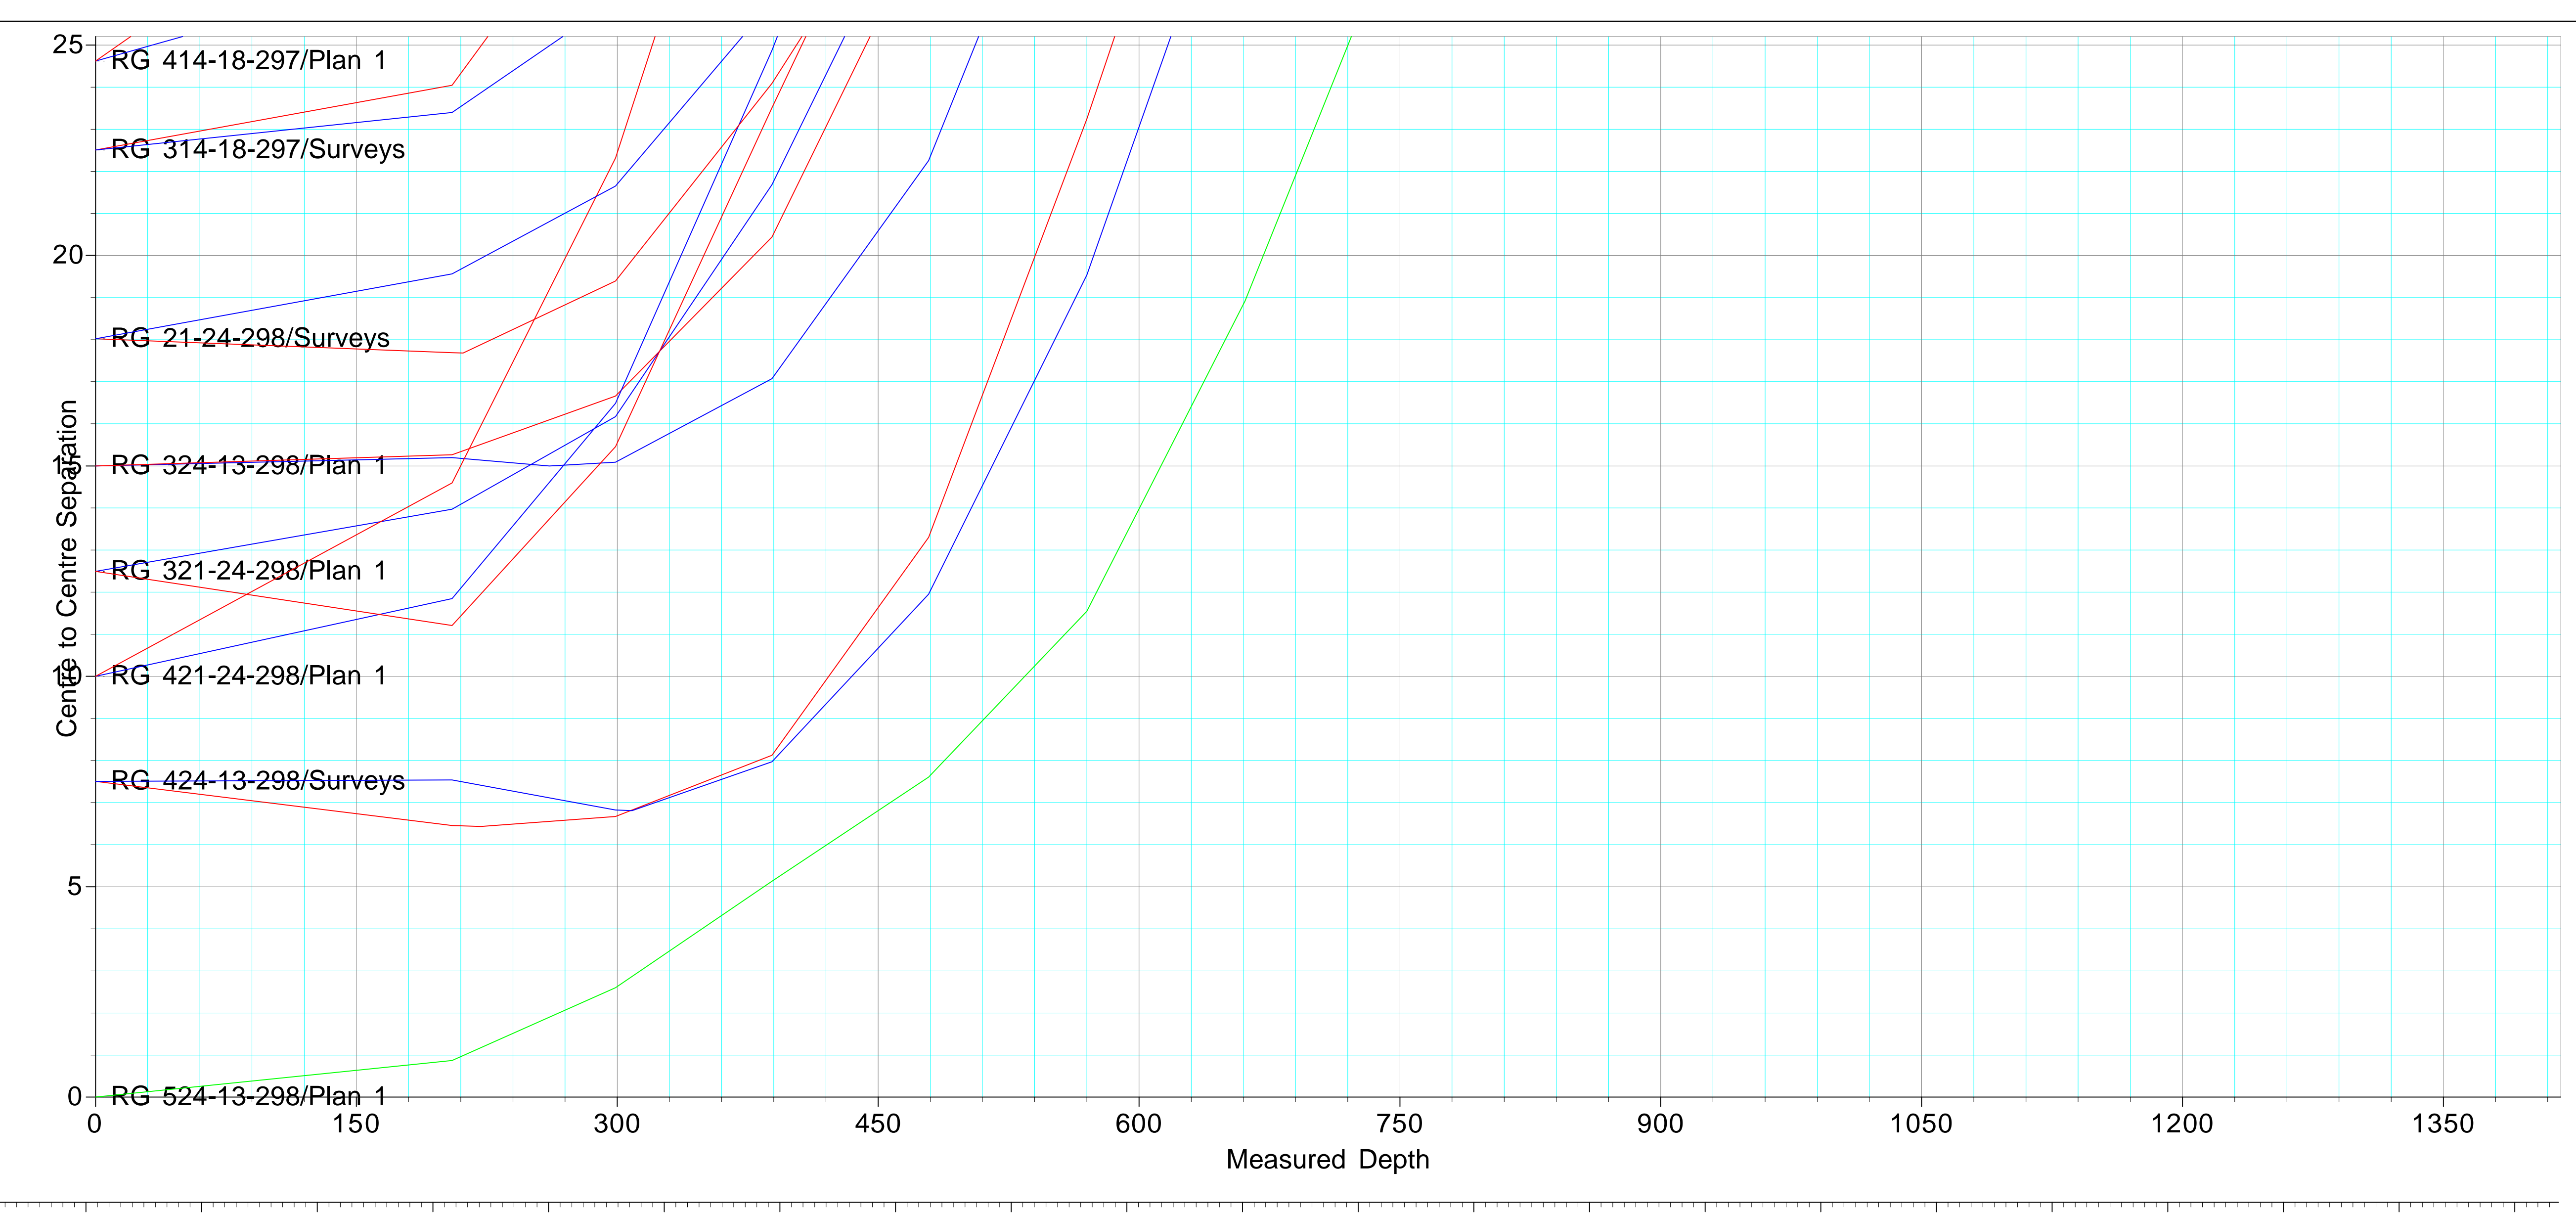



Terra Energy Partners, LLP

Garfield County, CO (Nad 83)

Fed 298-13-1 Pad

RG 524-13-298 - Slot RG 524-13-298 B1

OWB

Survey: Surveys

Standard Survey Report

23 April, 2024



Company:	Terra Energy Partners, LLP	Local Co-ordinate Reference:	Well RG 524-13-298 - Slot RG 524-13-298 B1
Project:	Garfield County, CO (Nad 83)	TVD Reference:	RKB @ 30' @ 6697.00ft
Site:	Fed 298-13-1 Pad	MD Reference:	RKB @ 30' @ 6697.00ft
Well:	RG 524-13-298	North Reference:	True
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	NN

Project	Garfield County, CO (Nad 83)		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Colorado Central Zone		

Site	Fed 298-13-1 Pad				
Site Position:		Northing:	1,754,850.440 usft	Latitude:	39.871723
From:	Map	Easting:	2,203,520.820 usft	Longitude:	-108.337998
Position Uncertainty:	0.00 ft	Slot Radius:	13-3/16 "	Grid Convergence:	-1.79 °

Well	RG 524-13-298 - Slot RG 524-13-298 B1					
Well Position	+N/-S	0.00 ft	Northing:	1,754,857.810 usft	Latitude:	39.871743
	+E/-W	0.00 ft	Easting:	2,203,514.060 usft	Longitude:	-108.338023
Position Uncertainty		0.00 ft	Wellhead Elevation:	6,697.00 ft	Ground Level:	6,667.00 ft

Wellbore	OWB				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	HDGM	12/31/2023	9.07	65.75	50,921

Design	Surveys				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.00	0.00	0.00	257.30	

Survey Program	Date	3/20/2024			
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
205.00	11,793.00	Surveys (OWB)	OWSG (REV5) MWD HDGM	OWSG MWD - Standard	

Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
205.00	0.96	286.39	204.99	0.48	-1.65	1.50	0.47	0.47	0.00	
First Survey @ 205 MD/ 204.9 TVD										
299.00	3.82	282.26	298.90	1.37	-5.46	5.03	3.05	3.04	-4.39	
389.00	7.11	270.75	388.48	2.08	-13.97	13.17	3.84	3.66	-12.79	
479.00	10.01	257.91	477.48	0.52	-27.19	26.41	3.84	3.22	-14.27	
570.00	14.06	251.41	566.46	-4.67	-45.41	45.32	4.69	4.45	-7.14	
661.00	16.74	249.92	654.19	-12.69	-68.20	69.32	2.98	2.95	-1.64	
751.00	19.07	247.98	739.82	-22.66	-94.00	96.68	2.67	2.59	-2.16	
842.00	20.03	245.17	825.58	-34.77	-121.93	126.59	1.48	1.05	-3.09	
933.00	20.83	243.32	910.85	-48.58	-150.53	157.53	1.13	0.88	-2.03	

Company:	Terra Energy Partners, LLP	Local Co-ordinate Reference:	Well RG 524-13-298 - Slot RG 524-13-298 B1
Project:	Garfield County, CO (Nad 83)	TVD Reference:	RKB @ 30' @ 6697.00ft
Site:	Fed 298-13-1 Pad	MD Reference:	RKB @ 30' @ 6697.00ft
Well:	RG 524-13-298	North Reference:	True
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	NN

Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
1,023.00	21.13	246.49	994.89	-62.24	-179.71	188.99	1.30	0.33	3.52
1,114.00	19.11	255.01	1,080.35	-72.64	-209.14	220.00	3.91	-2.22	9.36
1,204.00	17.62	264.95	1,165.79	-77.65	-236.95	248.23	3.85	-1.66	11.04
1,295.00	20.34	266.88	1,251.83	-79.72	-266.47	277.48	3.07	2.99	2.12
1,308.00	20.74	267.23	1,264.00	-79.96	-271.02	281.97	3.22	3.08	2.69
1,477.00	21.70	258.15	1,421.59	-87.82	-331.51	342.71	2.02	0.57	-5.37
1,568.00	21.44	254.10	1,506.22	-95.83	-363.97	376.13	1.66	-0.29	-4.45
1,660.00	21.35	254.81	1,591.88	-104.83	-396.30	409.65	0.30	-0.10	0.77
1,751.00	20.43	258.59	1,676.90	-112.31	-427.86	442.08	1.79	-1.01	4.15
1,841.00	20.34	257.62	1,761.26	-118.77	-458.54	473.43	0.39	-0.10	-1.08
1,932.00	20.47	254.72	1,846.56	-126.36	-489.33	505.14	1.12	0.14	-3.19
2,023.00	19.51	259.82	1,932.08	-133.24	-519.64	536.22	2.19	-1.05	5.60
2,113.00	19.33	260.34	2,016.96	-138.39	-549.12	566.11	0.28	-0.20	0.58
2,204.00	19.68	258.06	2,102.74	-144.09	-578.96	596.47	0.92	0.38	-2.51
2,294.00	19.33	254.37	2,187.58	-151.24	-608.13	626.50	1.42	-0.39	-4.10
2,385.00	16.21	256.48	2,274.22	-158.27	-634.99	654.25	3.50	-3.43	2.32
2,475.00	15.95	257.53	2,360.70	-163.87	-659.28	679.18	0.43	-0.29	1.17
2,566.00	19.02	264.39	2,447.50	-168.03	-686.26	706.40	4.06	3.37	7.54
2,657.00	18.72	257.97	2,533.62	-172.52	-715.30	735.73	2.30	-0.33	-7.05
2,749.00	19.24	255.77	2,620.62	-179.32	-744.43	765.64	0.96	0.57	-2.39
2,840.00	21.84	263.77	2,705.84	-184.85	-775.80	797.46	4.20	2.86	8.79
2,932.00	22.67	263.51	2,790.99	-188.71	-810.43	832.09	0.91	0.90	-0.28
3,023.00	23.95	262.54	2,874.56	-193.09	-846.17	867.92	1.47	1.41	-1.07
3,095.00	22.06	258.59	2,940.83	-197.66	-873.92	895.99	3.39	-2.63	-5.49
3,177.00	19.90	253.31	3,017.40	-204.72	-902.39	925.32	3.50	-2.63	-6.44
3,268.00	18.06	250.06	3,103.45	-213.98	-930.48	954.76	2.33	-2.02	-3.57
3,360.00	19.07	254.98	3,190.67	-222.74	-958.41	983.93	2.02	1.10	5.35
3,450.00	18.80	256.30	3,275.80	-229.98	-986.70	1,013.12	0.56	-0.30	1.47
3,542.00	19.78	262.54	3,362.64	-235.51	-1,016.54	1,043.45	2.48	1.07	6.78
3,633.00	20.39	264.04	3,448.11	-239.16	-1,047.57	1,074.52	0.88	0.67	1.65
3,725.00	20.12	266.67	3,534.42	-241.74	-1,079.31	1,106.05	1.03	-0.29	2.86
3,816.00	21.62	263.60	3,619.45	-244.52	-1,111.60	1,138.16	2.04	1.65	-3.37
3,908.00	23.77	265.18	3,704.32	-247.97	-1,146.92	1,173.38	2.43	2.34	1.72
4,000.00	21.84	262.54	3,789.13	-251.75	-1,182.37	1,208.79	2.37	-2.10	-2.87
4,091.00	22.58	256.13	3,873.39	-258.13	-1,216.12	1,243.12	2.78	0.81	-7.04
4,183.00	20.34	254.02	3,959.00	-266.77	-1,248.64	1,276.75	2.57	-2.43	-2.29
4,275.00	18.89	251.73	4,045.66	-275.84	-1,278.16	1,307.53	1.78	-1.58	-2.49
4,366.00	17.13	250.33	4,132.20	-284.97	-1,304.77	1,335.50	1.99	-1.93	-1.54
4,458.00	17.40	253.23	4,220.06	-293.50	-1,330.70	1,362.67	0.98	0.29	3.15
4,549.00	19.24	257.36	4,306.45	-300.71	-1,358.36	1,391.24	2.47	2.02	4.54
4,641.00	20.52	261.22	4,392.97	-306.49	-1,389.09	1,422.49	1.99	1.39	4.20
4,733.00	19.55	260.96	4,479.40	-311.37	-1,420.23	1,453.93	1.06	-1.05	-0.28
4,824.00	20.96	265.09	4,564.77	-315.15	-1,451.48	1,485.26	2.21	1.55	4.54

Company:	Terra Energy Partners, LLP	Local Co-ordinate Reference:	Well RG 524-13-298 - Slot RG 524-13-298 B1
Project:	Garfield County, CO (Nad 83)	TVD Reference:	RKB @ 30' @ 6697.00ft
Site:	Fed 298-13-1 Pad	MD Reference:	RKB @ 30' @ 6697.00ft
Well:	RG 524-13-298	North Reference:	True
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	NN

Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
4,916.00	19.59	264.48	4,651.07	-318.05	-1,483.23	1,516.87	1.51	-1.49	-0.66	
5,007.00	19.37	263.95	4,736.86	-321.10	-1,513.42	1,546.99	0.31	-0.24	-0.58	
5,099.00	18.45	263.33	4,823.90	-324.40	-1,543.06	1,576.62	1.02	-1.00	-0.67	
5,190.00	20.03	265.44	4,909.81	-327.32	-1,572.89	1,606.37	1.90	1.74	2.32	
5,282.00	18.98	261.58	4,996.53	-330.76	-1,603.40	1,636.89	1.81	-1.14	-4.20	
5,374.00	17.71	259.55	5,083.86	-335.49	-1,631.96	1,665.79	1.55	-1.38	-2.21	
5,465.00	17.92	255.60	5,170.50	-341.48	-1,659.14	1,693.62	1.35	0.23	-4.34	
5,557.00	18.94	253.49	5,257.78	-349.24	-1,687.16	1,722.67	1.32	1.11	-2.29	
5,648.00	19.33	251.73	5,343.75	-358.16	-1,715.62	1,752.39	0.77	0.43	-1.93	
5,739.00	20.83	252.43	5,429.22	-367.77	-1,745.35	1,783.50	1.67	1.65	0.77	
5,831.00	21.75	253.23	5,514.94	-377.62	-1,777.27	1,816.81	1.05	1.00	0.87	
5,922.00	20.83	251.82	5,599.73	-387.54	-1,808.78	1,849.73	1.16	-1.01	-1.55	
6,014.00	19.77	251.12	5,686.01	-397.68	-1,839.05	1,881.48	1.18	-1.15	-0.76	
6,106.00	18.06	250.76	5,773.04	-407.41	-1,867.24	1,911.12	1.86	-1.86	-0.39	
6,197.00	16.34	252.61	5,859.97	-415.89	-1,892.77	1,937.90	1.98	-1.89	2.03	
6,288.00	19.11	255.16	5,946.64	-423.53	-1,919.39	1,965.54	3.16	3.04	2.80	
6,380.00	18.72	259.20	6,033.68	-430.15	-1,948.45	1,995.35	1.48	-0.42	4.39	
6,472.00	17.57	257.44	6,121.10	-435.94	-1,976.51	2,023.99	1.38	-1.25	-1.91	
6,564.00	16.52	257.36	6,209.06	-441.82	-2,002.83	2,050.96	1.14	-1.14	-0.09	
6,656.00	14.89	255.42	6,297.62	-447.66	-2,027.03	2,075.86	1.86	-1.77	-2.11	
6,747.00	15.07	261.66	6,385.54	-452.32	-2,050.05	2,099.34	1.78	0.20	6.86	
6,838.00	14.37	259.11	6,473.55	-456.17	-2,072.85	2,122.42	1.05	-0.77	-2.80	
6,930.00	13.75	258.85	6,562.79	-460.44	-2,094.79	2,144.76	0.68	-0.67	-0.28	
7,023.00	12.70	263.42	6,653.33	-463.75	-2,115.79	2,165.98	1.59	-1.13	4.91	
7,114.00	11.29	262.45	6,742.34	-466.06	-2,134.55	2,184.79	1.57	-1.55	-1.07	
7,205.00	9.88	260.43	6,831.79	-468.53	-2,151.08	2,201.46	1.60	-1.55	-2.22	
7,297.00	8.26	262.28	6,922.63	-470.73	-2,165.42	2,215.93	1.79	-1.76	2.01	
7,388.00	8.04	262.54	7,012.72	-472.44	-2,178.20	2,228.78	0.25	-0.24	0.29	
7,479.00	7.38	271.42	7,102.90	-473.12	-2,190.36	2,240.78	1.49	-0.73	9.76	
7,571.00	5.62	270.80	7,194.30	-472.91	-2,200.77	2,250.90	1.91	-1.91	-0.67	
7,663.00	5.31	268.34	7,285.88	-472.97	-2,209.53	2,259.45	0.42	-0.34	-2.67	
7,754.00	4.74	267.02	7,376.53	-473.29	-2,217.49	2,267.29	0.64	-0.63	-1.45	
7,846.00	4.30	285.75	7,468.25	-472.55	-2,224.61	2,274.07	1.67	-0.48	20.36	
7,937.00	3.33	294.53	7,559.05	-470.52	-2,230.30	2,279.18	1.24	-1.07	9.65	
8,028.00	1.49	320.37	7,649.97	-468.52	-2,233.46	2,281.82	2.30	-2.02	28.40	
8,119.00	0.18	99.07	7,740.96	-467.63	-2,234.07	2,282.22	1.79	-1.44	152.42	
8,209.00	0.35	99.07	7,830.96	-467.69	-2,233.66	2,281.83	0.19	0.19	0.00	
8,301.00	1.05	155.14	7,922.95	-468.50	-2,233.03	2,281.40	0.98	0.76	60.95	
8,393.00	1.58	161.03	8,014.92	-470.47	-2,232.26	2,281.08	0.59	0.58	6.40	
8,484.00	1.45	184.32	8,105.89	-472.80	-2,231.94	2,281.28	0.69	-0.14	25.59	
8,576.00	1.18	186.87	8,197.87	-474.90	-2,232.14	2,281.94	0.30	-0.29	2.77	
8,668.00	1.53	204.89	8,289.84	-476.96	-2,232.77	2,283.00	0.59	0.38	19.59	
8,759.00	1.66	228.26	8,380.81	-478.94	-2,234.27	2,284.90	0.72	0.14	25.68	

Company:	Terra Energy Partners, LLP	Local Co-ordinate Reference:	Well RG 524-13-298 - Slot RG 524-13-298 B1
Project:	Garfield County, CO (Nad 83)	TVD Reference:	RKB @ 30' @ 6697.00ft
Site:	Fed 298-13-1 Pad	MD Reference:	RKB @ 30' @ 6697.00ft
Well:	RG 524-13-298	North Reference:	True
Wellbore:	OWB	Survey Calculation Method:	Minimum Curvature
Design:	Surveys	Database:	NN

Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)	
8,852.00	2.06	244.35	8,473.76	-480.56	-2,236.78	2,287.70	0.70	0.43	17.30	
8,944.00	2.50	241.01	8,565.69	-482.25	-2,240.02	2,291.24	0.50	0.48	-3.63	
9,035.00	2.85	232.31	8,656.59	-484.59	-2,243.55	2,295.20	0.59	0.38	-9.56	
9,127.00	3.07	235.38	8,748.47	-487.39	-2,247.39	2,299.55	0.29	0.24	3.34	
9,219.00	3.07	229.93	8,840.33	-490.37	-2,251.30	2,304.03	0.32	0.00	-5.92	
9,311.00	3.73	230.46	8,932.17	-493.86	-2,255.49	2,308.89	0.72	0.72	0.58	
9,402.00	4.17	233.89	9,022.96	-497.70	-2,260.45	2,314.56	0.55	0.48	3.77	
9,494.00	3.64	238.99	9,114.74	-501.17	-2,265.65	2,320.41	0.69	-0.58	5.54	
9,585.00	2.81	246.19	9,205.60	-503.56	-2,270.17	2,325.34	1.01	-0.91	7.91	
9,677.00	3.12	246.46	9,297.47	-505.47	-2,274.53	2,330.01	0.34	0.34	0.29	
9,768.00	1.88	284.08	9,388.39	-506.10	-2,278.25	2,333.77	2.19	-1.36	41.34	
9,859.00	1.75	346.39	9,479.35	-504.39	-2,280.02	2,335.13	2.07	-0.14	68.47	
9,949.00	1.75	323.10	9,569.31	-501.95	-2,281.17	2,335.71	0.78	0.00	-25.88	
10,042.00	1.75	298.67	9,662.27	-500.13	-2,283.27	2,337.36	0.80	0.00	-26.27	
10,133.00	1.88	279.07	9,753.23	-499.23	-2,285.96	2,339.79	0.69	0.14	-21.54	
10,224.00	1.66	276.17	9,844.18	-498.86	-2,288.75	2,342.42	0.26	-0.24	-3.19	
10,317.00	2.85	279.07	9,937.11	-498.35	-2,292.37	2,345.85	1.29	1.28	3.12	
10,409.00	3.16	264.65	10,028.98	-498.22	-2,297.15	2,350.49	0.89	0.34	-15.67	
10,500.00	1.23	191.97	10,119.93	-499.41	-2,299.85	2,353.38	3.33	-2.12	-79.87	
10,592.00	1.40	203.83	10,211.90	-501.41	-2,300.51	2,354.46	0.35	0.18	12.89	
10,684.00	2.46	231.69	10,303.85	-503.66	-2,302.52	2,356.91	1.51	1.15	30.28	
10,778.00	3.03	238.02	10,397.74	-506.22	-2,306.21	2,361.08	0.69	0.61	6.73	
10,872.00	3.42	221.41	10,491.60	-509.64	-2,310.17	2,365.69	1.07	0.41	-17.67	
10,967.00	3.60	230.20	10,586.42	-513.68	-2,314.33	2,370.64	0.60	0.19	9.25	
11,061.00	4.04	232.48	10,680.21	-517.58	-2,319.23	2,376.28	0.50	0.47	2.43	
11,155.00	4.39	228.70	10,773.95	-521.97	-2,324.56	2,382.44	0.48	0.37	-4.02	
11,248.00	2.85	225.01	10,866.77	-525.96	-2,328.87	2,387.52	1.67	-1.66	-3.97	
11,343.00	2.06	207.17	10,961.68	-529.15	-2,331.32	2,390.61	1.15	-0.83	-18.78	
11,437.00	2.59	199.17	11,055.60	-532.66	-2,332.79	2,392.81	0.66	0.56	-8.51	
11,531.00	3.86	215.78	11,149.45	-537.23	-2,335.33	2,396.31	1.66	1.35	17.67	
11,625.00	5.09	222.29	11,243.17	-542.88	-2,339.99	2,402.09	1.41	1.31	6.93	
11,718.00	5.62	225.19	11,335.76	-549.14	-2,346.00	2,409.33	0.64	0.57	3.12	
11,793.00	5.62	225.19	11,410.40	-554.32	-2,351.21	2,415.55	0.00	0.00	0.00	
PTB @ 11793 MD/ 11410.4 TVD										

Survey Annotations					
Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment	
		+N/-S (ft)	+E/-W (ft)		
205.00	204.99	0.48	-1.65	First Survey @ 205 MD/ 204.9 TVD	
11,793.00	11,410.40	-554.32	-2,351.21	PTB @ 11793 MD/ 11410.4 TVD	

Checked By: _____ Approved By: _____ Date: _____
