



Closure Checklist

Closure Type: Wellhead Closure

Site Name: Miller 7-10

Remediation #:: 40001

Latitude, Longitude:: 40.241700,-104.761440

General Condition of Site: Good

USCS Soil Type: SM - Sands with fines - sand/silt mixture

Estimated Depth of Groundwater **less than 20' bgs**

Hydrocarbon Impacted Soils/Spills **None Observed**

Salt Crusted Soils or Impacted Vegetation **None Observed**

Soil Samples

#	Date	Time	Sample ID	PID	Visual	Olfactory	Equipment	Lab
1	05/12/2025	12:30	WH-B01@6'	0.3	No Staining	No odor	Wellhead	
2	05/12/2025	12:32	WH-B01-01@6'	0.3	No Staining	No odor	Wellhead	
3	05/12/2025	12:34	WH-RIS@4'	1.4	No Staining	No odor	Flowline at Wellhead	
4	05/12/2025	12:36	WH-RIS-01@4'	1.4	No Staining	No odor	Flowline at Wellhead	
5	05/05/2025	12:38	WH-N01@5'	2.2	No Staining	No odor	Wellhead	
6	05/12/2025	12:40	WH-E01@5'	2.8	No Staining	No odor	Wellhead	
7	05/12/2025	12:42	WH-S01@5'	2.6	No Staining	No odor	Wellhead	
8	05/05/2025	12:44	WH-W01@5'	3.1	No Staining	No odor	Wellhead	
9	05/12/2025	12:46	WHS-N01@3"	2.0	No Staining	No odor	Wellhead Surface	
10	05/12/2025	12:48	WHS-E01@3"	1.7	No Staining	No odor	Wellhead Surface	
11	05/12/2025	12:50	WHS-S01@3"	1.6	No Staining	No odor	Wellhead Surface	
12	05/12/2025	12:52	WHS-W01@3"	2.3	No Staining	No odor	Wellhead Surface	
13	05/12/2025	12:00	WH-BG01@3'	2.4	No Staining	No odor	Wellhead Background	
14	05/12/2025	12:02	WH-BG01@6'	2.1	No Staining	No odor	Wellhead Background	
15	05/12/2025	12:04	WH-BG02@3'	1.8	No Staining	No odor	Wellhead Background	
16	05/12/2025	12:06	WH-BG02@6'	2.2	No Staining	No odor	Wellhead Background	
17	05/12/2025	12:08	WH-BG03@3'	1.7	No Staining	No odor	Wellhead Background	
18	05/12/2025	12:10	WH-BG03@6'	2.8	No Staining	No odor	Wellhead Background	

1 - P1



Facing South

4 - P1



Facing North

6 - P1




Facing East

8 - P1



Facing West

13 - P1

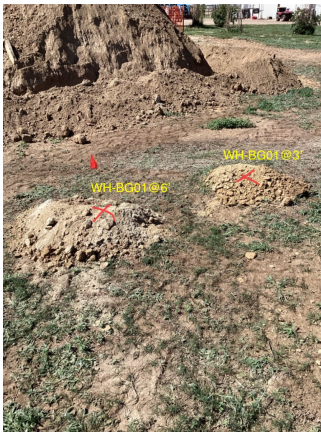

Facing Southwest

13 - P2



WH-BG01

15 - P1



Facing Southwest

15 - P2



WH-BG02

17 - P1



Facing South

17 - P2



WH-BG03

Was impacted soil identified? No

Total number of soil samples field screened: 18

Total number of soil samples collected: 18

Highest PID reading: 3.1

Total number of soil samples submitted for analysis: 10

Was groundwater encountered during the investigation No

Measured Depth to Groundwater:

Was remedial groundwater removal conducted?

**Date groundwater
was encountered:**

**Commencement date
of removal:**

Sheen on groundwater?

Free product observed?

**Volume of
groundwater
removed prior to
sampling:**

**Volume of
groundwater
removed post
sampling:**

**Total volume of
groundwater
removed:**

**Total volume of
groundwater
samples collected:**

**Total volume of
groundwater
samples submitted
to lab for analysis:**

Signature

A handwritten signature in black ink, appearing to be "P. J. R.", written in a cursive style.
