



FINAL APPROVED PTA  
30 APR 26

STRACHAN EXPLORATION, INC  
STAVELY #1  
API 05-061-06459  
SPUD 7/10/85  
STR SENW 26-185-51W  
COUNTY KIOWA  
LOCID 324846  
FACILITYID 213098  
LAT/LNG 38.463788/-103.092345  
FED LEASE  
MORROW 5365-86' - GELLED ACID FRAC

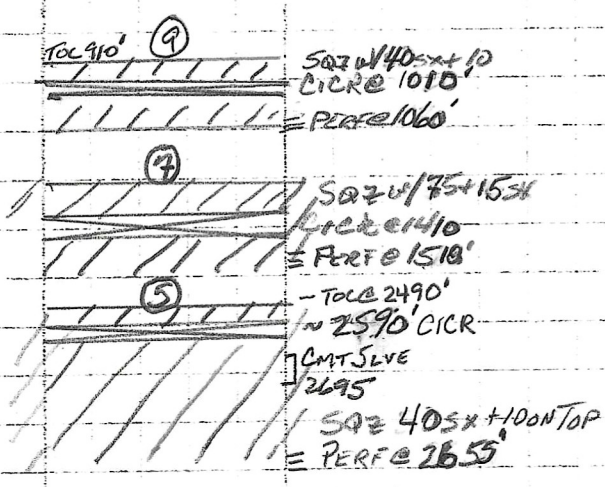

- APPROVED PROCEDURE  
RUN BH TEST REPORT #'S TO SDR.
- 1) MIRR - PULL RODS, PUMP, TEG
  - 2) PU CIRC - RIM @ 5300', DUMP 4 SX ON TBG
  - 3) PERF 2655'  
1510'  
1060'  
535'
  - 4) PU CIRC ON TBG RIM, SET @ 2590'
  - 5) MIX & PUMP 50 SX TOTAL - 40 THRU / 10 ON TOP
  - 6) PU CIRC ON TBG RIM, SET @ 1410'
  - 7) MIX & PUMP 90 SX TOTAL - 75 THRU + 15 ON TOP
  - 8) PU CIRC ON TBG RIM, SET @ 1010'
  - 9) MIX & PUMP 50 SX, 40 THRU TOP + 10 ON TOP
  - 10)  $4\frac{1}{2} \times 8\frac{5}{8} \Rightarrow (.2471) \times 935' / 1.15 \Rightarrow 94 \text{ SX}$   
 $4\frac{1}{2} \times 9" \Rightarrow (.3313) \times 101' / 1.15 \Rightarrow 29 \text{ SX}$   
 $4\frac{1}{2} \text{ CS6} \Rightarrow (.0872) \times 535' / 1.15 \Rightarrow 41 \text{ SX}$   
 mix + pump 164 SX CIRC TO SURF

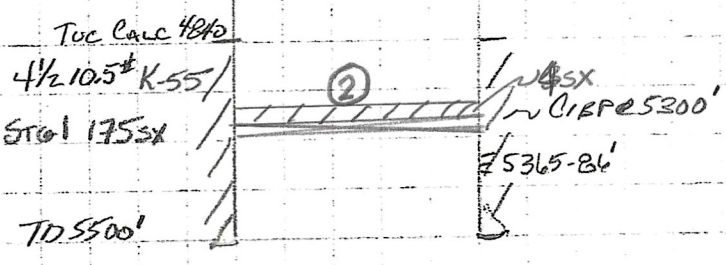

2 3/8" TBG W PRR @ 5284'  
NO CEL - NO EVIDENCE OF CMT SLVE JOB
