J-W WIRELINE COMPANY

GAMMA RAY CCL
CEMENT BOND VDL

Company	Kerr-McGee Oil & Gas Onshore LP
Well	Zeiler 13-8
Field	Wattenberg
County	Weld
State	Colo

Company Kerr-McGee Oil & Gas Onshore LP
Well Zeiler 13-8
Field Wattenberg
County Weld State Colo

Location: API #: 05-123-26507-0000
SURF: 2607' FSL X 1504' FWL NESW
BHL: 657' FSL X 637' FWL SWSW
SEC 8 TWP 5N RGE 67W

Other Services

Permanent Datum GL Elevation 4920
Log Measured From KB
Drilling Measured From KB

Elevation
K.B. 4932
D.F. 4931
G.L. 4920

Date	OCT-9-2008	
Run Number	ONE	Sussex
Depth Driller	8261	
Depth Logger	8228	
Bottom Logged Interval	8227	5000
Top Log Interval	5000	850
Open Hole Size		
Type Fluid	WATER	
Density / Viscosity		
Max. Recorded Temp.	252	
Estimated Cement Top	950	
Time Well Ready		
Time Logger on Bottom		
Equipment Number	2829	
Location	STERLING	
Recorded By	Kyle Girdler	
Witnessed By	Lewis Camp	

Borehole Record				Tubing Record			
Run Number	Bit	From	To	Size	Weight	From	To

Casing Record	Size	Wgt/Ft	Top	Bottom
Surface String				
Prot. String				
Production String				
Liner				

<<< Fold Here >>>

All interpretations are opinions based on inferences from electrical or other measurements and we cannot and do not guarantee the accuracy or correctness of any interpretation, and we shall not, except in the case of gross or willful negligence on our part, be liable or responsible for any loss, costs, damages, or expenses incurred or sustained by anyone resulting from any interpretation made by any of our officers, agents or employees. These interpretations are also subject to our general terms and conditions set out in our current Price Schedule.

Comments

CORRECTED DOWN 17' TO SCHLUMBERGER LOG DATED 17-JUN-2008

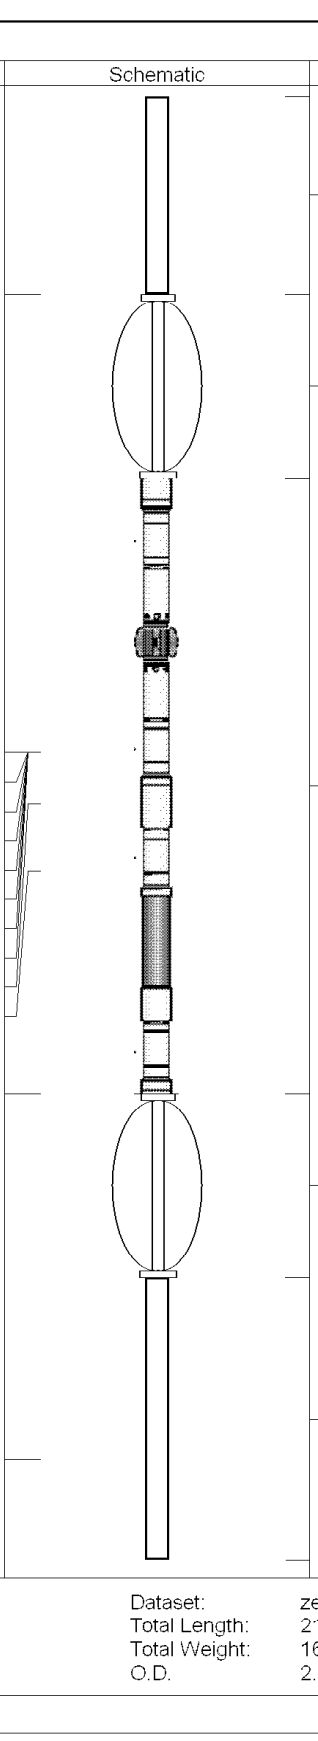

Sensor	Offset (ft)	Description	Len (ft)	OD (in)	Wt (lb)
		CCL-S_101 (101)	2.92	1.69	11.00
CCL	18.71				
		CENT-TEKCO (101)	2.73	2.75	10.00
WVFS1	11.94	SCBL-TEKCO-CT (101) TEKCO 2.75 RIB - CT	9.08	2.75	108.00
WVFS2	11.94				
WVFS3	11.94				
WVFS4	11.94				
WVFS5	11.94				
WVFS6	11.94				
WVFS7	11.94				
WVFS8	11.94				
WVF3FT	11.19				
WVF5FT	10.19				
WVFCAL	6.90				
		CENT-TEKCO (102)	2.73	2.75	10.00
		GR-S_101 (101)	4.17	1.69	25.00
GR	1.50				

Dataset: zeilier 13-8 log.db: field/well/run1/pass6
Total Length: 21.63 ft
Total Weight: 164.00 lb
O.D. 2.75 in

Database File: zeilier 13-8 log.db
Dataset Pathname: pass6
Presentation Format: scbl_dr
Dataset Creation: Thu Oct 09 01:56:39 2008 by Log Std Casedhole 07122
Charted by: Depth in Feet scaled 1:240

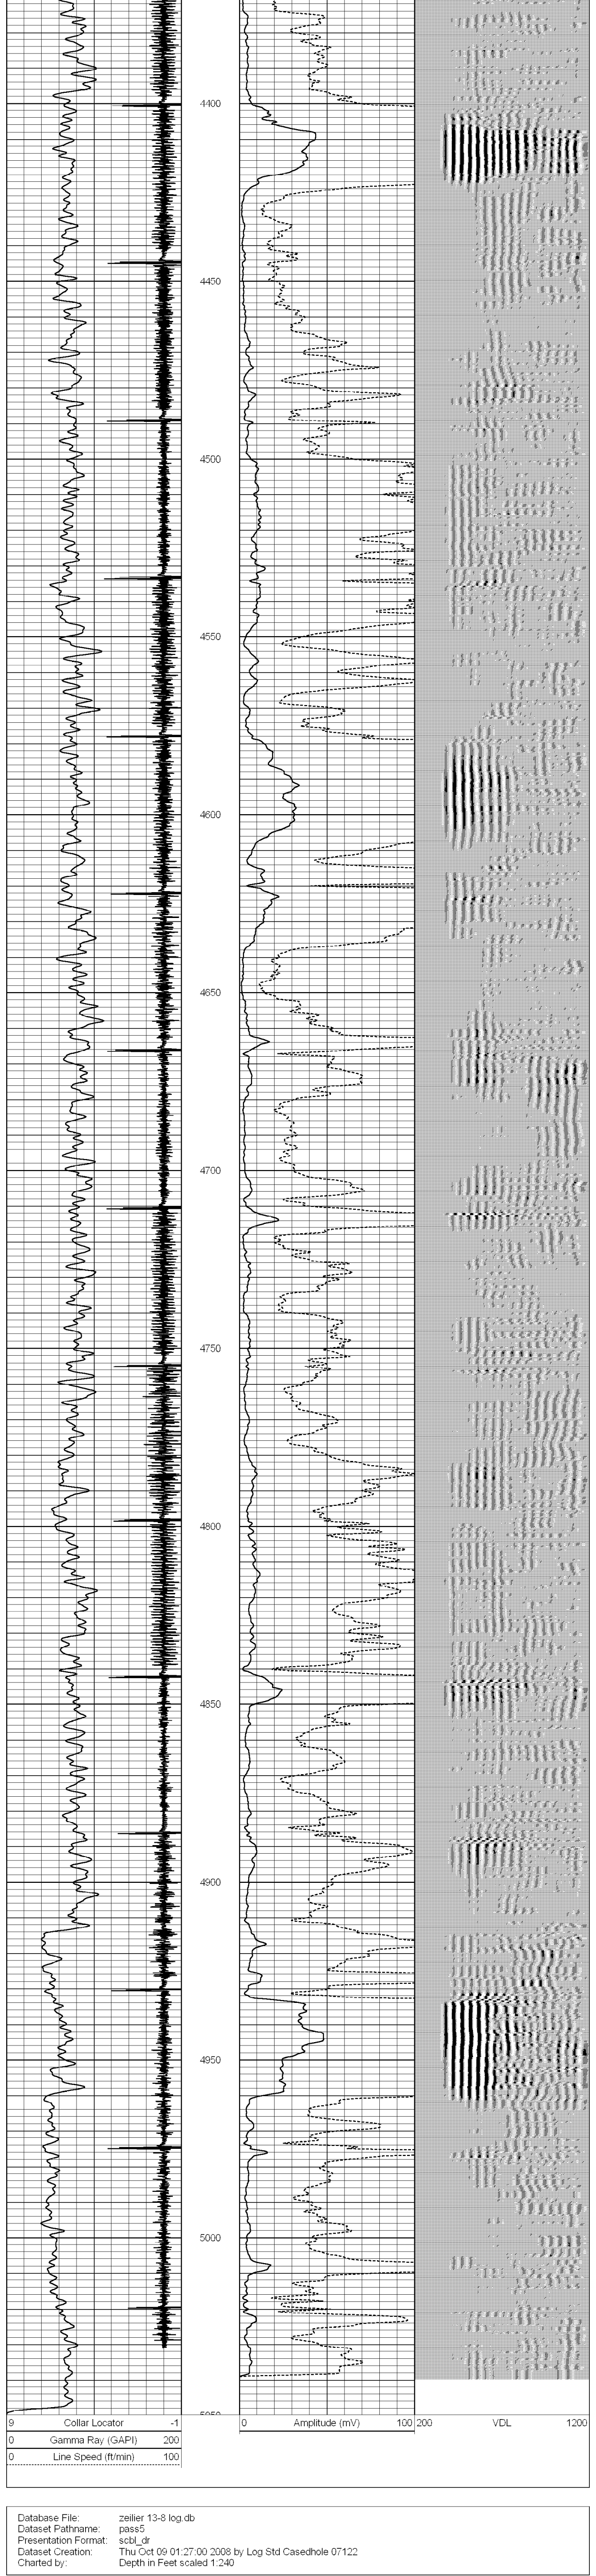

Database File: zeilier 13-8 log.db
Dataset Pathname: pass5
Presentation Format: scbl_dr
Dataset Creation: Thu Oct 09 01:27:00 2008 by Log Std Casedhole 07122
Charted by: Depth in Feet scaled 1:240

Database File: zeilier 13-8 log.db
Dataset Pathname: pass4
Presentation Format: scbl_dr
Dataset Creation: Thu Oct 09 01:21:12 2008 by Log Std Casedhole 07122
Charted by: Depth in Feet scaled 1:240

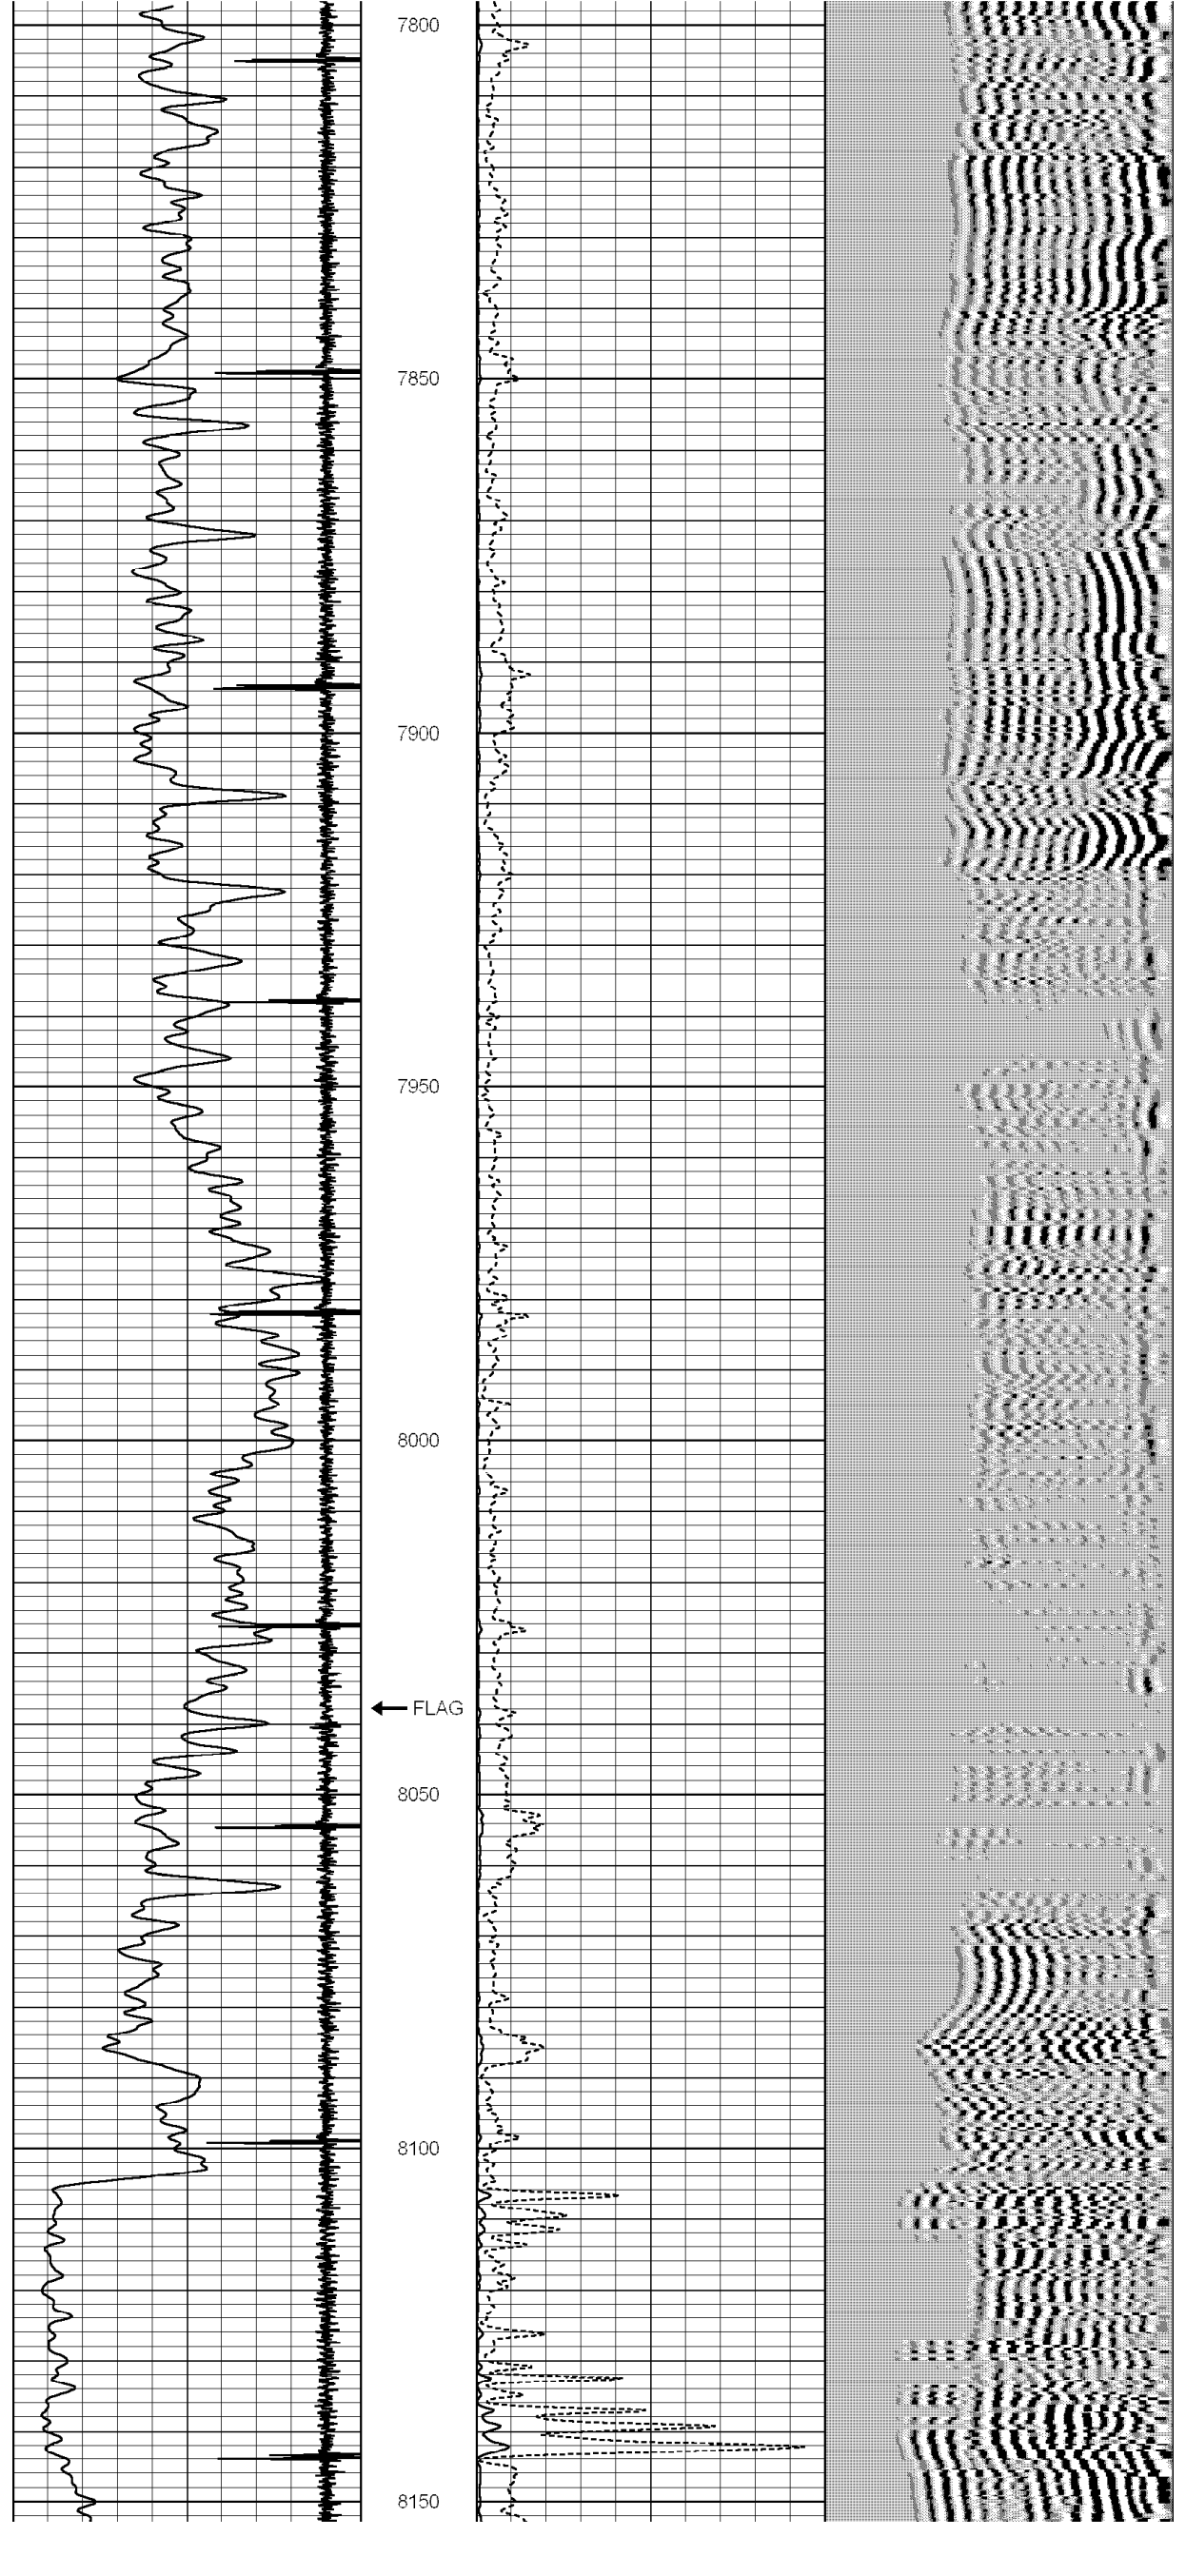

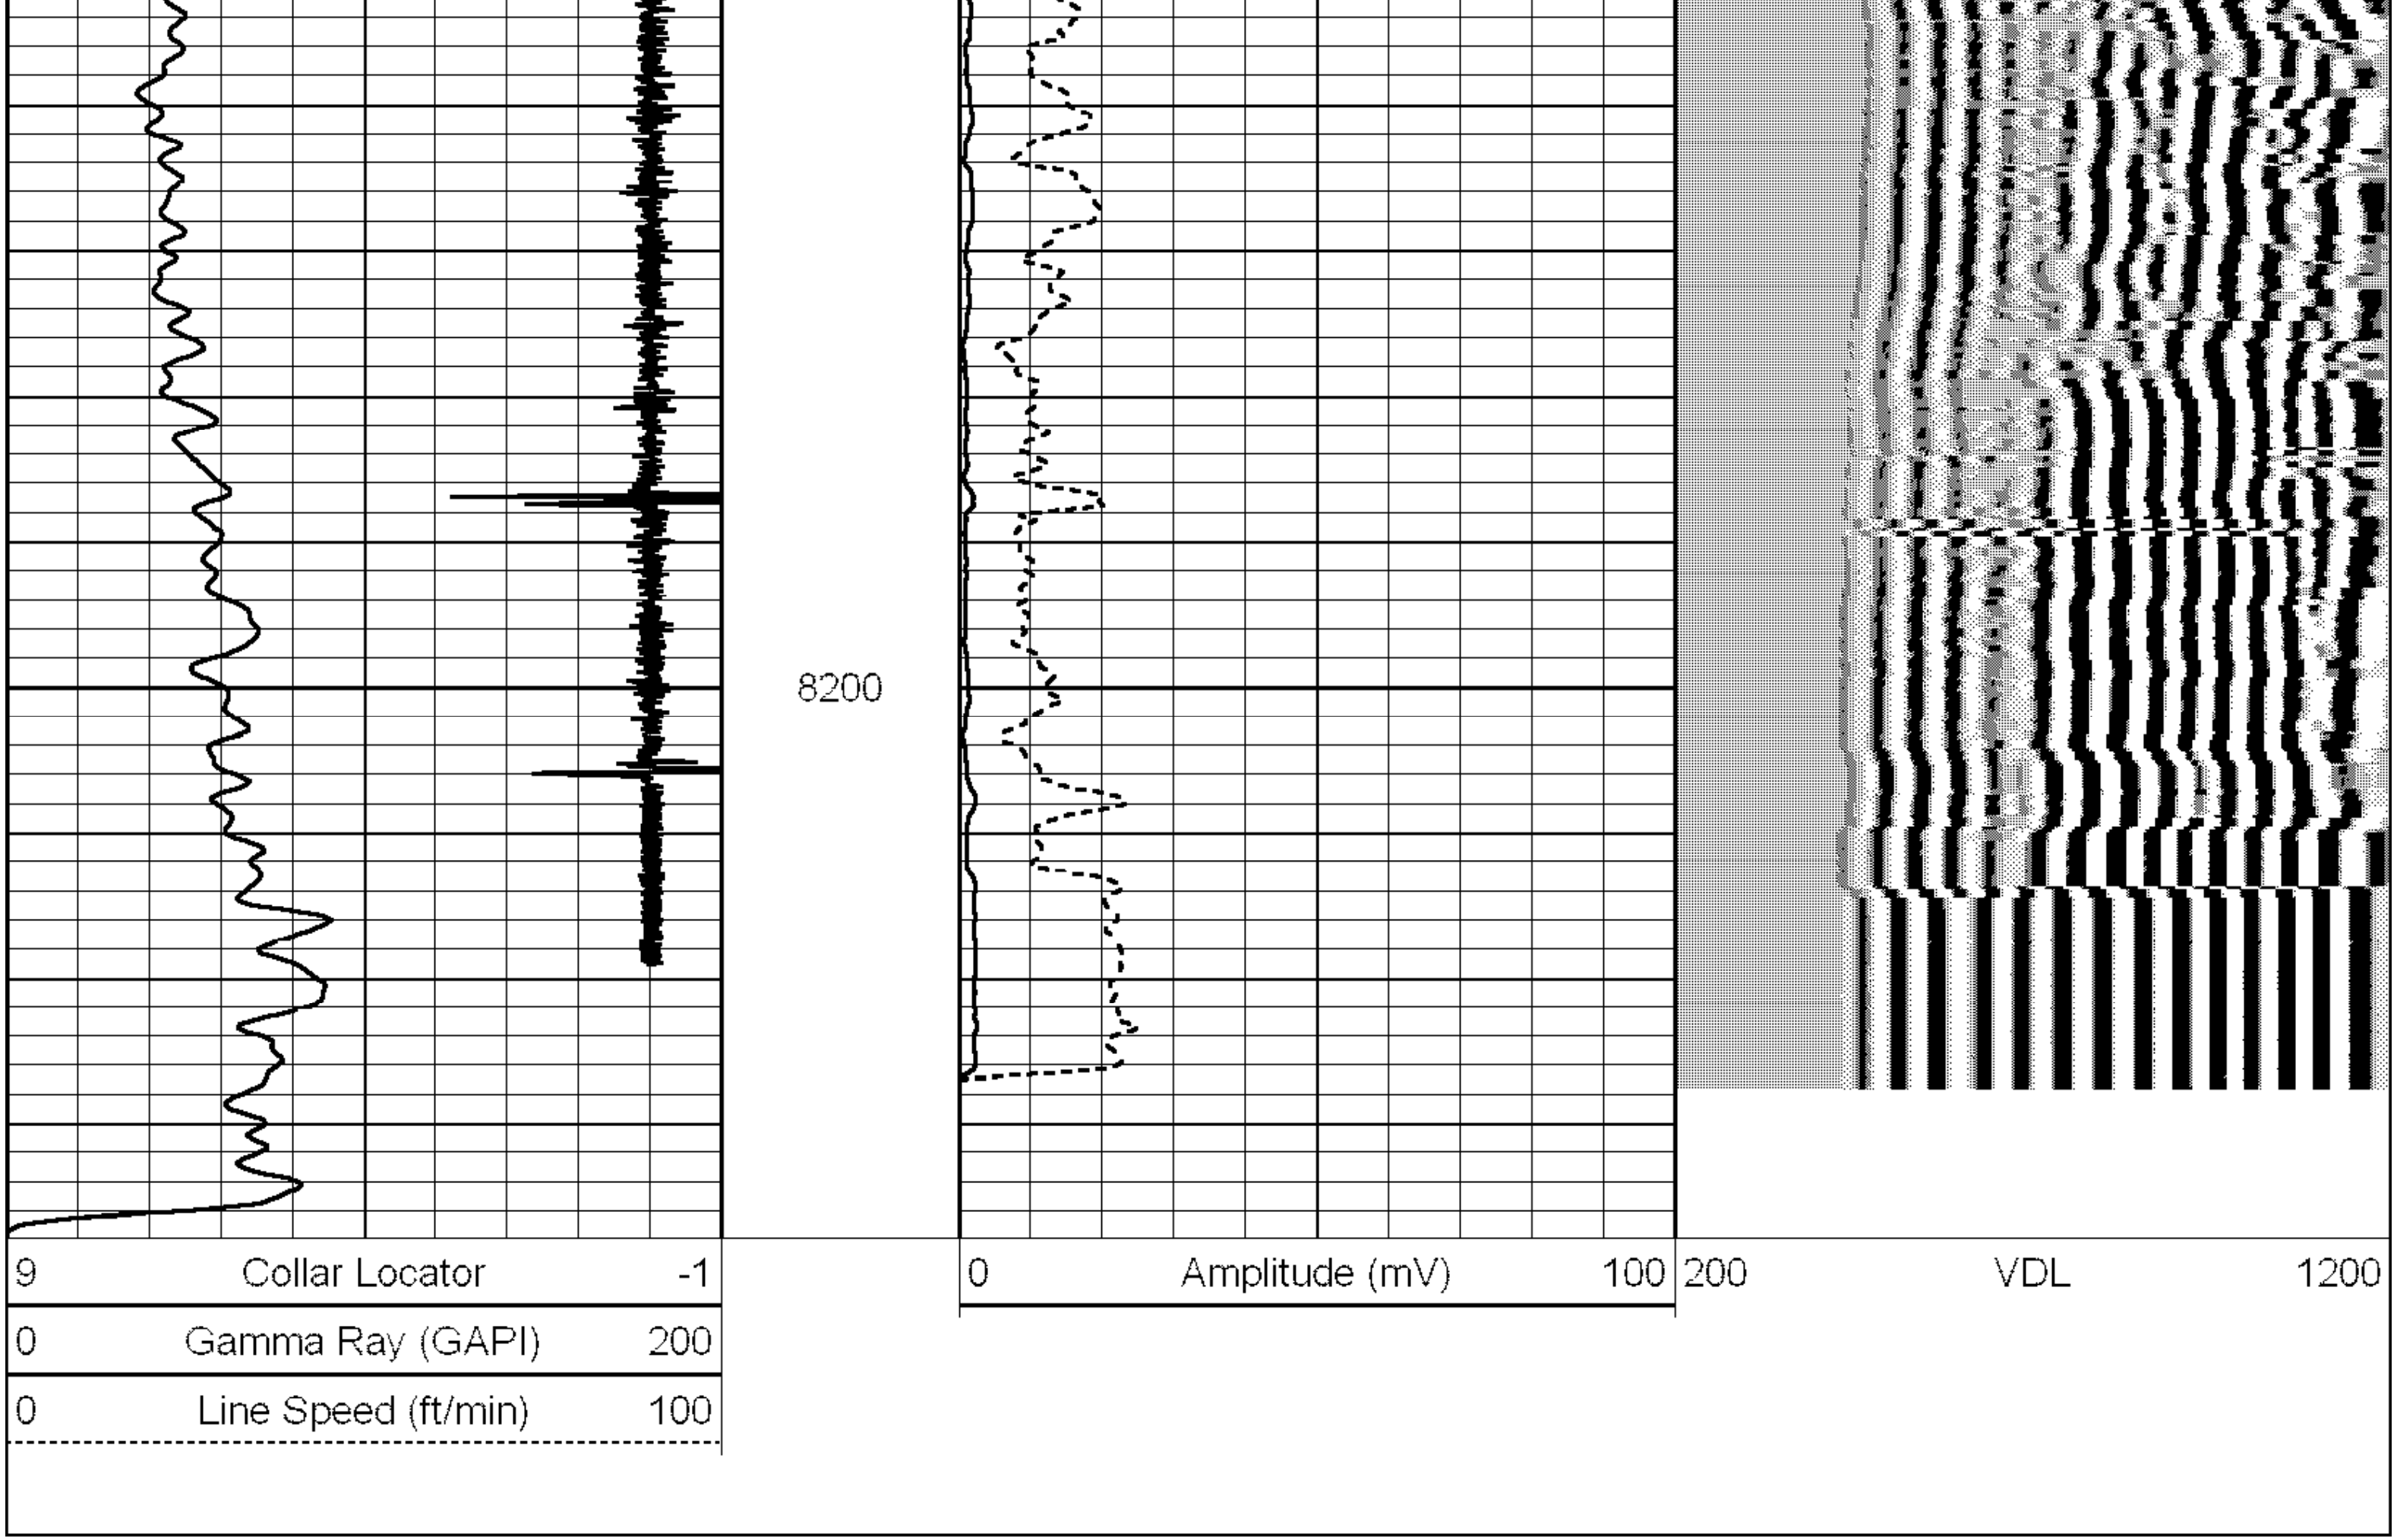
8200
9 Collar Locator -1
0 Gamma Ray (GAPI) 200
0 Line Speed (ft/min) 100
0 Amplitude (mV) 100
200 VDL 1200
