Operator: Chevron Australia Pty Ltd
Well: Gorgon-2
Basin: Carnarvon
Permit: WA-37-R
Rig: Transocean Legend
Elevation: RT 25.0 m above MSL
Water Depth: 200.0 m
Spud Date: 14 Jan 2010
Completion Date: 28 Feb 2010
Status: Gas Appraisal
Coordinates: 20° 29' 15.42" S, 115° 24' 26.18" E
Datum: GDA94

GORGON-2 DST AND LOGGING OPERATIONS

Drill Stem Test Summary

Test	Interval (m MD)	Duration	Flow Rate	Choke	Result
DST-1	3,142 – 3,168	6 hr flow / 12 hr shut-in	18.4 MMscf/d gas, 210 bbl/d cond.	48/64"	Gas and condensate
DST-2	3,168 – 3,201	8 hr flow / 16 hr shut-in	24.1 MMscf/d gas, 265 bbl/d cond.	56/64"	Gas and condensate
DST-3	3,201 – 3,236	10 hr flow / 20 hr shut-in	31.6 MMscf/d gas, 340 bbl/d cond.	64/64"	Gas and condensate

Wireline Logging Runs

Run	Suite	Interval (m MD)	Logged
1	Triple Combo	1,180 – 3,240	28 Jan 2010
2	Dipole Sonic / Image	1,180 – 3,240	29 Jan 2010
3	VSP	1,180 – 3,240	30 Jan 2010
4	Formation Pressure / Sampling	3,142 – 3,236	31 Jan 2010

Completion Schematic



Prepared by: Chevron Australia Pty Ltd
Reviewed by: Chevron Australia Pty Ltd
Approved by: Chevron Australia Pty Ltd
Date: 28 Feb 2010

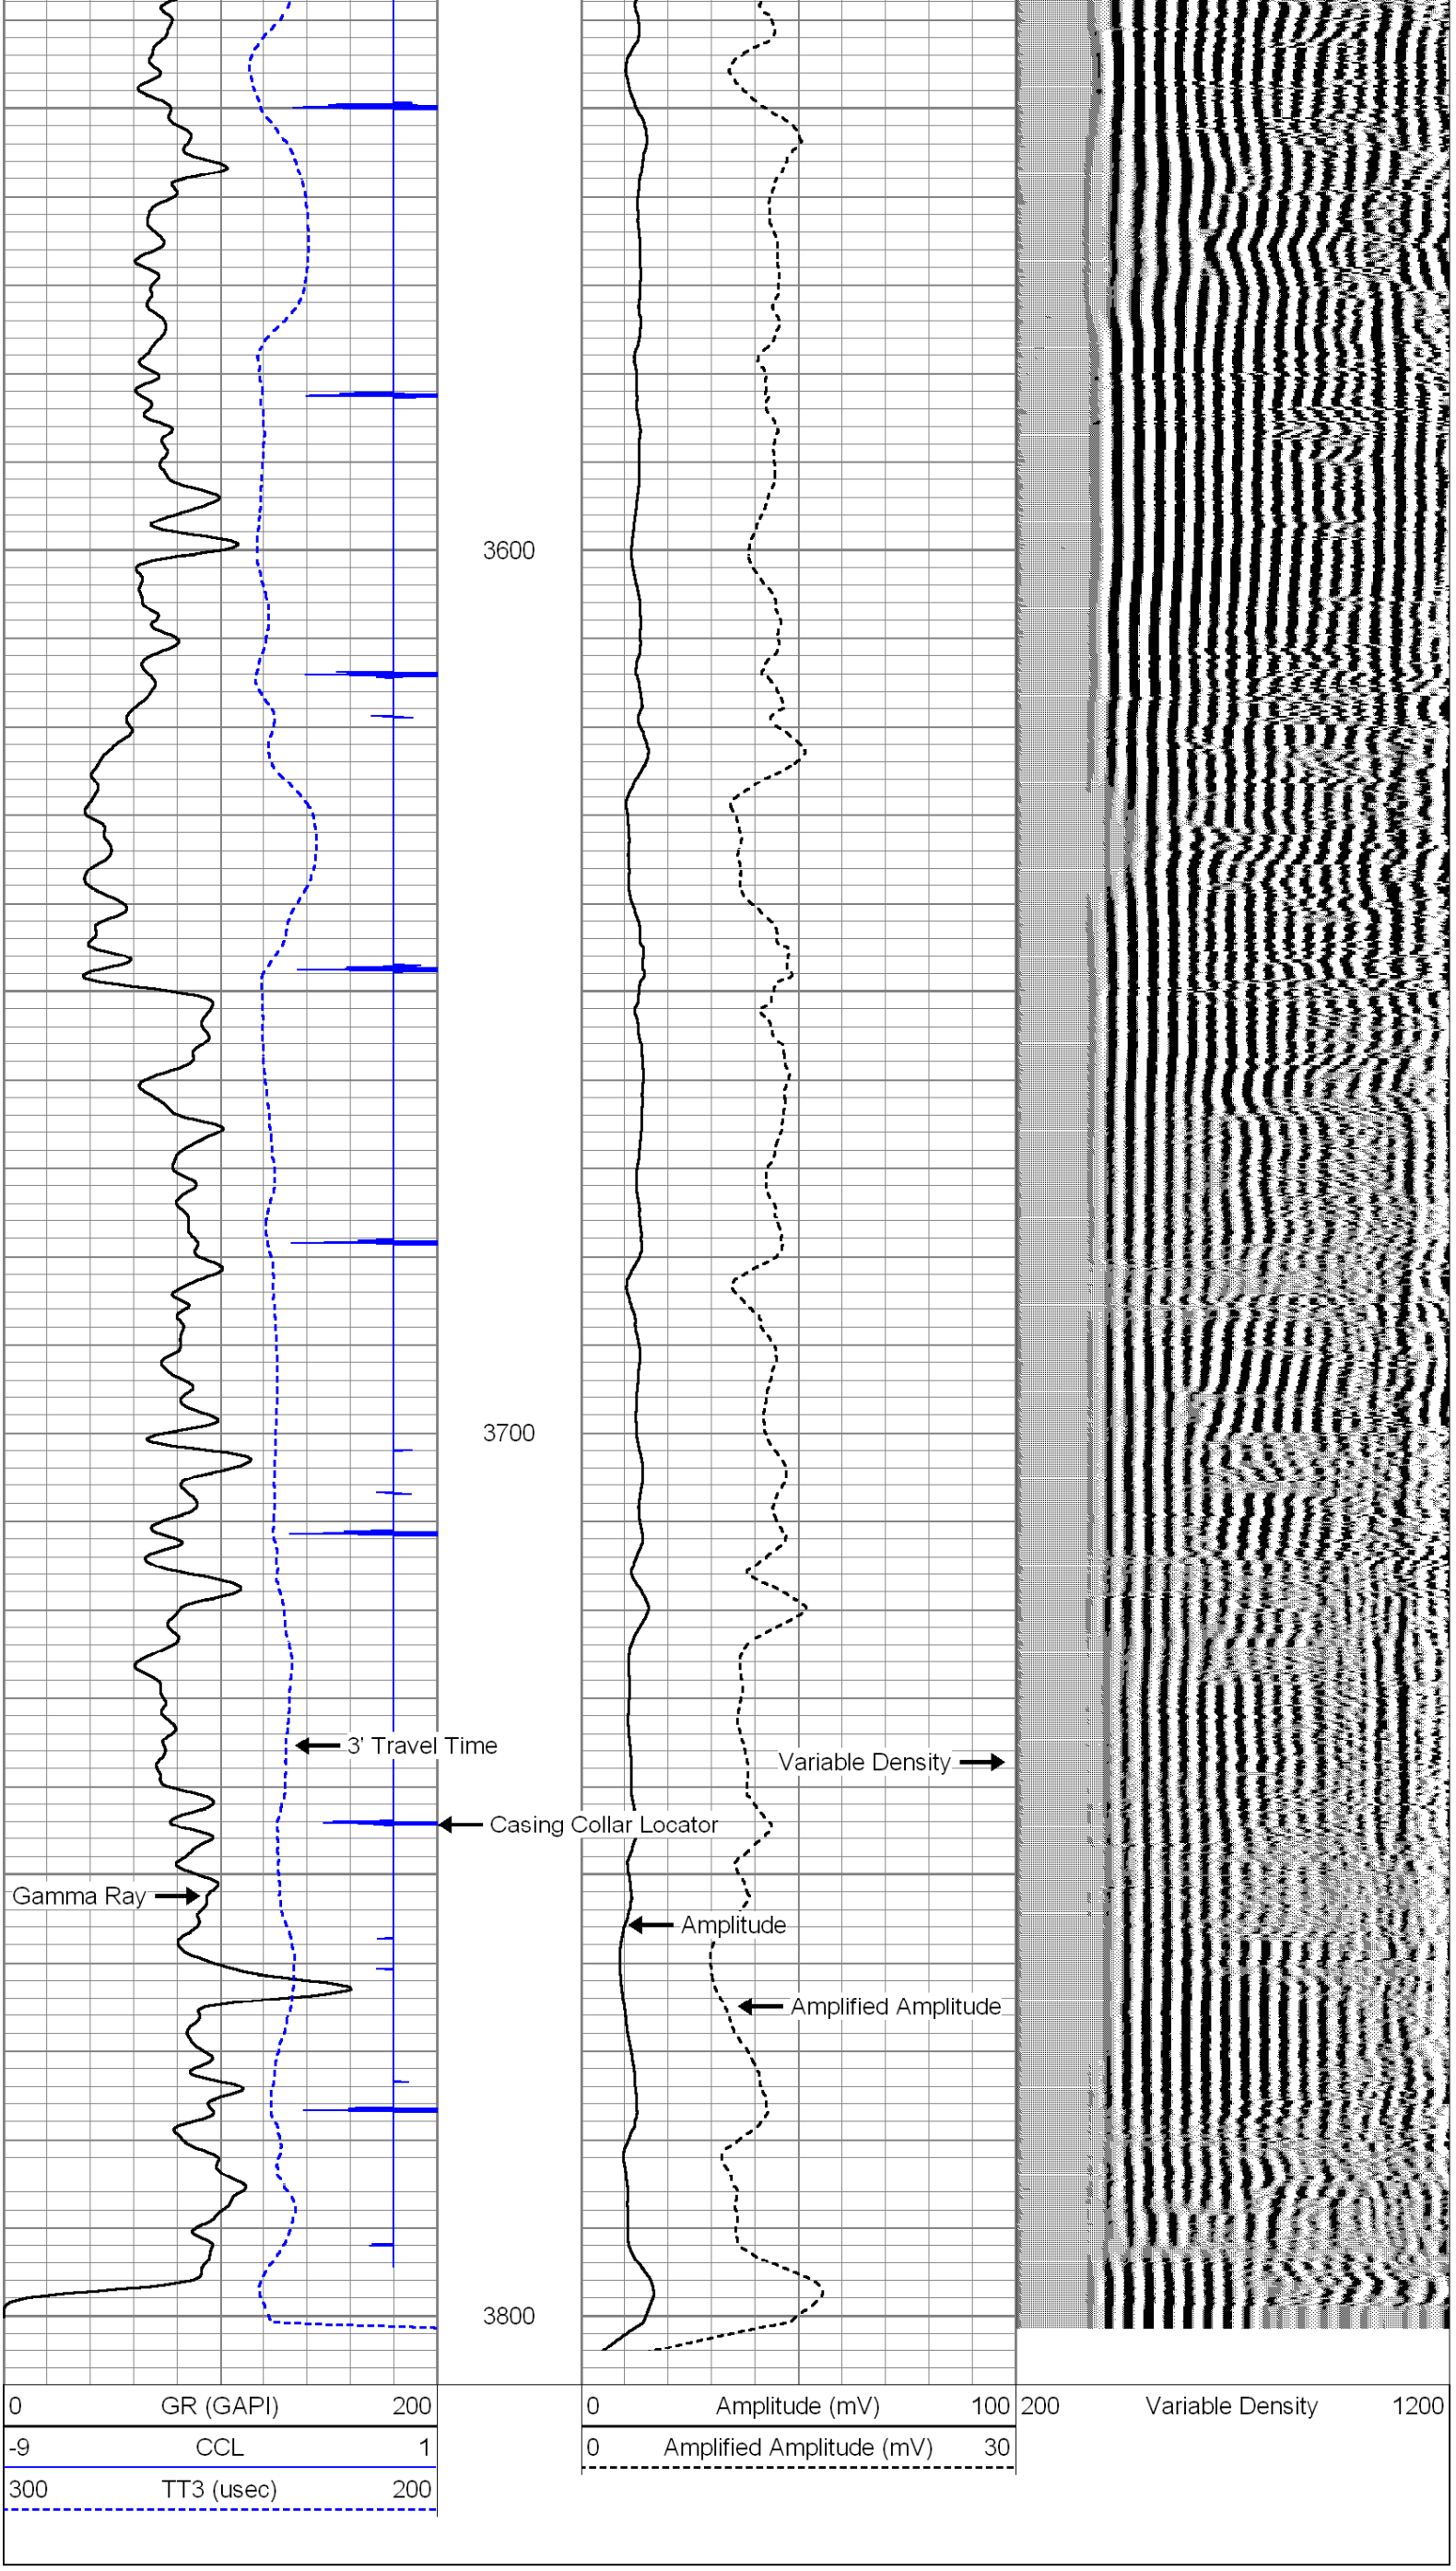
3600
3700
3800
3' Travel Time
Casing Collar Locator
Gamma Ray
Amplitude
Amplified Amplitude
Variable Density
0
GR (GAPI)
200
-9
CCL
1
300
TT3 (usec)
200
0
Amplitude (mV)
100
0
Amplified Amplitude (mV)
30
200
Variable Density
1200
