6 3/4 in. & 4 3/4 in. WeatherfordLWD™ Spectral Gamma Ray & Resistivity 1 in. & 5 in. MEASURED DEPTH RECORDED DATA FINAL PRINT

Company: Anadarko
Well: Haymaker 4C-9HZ
Field: Wattenberg
Rig: H & P 307
County: Weld

COMPANY	**Anadarko**
WELL	**Haymaker 4C-9HZ**
FIELD	**Wattenberg**
RIG	**H & P 307**
COUNTY	**Weld** STATE **Colorado**
API #	**05-123-35661-0000**

Location

Latitude:	40.14717° N	x = 3,229,999.00 ft	Mag Decl: 8.57°
Longitude:	104.67724° W	y = 1,297,525.20 ft	Mag Dip: 66.94°

Other Services: Temperature and Directional

Permanent Datum: Mean Sea Level
Log Measured From: Drill Floor Elev: 4922.0 ft above perm. datum
Depth Reference: Drillers Tally Total Depth: 11667 ft

Depth Logged: 6630 ft to 11667 ft
Date Logged: 2-Nov-12 to 8-Nov-12
Runs: 3
Spud Date: 16-Oct-12

Elevation

K.B.	Top Drive
G.L.	4897.0 ft
D.F.	4922.0 ft
W.D.	Land

Borehole Record

Hole Size	From	To
8.750 in.	1125 ft	7658ft
6.125 in.	7658 ft	11667 ft

Casing Record

Size	Weight	From	To
9.625 in.	53.5 lb/ft	Surface	1125 ft
7.000 in.	26.0 lb/ft	Surface	7658 ft

Borehole Deviation Record

Hole Size	Min. Inc.	Max. Inc.
8.750 in.	0.25°	88.46°
6.125 in.	87.66°	91.60°

Mud Record

Type	Weight	From	To
WBM	8.40 - 8.60 ppg	1125 ft	6673 ft
WBM	8.60 - 10.25 ppg	6673 ft	7658 ft
WBM	8.60 - 10.30 ppg	7658 ft	11667 ft

All interpretations of log data are opinions based on inferences from electrical or other measurements. Weatherford International does not guarantee the accuracy or correctness of any interpretation or recommendation and we shall not be liable or responsible for any loss, cost, damages or expenses incurred or sustained by anyone resulting from any interpretation or recommendation made by any of our employees or agents.

RUN SUMMARY

M/LWD Run Number		1	2	3				
Bit Size	in.	8.750	8.750	6.125				
Bit Type		PDC	PDC	PDC				
Bit TFA	sq.in.	0.650	0.650	0.648				
Bit Start Depth	ft	1125	6673	7658				
Bit End Depth	ft	6673	7658	11667				
Top Log Interval	ft	No Logging	6630	7589				
Bottom Log Interval	ft	No Logging	7658	11667				
Begin Log Time	hrs	No Logging	9:58	18:40				
Begin Log Date	DD-MMM-YY	No Logging	2-Nov-12	6-Nov-12				
End Log Time	hrs	No Logging	2:07	10:46				
End Log Date	DD-MMM-YY	No Logging	4-Nov-12	8-Nov-12				
Drill or Wipe		Drill	Drill	Drill				
Flow Rate	gal/min	615	607	292				
Max AV / CV @ MWD	ft/min	486 / 166	480 / 404	478 / 387				
Min Inc @ Depth	deg @ ft	0.25 @ 6444	0.44 @ 6635	87.66 @ 10481				
Max Inc @ Depth	deg @ ft	20.21 @ 6952	88.46 @ 7584	91.60 @ 10861				
MUD DATA								
Depth	ft	6673	7658	11667				
Fluid Type		WBM	WBM	WBM				
Mud Weight	ppg	8.60	10.25	10.30				
Plastic Viscosity	cP	2	16	15				
Solids / Sand	%	1.7 / 0.25	7.7 / 0.25	8.7 / 0.25				
Total Chlorides	ppm	1200	1200	1300				
pH		8.5	8.9	10.1				
Oil:Water Ratio	% Vol	98.0:2.0	89.0:11.0	89.0:11.0				
Rm @ Temperature	ohm-m @ deg F	N/A	N/A	1.96 @ 66				
Rmc @ Temperature	ohm-m @ deg F	N/A	N/A	1.96 @ 63				
Rmf @ Temperature	ohm-m @ deg F	N/A	N/A	1.95 @ 67				
KCl	% Vol	0	0	0				
Client Representative		D. Barone	D. Barone	D. Barone				
WeatherfordM/LWD Engineer		R. Komrs	R. Komrs	V. Campos				

EQUIPMENT SUMMARY

M/LWD Run Number		**1**	**2**	**3**		
MWD Build Number		CP20703PDYBG-01	CP20703PDYBG-02	N/A		
HEL Serial Number		N/A	N/A	NW22040PDB4.75-M3		
MFR Serial Number		N/A	N/A	NW22041RBBK4.75-M1		
IDS Serial Number		N/A	N/A	NW22046BI4.75		
SAGR Serial Number		N/A	N/A	NW22349JB4.75		
Sensor to Bit Offsets / Acquisition Rates						
Directional	ft / sec	57.92 / RT	57.51 / RT	52.29 / RT		
Gamma Ray	ft / sec	43.71 / RT	43.67 / RT	37.73 / 5		
Resistivity	ft / sec	N/A	N/A	73.53 / 5		
Other Information						
Total BHA Length	ft	96.68	96.27	133.98		
BHA Assembly Type		Steerable	Steerable	Steerable		
Stabilizer Location	ft	N/A	N/A	34.20		
Stabilizer Location	ft	N/A	N/A	N/A		
Run Circulating Time	hr	45.65	39.64	54.37		
Run Drilling Time	hr	25.26	20.12	22.86		

MUD SUMMARY

Date and Time	Run	Bit Depth	Mud Weight	% K	Rm @ Temp	Rmf @ Temp	Rmc @ Temp	BHCT
02 Nov 12 @ 03:30	01	6673 ft	8.60 ppg	0	N/A	N/A	N/A	166 F
04 Nov 12 @ 10:15	02	7658 ft	10.25 ppg	0	N/A	N/A	N/A	176 F
08 Nov 12 @ 14:00	03	11667 ft	10.30 ppg	0	1.96 @ 66	1.95 @ 67	1.96 @ 63	231 F

M/LWD RUN REMARKS

Run Number: 1 :: REAL TIME DATA LOG

WFT Services Provided:

Real Time Logging: Gamma Ray and Temperature.

Directional Services: On demand Inclination and Azimuth.

Borehole and Environmental Correction:

Collar O.D.:	6.75 in.
Collar I.D.:	3.250 in.
K1 Factor:	3.012
KCl Concentration:	0%

Gamma Ray: Collar O.D., collar I.D. and K1 factor.

Run Number: 2 :: REAL TIME DATA LOG

WFT Services Provided:

Real Time Logging: Gamma Ray and Temperature.

Directional Services: On demand Inclination and Azimuth.

Borehole and Environmental Correction:

Collar O.D.:	6.75 in.
Collar I.D.:	3.250 in.
K1 Factor:	3.012
KCl Concentration:	0%

Gamma Ray: Collar O.D., collar I.D. and K1 factor.

Run Number: 3 :: RECORDED DATA LOG

WFT Services Provided:

Recorded and Real Time Logging: Gamma Ray, Deep, Medium and Shallow Resistivity, and Temperature.

Directional Services: On demand Inclination and Azimuth.

Borehole and Environmental Correction:

Hole Size:	6.125 in.
Mud Weight:	10.30 ppg
Borehole Temperature:	231° F
Drilling Fluid Resistivity:	1.96 ohm-m
KCl Concentration:	0%

Gamma Ray: Corrected for mud weight, hole size and KCl concentration.

Resistivities: Corrected for borehole temperature, hole size, drilling fluid resistivity and dielectric correction.

M/LWD LOG COMMENTS

Comment No. 1-1

REAL TIME DATA LOG
Start of MWD Drilling Run 01
Weatherford International provided 6 3/4 in. Directional and Temperature for Run 01.
Run 01 started formation drilling October 30, 2012 at 05:00 at 1125 MD / 1124 TVD. Weatherford International logged the 8.750 in. borehole.
The WBM at the start of drilling was 8.40 ppg.

Comment No. 1-2

End of MWD Drilling Run 01
Run 01 ended drilling formation November 2, 2012 at 03:30 at 6673 MD / 6631 TVD.
The WBM at the end of drilling was 8.60 ppg.

Comment No. 2-1

RECORDED DATA LOG
Start of MWD Drilling Run 02
Weatherford International provided 6 3/4 in. Directional, Gamma Ray and Temperature for Run 02.
Run 02 started formation drilling November 2, 2012 at 09:58 at 6673 MD / 6631 TVD. Weatherford International logged the 8.750 in. borehole.
The WBM at the start of drilling was 8.60 ppg.

Comment No. 2-2

End of MWD Drilling Run 02
Run 02 ended drilling formation November 4, 2012 at 02:07 at 7658 MD / 7236 TVD.
The WBM at the end of drilling was 10.25 ppg.

Comment No. 3-1

RECORDED DATA LOG
Start of LWD Drilling Run 03
Weatherford International provided 4 3/4 in. Directional, Resistivity, Gamma Ray, and Temperature for Run 03.
Run 03 started formation drilling November 6, 2012 at 18:40 at 7658 MD / 7236 TVD. Weatherford International logged the 6.125 in. borehole.
The WBM at the start of drilling was 8.60 ppg.

Comment No. 3-2

End of LWD Drilling Run 03
Run 03 ended drilling formation November 8, 2012 at 10:46 at 11667 MD / 7264 TVD.
The WBM at the end of drilling was 10.30 ppg.

CURVE SPECIFICATIONS

CURVE TYPE	MNEMONIC	UNITS	COMMENTS	CORRECTIONS
Rate of Penetration	ROP	fph	Rate of Penetration 3.0 ft window 0.5 ft Exponential Smoothing	None
Gamma Ray	GR	AAPI	Gamma Ray 3.0 ft window 0.5 ft Exponential Smoothing	See M/LWD Run Remarks
Deep Phase Resistivity	RPD2	ohm-m	2 MHz Deep Phase Resistivity 3.0 ft window 0.5 ft Exponential Smoothing	
Deep Attenuation Resistivity	RAD2	ohm-m	2 MHz Deep Attenuation Resistivity 3.0 ft window 0.5 ft Exponential Smoothing	
Deep Attenuation Resistivity	RAD4	ohm-m	400 kHz Deep Attenuation Resistivity 3.0 ft window 0.5 ft Exponential Smoothing	
Shallow Phase Resistivity	RPS2	ohm-m	2 MHz Shallow Phase Resistivity 3.0 ft window 0.5 ft Exponential Smoothing	
Deep Phase Conductivity	CPD2	mmho/m	2 MHz Deep Phase Conductivity 3.0 ft window 0.5 ft Exponential Smoothing	
Temperature	TEMP	F	Temperature 3.0 ft window 0.5 ft Exponential Smoothing	None

1 Inch - Measured Depth

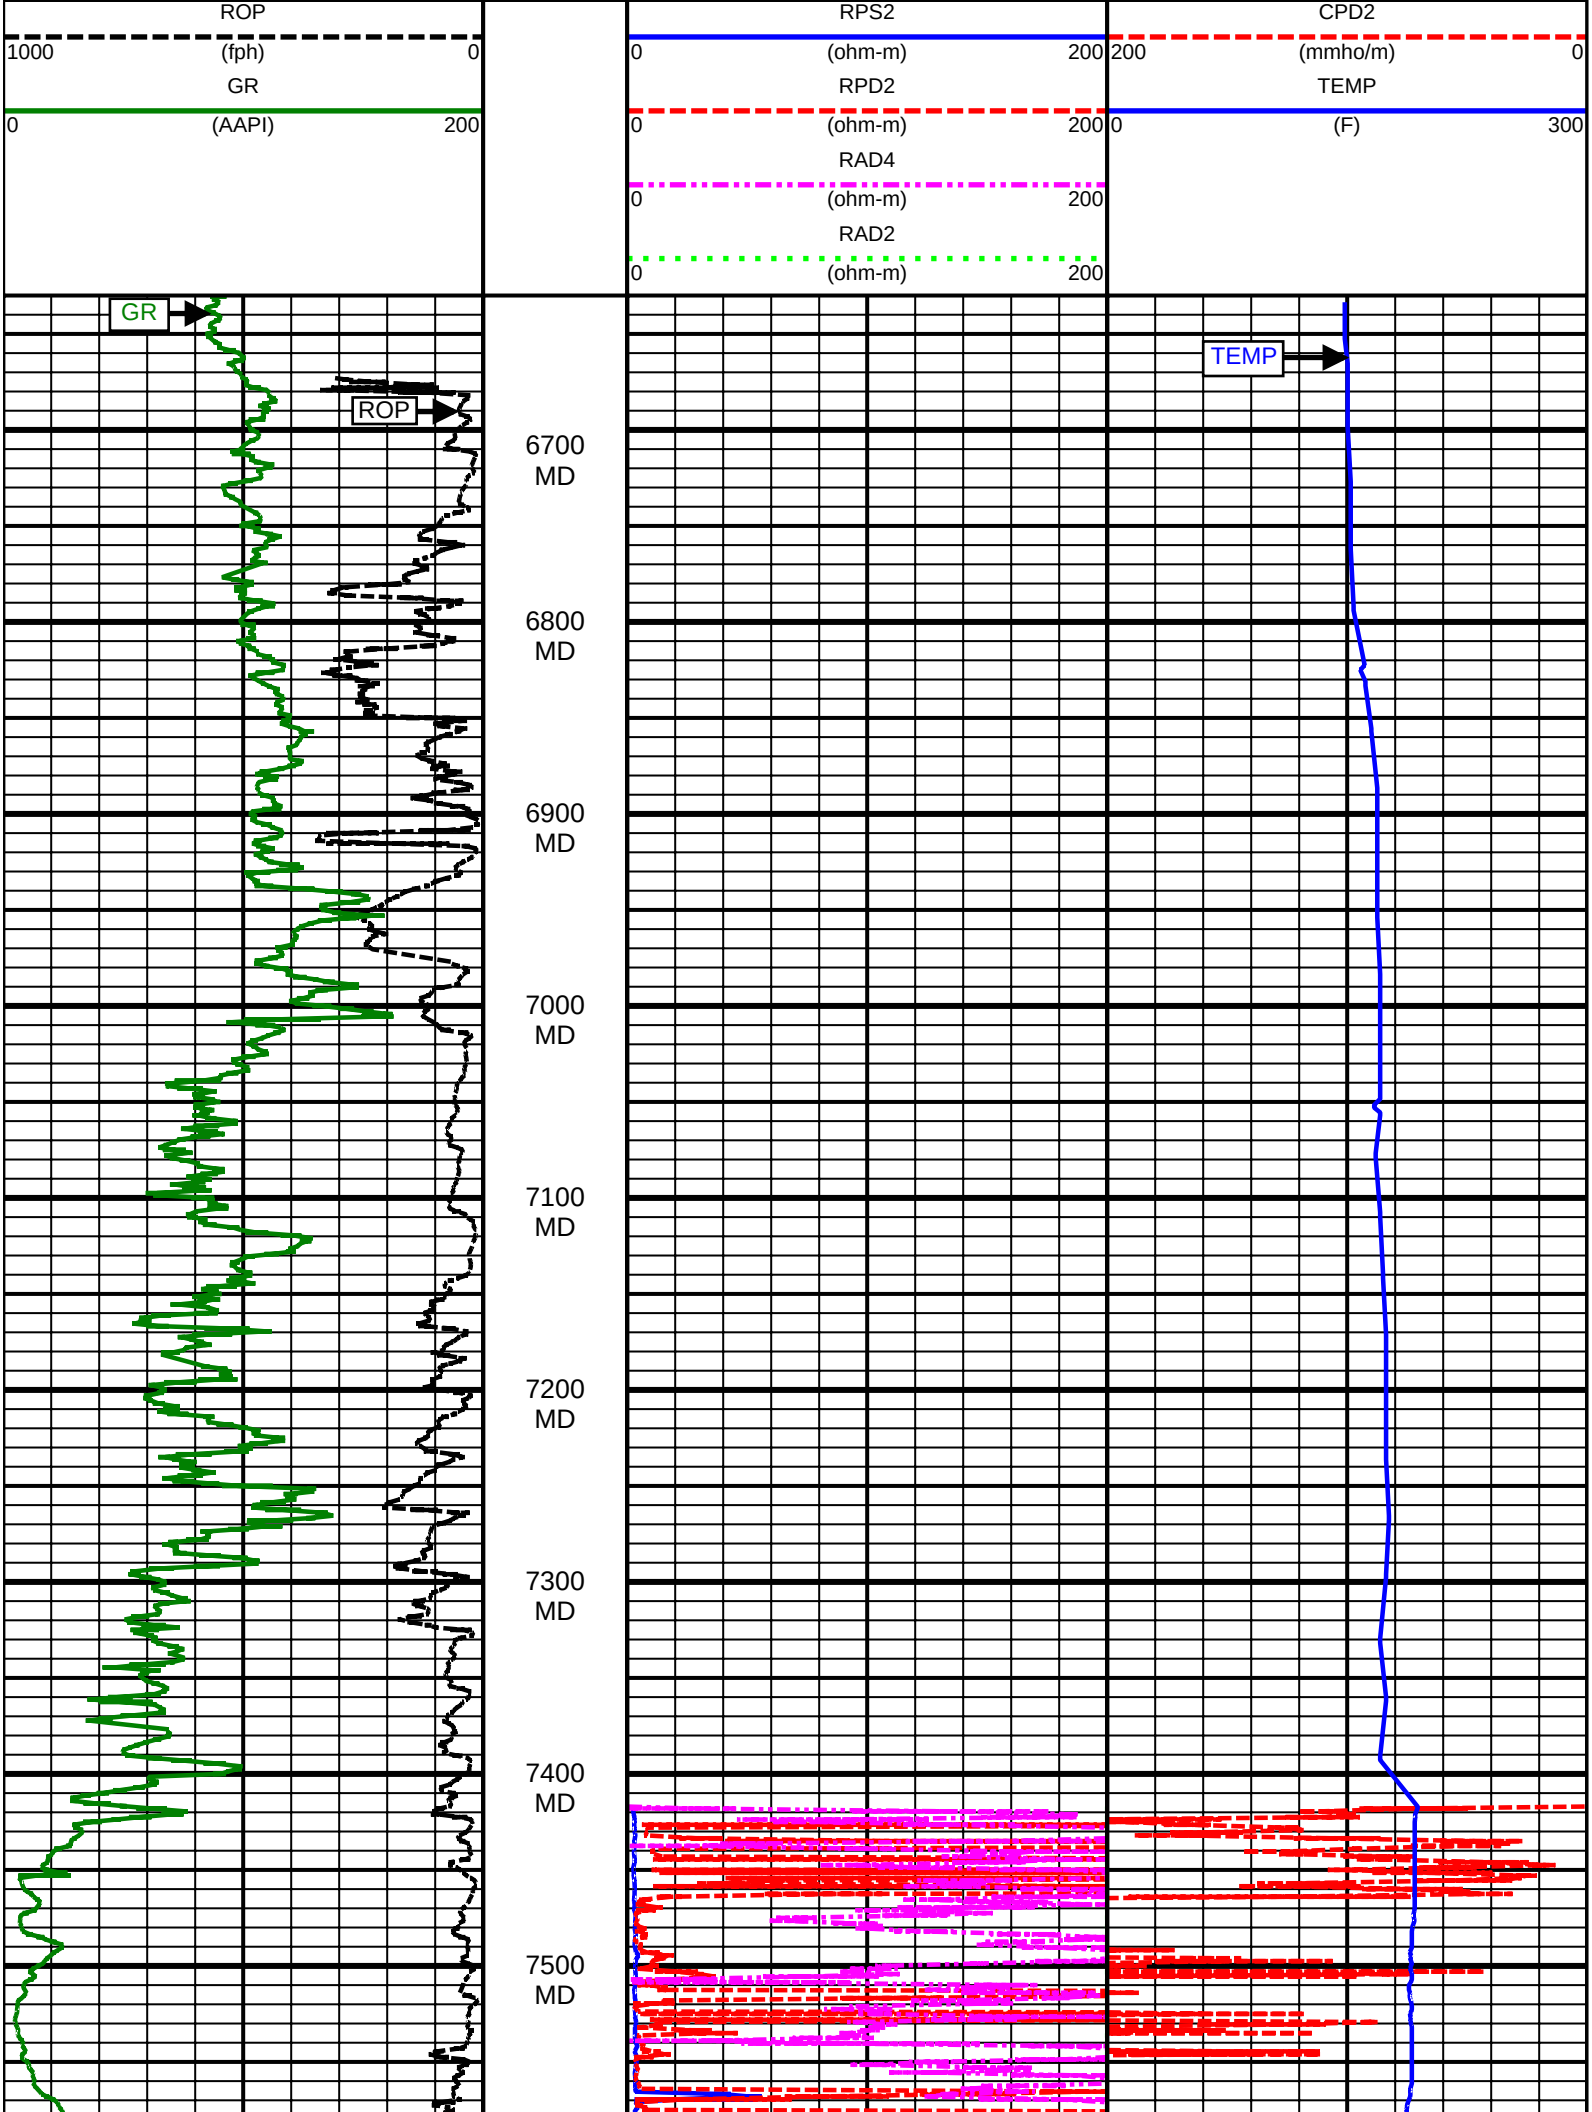
ROP
1000
(fph)
0
GR
0
(AAPI)
200
RPS2
0
(ohm-m)
200
RPD2
0
(ohm-m)
200
RAD4
0
(ohm-m)
200
RAD2
0
(ohm-m)
200
CPD2
200
(mmho/m)
0
TEMP
0
(F)
300
GR
ROP
TEMP
6700
MD
6800
MD
6900
MD
7000
MD
7100
MD
7200
MD
7300
MD
7400
MD
7500
MD

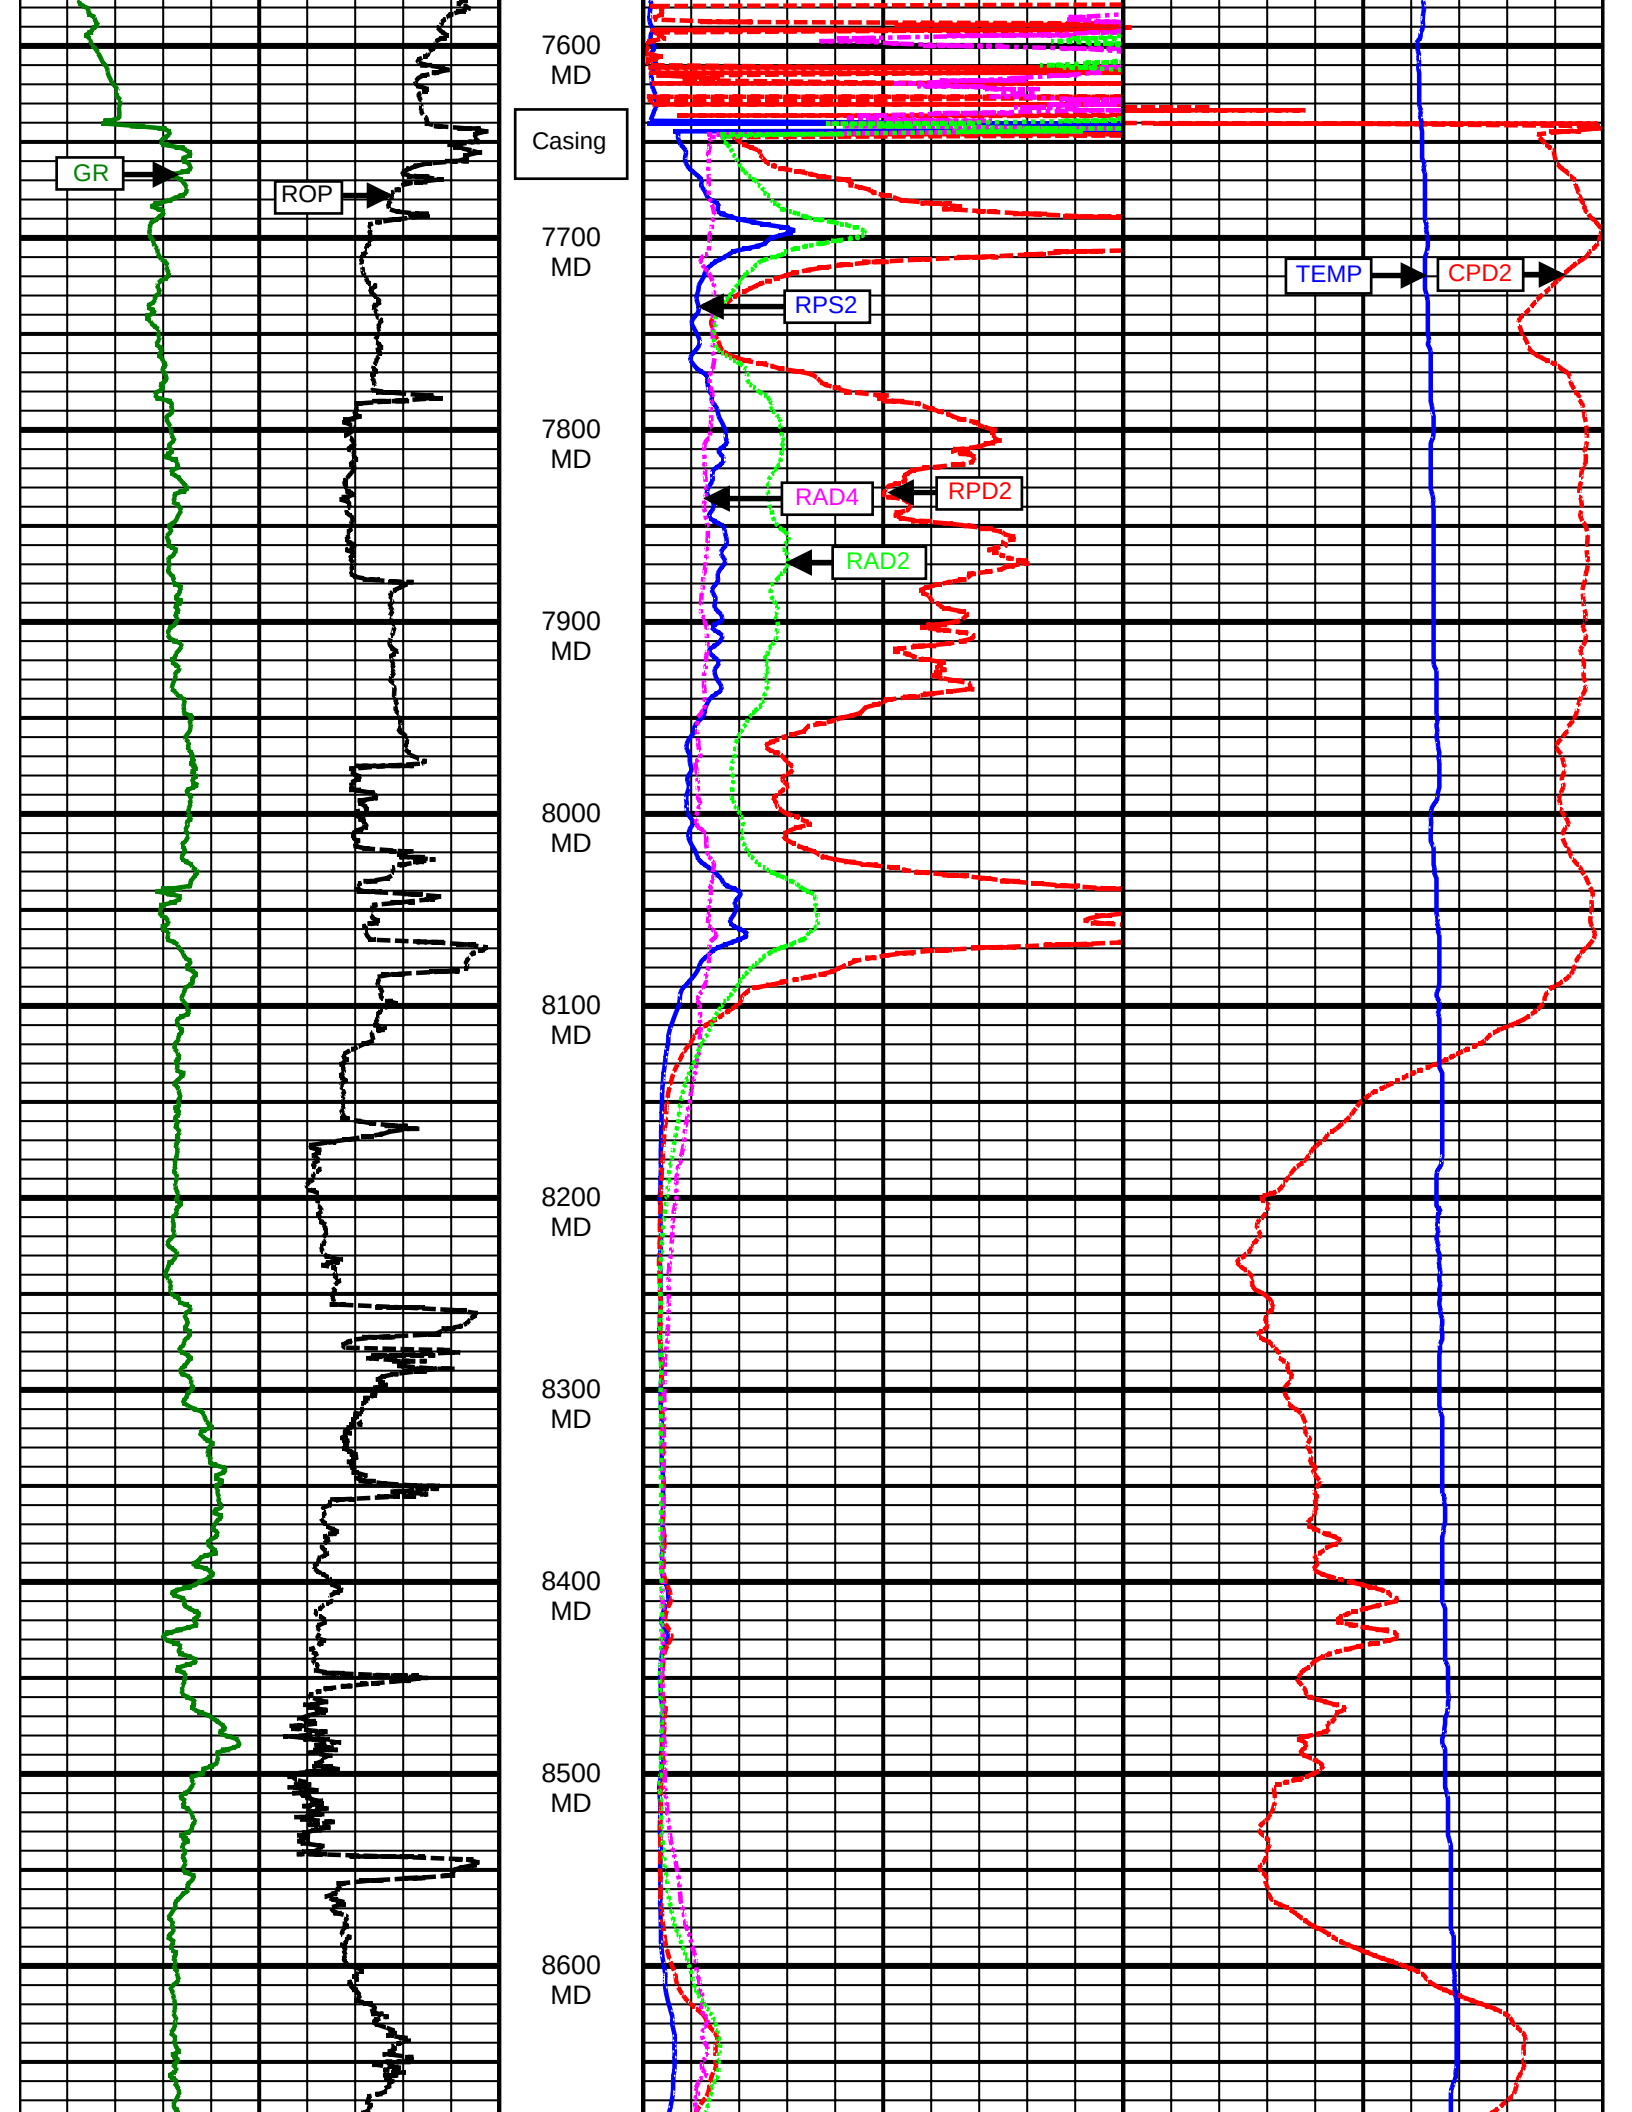
7600
MD
Casing
7700
MD
7800
MD
7900
MD
8000
MD
8100
MD
8200
MD
8300
MD
8400
MD
8500
MD
8600
MD
GR
ROP
RPS2
RAD4
RPD2
RAD2
TEMP
CPD2

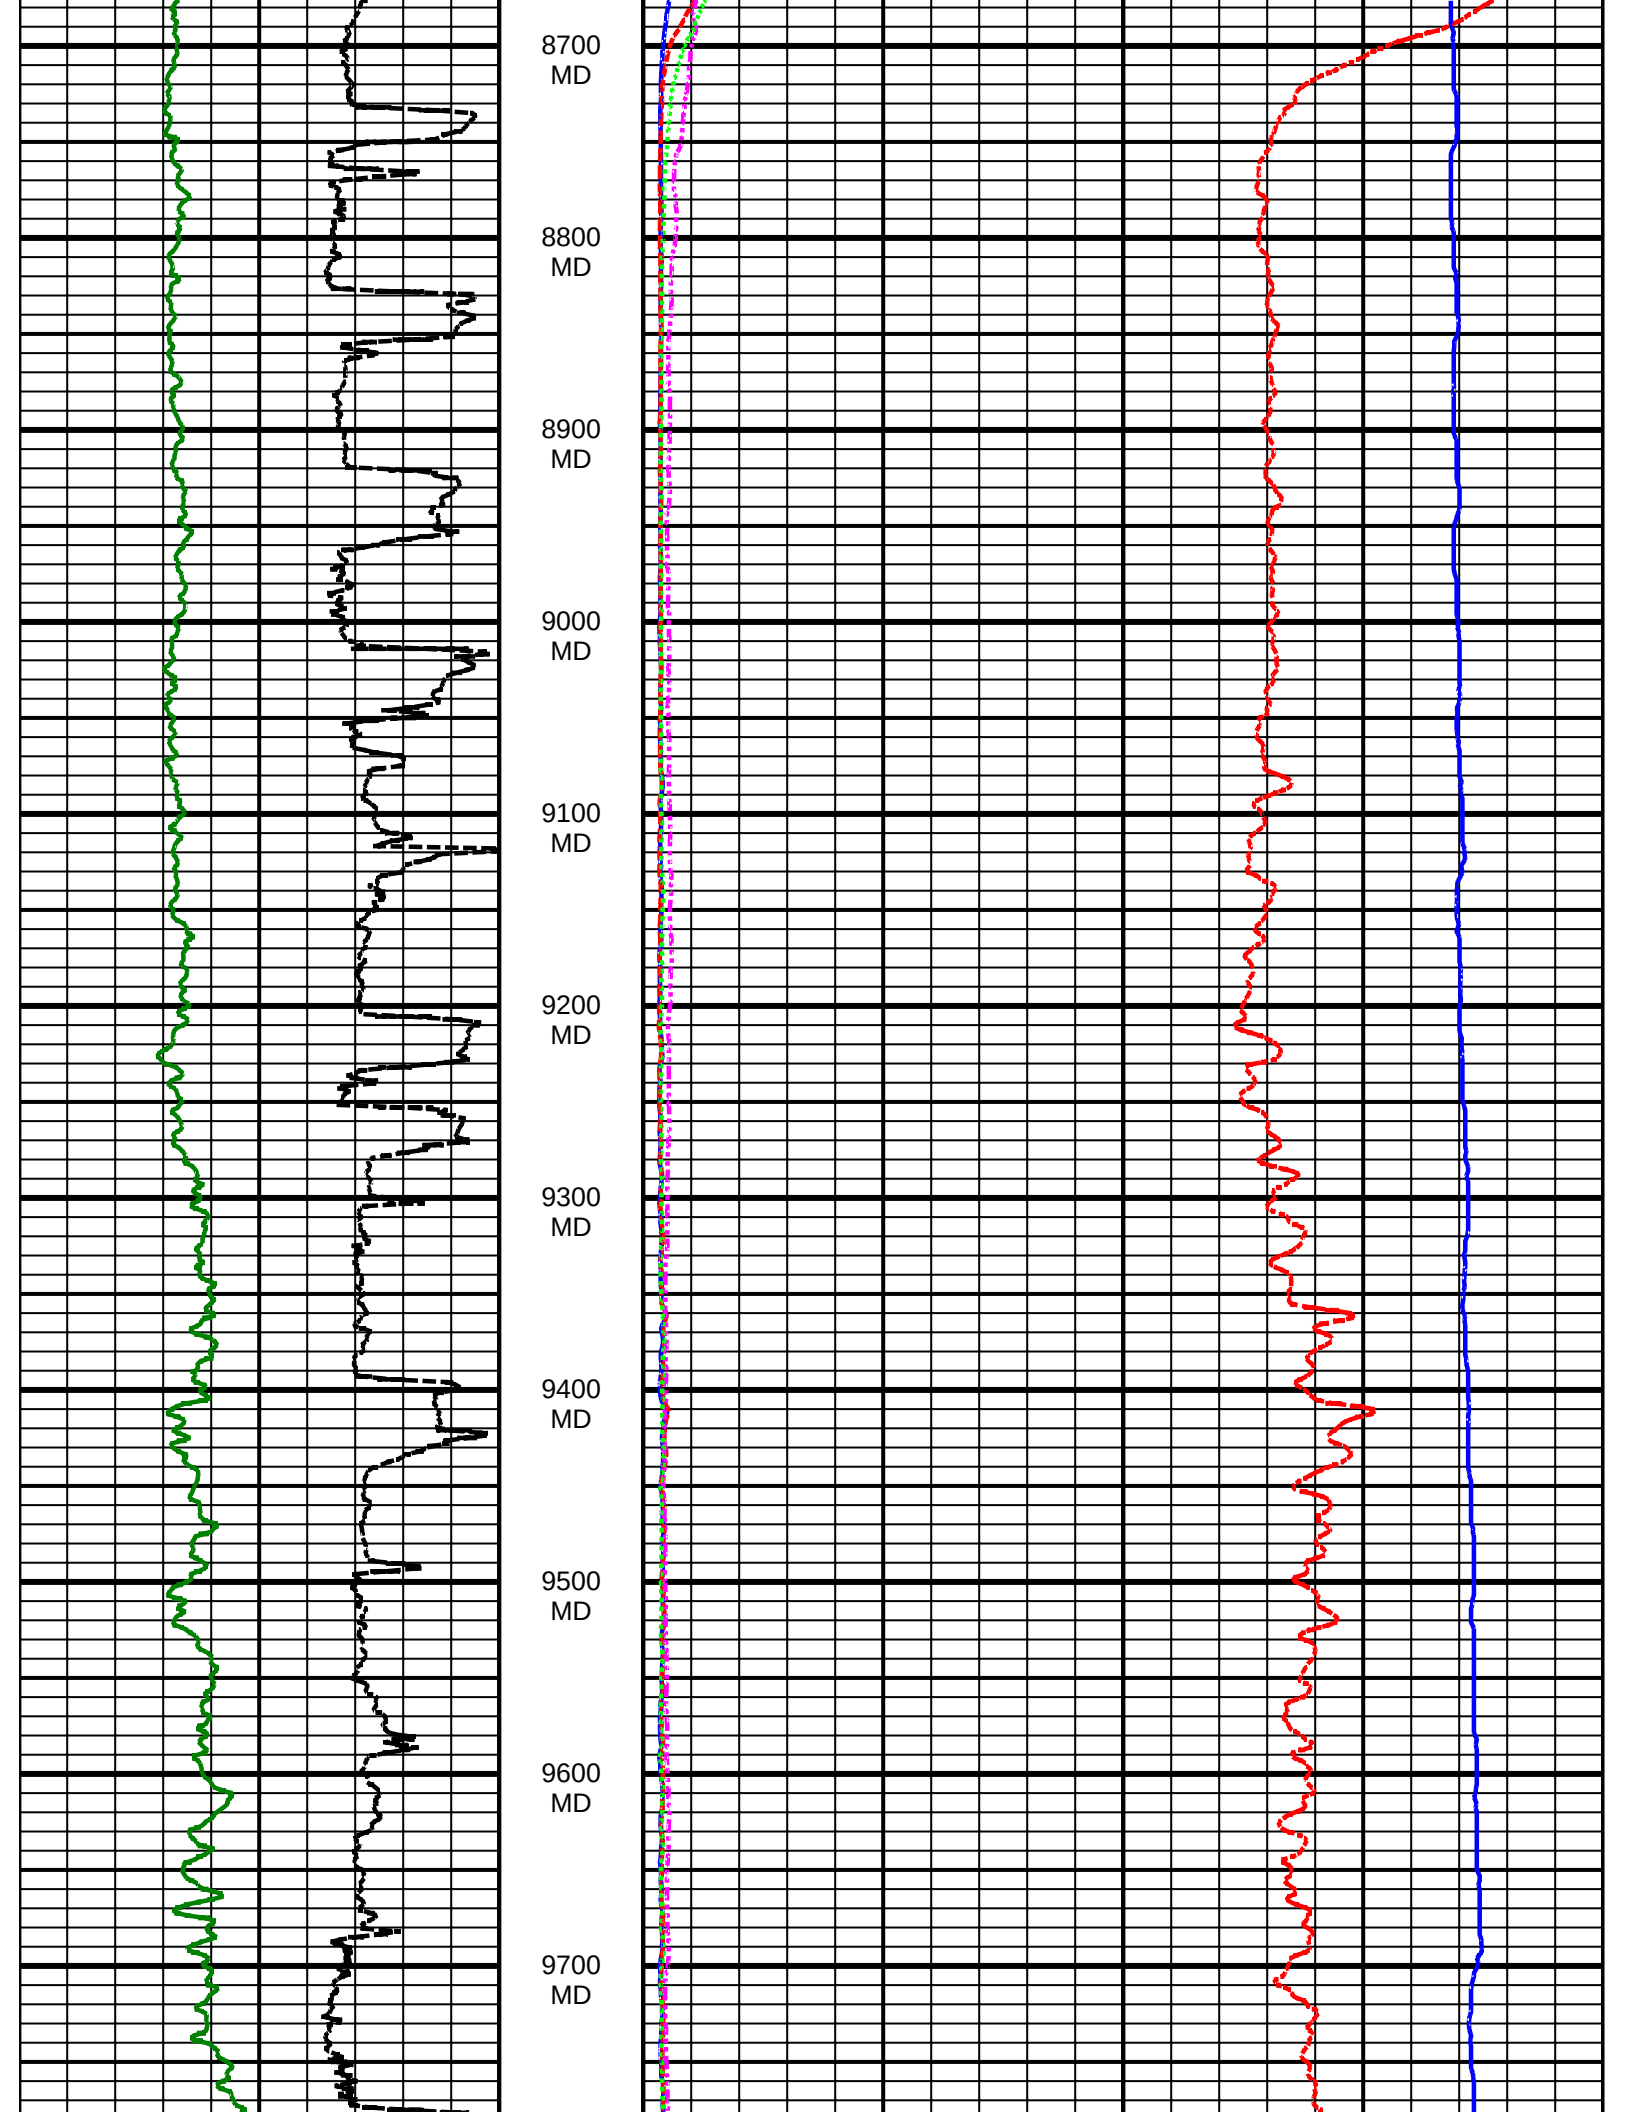
8700
MD
8800
MD
8900
MD
9000
MD
9100
MD
9200
MD
9300
MD
9400
MD
9500
MD
9600
MD
9700
MD

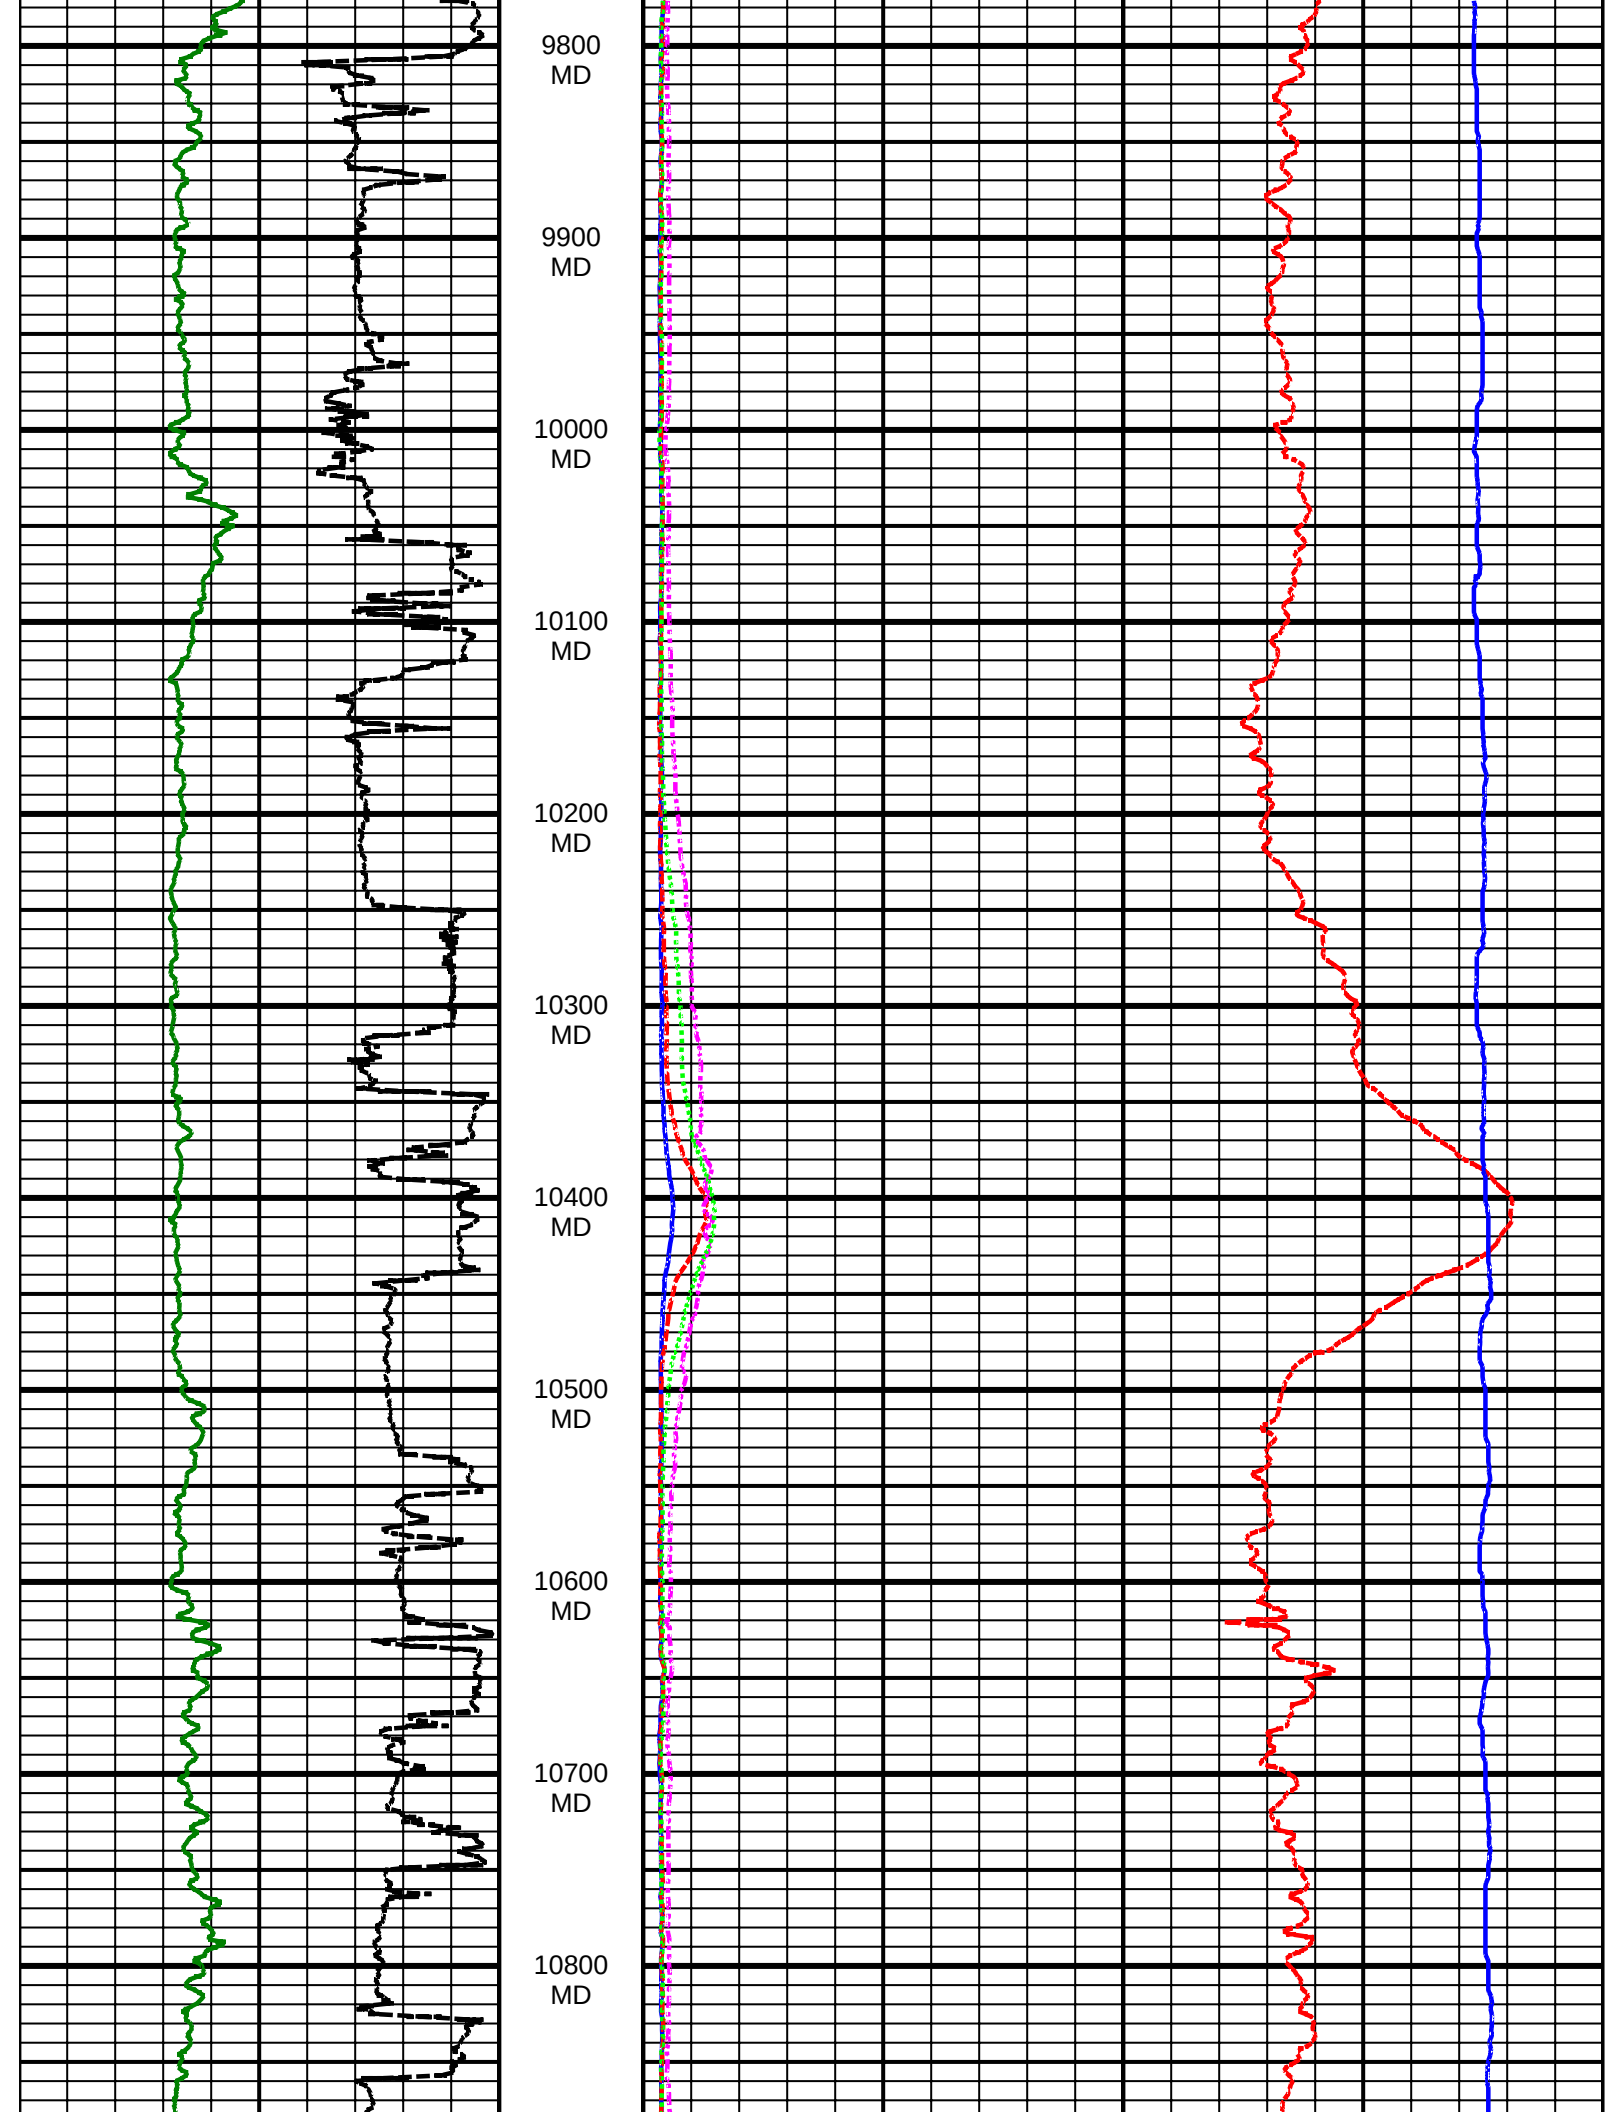
9800
MD
9900
MD
10000
MD
10100
MD
10200
MD
10300
MD
10400
MD
10500
MD
10600
MD
10700
MD
10800
MD

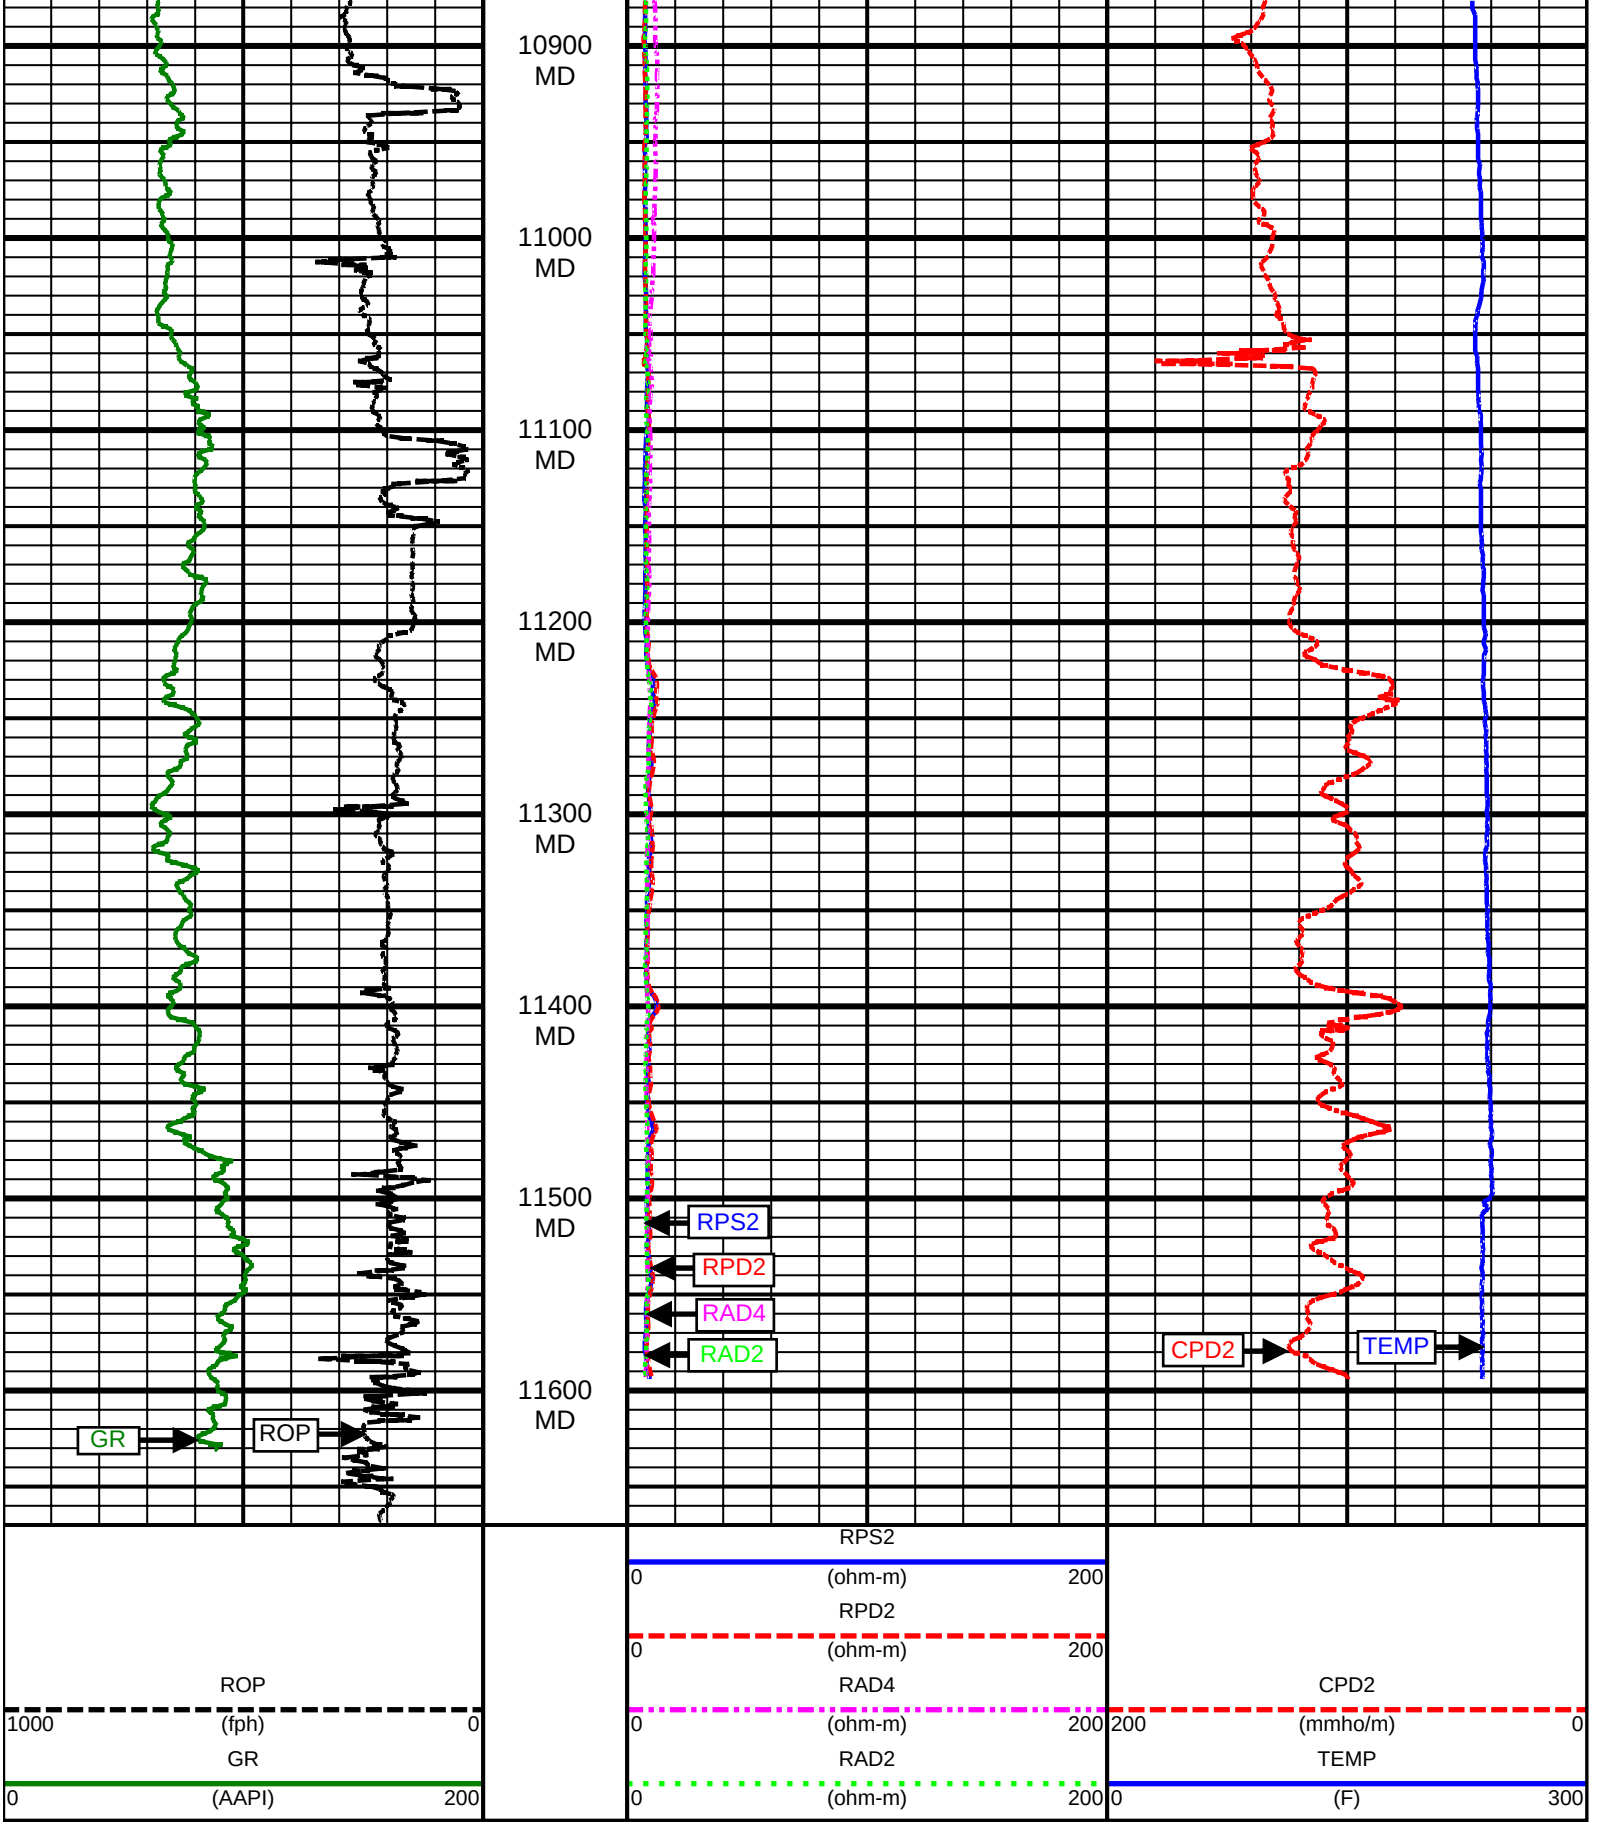
10900
MD
11000
MD
11100
MD
11200
MD
11300
MD
11400
MD
11500
MD
11600
MD
GR
ROP
RPS2
RPD2
RAD4
RAD2
CPD2
TEMP
ROP
1000
(fph)
0
GR
0
(AAPI)
200
RPS2
0
(ohm-m)
200
RPD2
0
(ohm-m)
200
RAD4
0
(ohm-m)
200
RAD2
0
(ohm-m)
200
CPD2
200
(mmho/m)
0
TEMP
0
(F)
300

5 Inch - Measured Depth

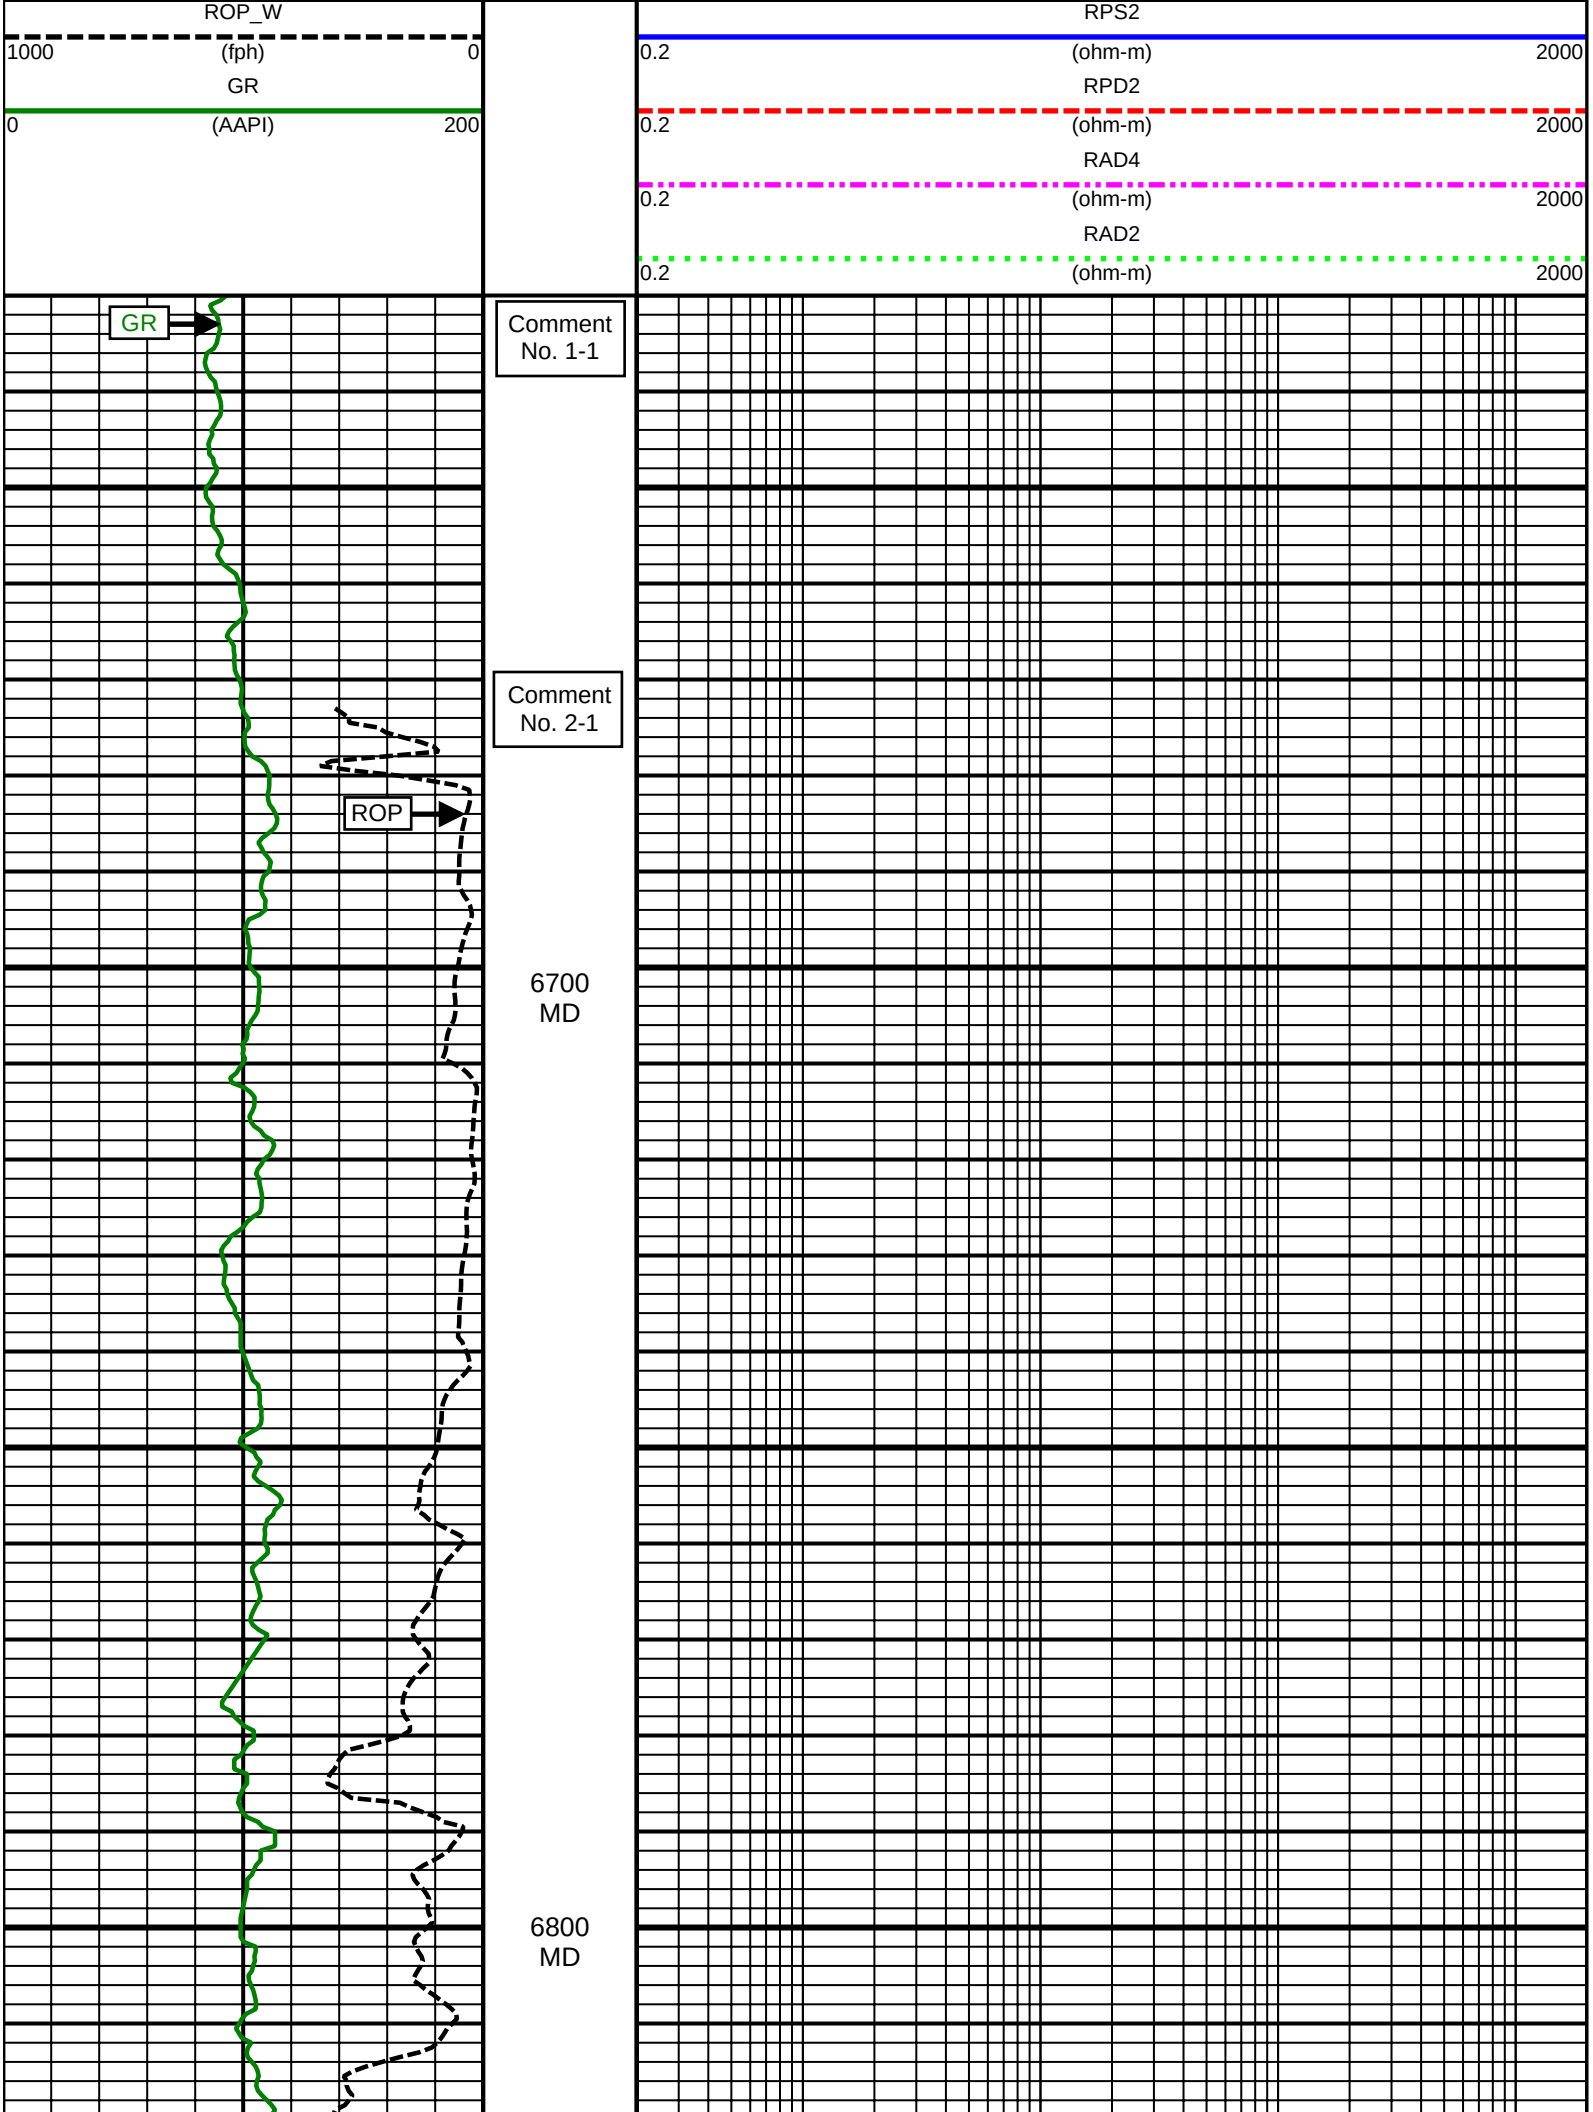
ROP_W
1000
(fph)
0
GR
0
(AAPI)
200
RPS2
0.2
(ohm-m)
2000
RPD2
0.2
(ohm-m)
2000
RAD4
0.2
(ohm-m)
2000
RAD2
0.2
(ohm-m)
2000
GR
Comment No. 1-1
Comment No. 2-1
ROP
6700 MD
6800 MD

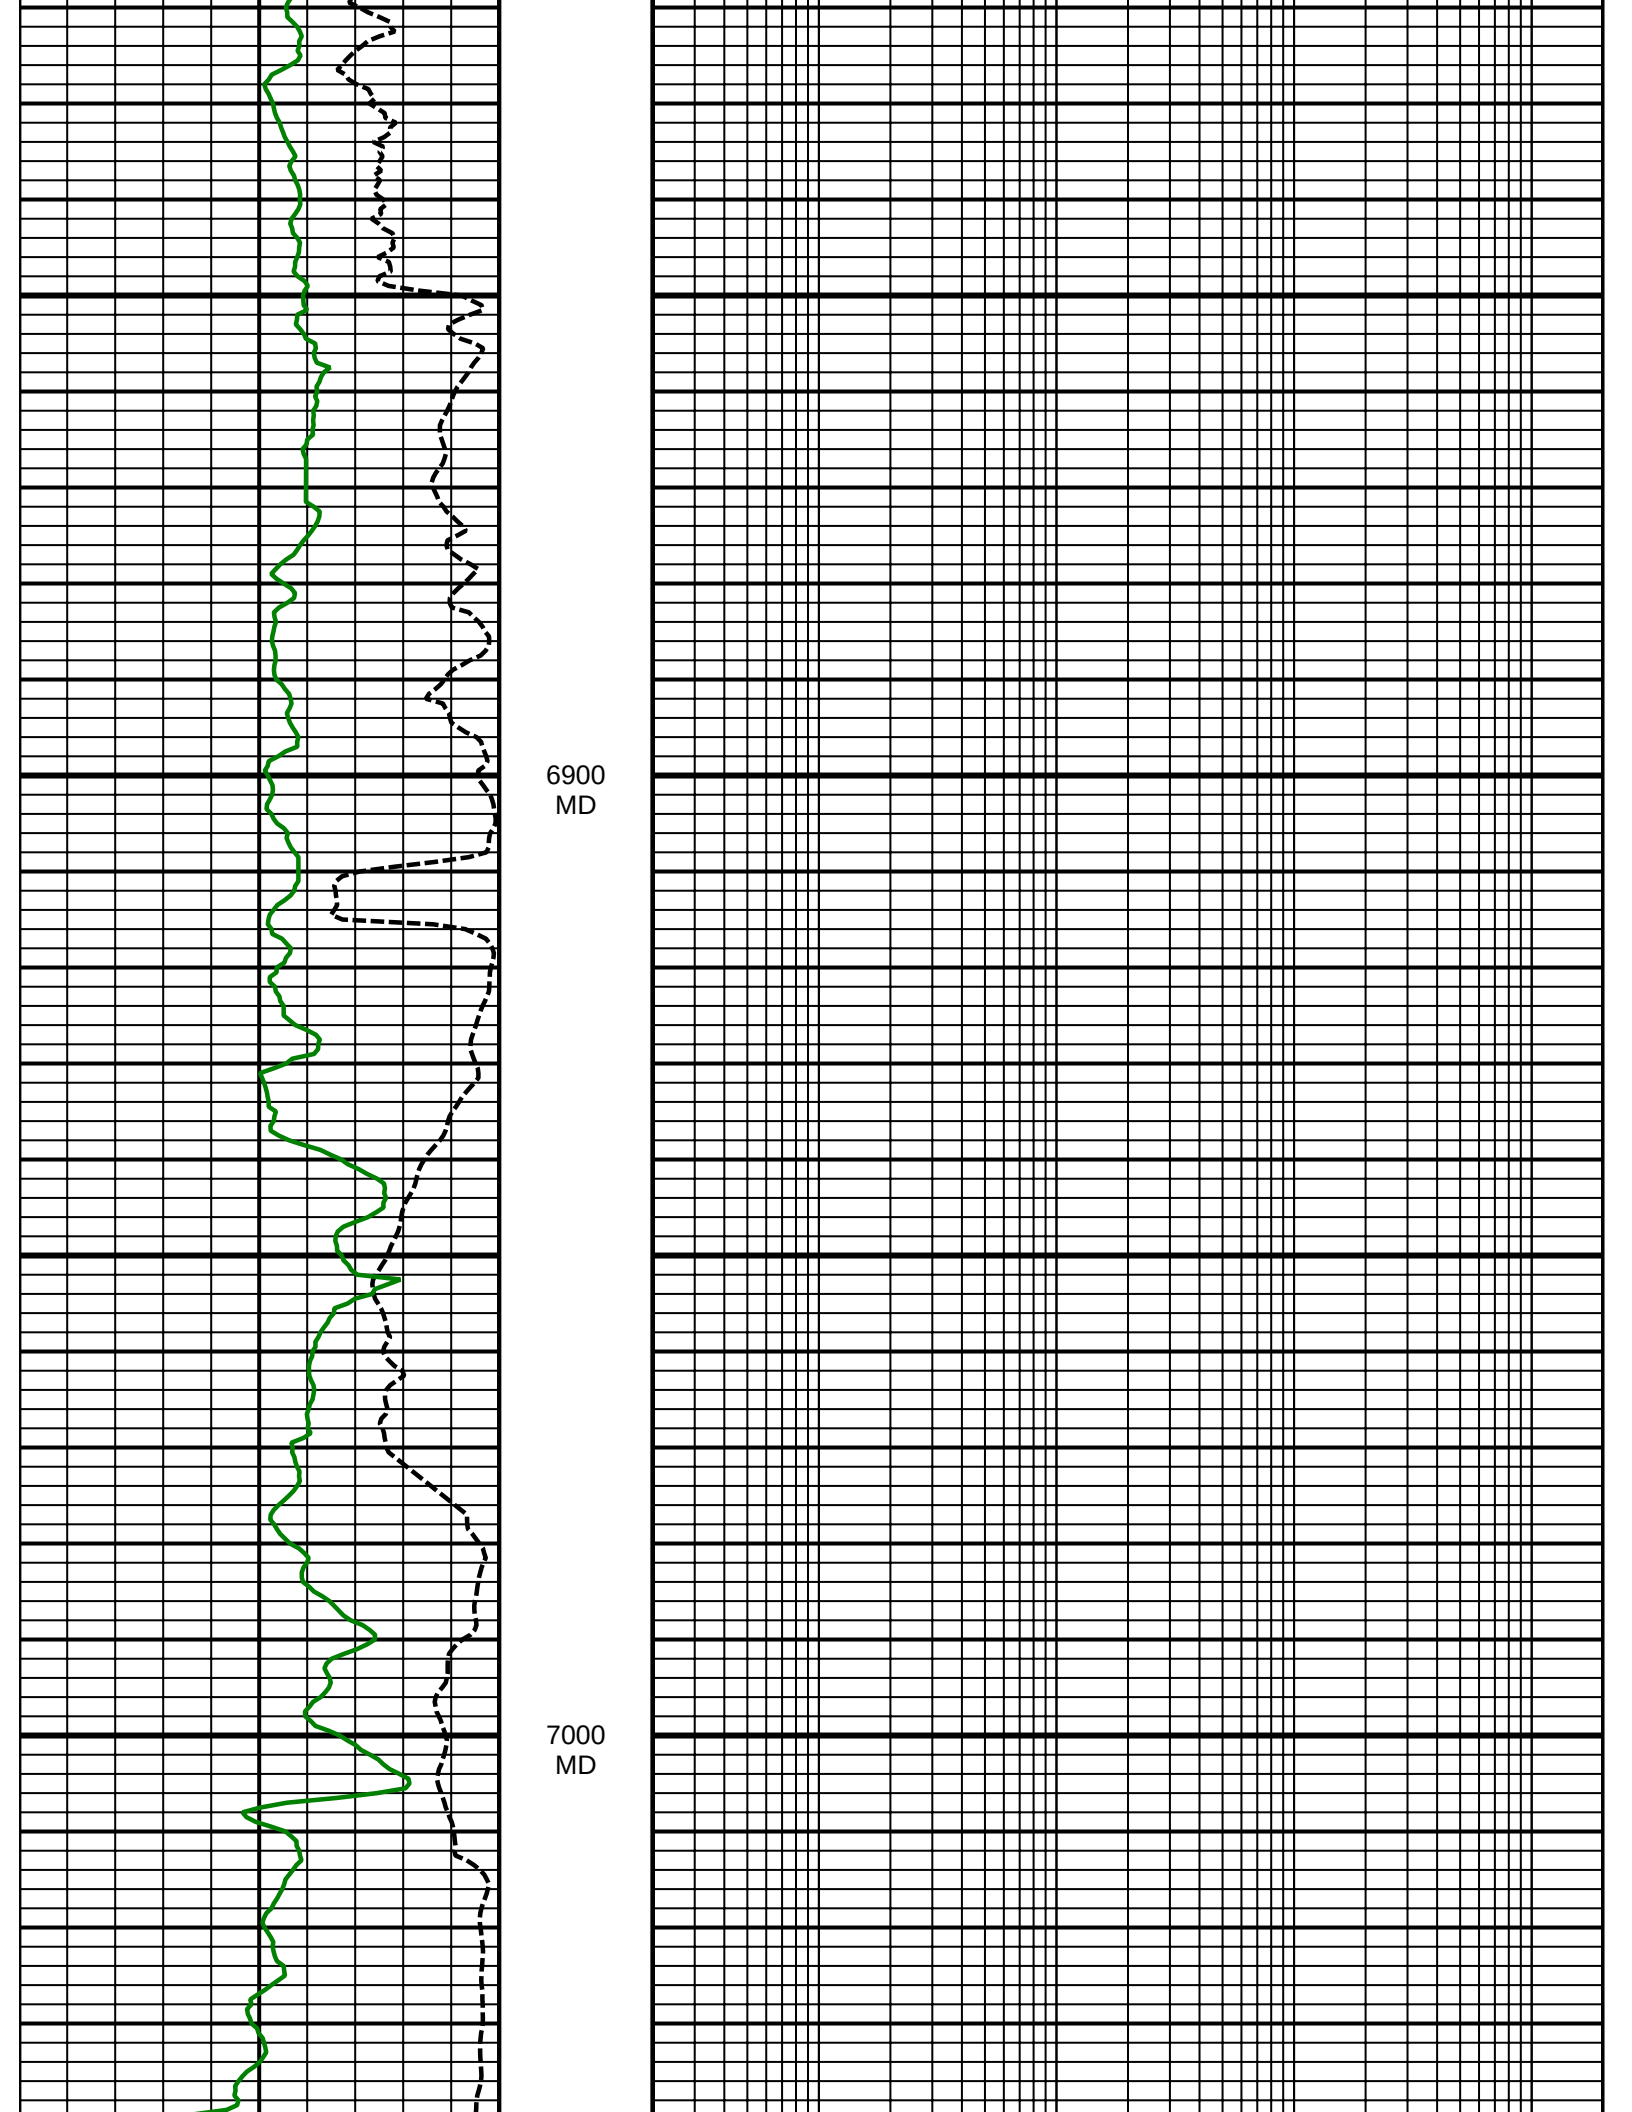
6900
MD
7000
MD

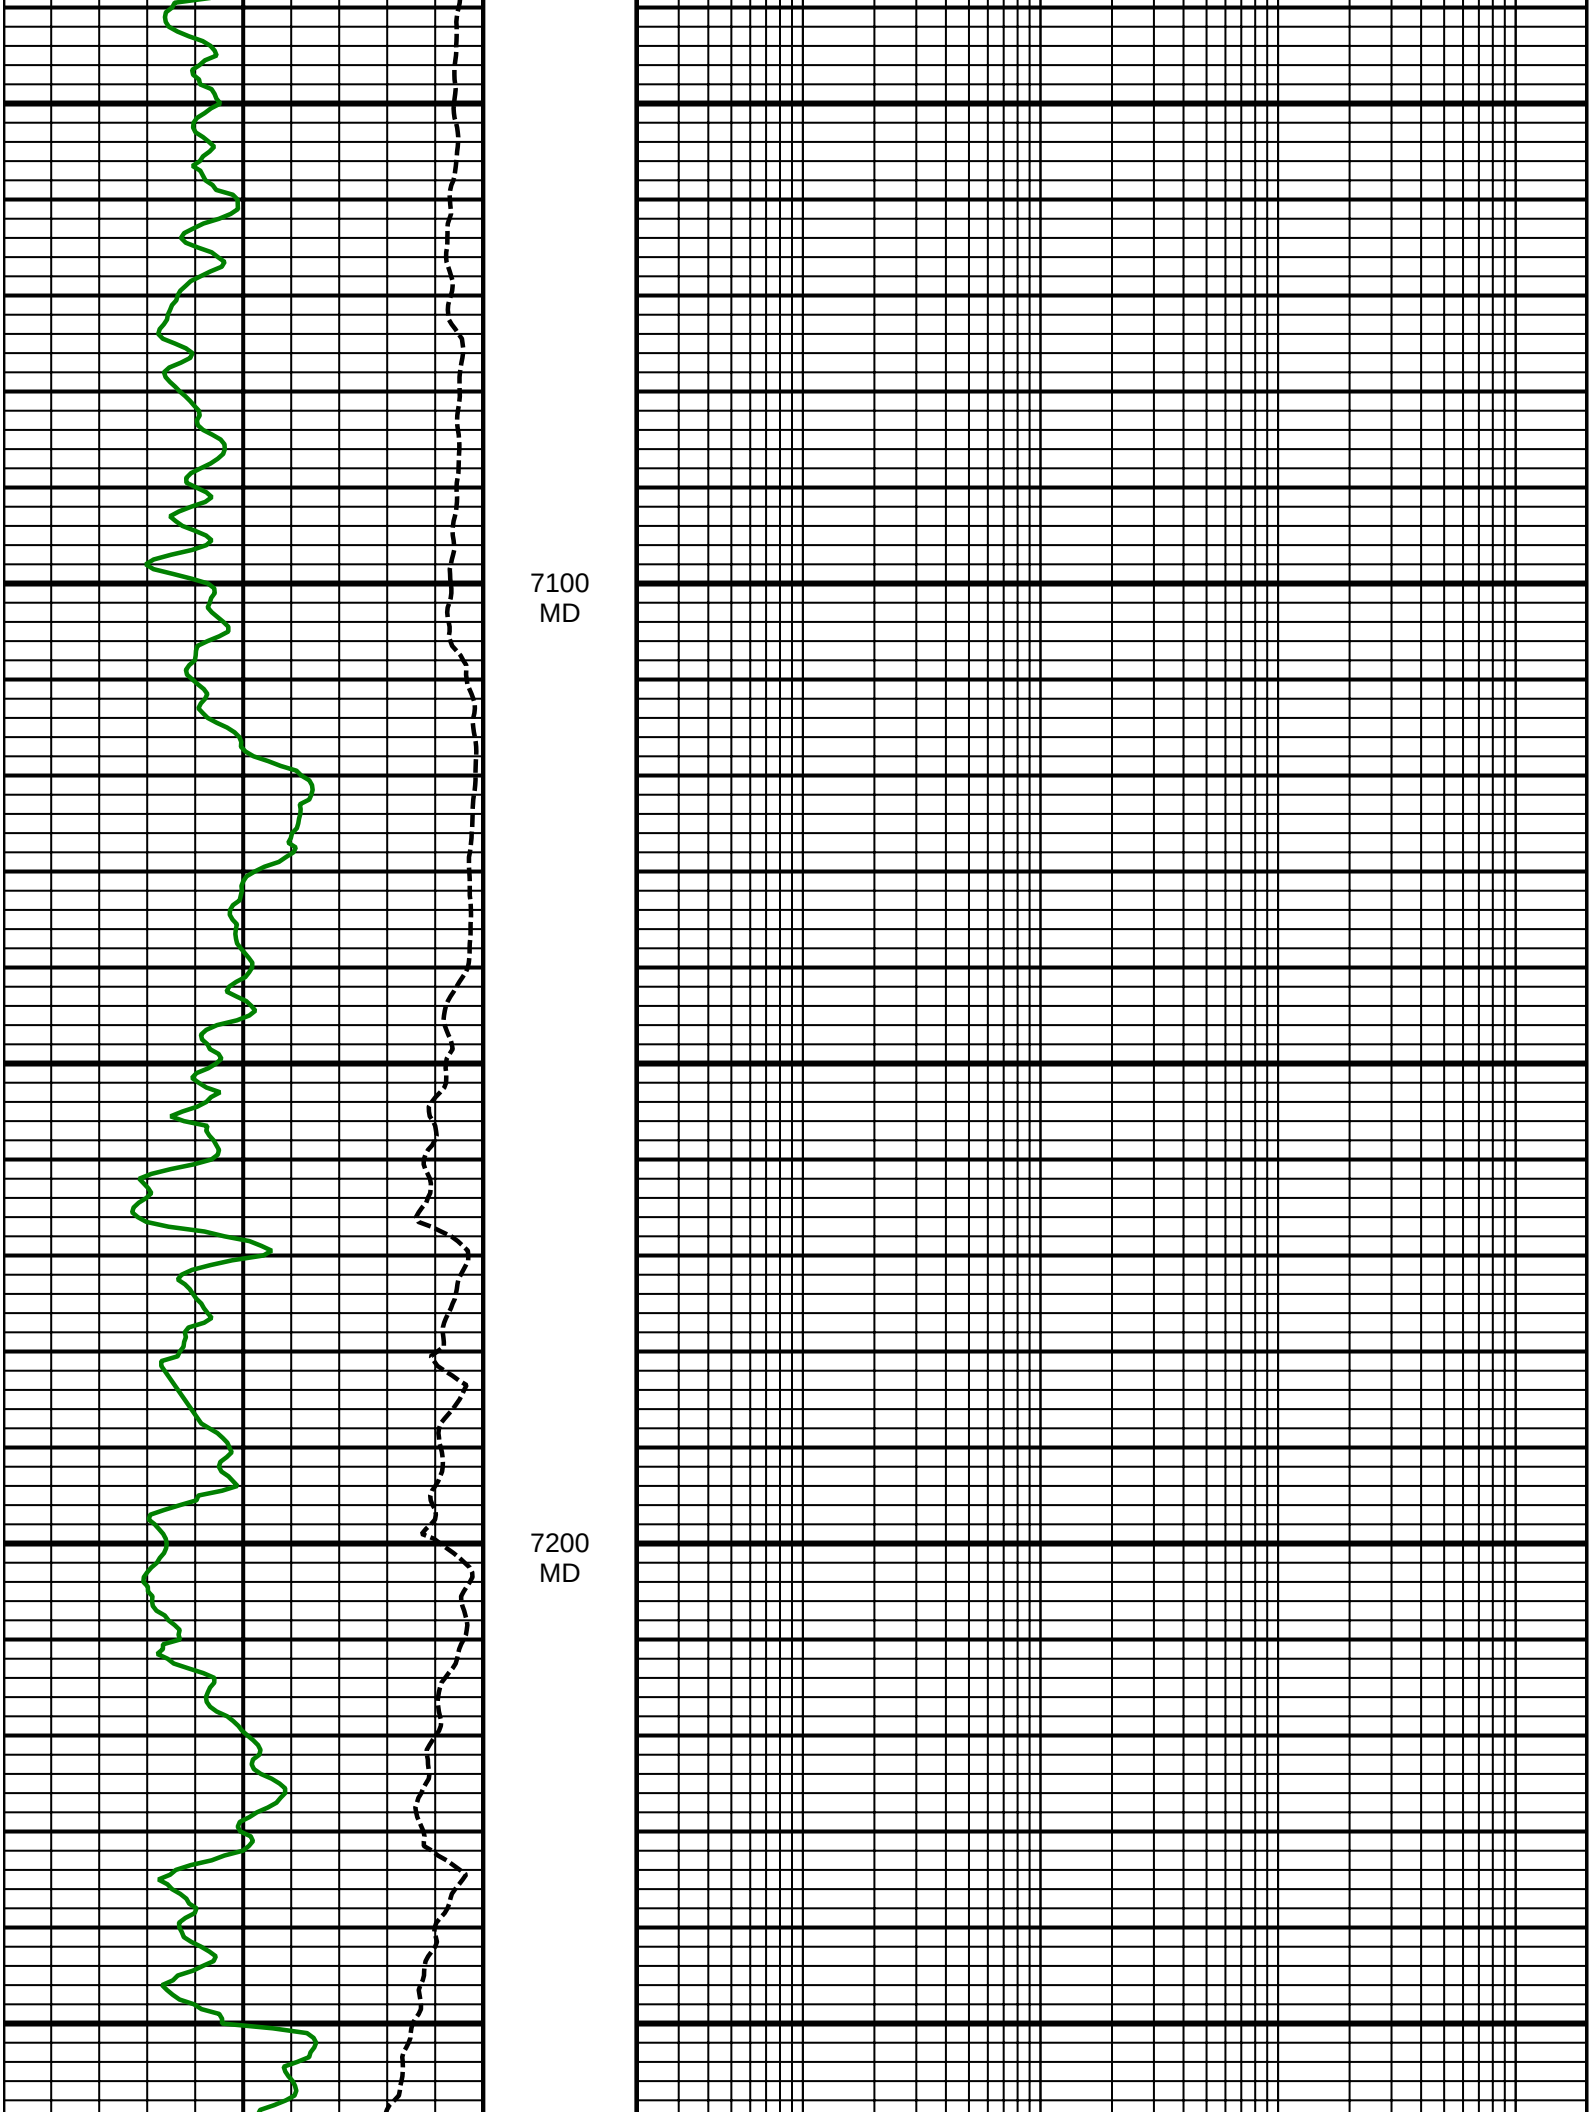
7100
MD
7200
MD

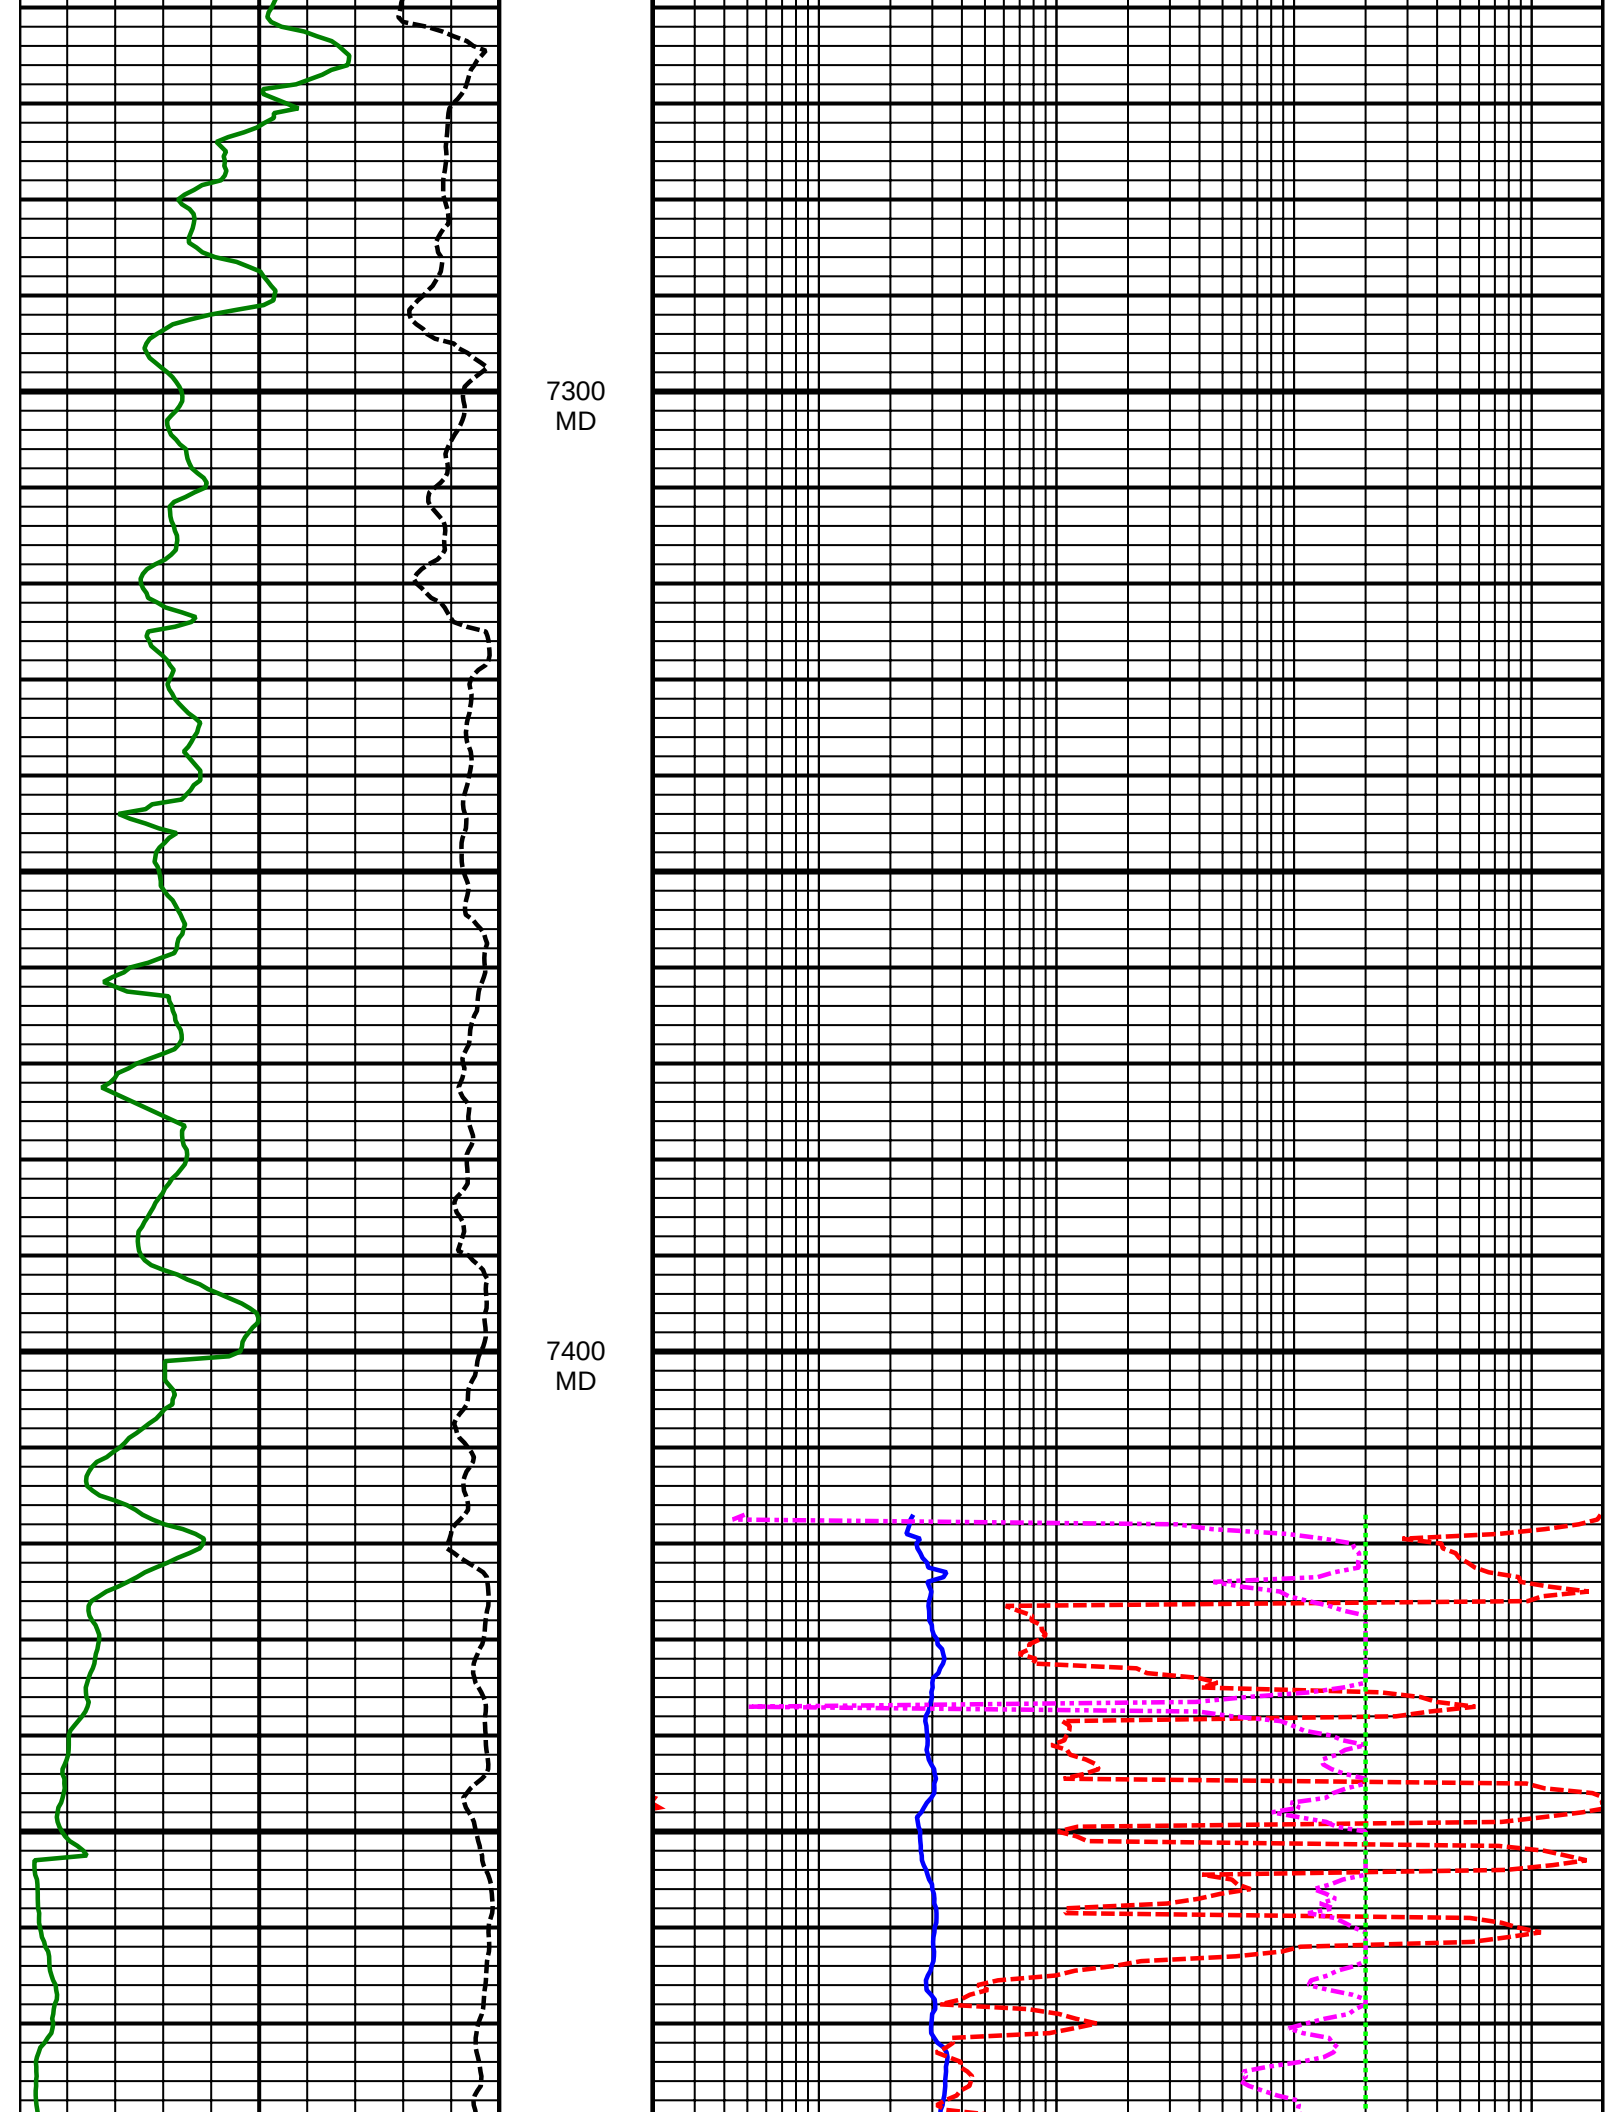
7300
MD
7400
MD

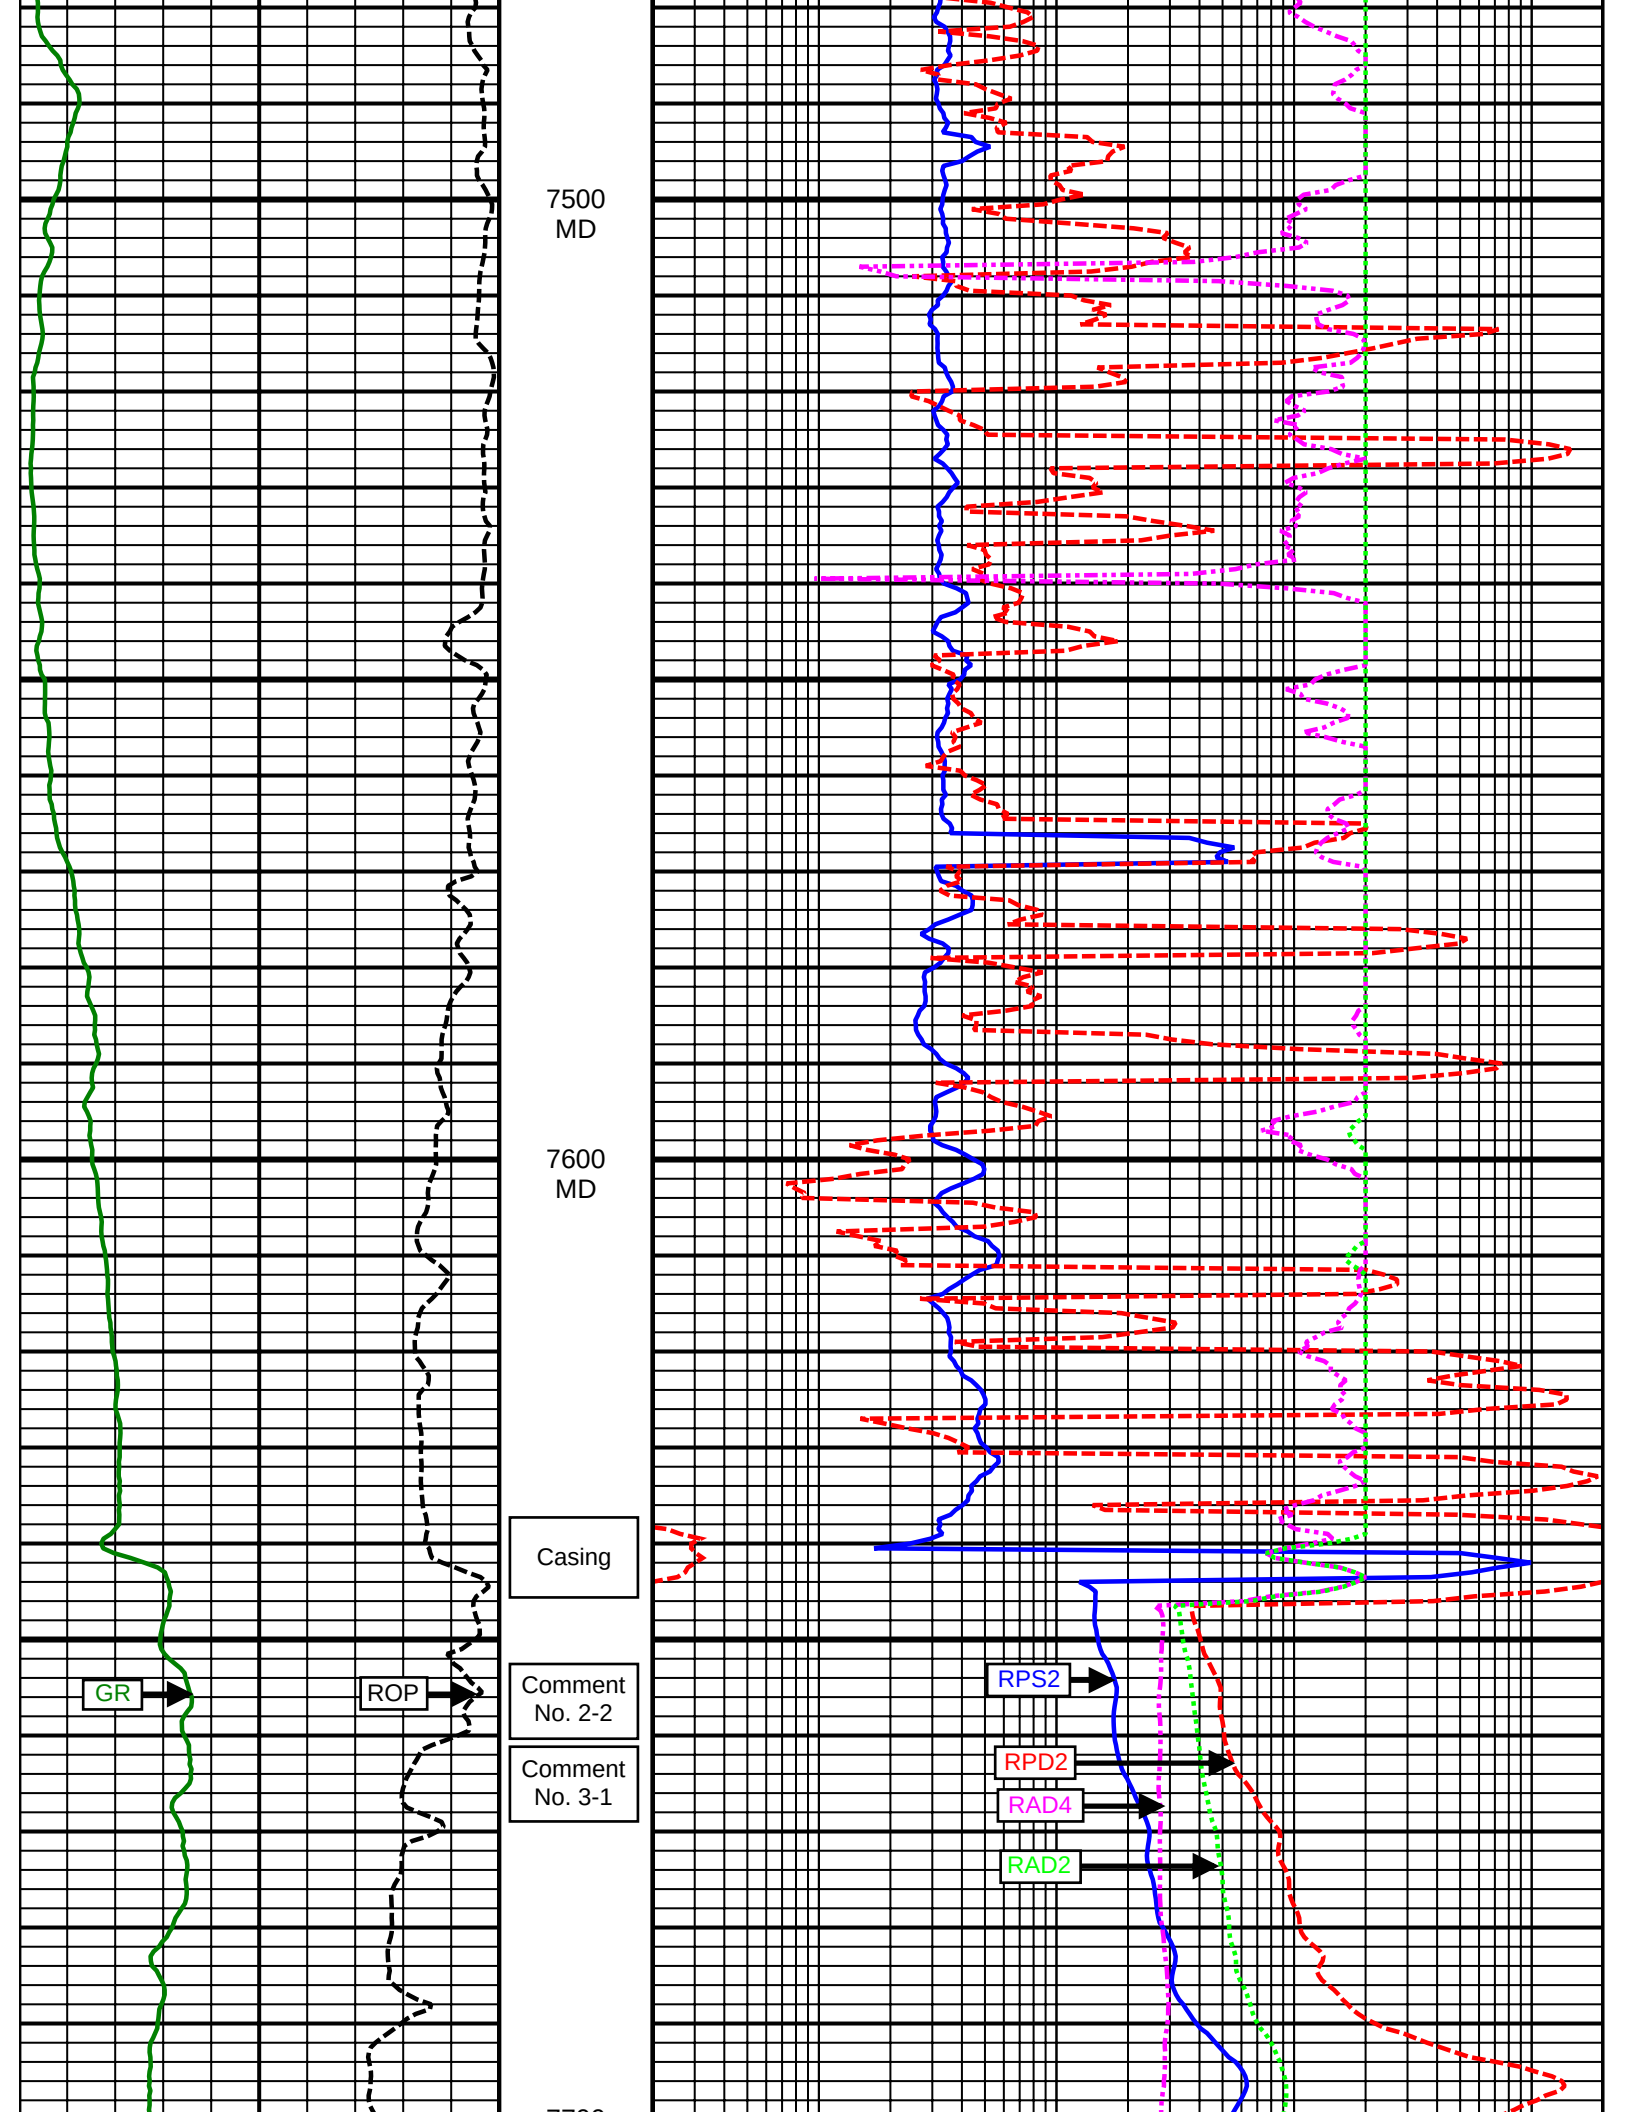
7500
MD
7600
MD
Casing
GR
ROP
Comment
No. 2-2
Comment
No. 3-1
RPS2
RPD2
RAD4
RAD2

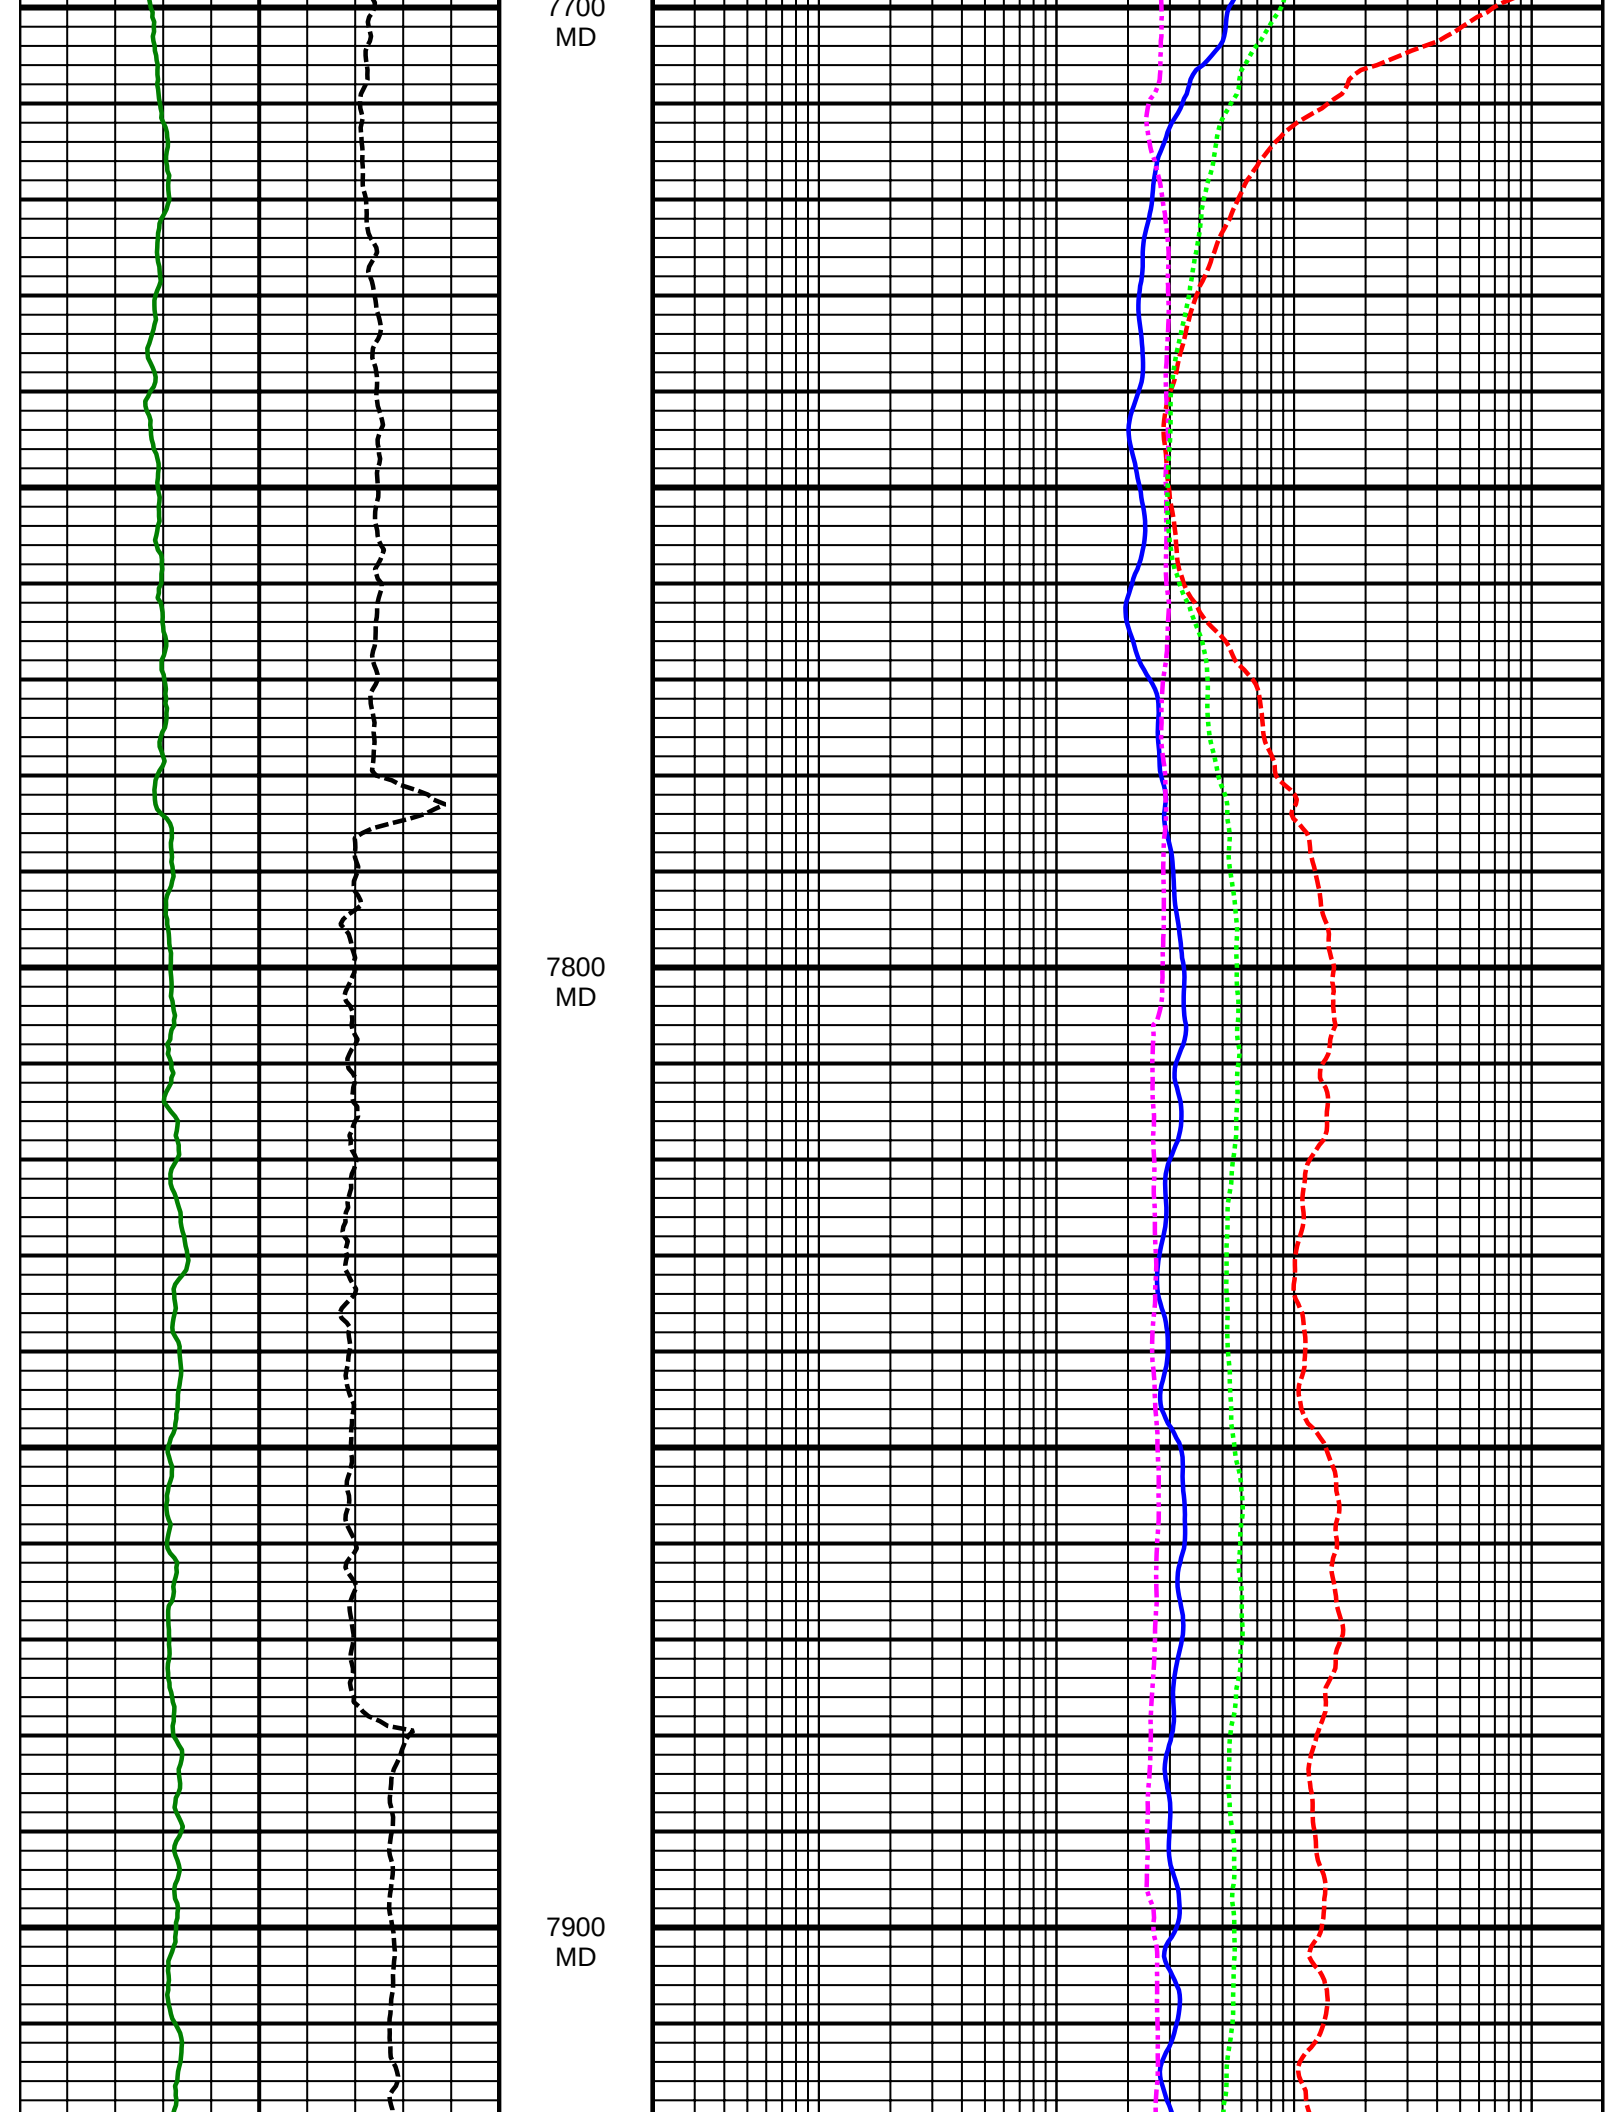
7700
MD
7800
MD
7900
MD

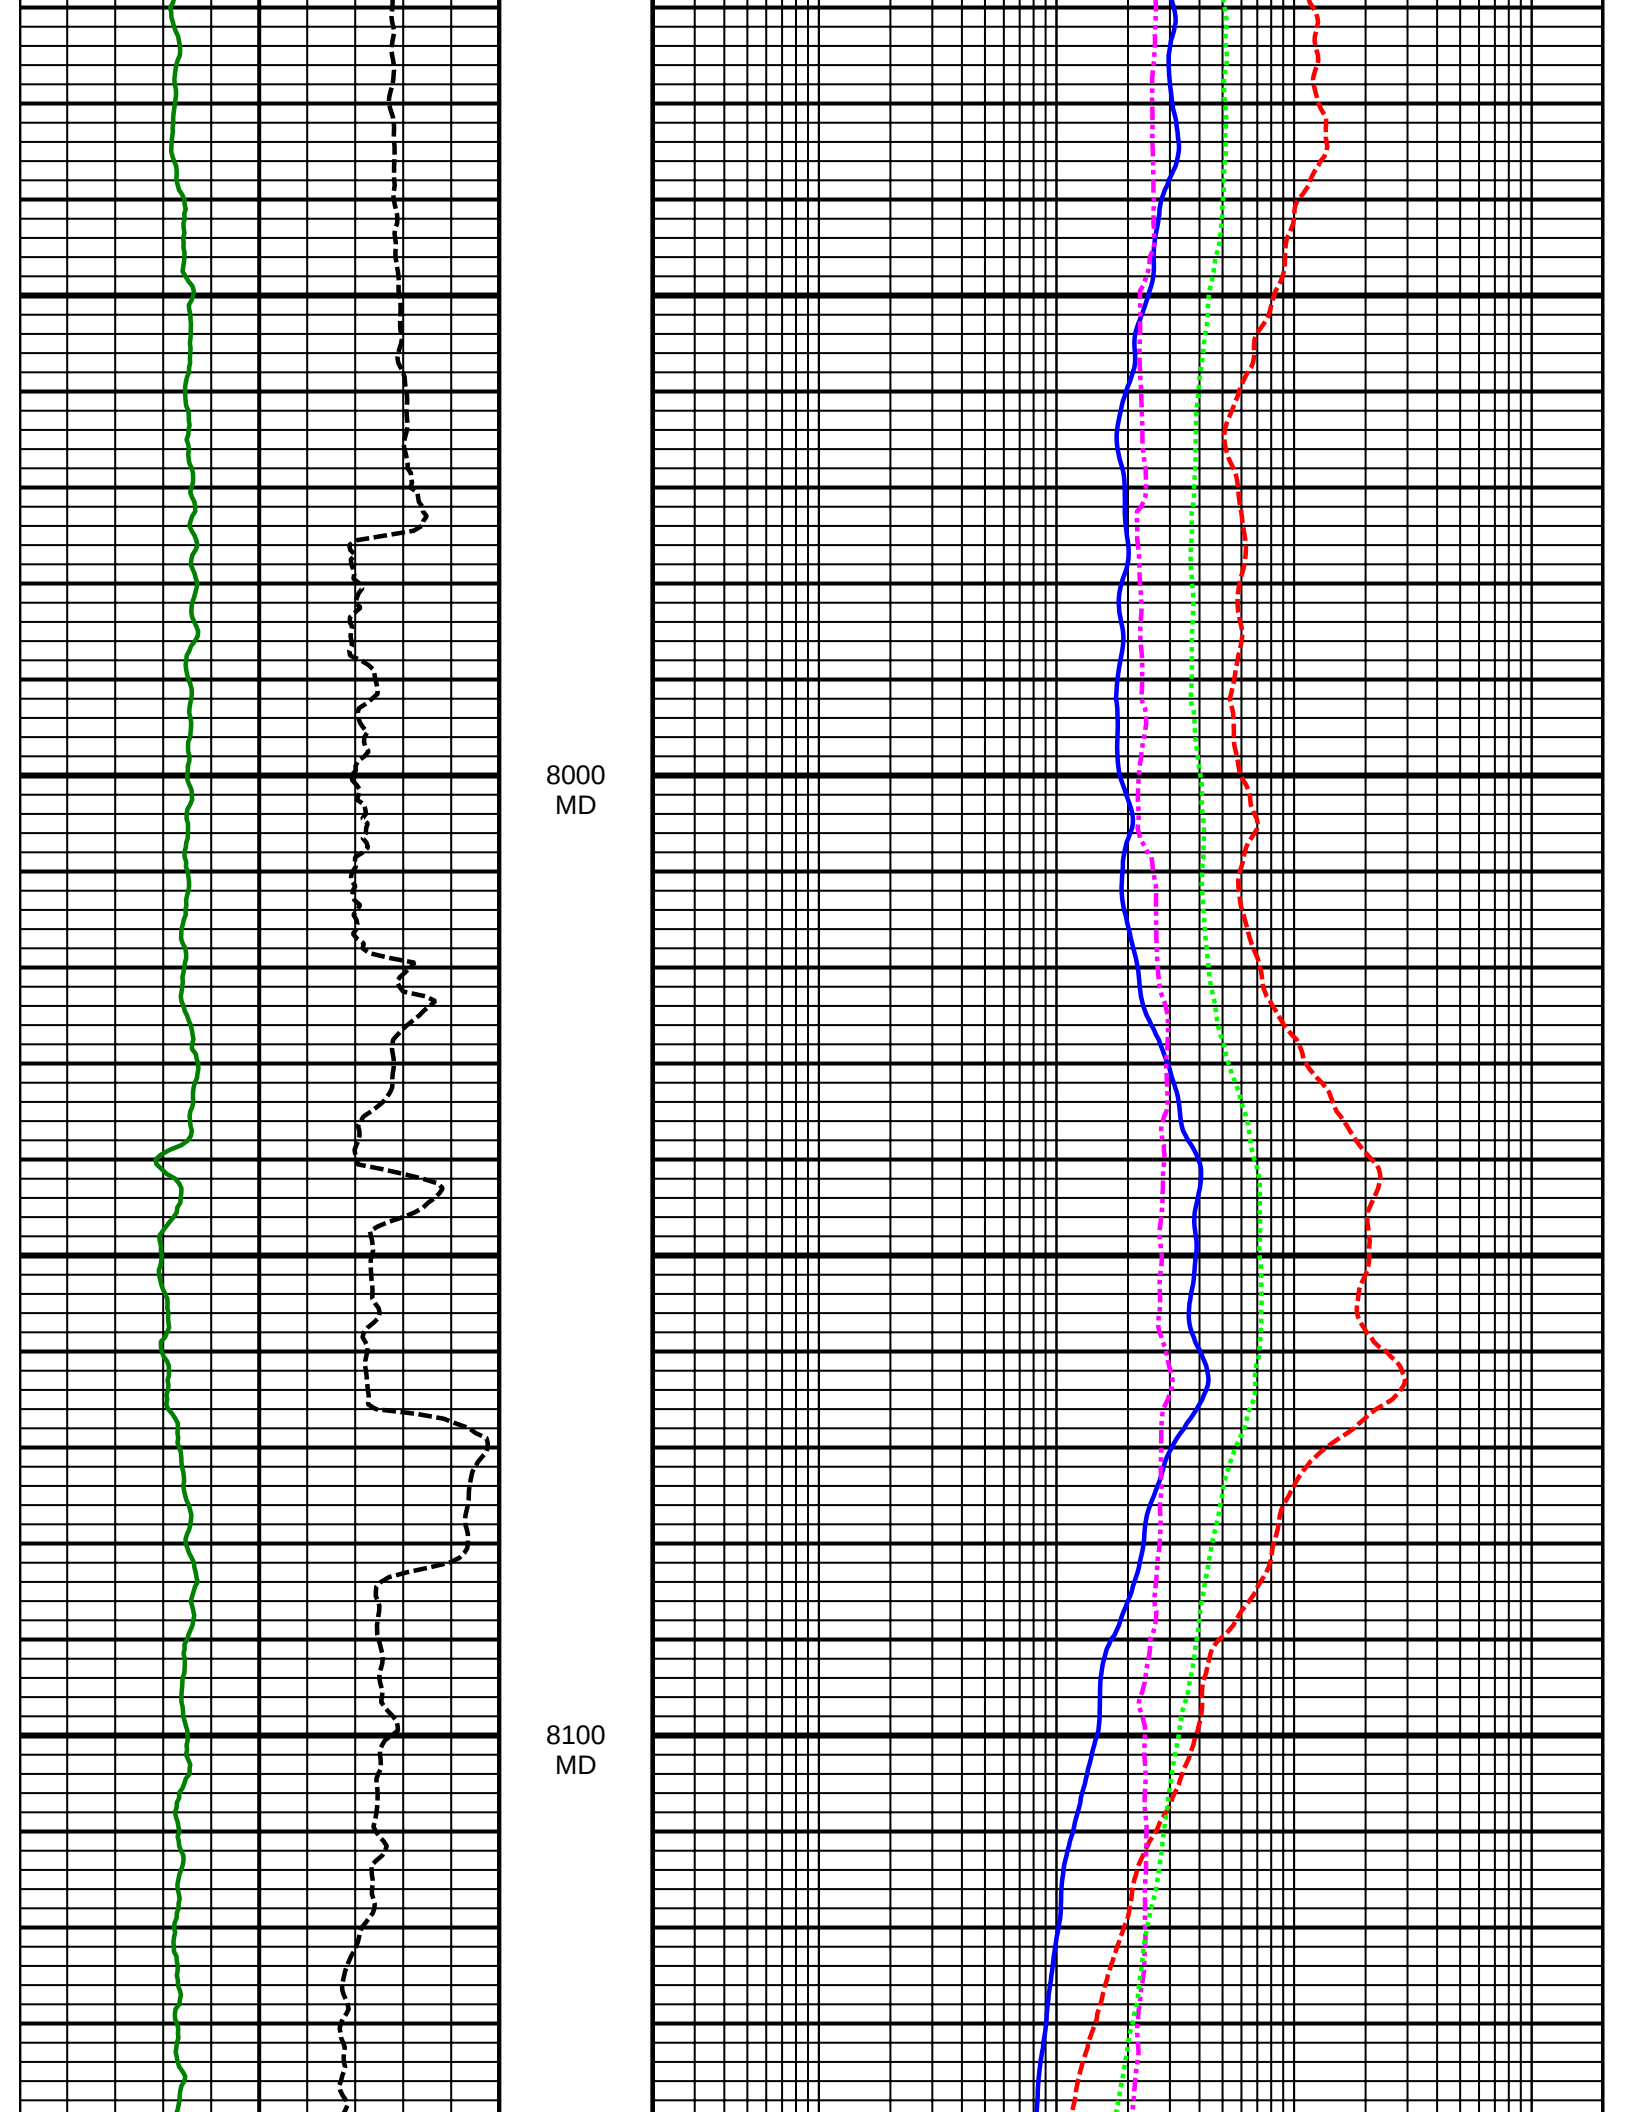
8000
MD
8100
MD

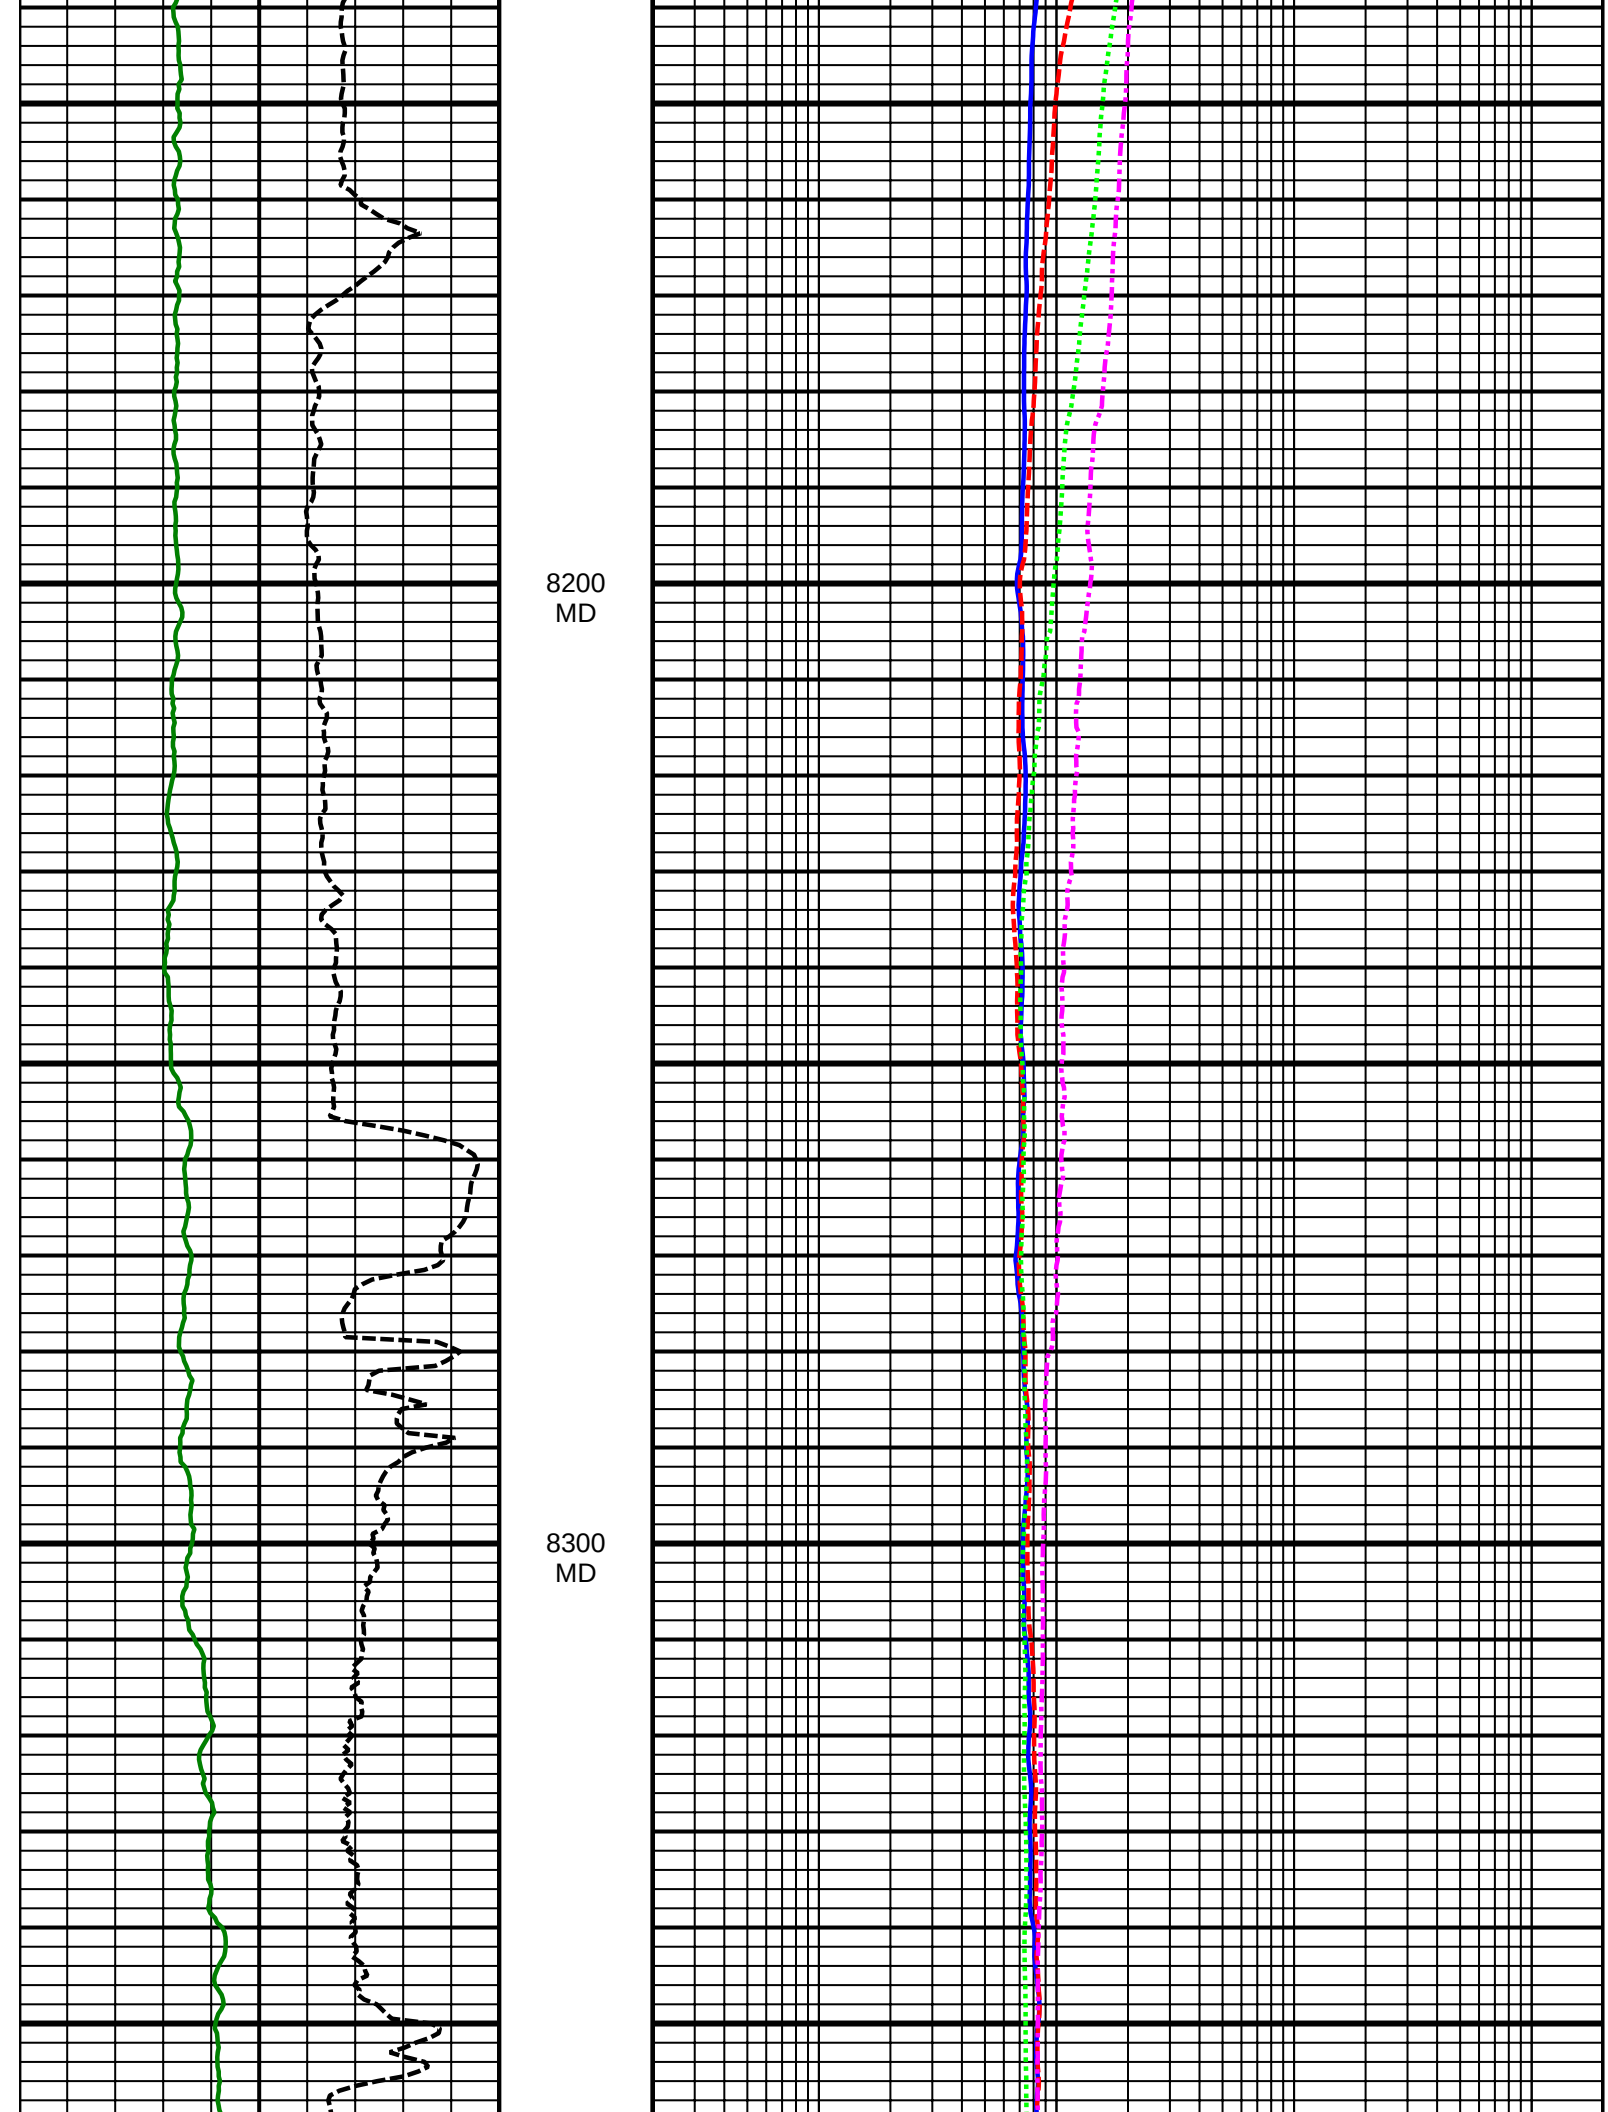
8200
MD
8300
MD

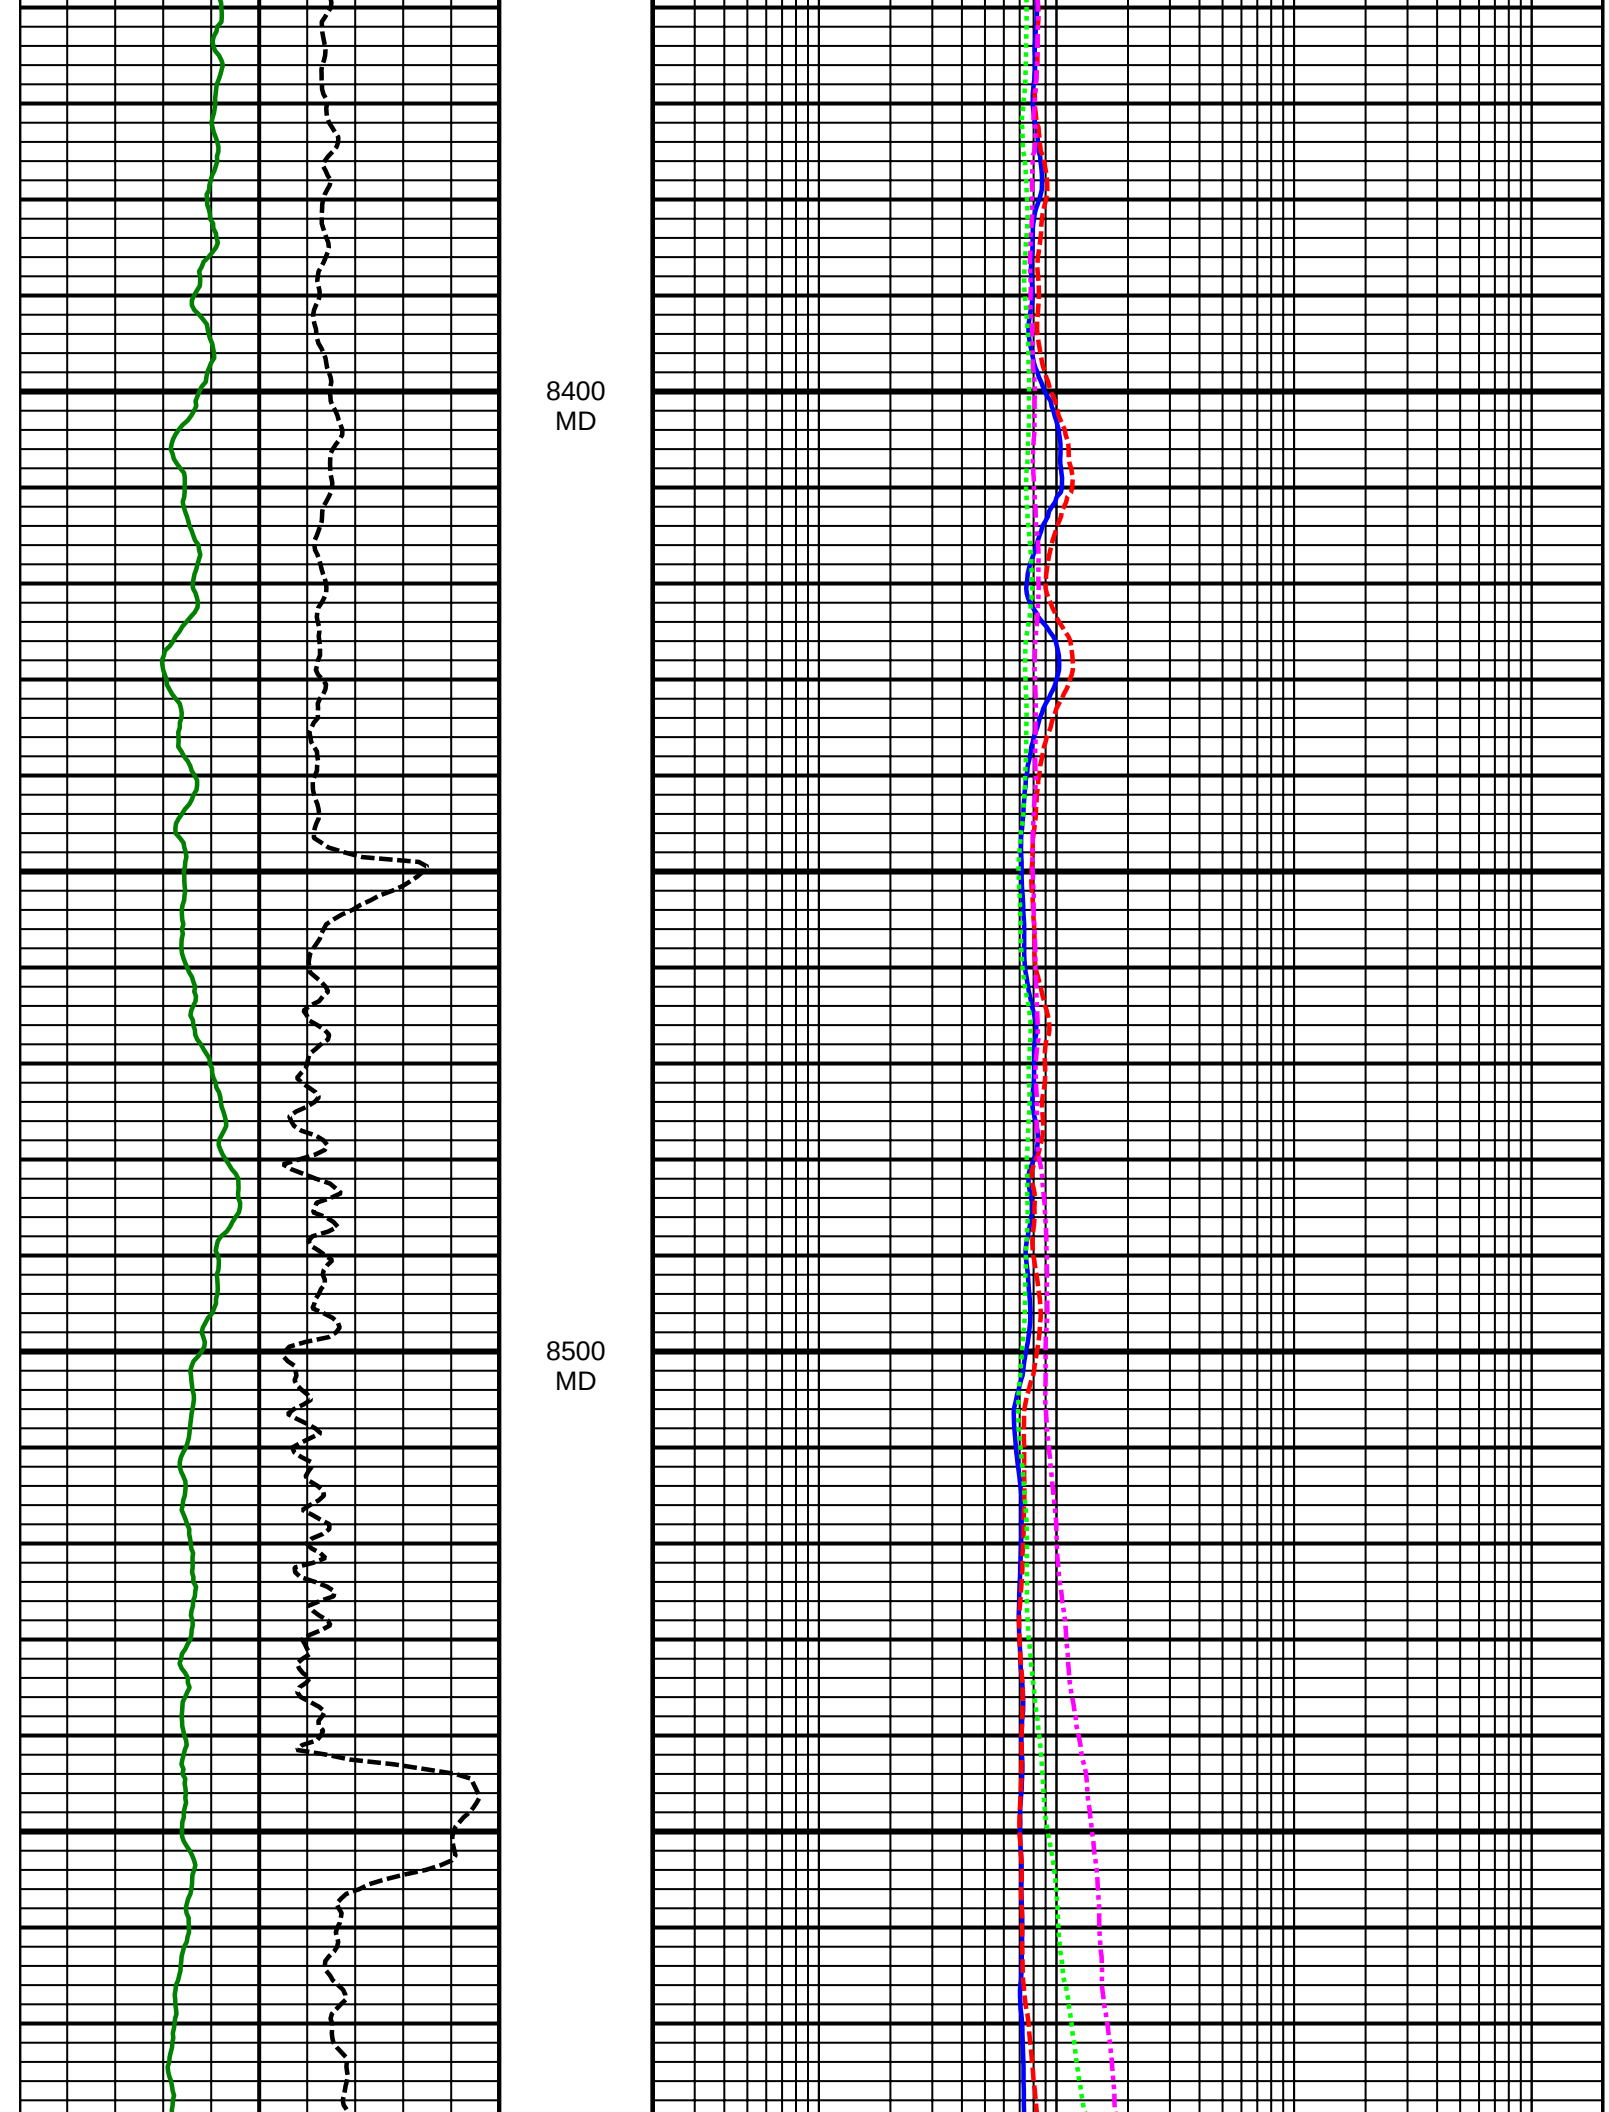
8400
MD
8500
MD

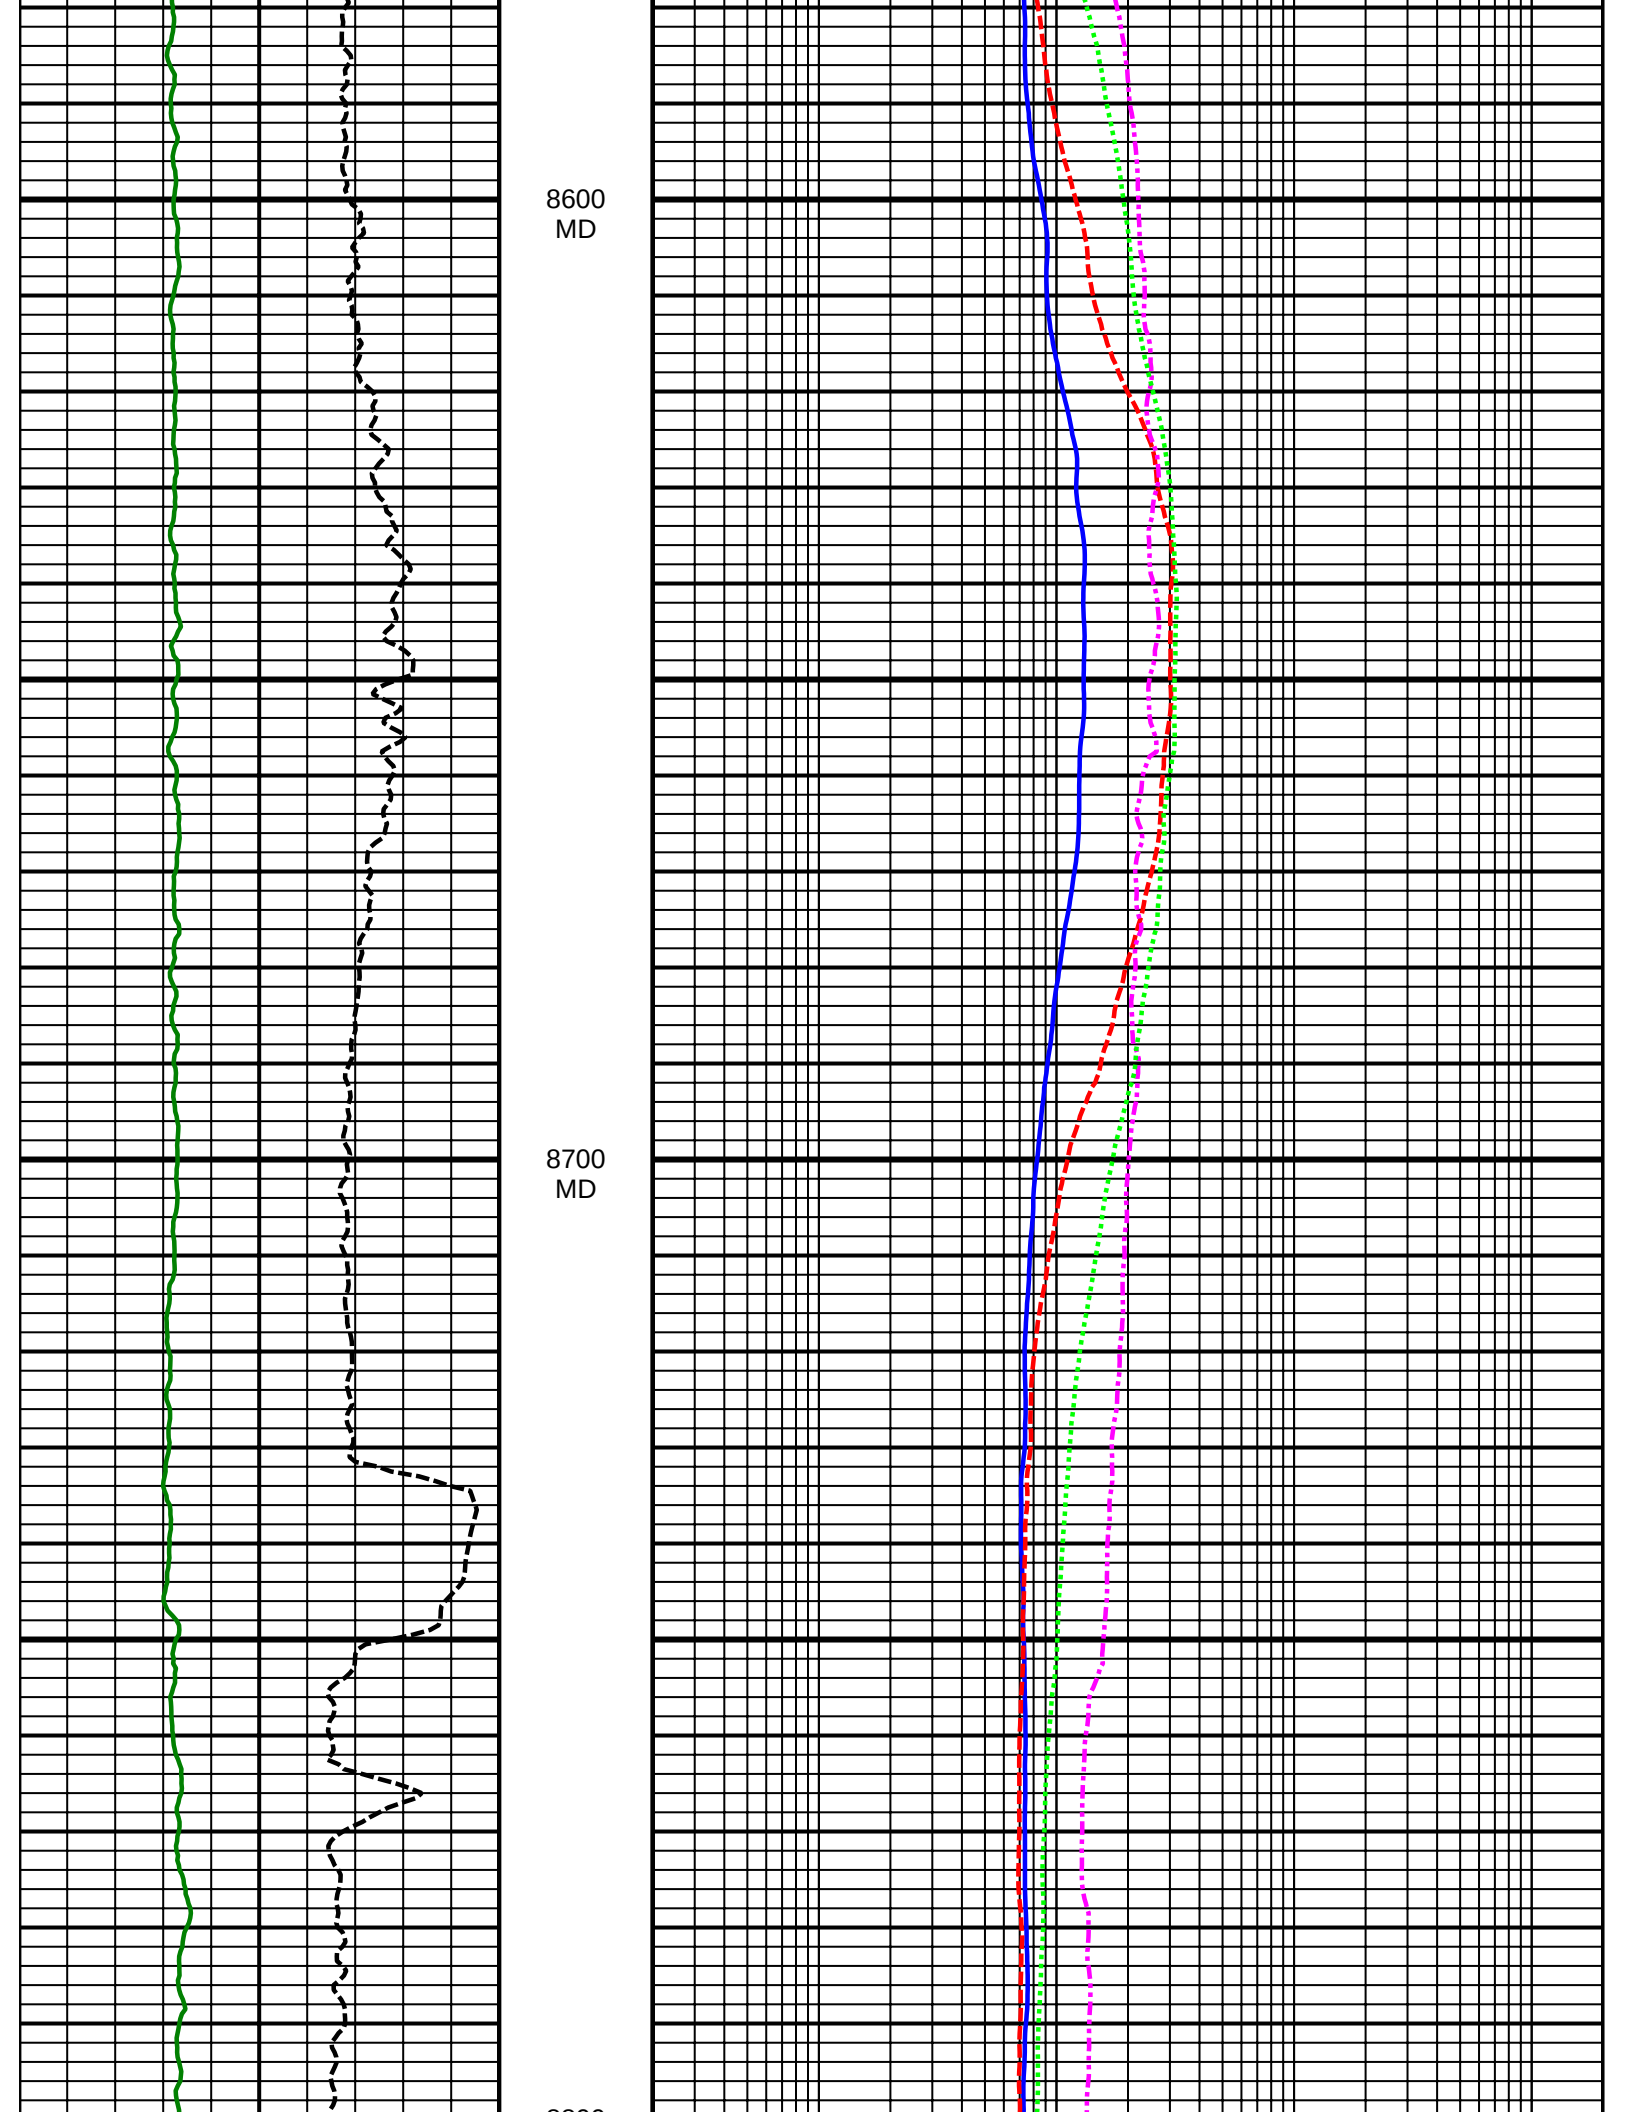
8600
MD
8700
MD

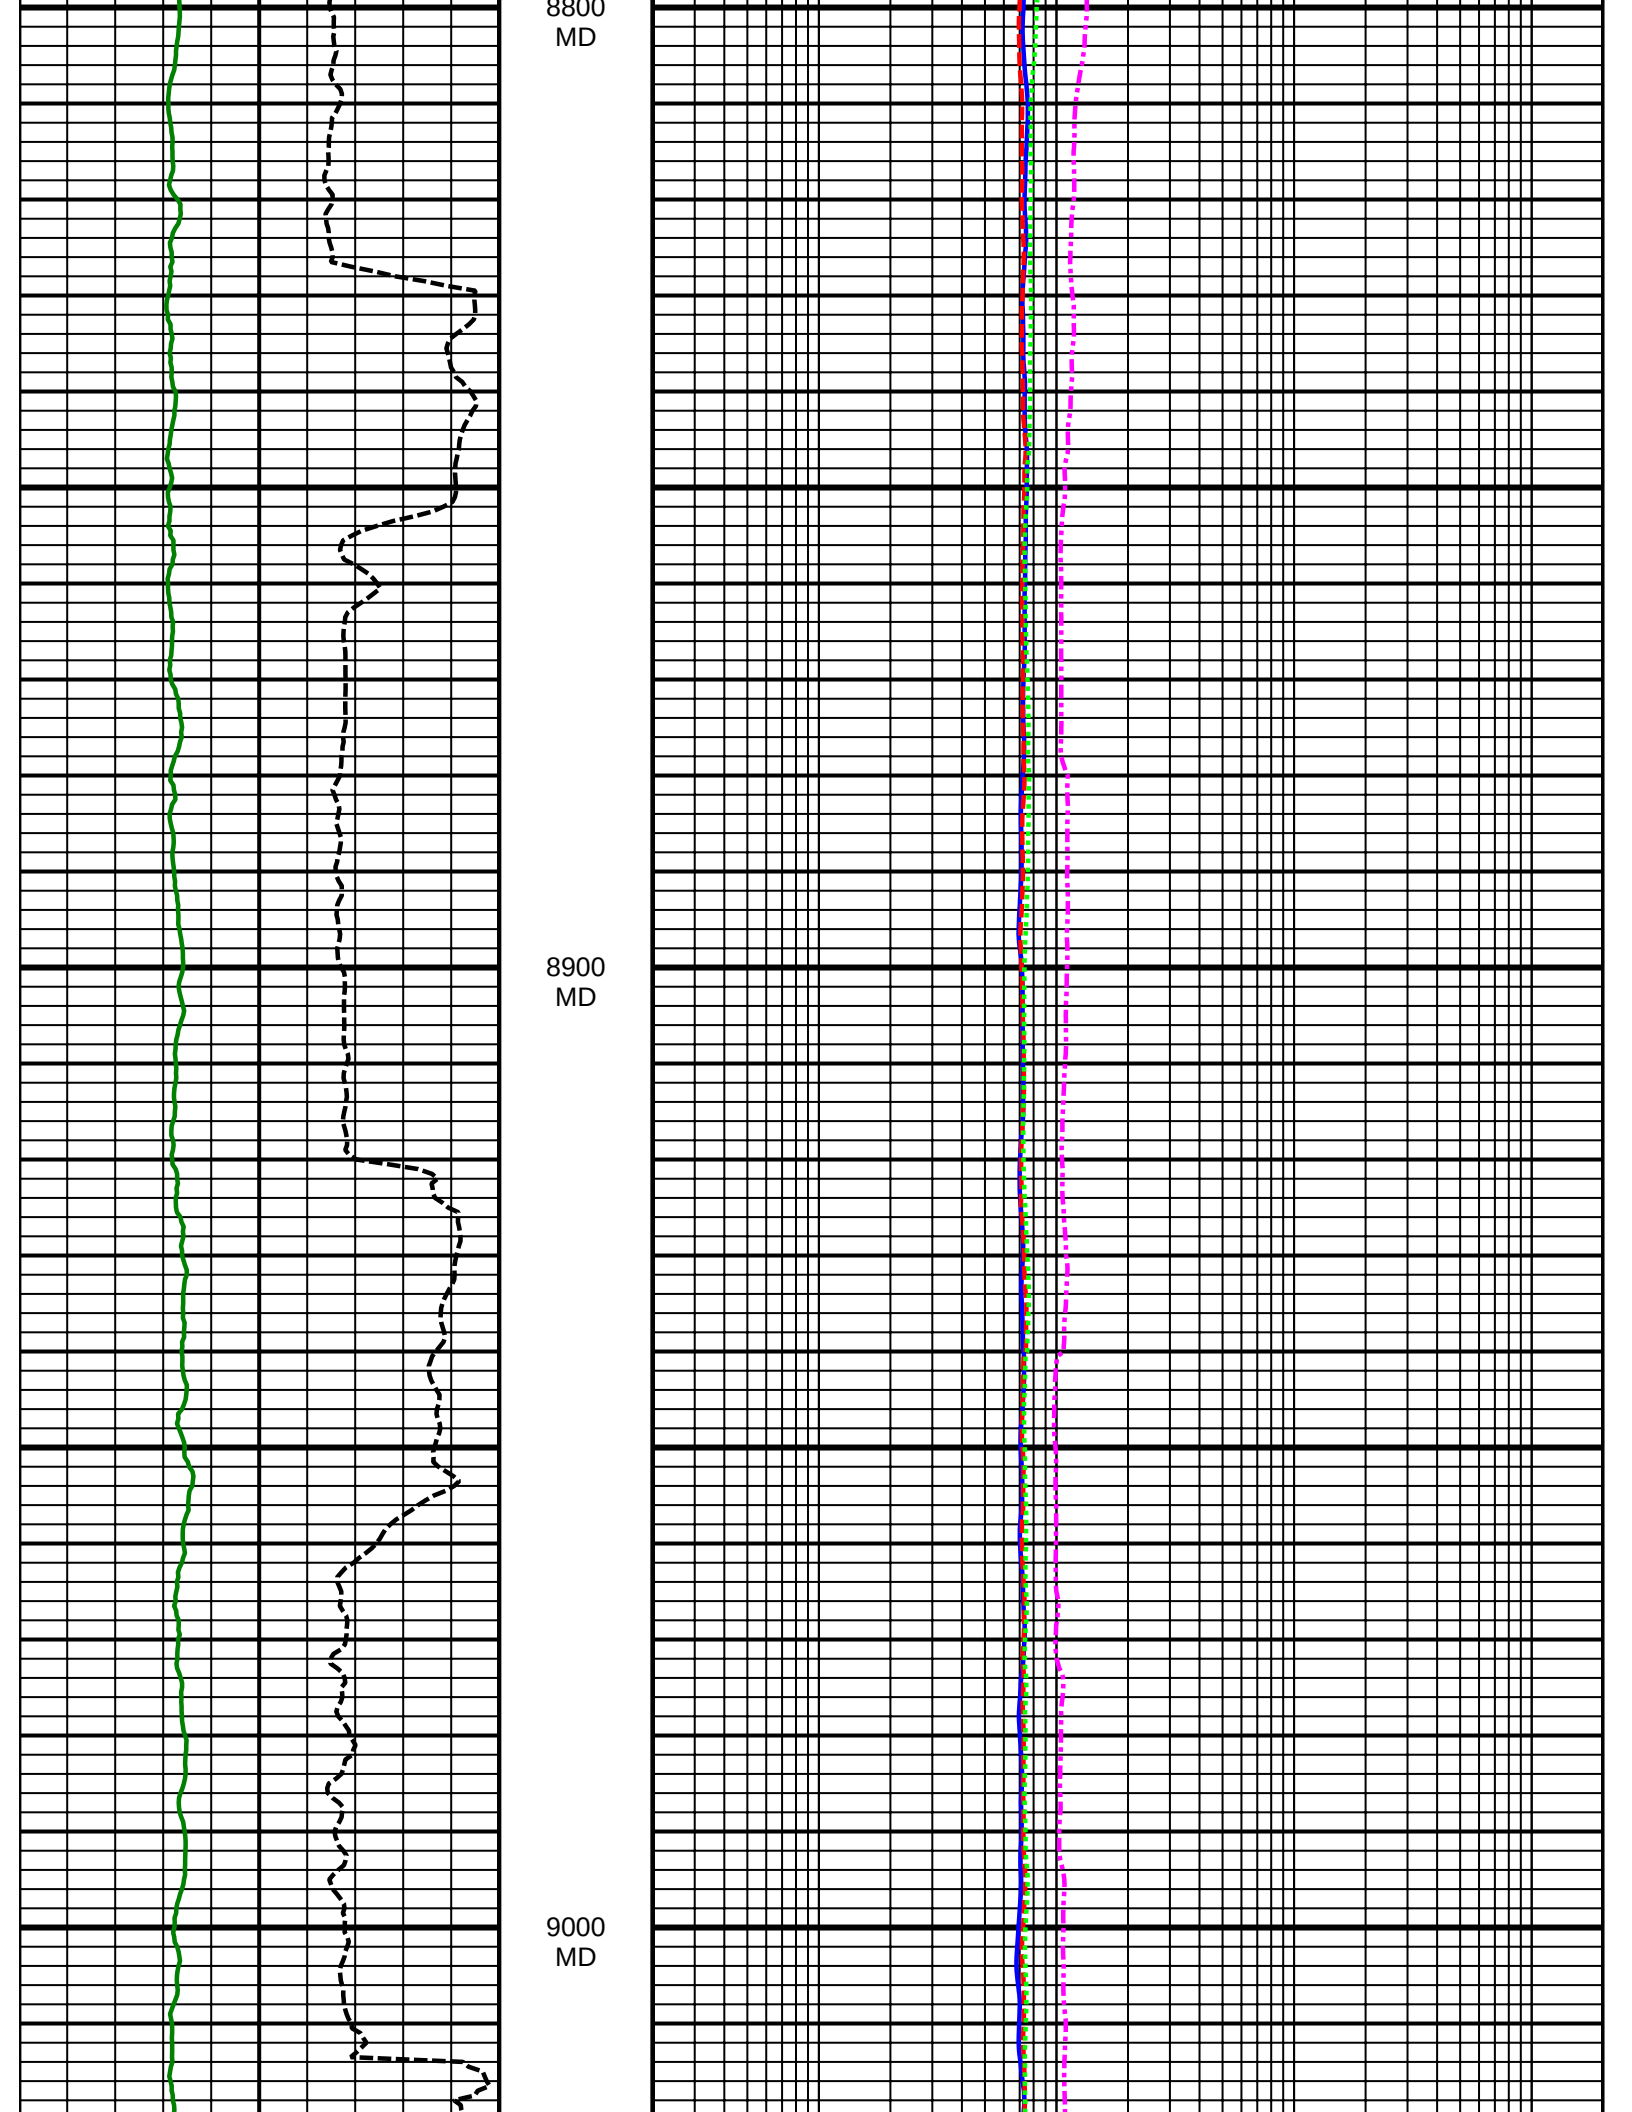
8800
MD
8900
MD
9000
MD

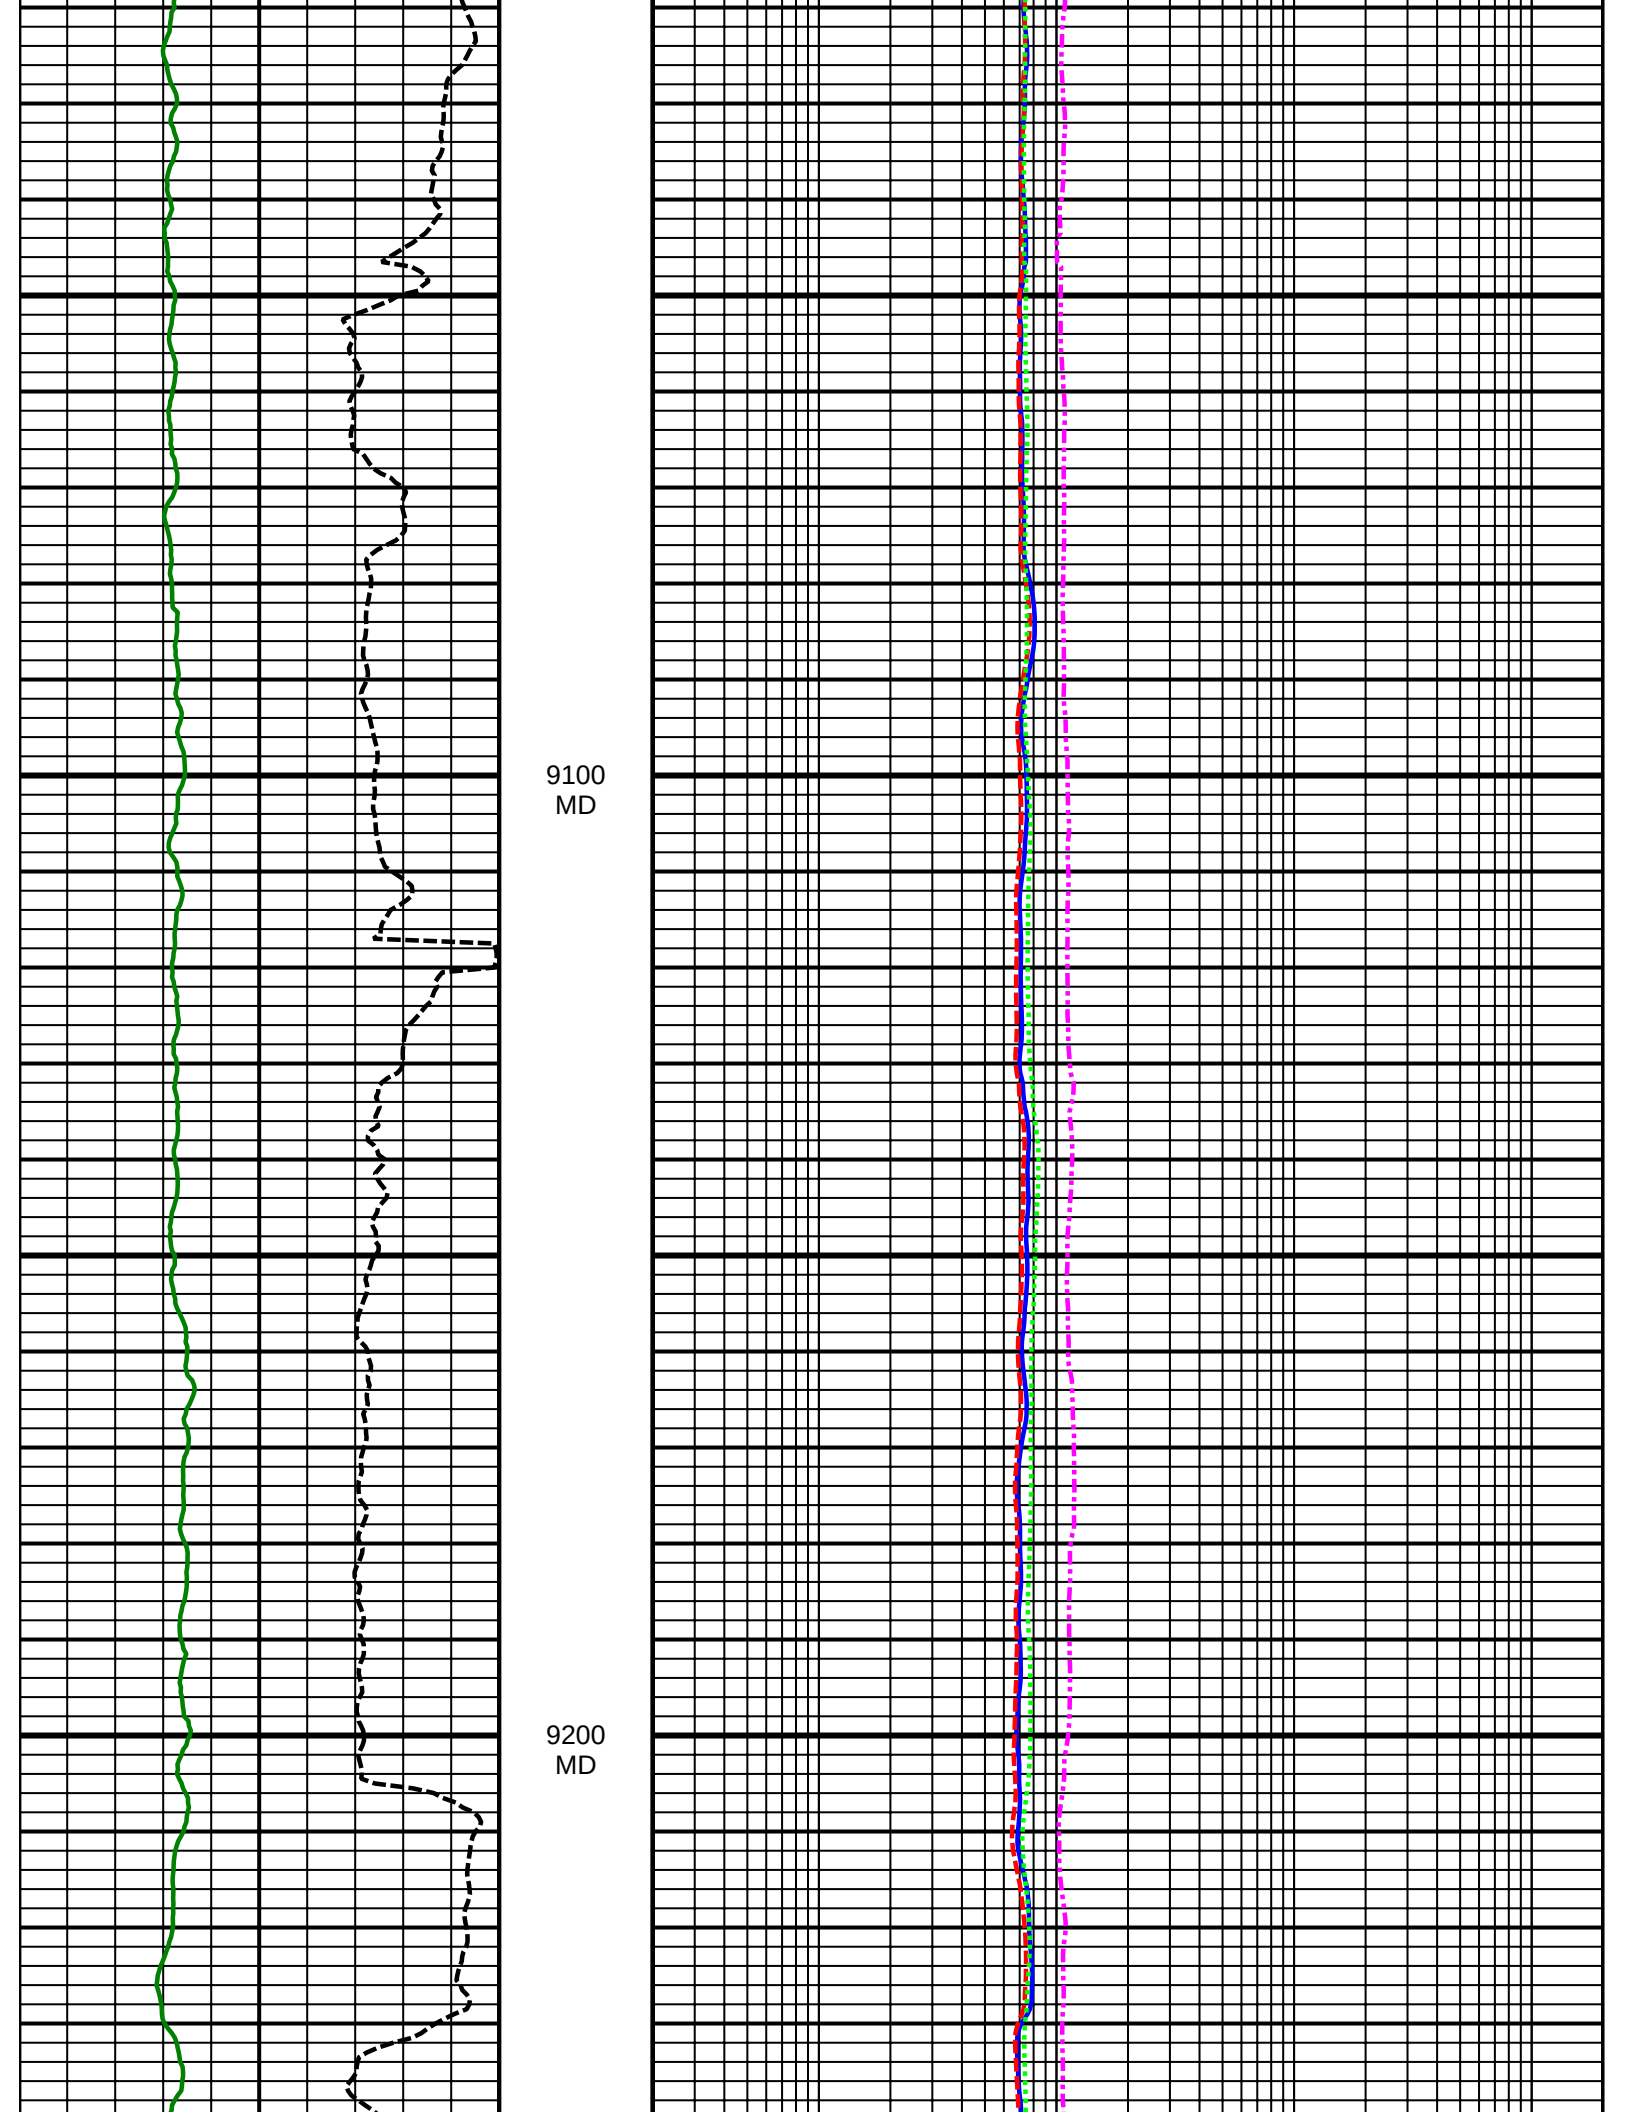
9100
MD
9200
MD

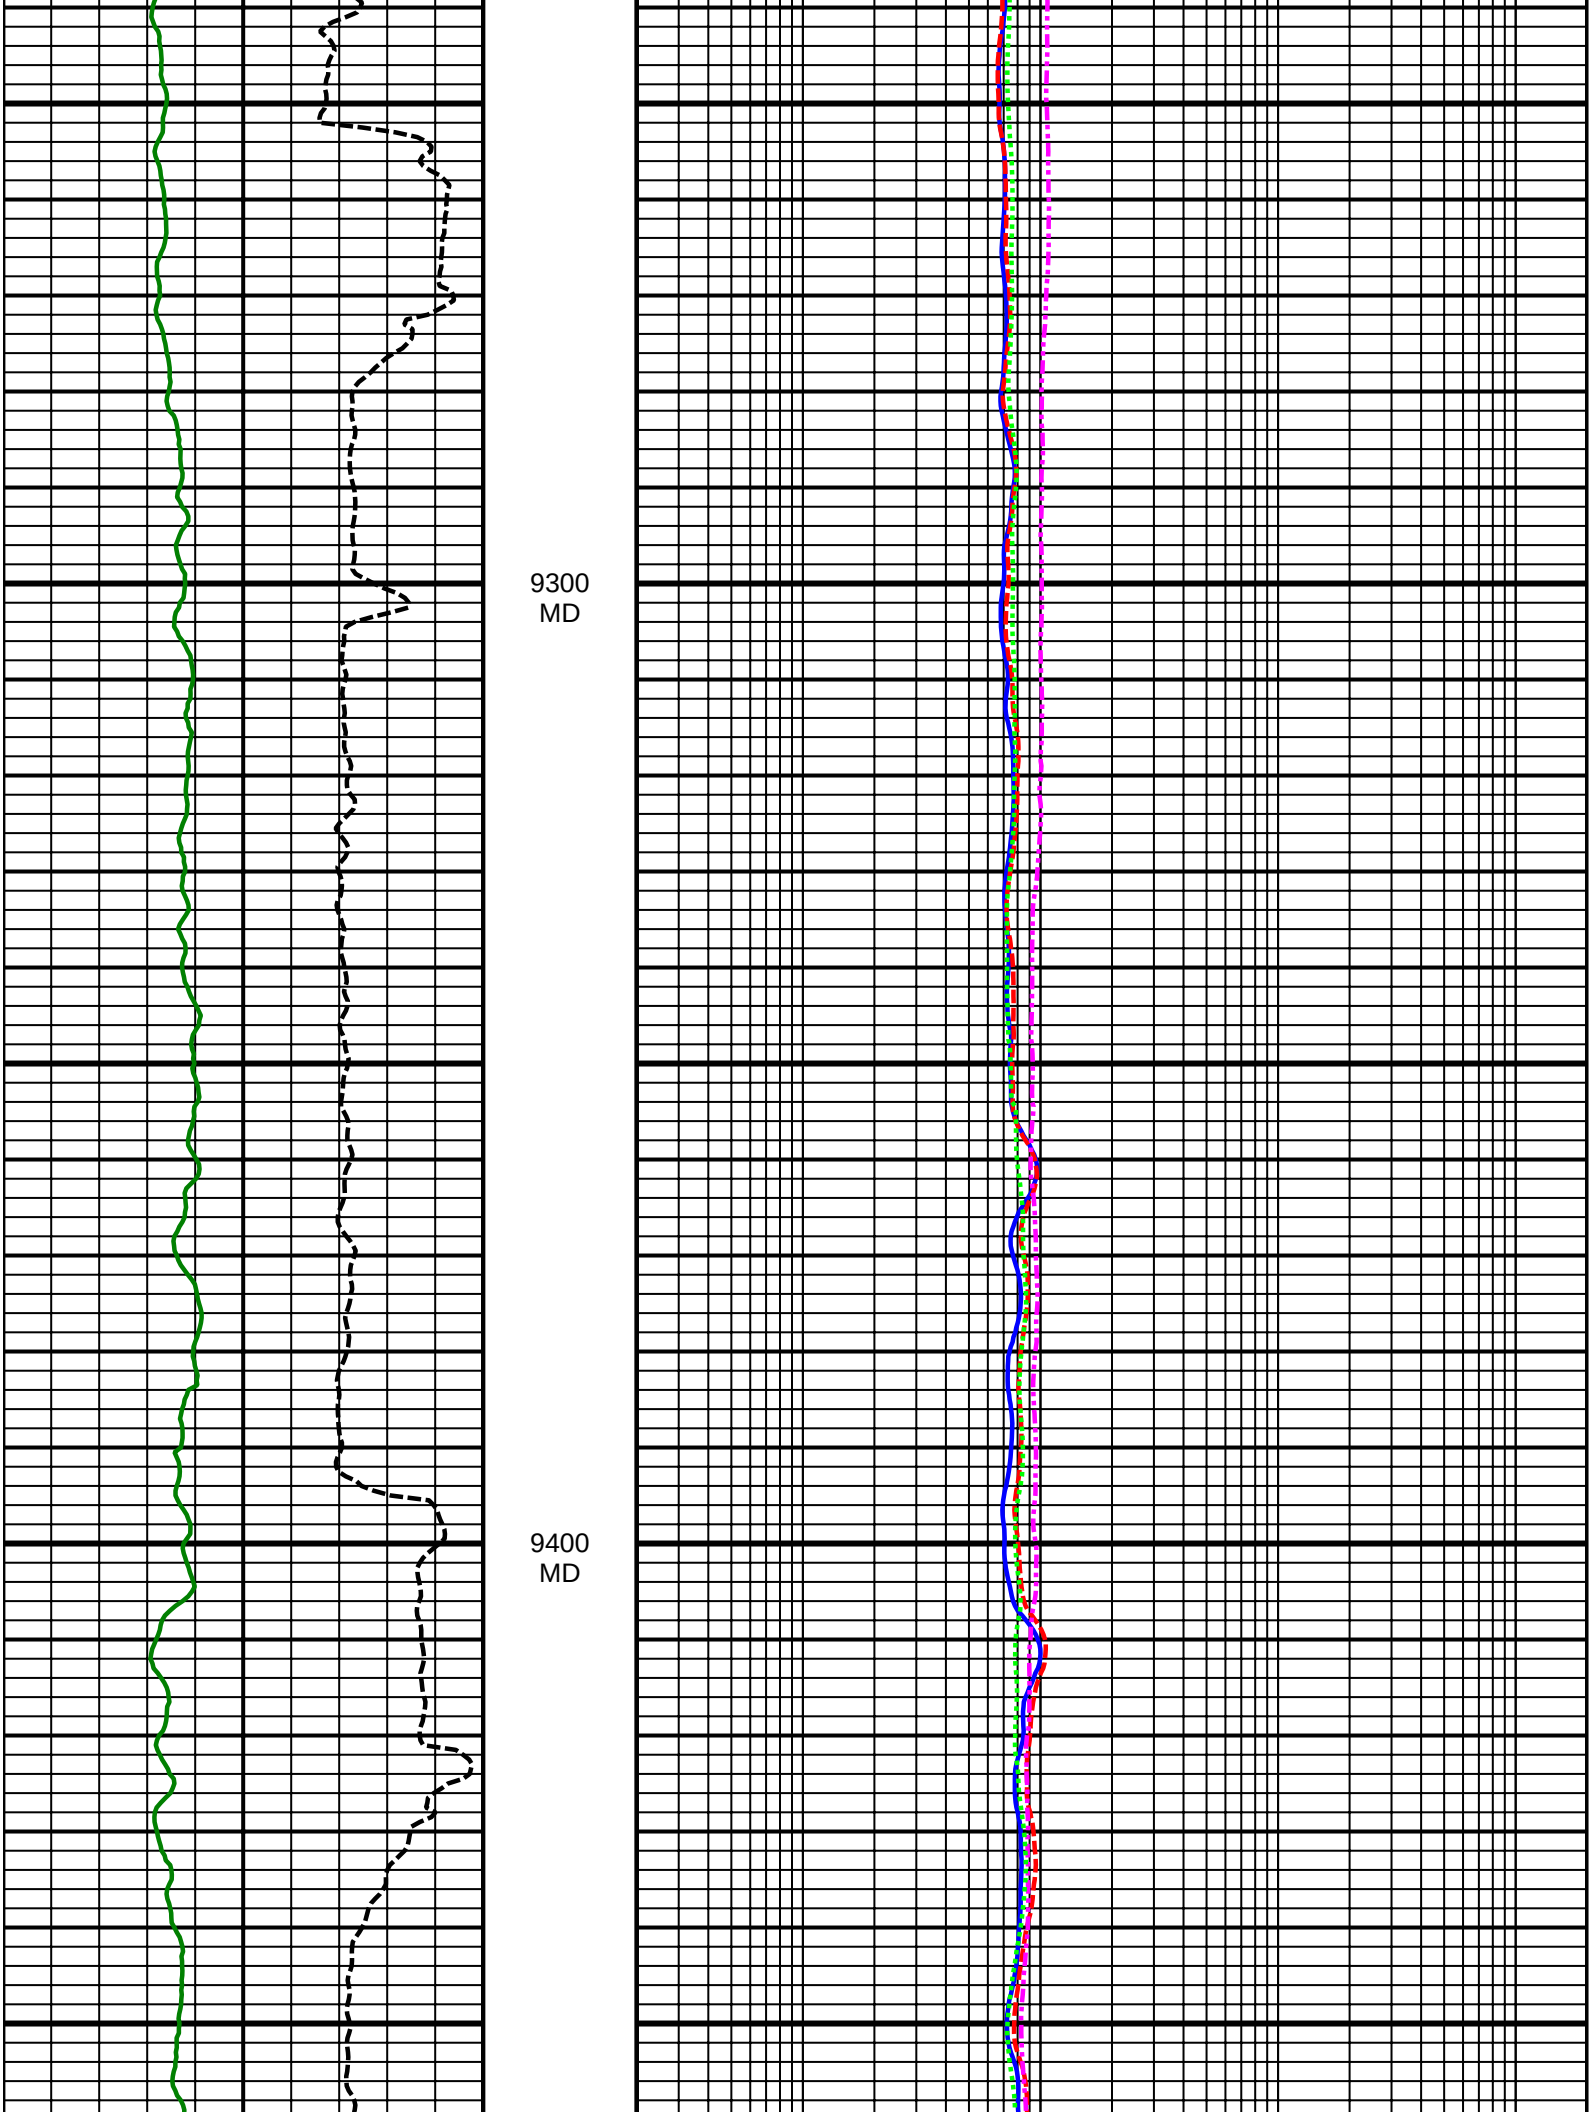
9300
MD
9400
MD

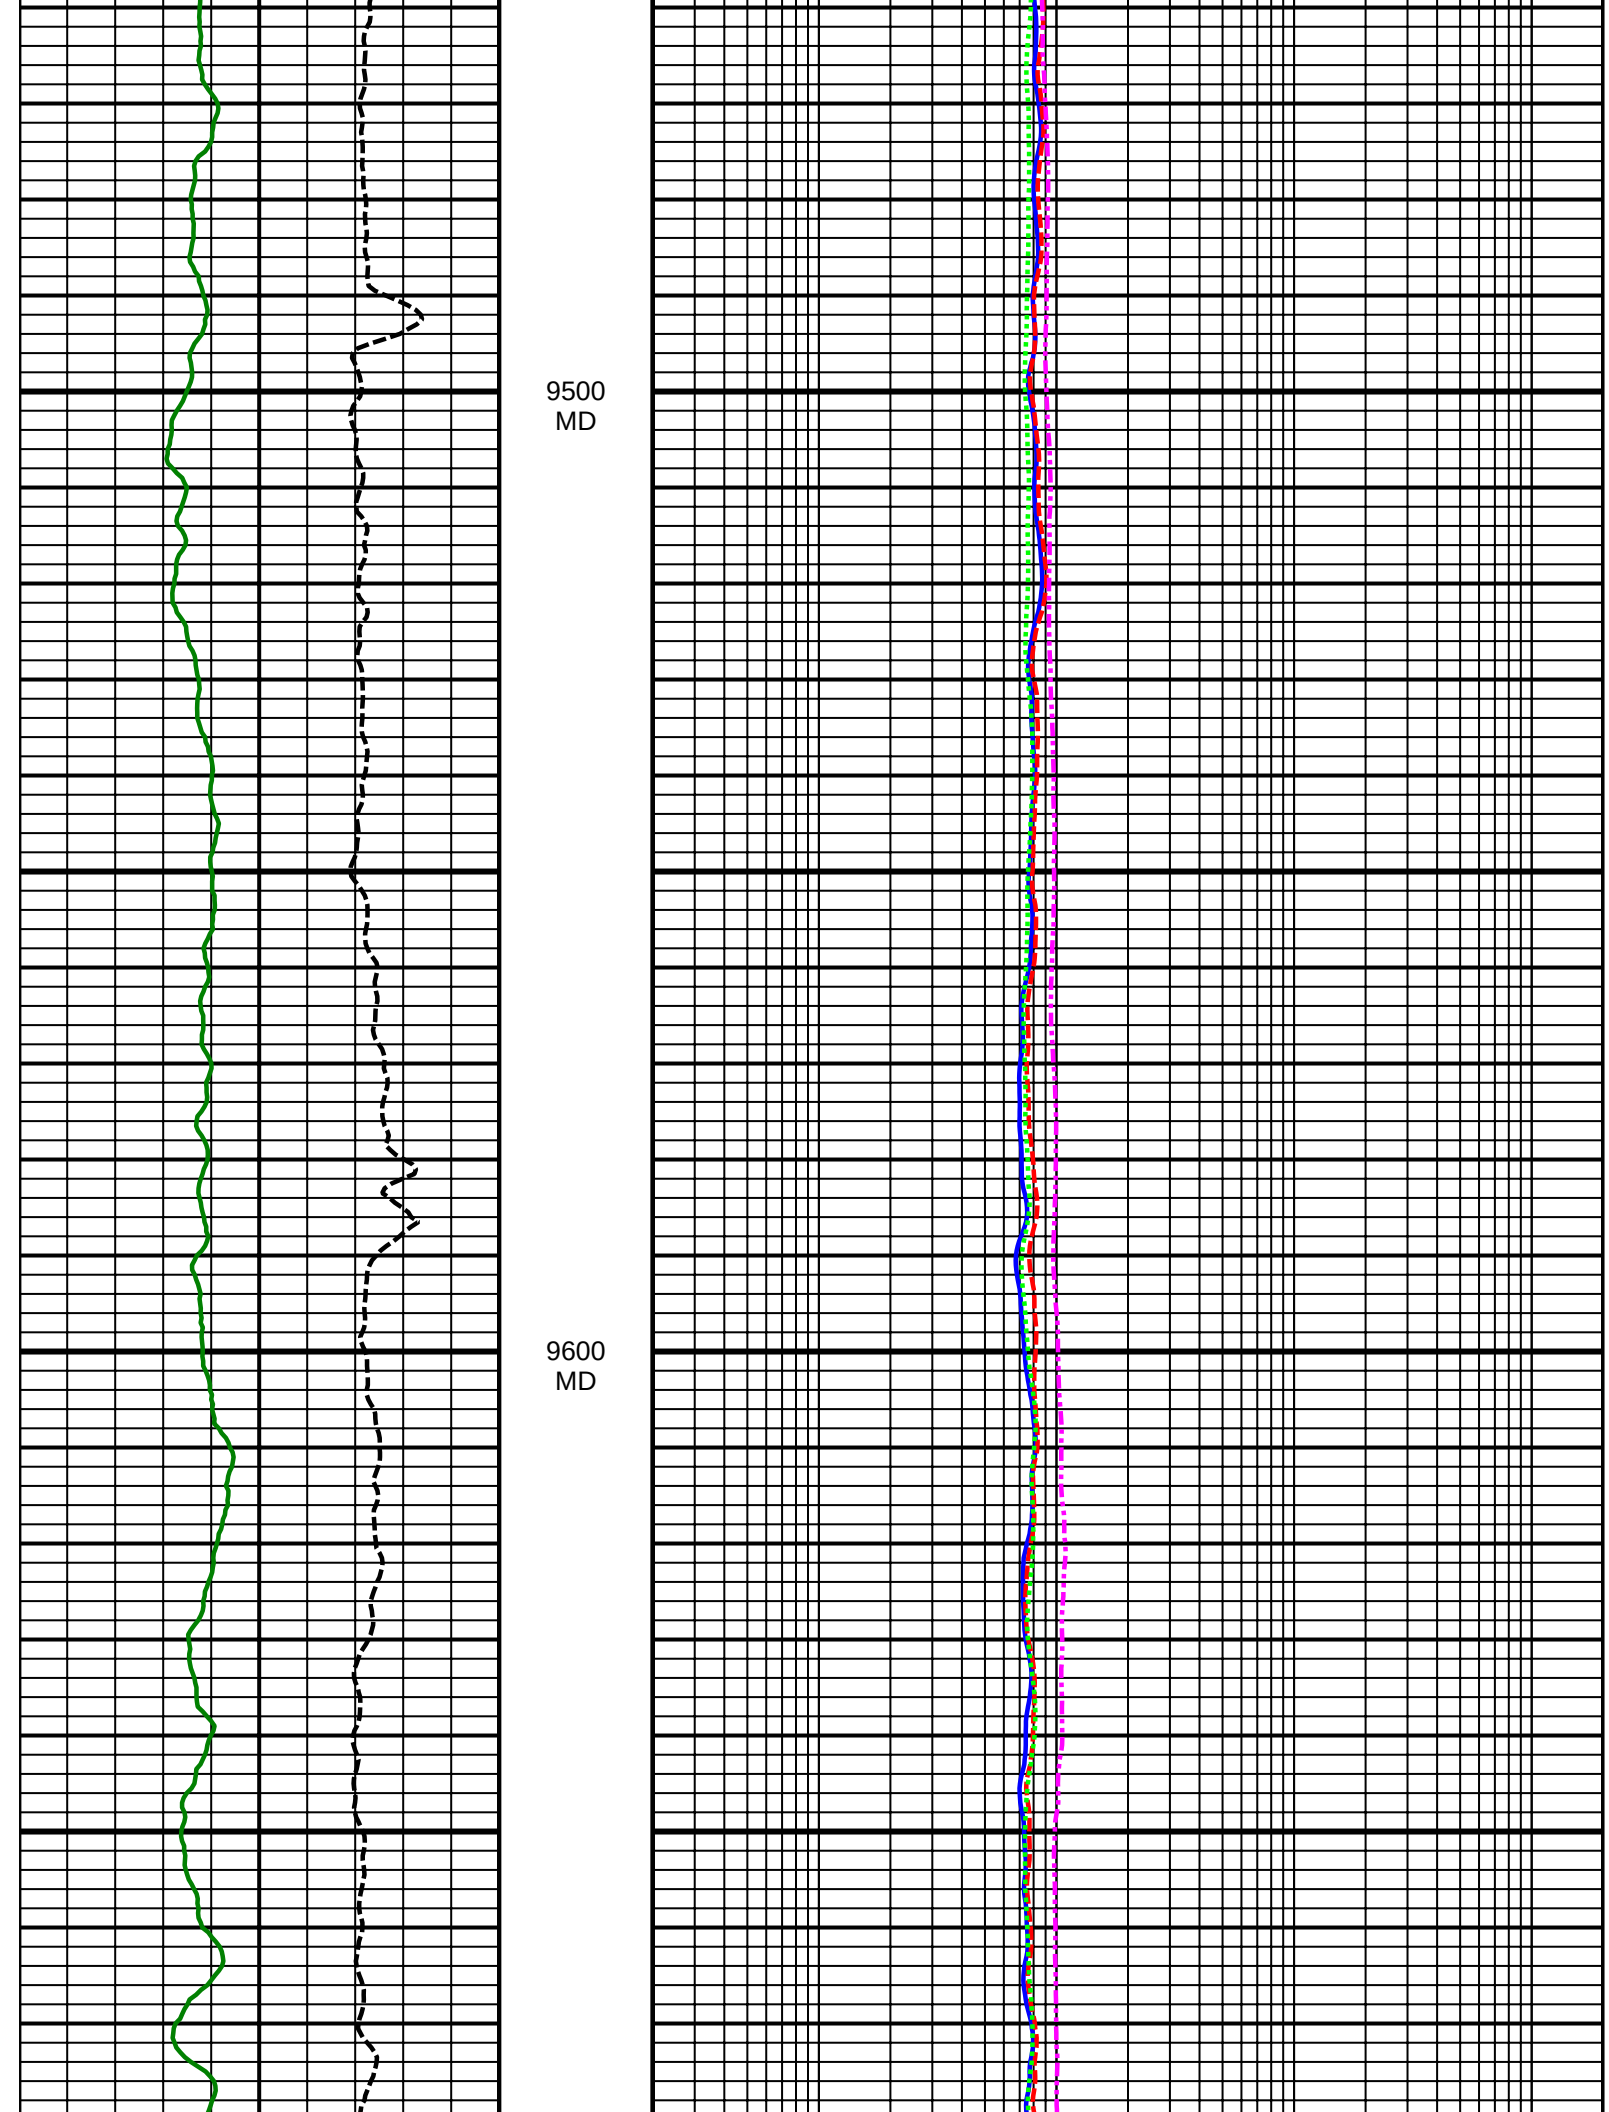
9500
MD
9600
MD

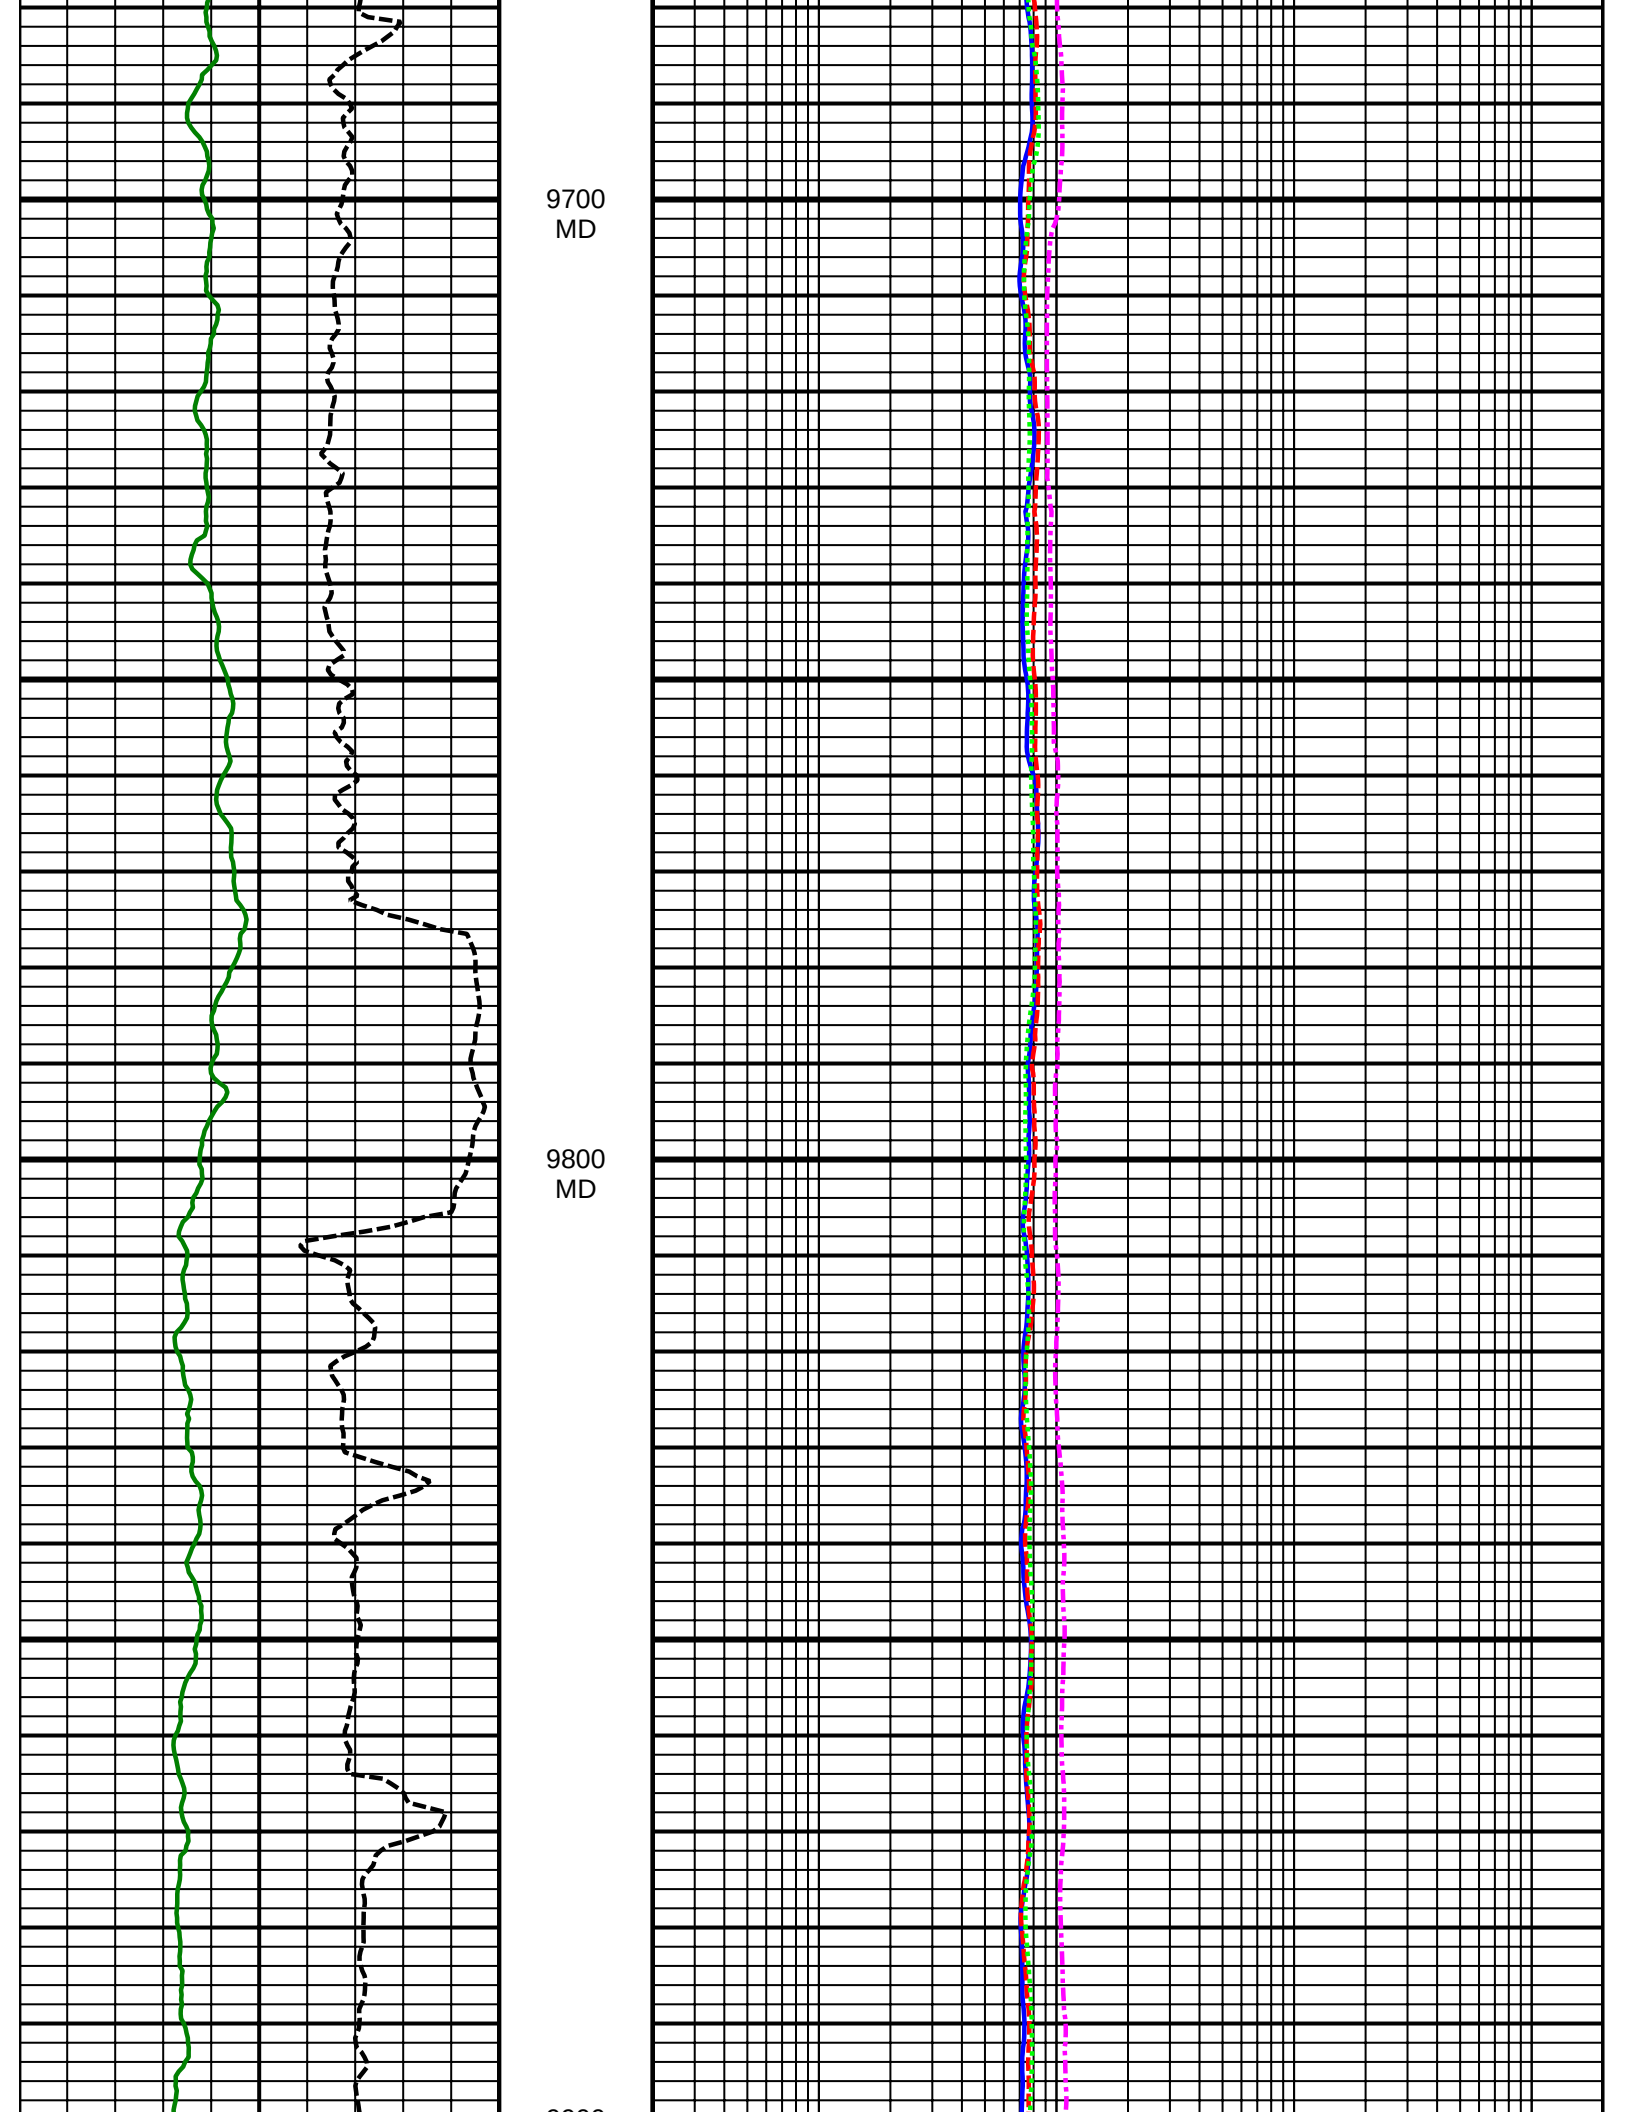
9700
MD
9800
MD

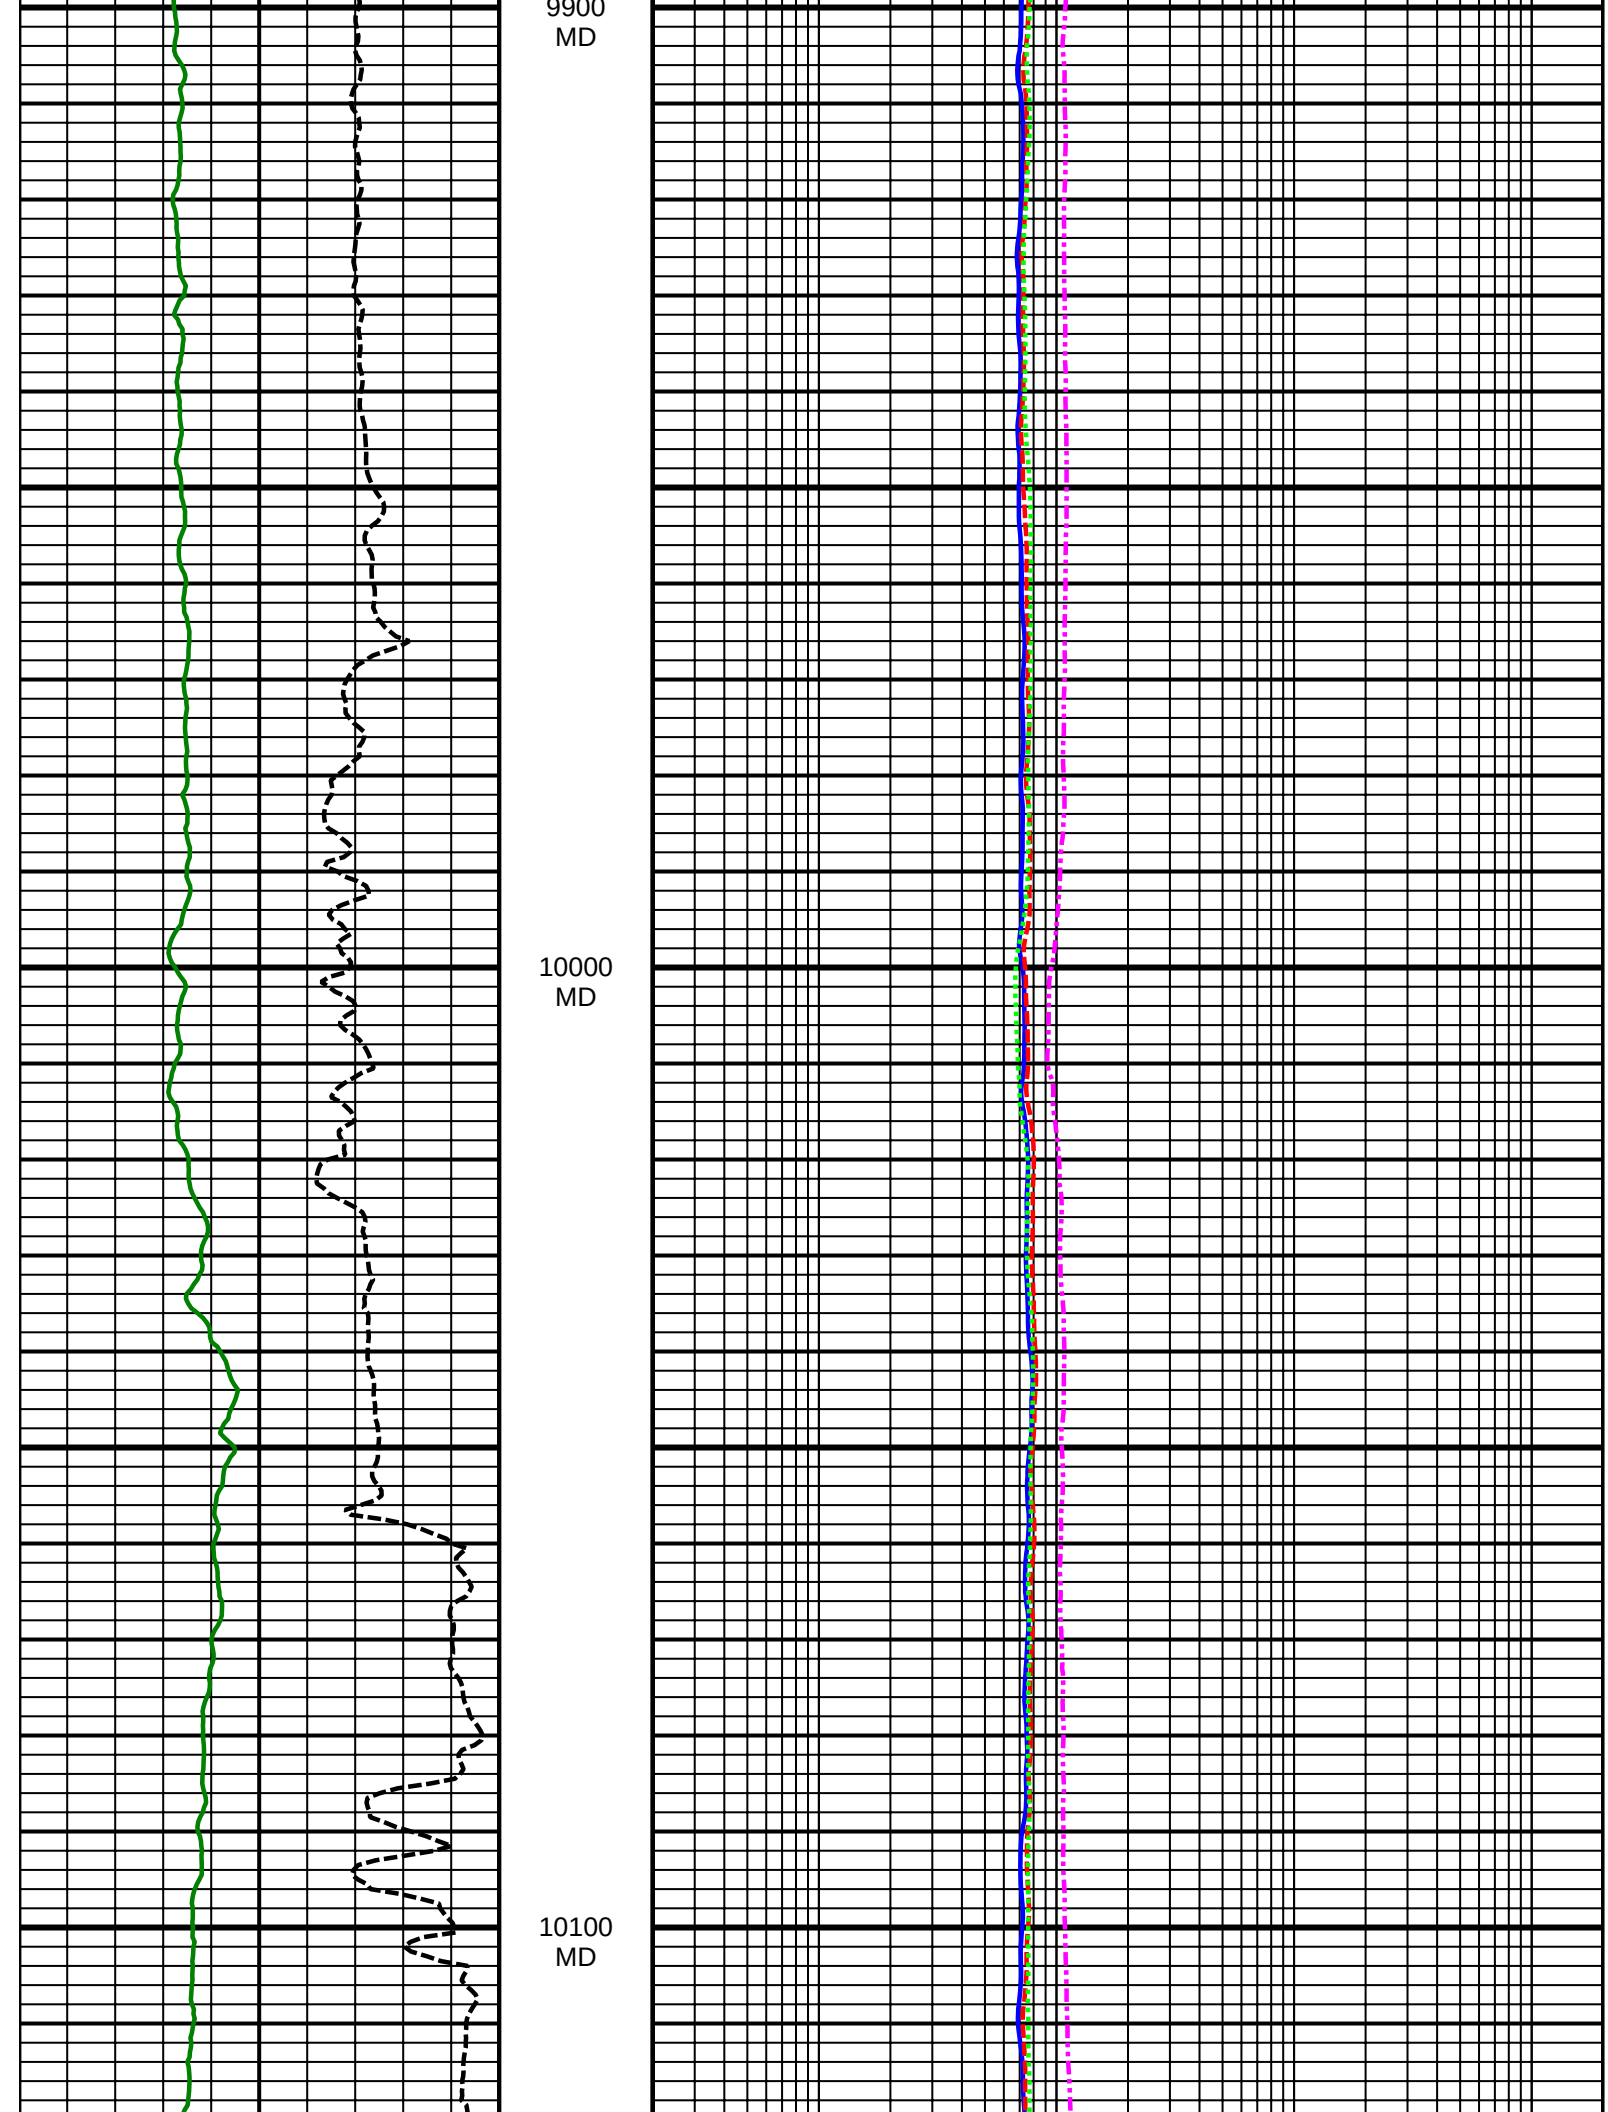
9900
MD
10000
MD
10100
MD

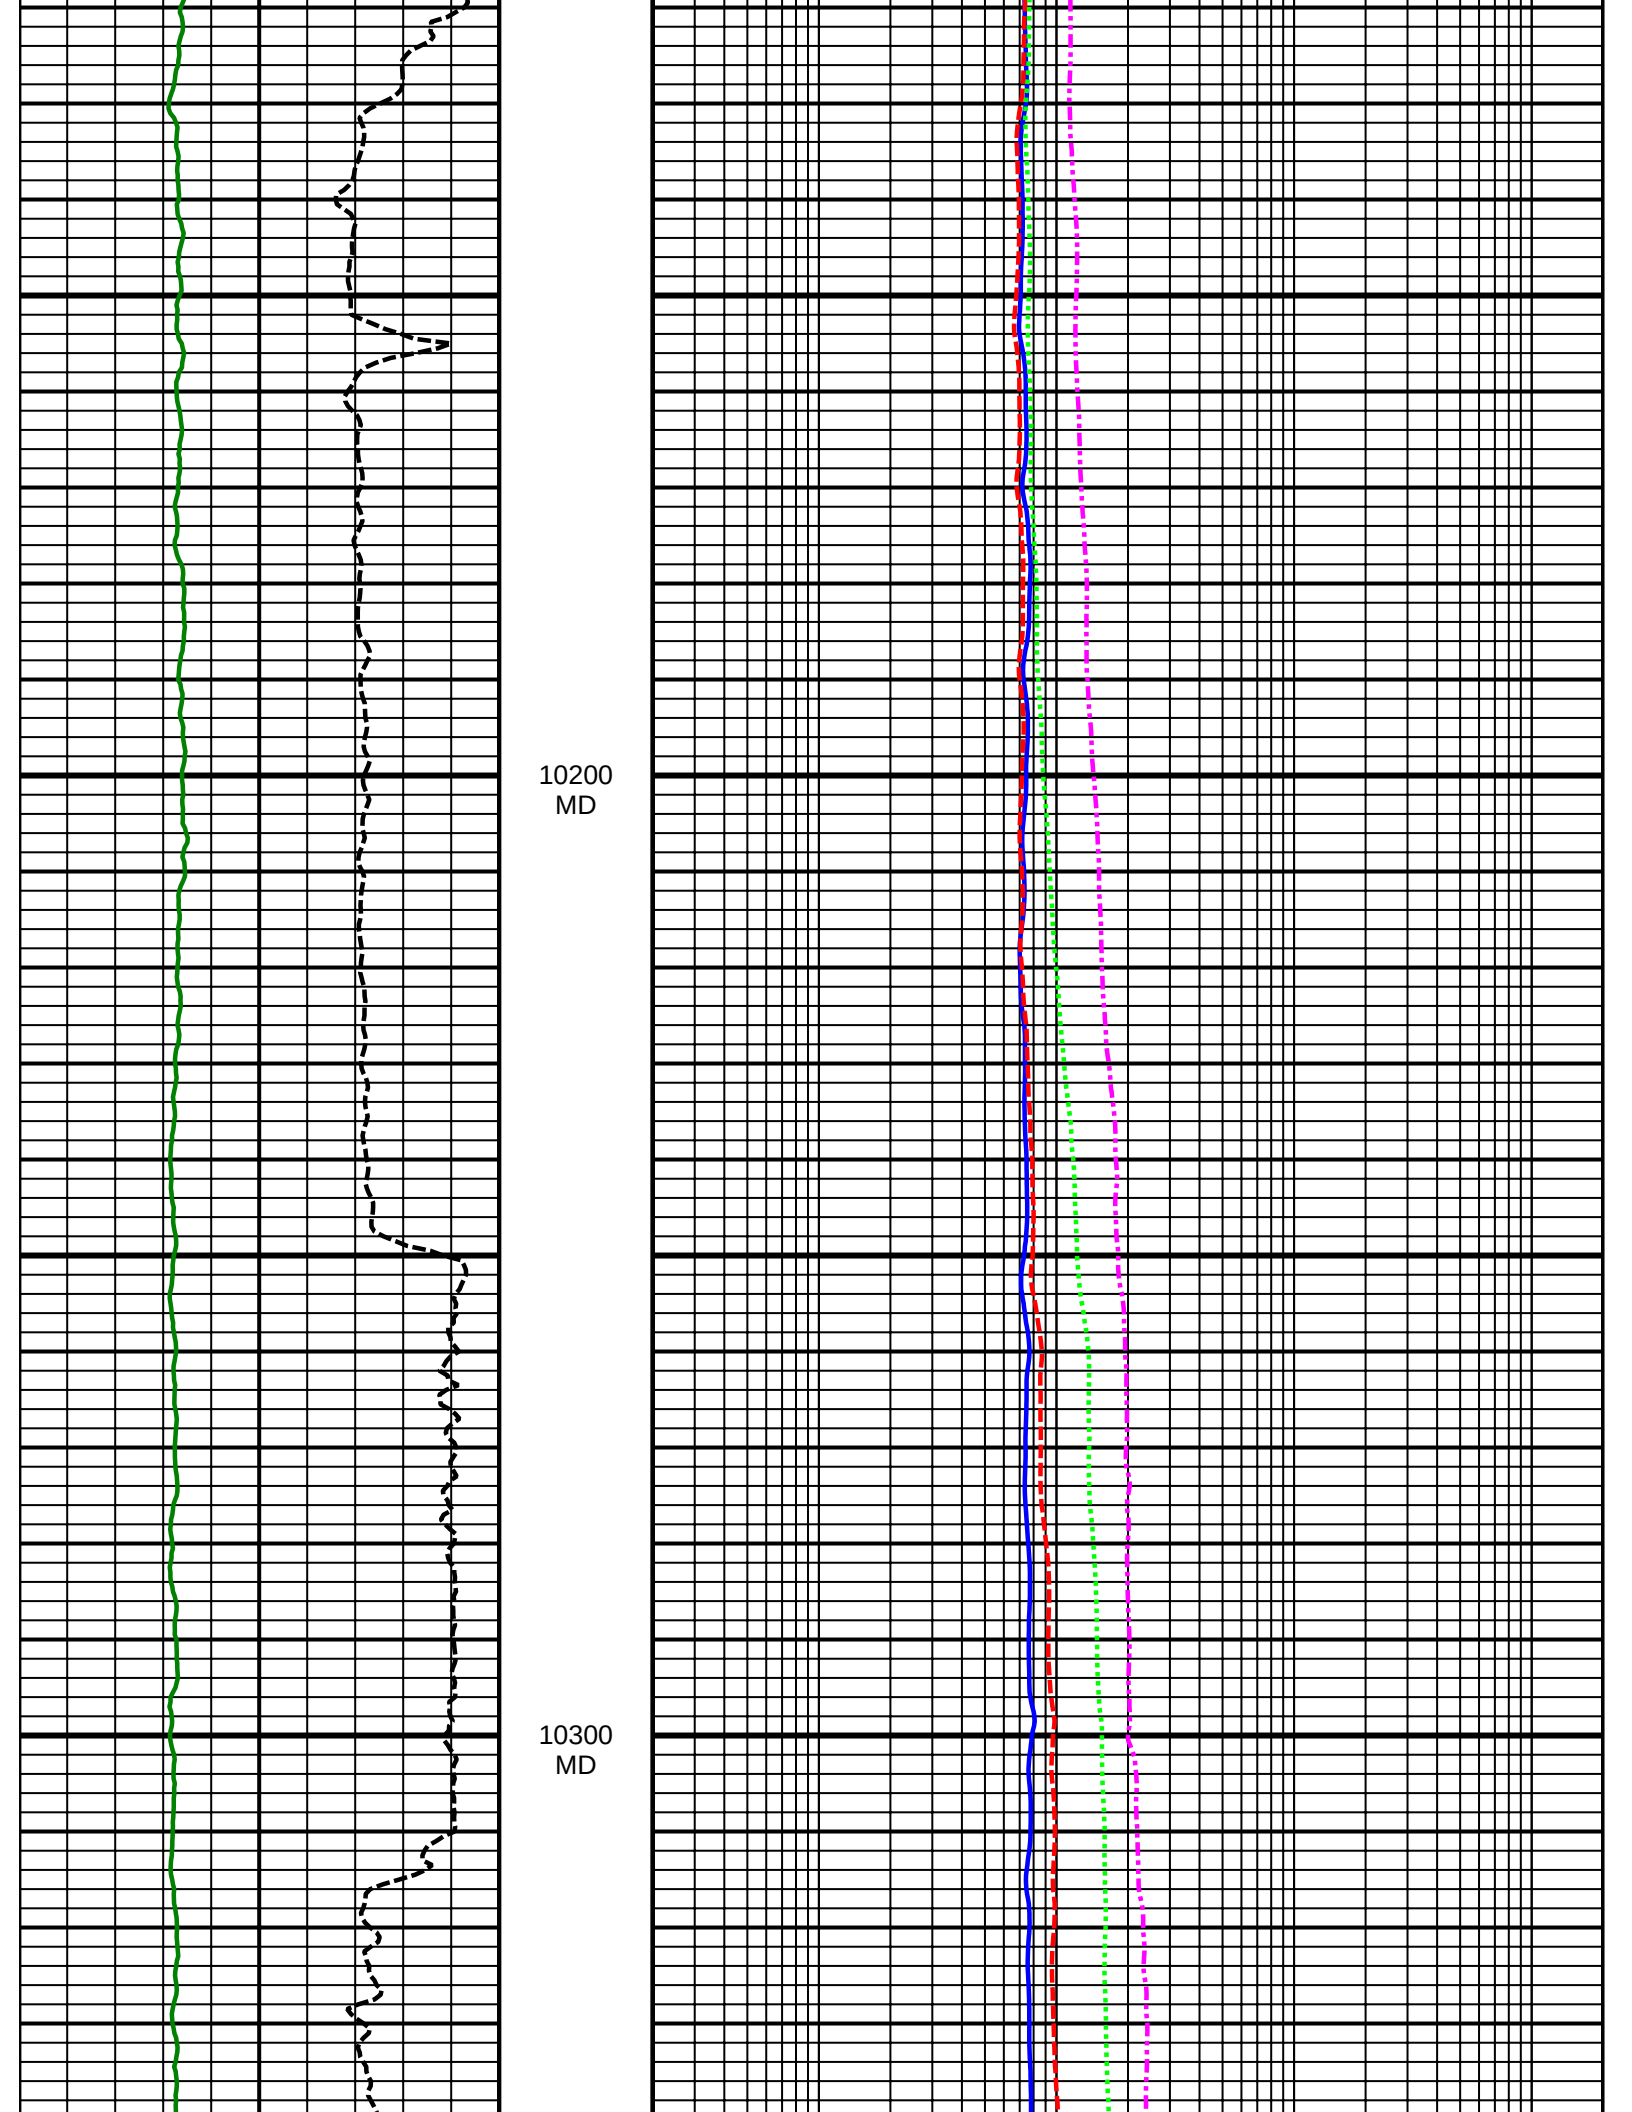
10200
MD
10300
MD

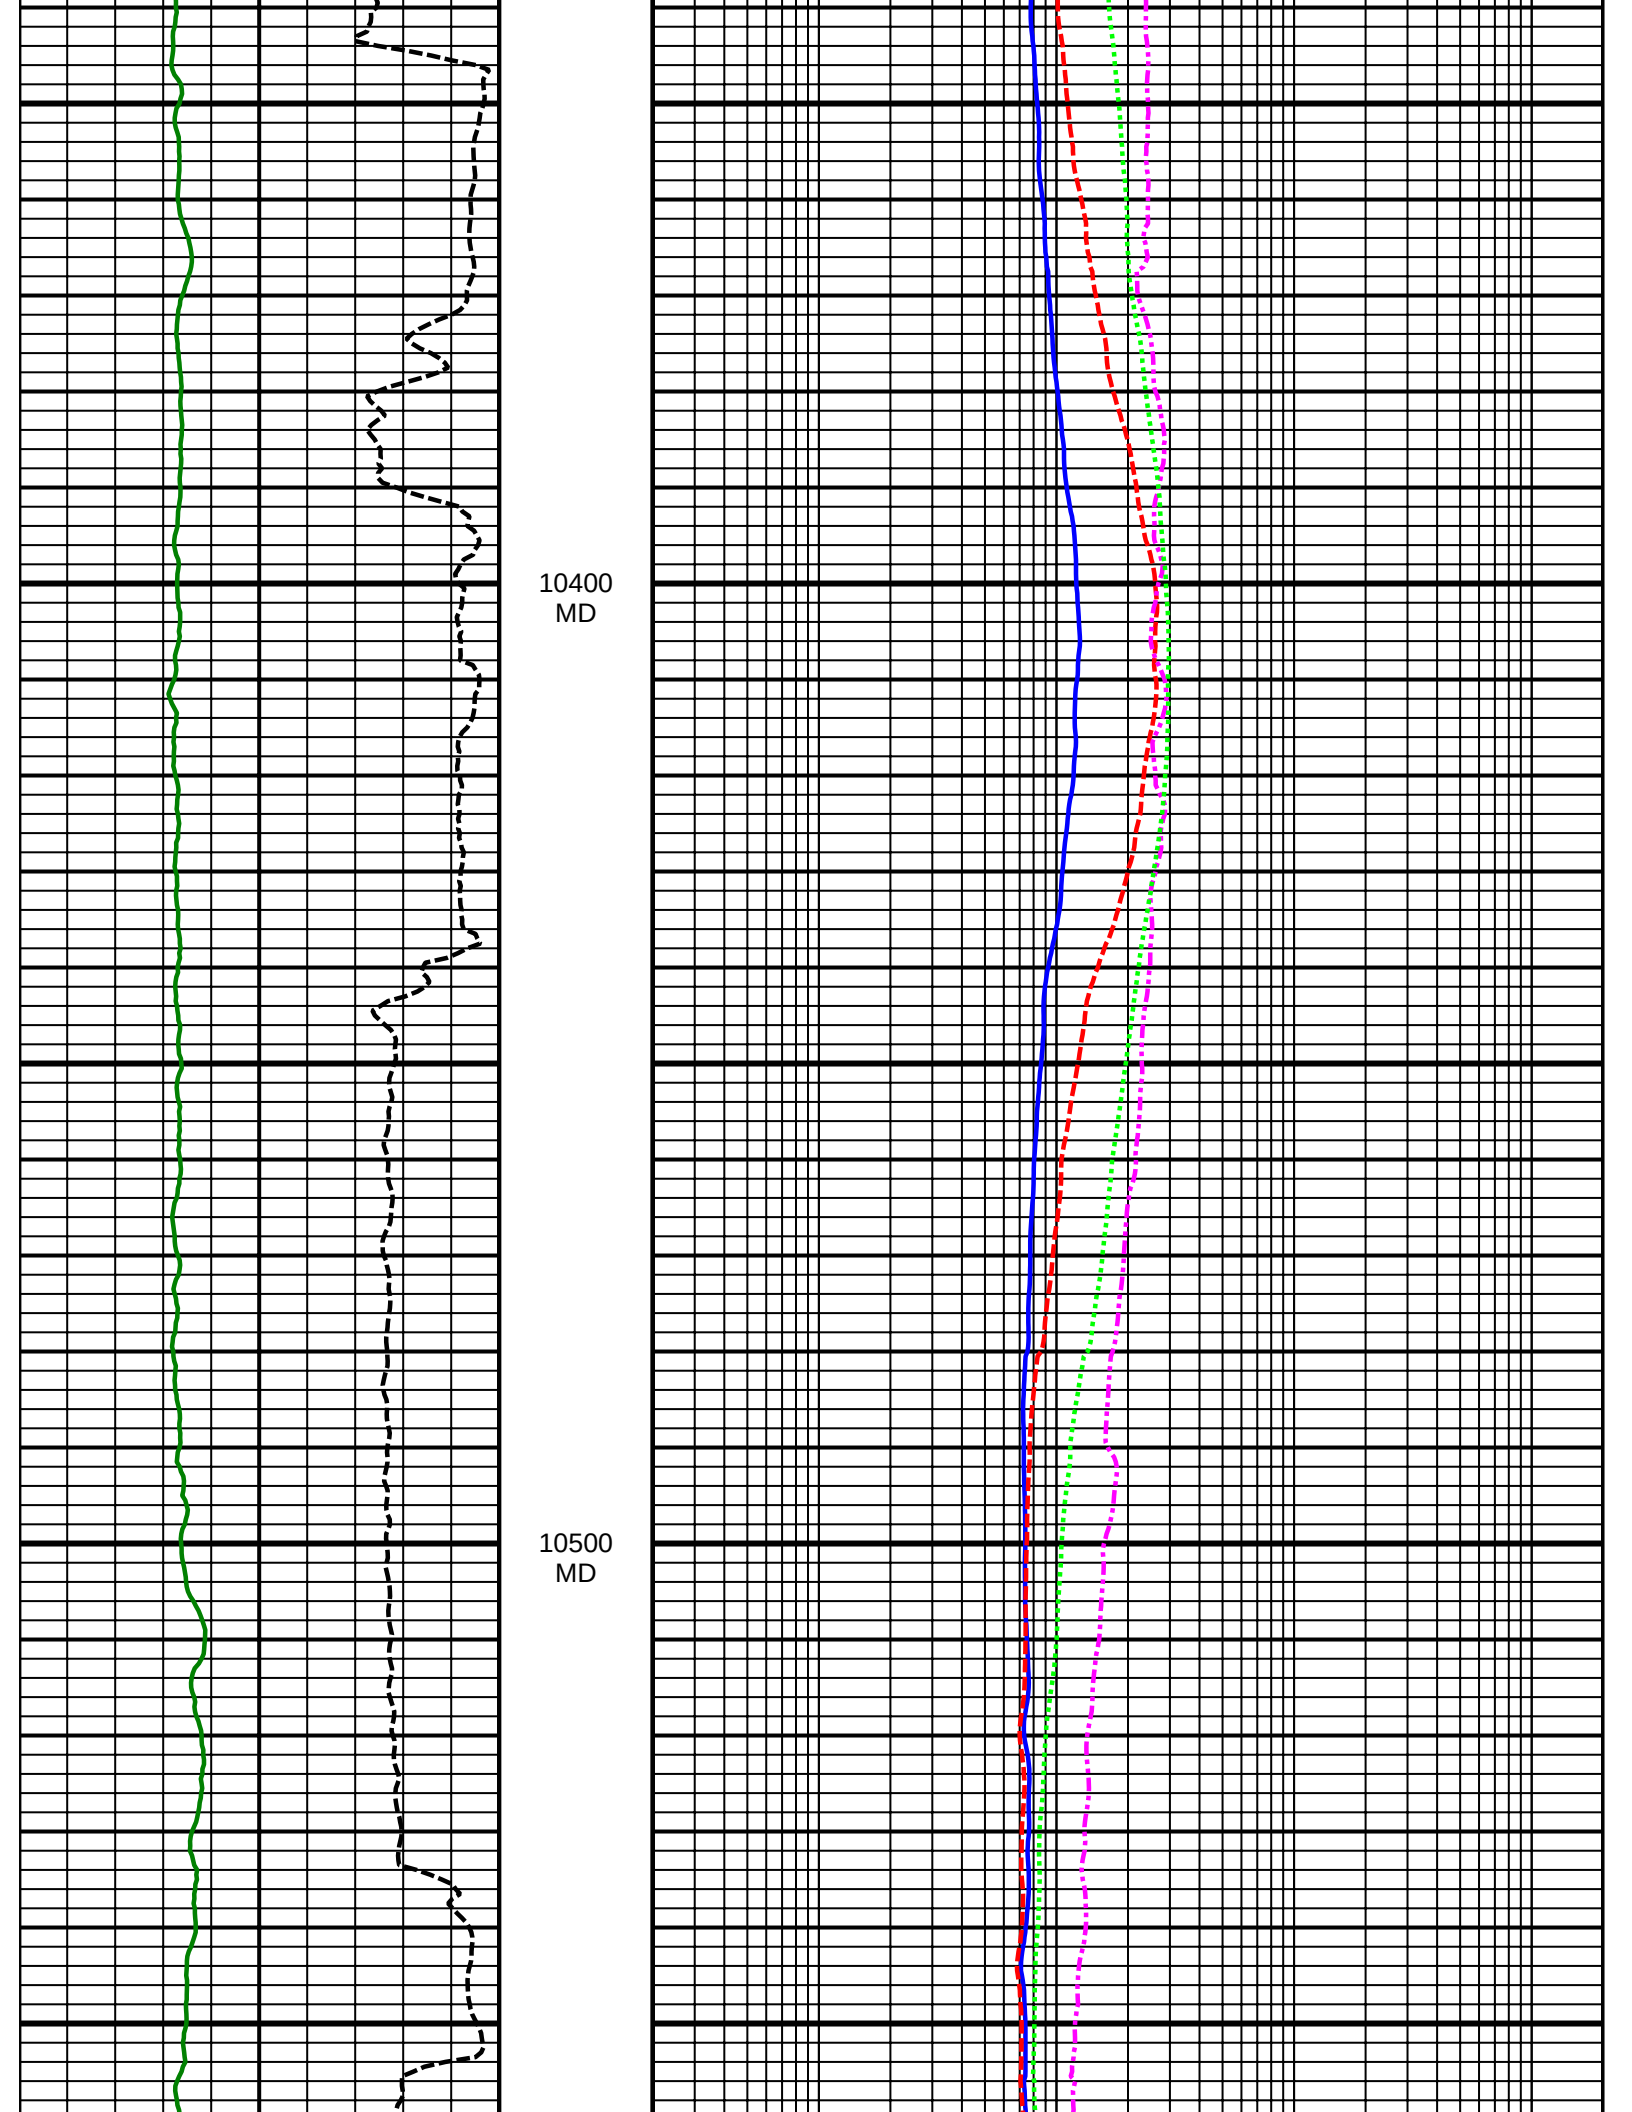
10400
MD
10500
MD

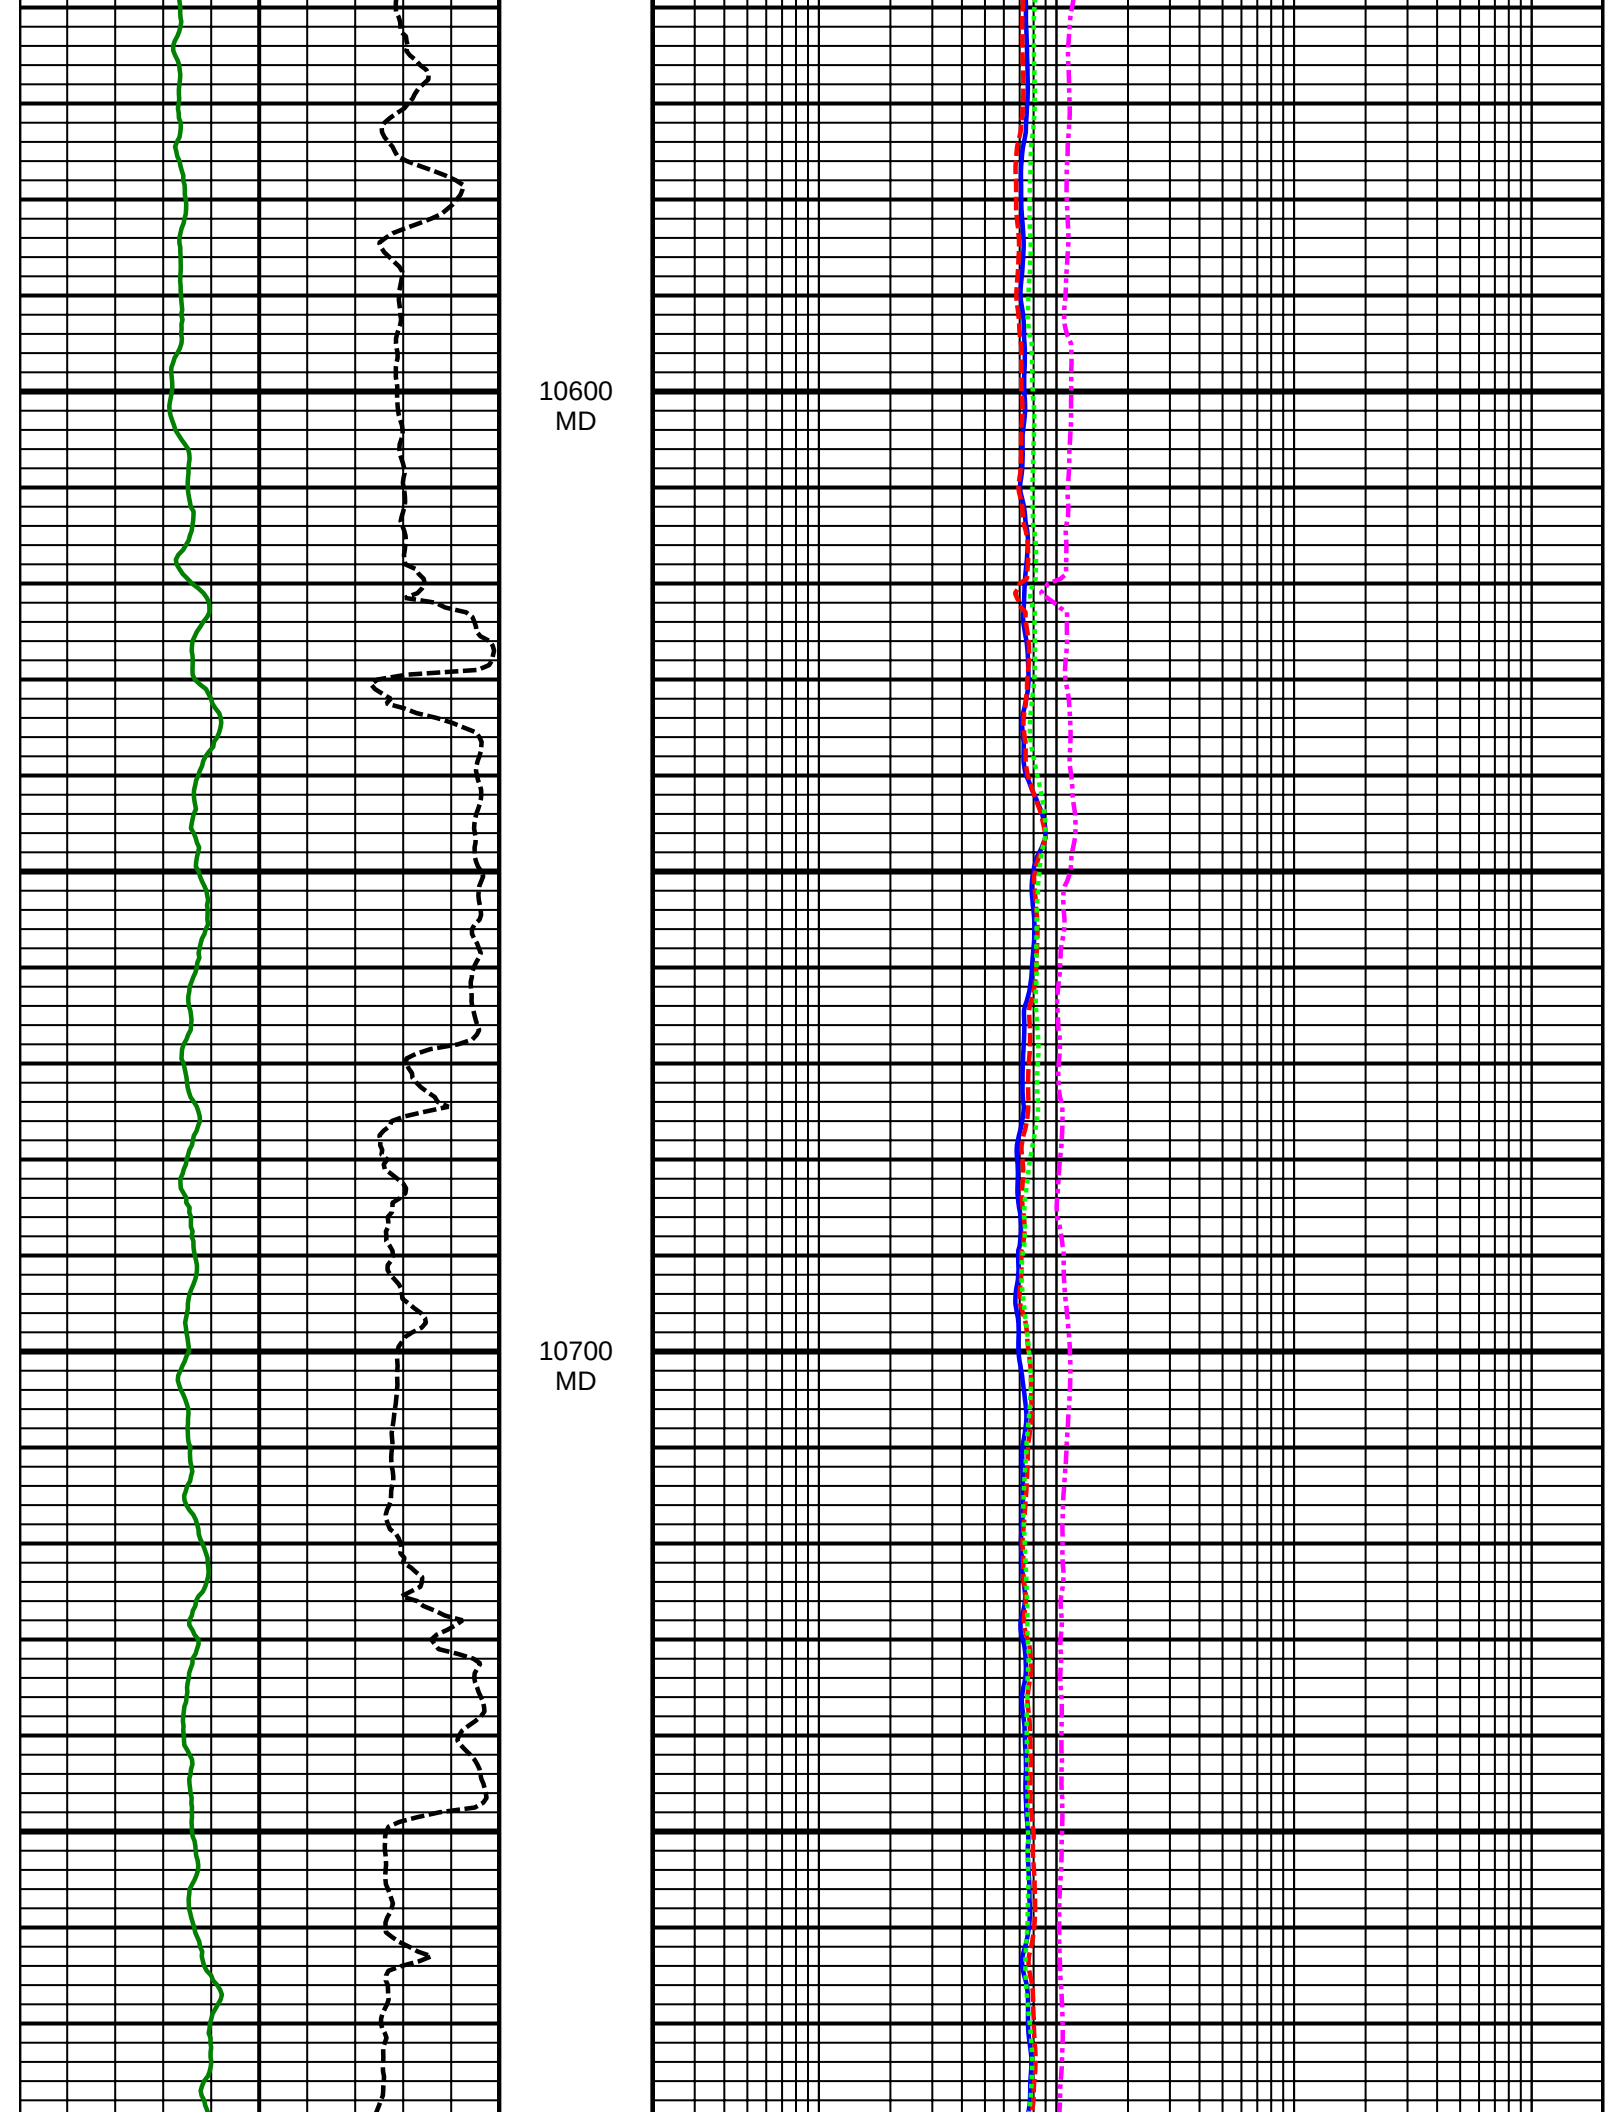
10600
MD
10700
MD

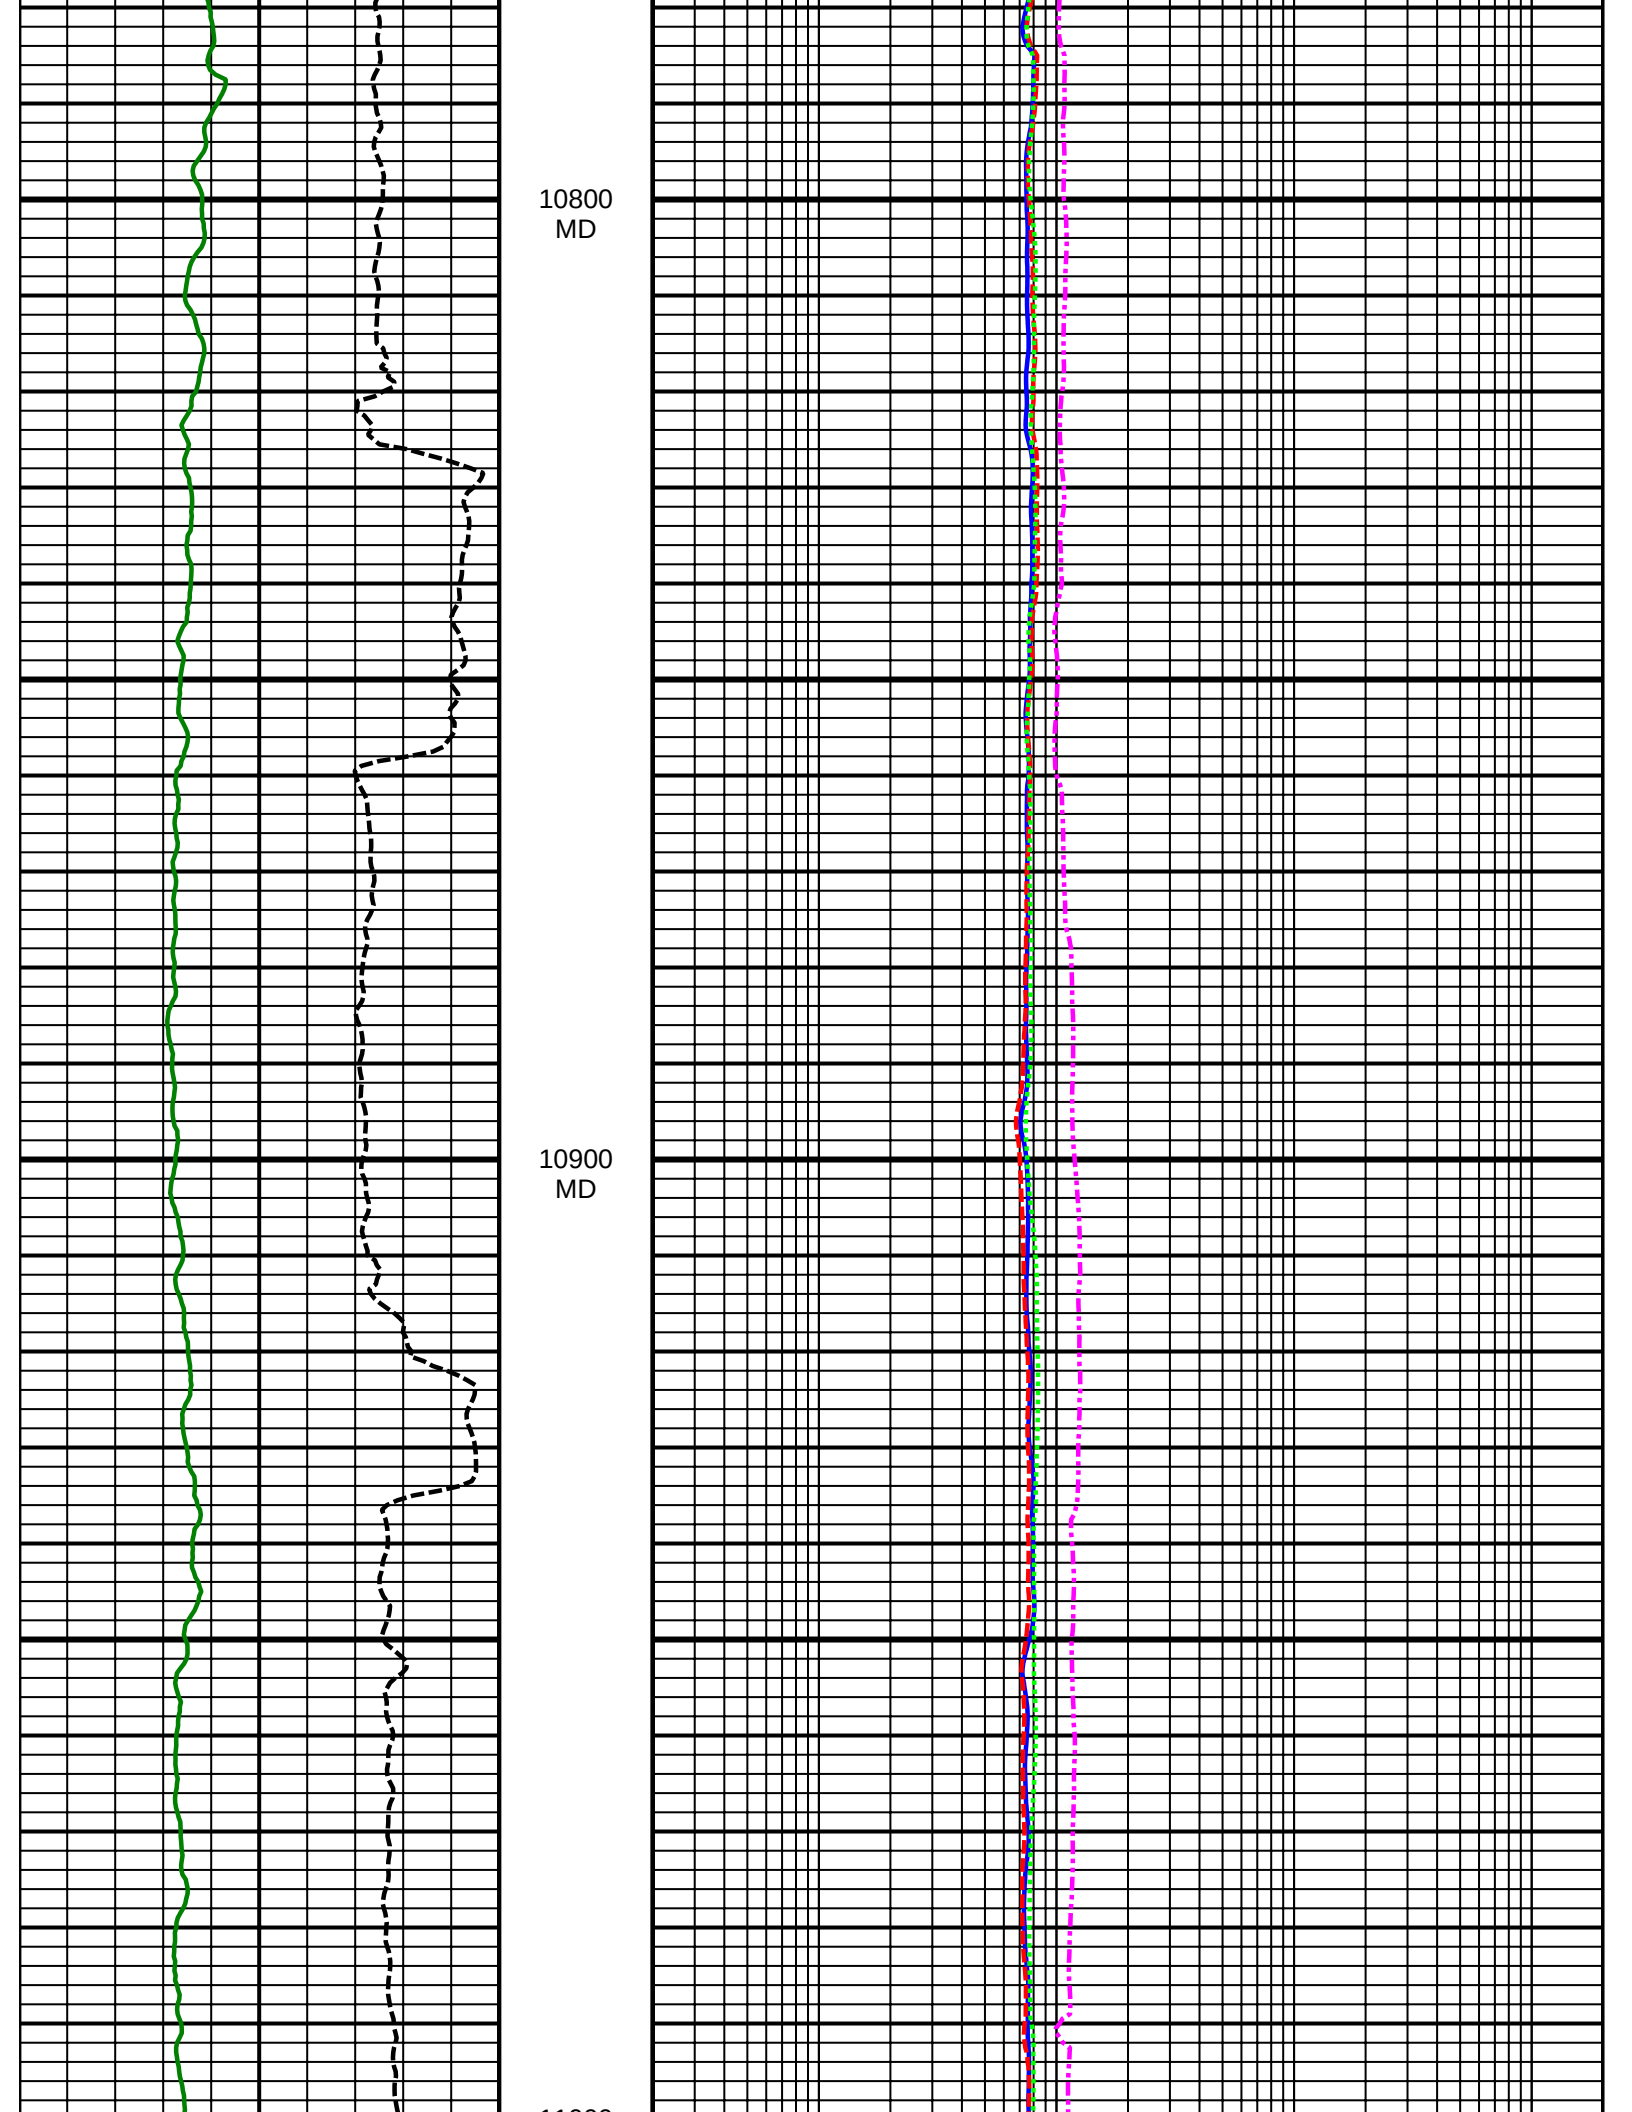
10800
MD
10900
MD

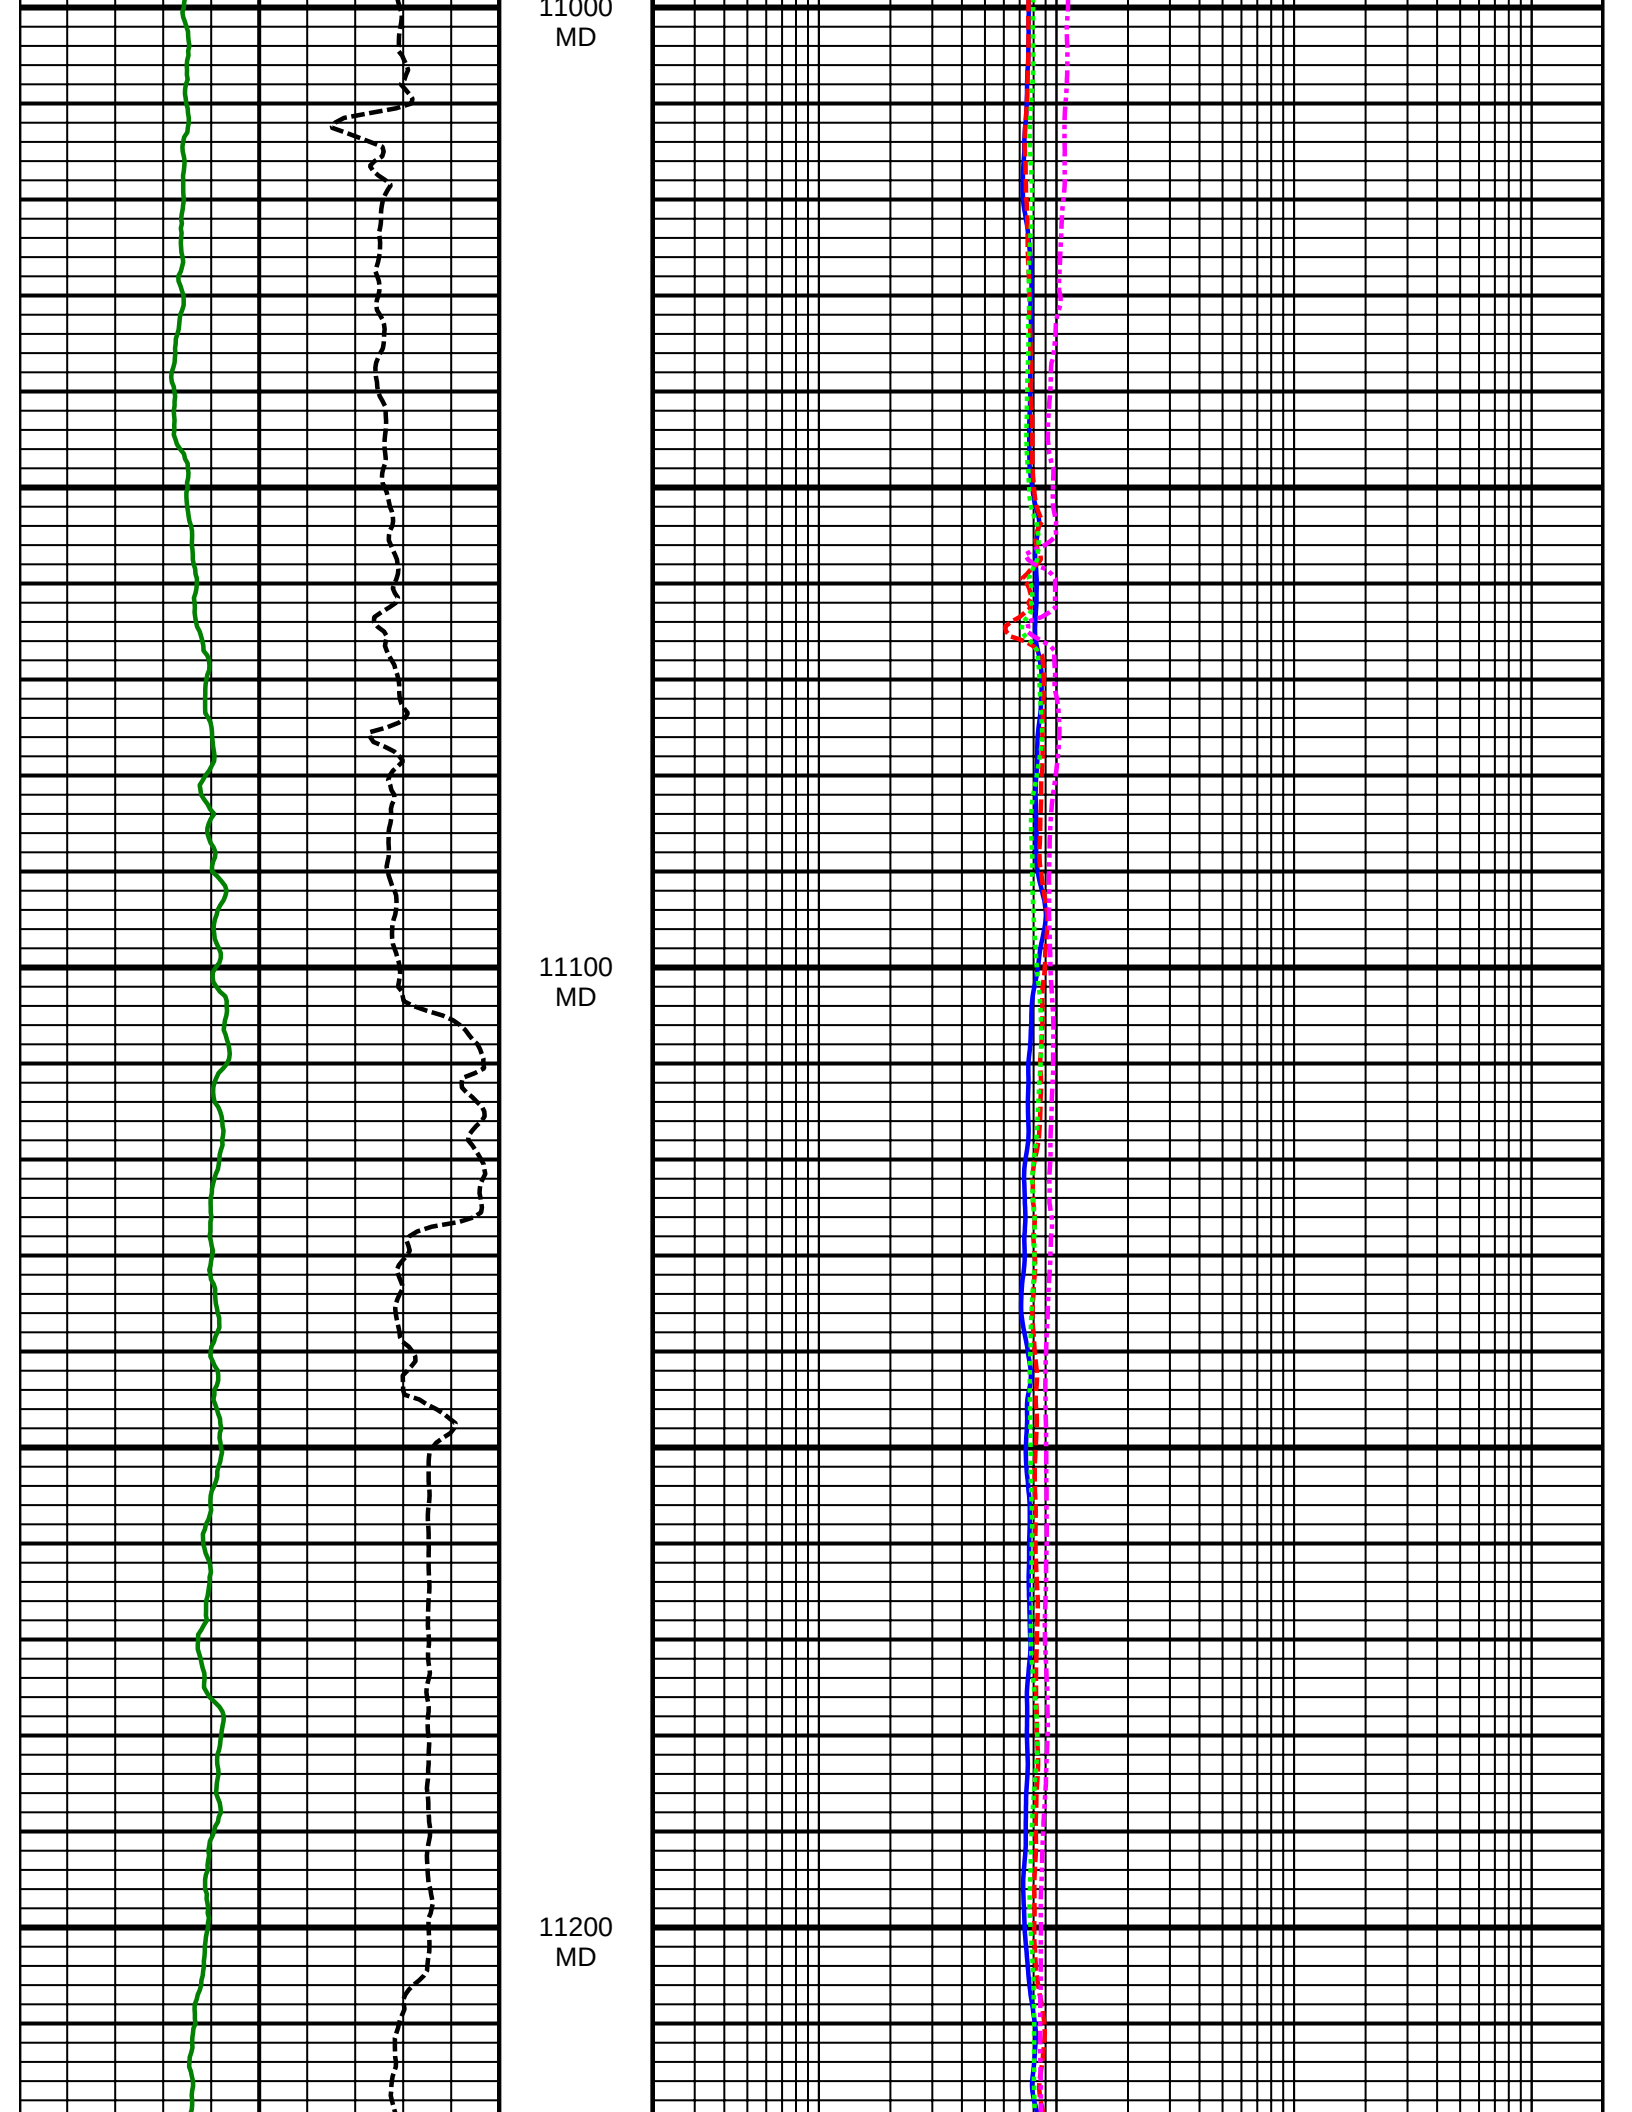
11000
MD
11100
MD
11200
MD

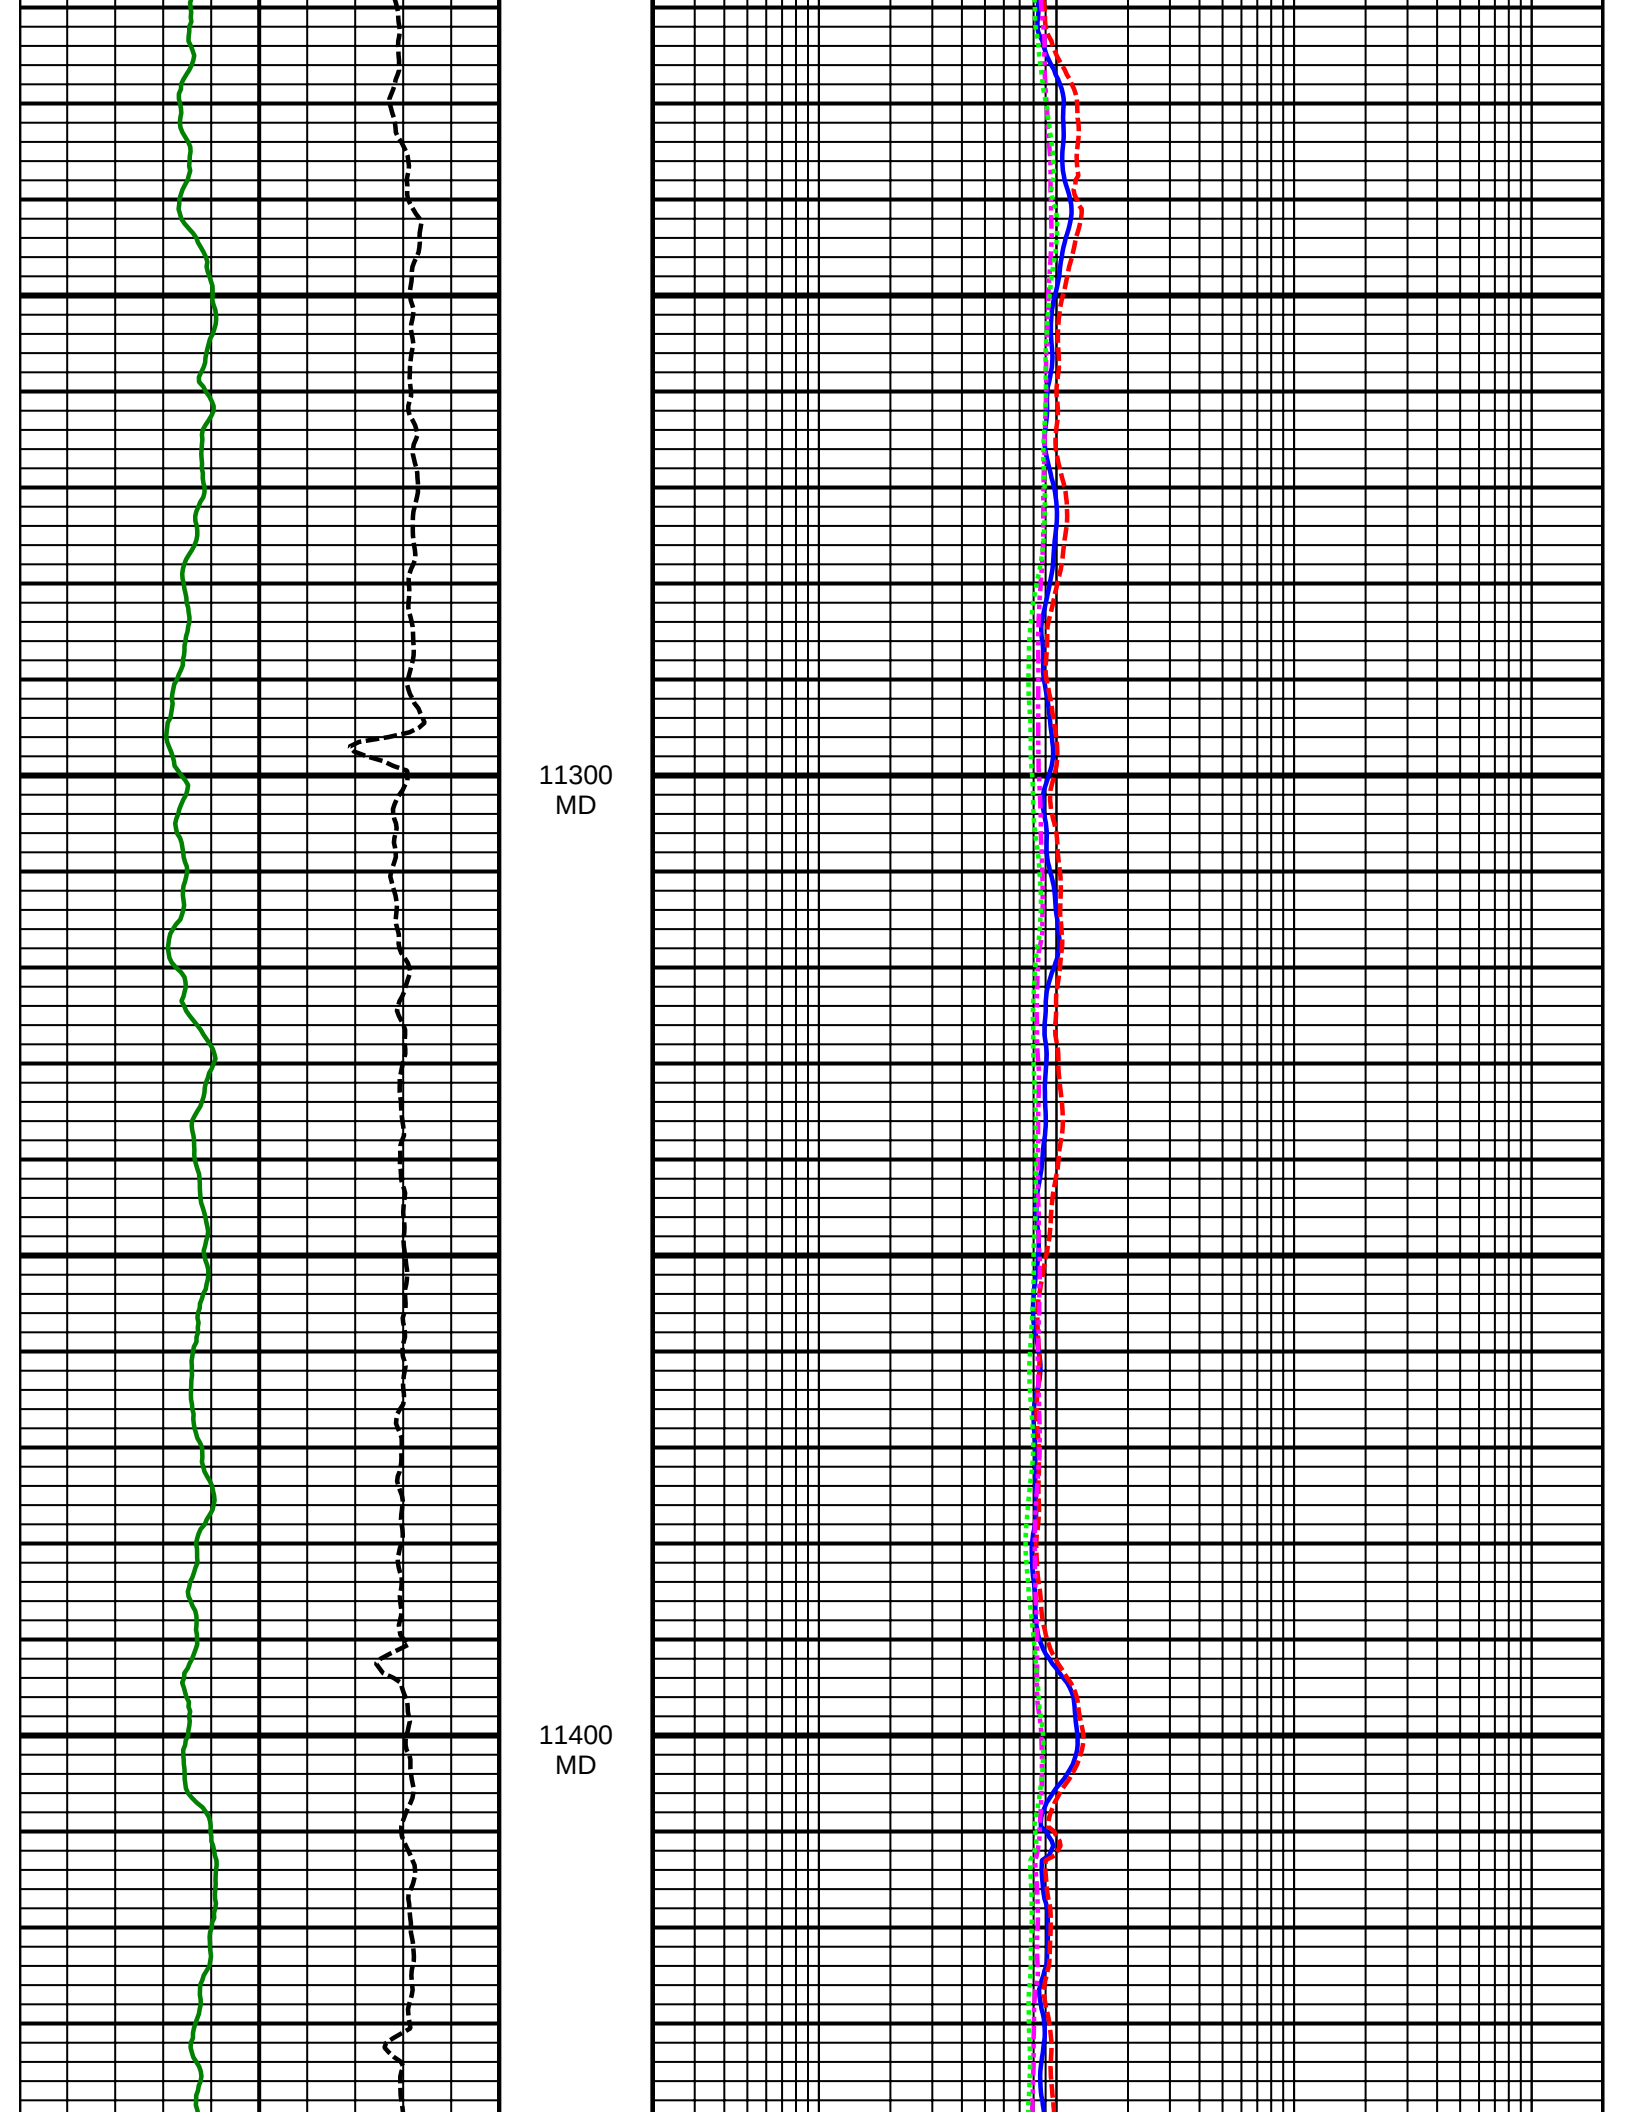
11300
MD
11400
MD

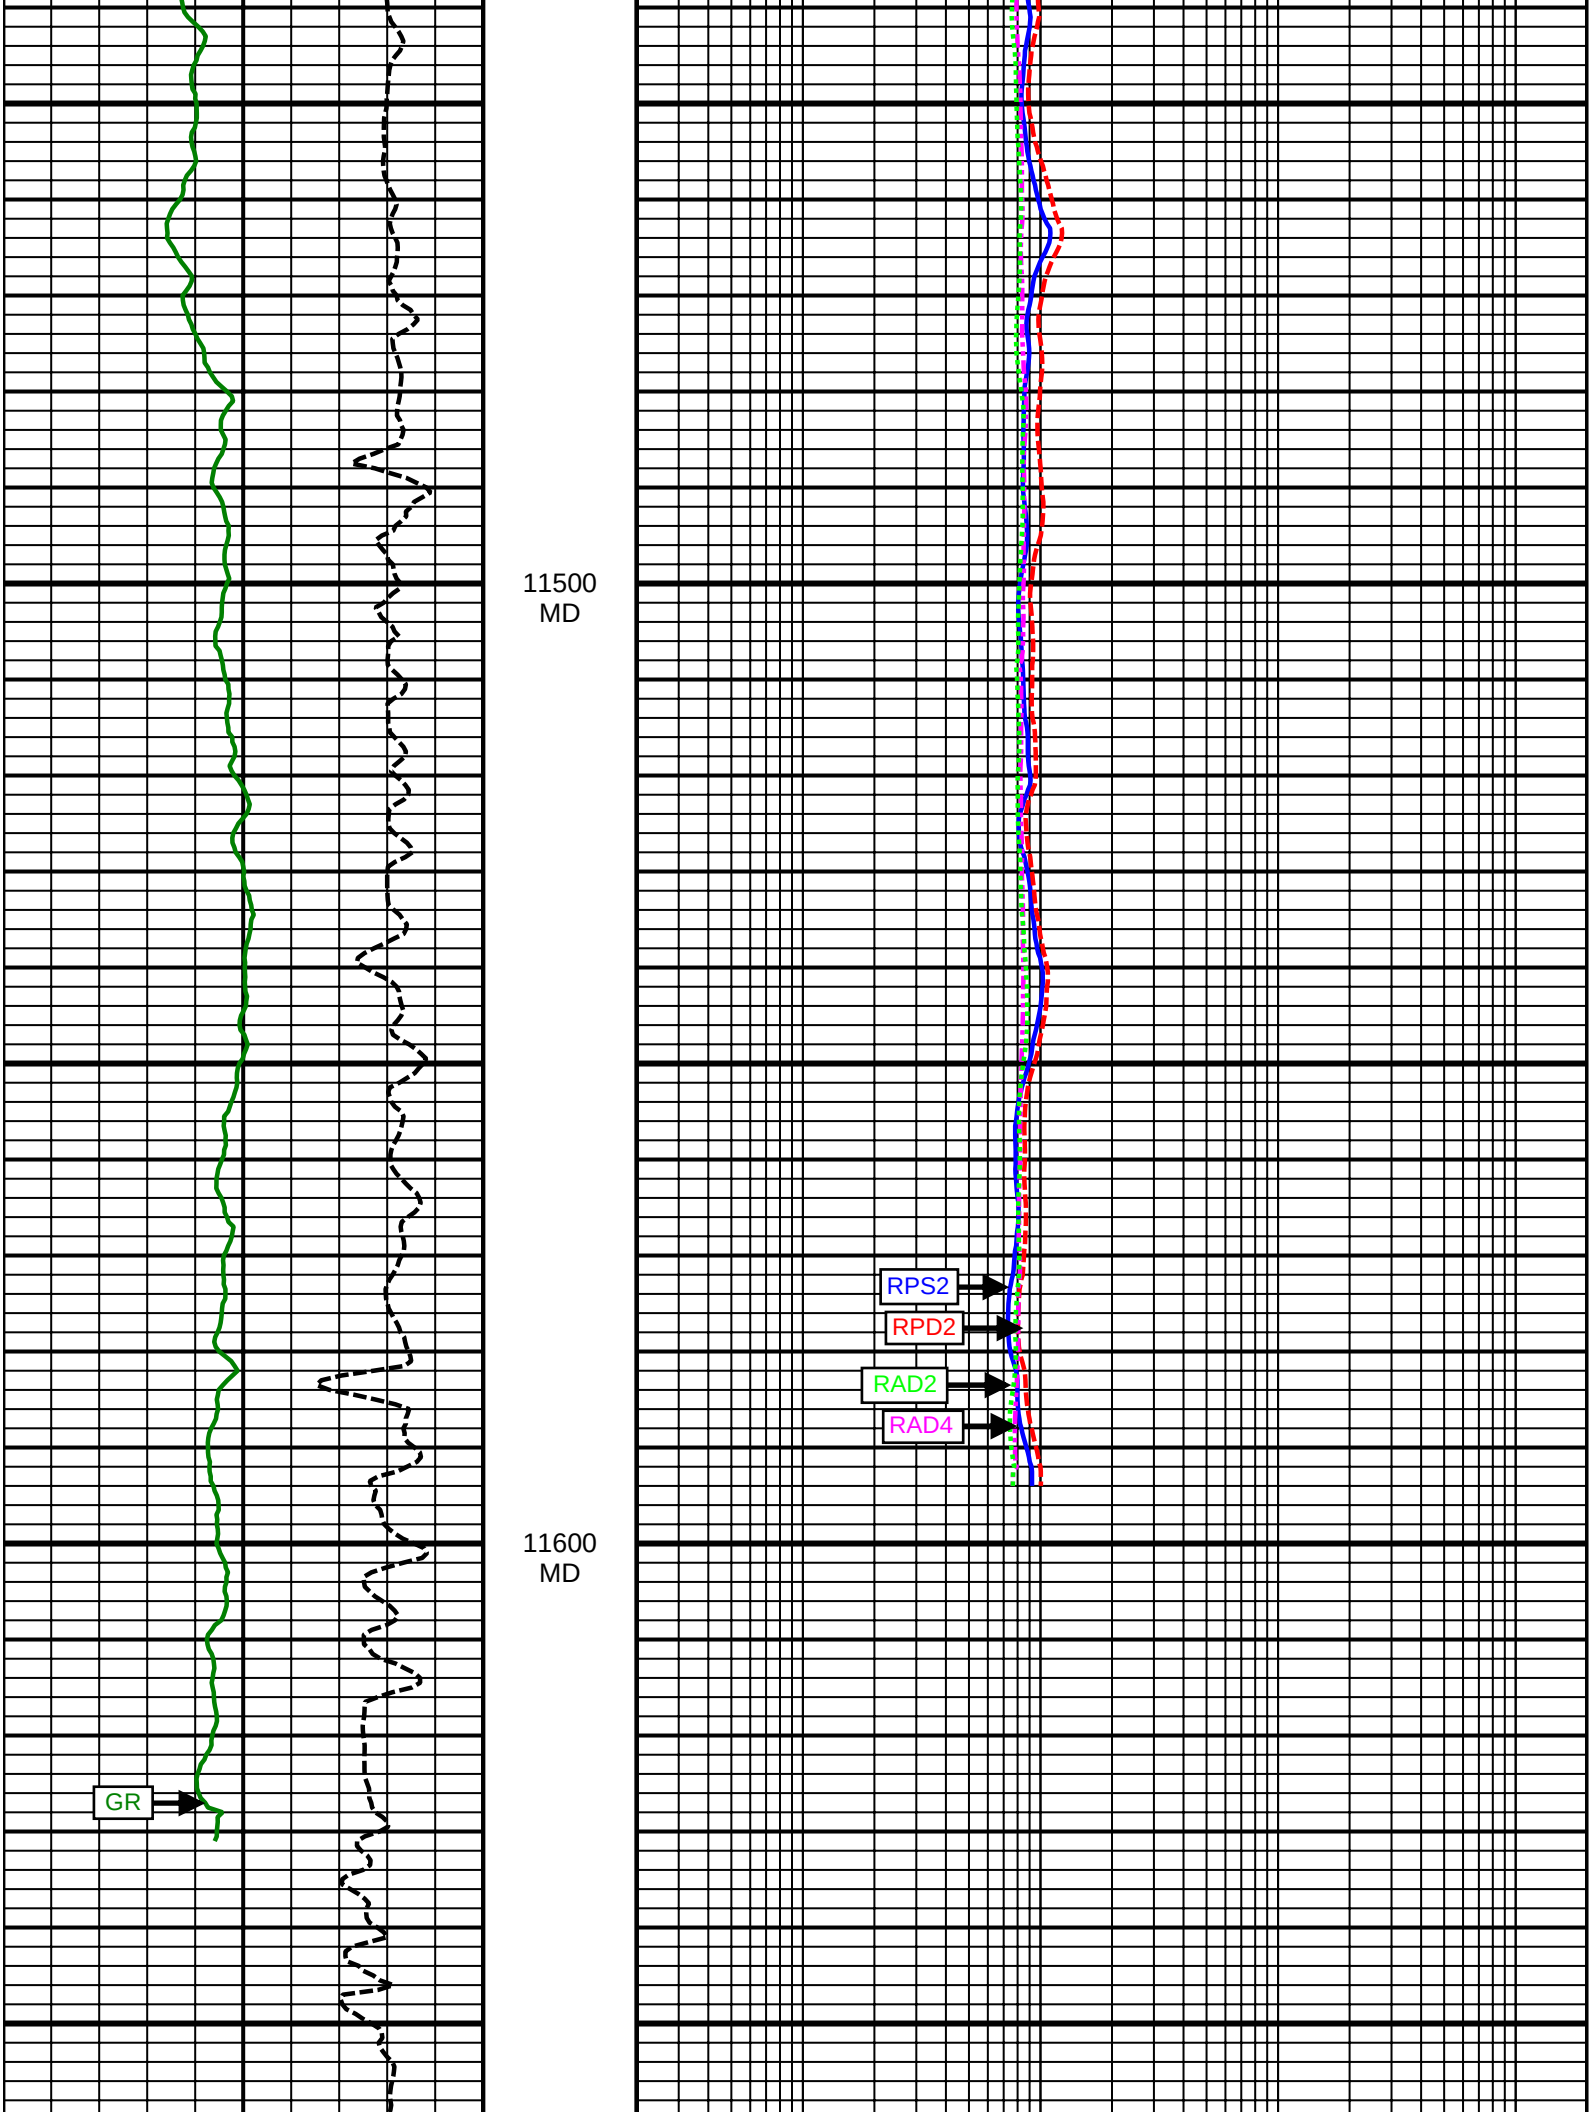
11500
MD
11600
MD
RPS2
RPD2
RAD2
RAD4
GR

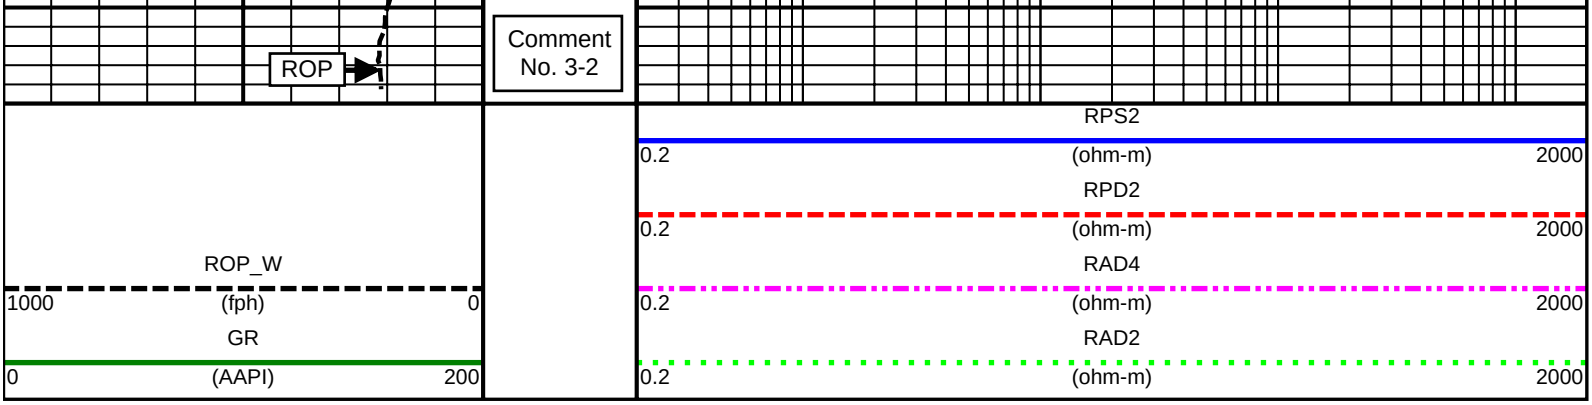
ROP
Comment
No. 3-2
RPS2
0.2
(ohm-m)
2000
RPD2
0.2
(ohm-m)
2000
RAD4
0.2
(ohm-m)
2000
RAD2
0.2
(ohm-m)
2000
ROP_W
1000
(fph)
0
GR
0
(AAPI)
200

SURVEY

Survey Calculation Method: **Minimum Curvature**

Magnetic Reference	Target Direction	Total Magnetic Field	Magnetic Dip Angle	Magnetic Declination	Grid Convergence	Total Correction
True North	**6.83 deg**	**52936 nT**	**66.94 deg**	**8.57 deg**	**0.00 deg**	**8.57 deg**

Survey Tie-On	Depth	INC	AZ	TVD	NS	EW
	1125.00 ft	**0.83 deg**	**305.45 deg**	**1124.98 ft**	**-0.23 ft**	**-5.91 ft**

Depth (ft)	Inc (deg)	Azm (deg)	TVD (ft)	Well Head NS (ft)	Well Head EW (ft)	VSect (ft)	Dogleg (deg/100ft)
1191.00	1.04	287.00	1190.97	0.22	-6.87	-0.60	0.55
1323.00	3.53	234.80	1322.87	-1.77	-11.34	-3.11	2.28
1415.00	3.76	231.75	1414.68	-5.27	-16.02	-7.14	0.33
1509.00	4.14	234.39	1508.46	-9.15	-21.20	-11.61	0.45
1605.00	4.48	236.44	1604.18	-13.24	-27.14	-16.38	0.39
1699.00	3.09	218.04	1697.98	-17.27	-31.76	-20.92	1.95
1794.00	0.95	180.33	1792.92	-20.07	-33.35	-23.90	2.54
1889.00	0.76	173.79	1887.91	-21.49	-33.28	-25.29	0.22
1984.00	0.85	179.00	1982.90	-22.82	-33.20	-26.61	0.12
2078.00	2.22	131.11	2076.87	-24.71	-31.82	-28.32	1.88
2173.00	4.16	119.45	2171.71	-27.62	-27.43	-30.68	2.14
2267.00	5.59	108.68	2265.37	-30.76	-20.12	-32.94	1.80
2362.00	6.86	107.00	2359.81	-33.90	-10.32	-34.89	1.35
2457.00	8.93	105.78	2453.91	-37.57	2.21	-37.04	2.19
2552.00	7.54	103.65	2547.93	-41.04	15.36	-38.92	1.50
2646.00	8.63	112.39	2640.99	-45.18	27.87	-41.55	1.74
2741.00	10.00	116.24	2734.74	-51.55	41.86	-46.20	1.58
2836.00	9.50	115.30	2828.37	-58.54	56.35	-51.43	0.55
2932.00	9.01	116.27	2923.12	-65.26	70.25	-56.44	0.54
3027.00	8.78	110.34	3016.98	-71.07	83.72	-60.61	0.99
3122.00	7.27	107.10	3111.04	-75.36	96.27	-63.37	1.66
3217.00	7.72	107.90	3205.23	-79.09	108.08	-65.67	0.49
3312.00	8.49	104.41	3299.28	-82.79	120.95	-67.82	0.96
3407.00	7.07	103.80	3393.41	-85.93	133.42	-69.46	1.50
3502.00	8.25	111.22	3487.56	-89.79	145.45	-71.86	1.62
3597.00	9.45	111.45	3581.43	-95.11	159.06	-75.52	1.26
3692.00	7.26	110.08	3675.41	-100.03	171.96	-78.87	2.31
3787.00	7.64	110.41	3769.61	-104.29	183.52	-81.72	0.40
3882.00	8.52	110.93	3863.67	-109.01	196.01	-84.92	0.93
3976.00	9.71	110.84	3956.48	-114.31	209.92	-88.54	1.27
4071.00	10.85	111.19	4049.95	-120.40	225.75	-92.69	1.20
4166.00	10.73	110.87	4143.27	-126.78	242.35	-97.06	0.14
4261.00	9.60	104.70	4236.78	-131.94	258.27	-100.29	1.65
4356.00	8.20	103.75	4330.64	-135.56	272.52	-102.19	1.48
4451.00	8.59	117.88	4424.63	-140.49	285.37	-105.55	2.20
4545.00	8.45	111.44	4517.59	-146.30	298.01	-109.82	1.03
4641.00	8.35	114.72	4612.56	-151.79	310.90	-113.74	0.51
4736.00	10.46	112.90	4706.28	-158.03	325.11	-118.24	2.24
4831.00	9.65	107.09	4799.82	-163.73	340.67	-122.05	1.37
4926.00	8.39	102.99	4893.65	-167.62	355.03	-124.21	1.49
5021.00	8.62	105.49	4987.60	-171.08	368.65	-126.03	0.46
5116.00	8.94	113.02	5081.49	-175.87	382.30	-129.16	1.25

5211.00	10.63	115.00	5175.11	-182.46	397.04	-133.95	1.81
5307.00	8.85	114.64	5269.72	-189.28	411.78	-138.97	1.86
5402.00	9.15	116.32	5363.55	-195.68	425.19	-143.72	0.42
5496.00	7.55	116.24	5456.55	-201.72	437.43	-148.27	1.70
5591.00	6.14	114.78	5550.87	-206.61	447.64	-151.91	1.50
5686.00	4.75	112.25	5645.44	-210.23	455.89	-154.52	1.48
5780.00	5.70	114.01	5739.05	-213.60	463.76	-156.94	1.02
5875.00	4.87	112.02	5833.64	-217.04	471.81	-159.39	0.89
5970.00	4.86	108.44	5928.30	-219.82	479.36	-161.25	0.32
6065.00	2.83	106.93	6023.08	-221.78	485.43	-162.47	2.14
6160.00	1.09	112.54	6118.02	-222.81	488.50	-163.13	1.84
6254.00	0.29	67.29	6212.02	-223.06	489.55	-163.25	0.97
6349.00	0.36	40.70	6307.02	-222.74	489.97	-162.89	0.17
6444.00	0.25	24.58	6402.01	-222.32	490.25	-162.44	0.15
6540.00	0.29	8.18	6498.01	-221.89	490.37	-162.00	0.09
6615.00	0.30	346.78	6573.01	-221.51	490.35	-161.63	0.15
6635.00	0.44	354.48	6593.01	-221.39	490.33	-161.50	0.74
6666.00	0.98	351.87	6624.01	-221.00	490.28	-161.13	1.74
6697.00	3.86	3.23	6654.98	-219.70	490.30	-159.83	9.37
6729.00	7.45	0.14	6686.82	-216.55	490.37	-156.70	11.25
6761.00	10.95	349.60	6718.40	-211.48	489.83	-151.73	12.10
6792.00	13.63	343.11	6748.69	-205.09	488.23	-145.57	9.71
6825.00	14.18	341.79	6780.72	-197.53	485.84	-138.35	1.92
6856.00	13.92	347.37	6810.80	-190.29	483.84	-131.40	4.45
6888.00	14.62	357.56	6841.82	-182.49	482.82	-123.78	8.14
6919.00	16.58	358.51	6871.67	-174.16	482.54	-115.54	6.38
6952.00	20.21	359.37	6902.98	-163.75	482.36	-105.23	11.03
6984.00	23.57	1.71	6932.67	-151.83	482.49	-93.37	10.85
7015.00	26.60	2.69	6960.74	-138.70	483.00	-80.27	9.87
7047.00	30.15	4.18	6988.89	-123.52	483.92	-65.09	11.31
7078.00	33.81	4.47	7015.19	-107.15	485.16	-48.69	11.82
7109.00	37.32	4.09	7040.40	-89.17	486.50	-30.68	11.34
7141.00	40.79	3.33	7065.24	-69.06	487.80	-10.55	10.95
7172.00	44.12	0.36	7088.12	-48.15	488.46	10.28	12.54
7204.00	47.59	359.05	7110.40	-25.19	488.33	33.06	11.23
7236.00	51.55	357.22	7131.15	-0.85	487.53	57.13	13.12
7267.00	55.60	355.45	7149.55	24.03	485.93	81.65	13.85
7299.00	59.90	354.90	7166.62	50.99	483.65	108.15	13.52
7330.00	64.49	354.91	7181.08	78.30	481.21	134.97	14.81
7362.00	69.05	354.87	7193.70	107.58	478.59	163.73	14.25
7393.00	71.86	354.78	7204.07	136.67	475.96	192.30	9.07
7425.00	74.36	355.80	7213.37	167.18	473.45	222.30	8.39
7458.00	77.81	356.80	7221.30	199.14	471.38	253.79	10.86
7489.00	81.50	357.18	7226.87	229.59	469.78	283.83	11.96
7521.00	83.83	358.11	7230.95	261.30	468.48	315.16	7.83
7552.00	87.34	359.79	7233.34	292.20	467.91	345.77	12.55
7584.00	88.46	1.60	7234.51	324.17	468.30	377.56	6.65
7600.00	88.25	1.25	7234.97	340.16	468.70	393.49	2.55
7730.00	89.38	1.92	7237.66	470.08	472.29	522.91	1.01
7825.00	89.69	2.21	7238.43	565.02	475.72	617.58	0.45
7920.00	89.69	2.33	7238.94	659.94	479.48	712.28	0.13
8014.00	90.80	3.06	7238.54	753.83	483.90	806.03	1.41
8109.00	88.52	0.45	7239.11	848.77	486.81	900.64	3.65
8204.00	87.96	358.75	7242.02	943.72	486.15	994.84	1.88
8300.00	89.07	359.56	7244.51	1039.68	484.73	1089.94	1.43
8395.00	89.44	359.72	7245.75	1134.67	484.13	1184.19	0.42
8490.00	89.57	359.62	7246.57	1229.66	483.59	1278.44	0.17
8585.00	90.99	359.52	7246.10	1324.65	482.87	1372.68	1.50
8680.00	87.72	355.31	7247.17	1419.52	478.59	1466.36	5.61
8774.00	88.64	355.42	7250.16	1513.16	471.00	1558.44	0.99
8869.00	89.81	355.51	7251.44	1607.85	463.49	1651.56	1.24

8964.00	90.06	358.03	7251.55	1702.70	458.14	1745.10	2.67
9059.00	90.44	0.11	7251.14	1797.68	456.60	1839.22	2.23
9153.00	90.12	359.11	7250.68	1891.67	455.96	1932.47	1.12
9248.00	89.75	0.89	7250.78	1986.67	455.96	2026.79	1.91
9342.00	89.51	0.01	7251.39	2080.66	456.69	2120.21	0.97
9437.00	90.31	1.33	7251.54	2175.65	457.80	2214.66	1.62
9532.00	90.49	1.74	7250.88	2270.62	460.35	2309.25	0.47
9627.00	90.06	1.03	7250.42	2365.59	462.65	2403.82	0.87
9721.00	89.51	0.88	7250.77	2459.57	464.21	2497.32	0.61
9816.00	90.56	4.84	7250.72	2554.43	468.95	2592.08	4.31
9911.00	89.81	4.28	7250.41	2649.13	476.50	2687.00	0.99
10006.00	89.38	3.31	7251.08	2743.92	482.79	2781.86	1.12
10101.00	91.30	4.21	7250.52	2838.71	489.02	2876.72	2.23
10196.00	90.80	4.23	7248.78	2933.43	496.01	2971.60	0.53
10292.00	89.81	4.24	7248.27	3029.17	503.10	3067.50	1.03
10387.00	90.49	1.09	7248.02	3124.05	507.52	3162.24	3.39
10481.00	87.66	357.40	7249.53	3218.01	506.28	3255.38	4.95
10576.00	88.83	357.20	7252.44	3312.86	501.81	3349.02	1.25
10672.00	89.57	359.01	7253.78	3408.79	498.63	3443.90	2.04
10767.00	89.75	0.29	7254.35	3503.78	498.05	3538.15	1.36
10861.00	91.60	1.89	7253.24	3597.75	499.84	3631.66	2.60
10957.00	89.26	1.69	7252.52	3693.70	502.84	3727.28	2.45
11052.00	88.58	1.35	7254.31	3788.65	505.36	3821.86	0.80
11147.00	89.74	3.46	7255.70	3883.54	509.34	3916.56	2.53
11242.00	89.32	3.01	7256.48	3978.39	514.70	4011.37	0.65
11337.00	89.32	3.61	7257.61	4073.22	520.19	4106.18	0.63
11433.00	89.07	2.58	7258.96	4169.07	525.37	4201.97	1.10
11528.00	88.27	1.81	7261.16	4263.98	529.01	4296.63	1.17
11615.00	88.52	2.03	7263.60	4350.89	531.92	4383.28	0.38
Projected to Total Depth:							
11667.00	88.52	2.03	7264.96	4403.30	533.78	4435.53	0.00

Weatherford M/LWD surveys from 1191.00 ft MD to 11615.00 ft MD.
TD at 11667.00 ft MD.
The total correction is 8.57 deg relative to True North.

Weatherford®

Final Print

COMPANY	Anadarko
WELL	Haymaker 4C-9HZ
FIELD	Wattenberg
RIG	H & P 307
LOC.	Colorado
COUNTY	Weld
