WELLBORE DIAGRAM

COGCC Document No. 2056036

OPERATOR: SCHLUMBERGER CARBON SERVICES
WELL: RMCCS ST 1
RIG: PATTERSON 166
SPUDDED: January 15, 2012
COMPLETION DATE: March 5, 2012
API No: 05-081-07694

KB: 6,857.60
GL: 6,837.10

LOCATION: SEC 34 TWN 6N RNG 91W
QTR/QTR: SWSE
COUNTY: MOFFAT
STATE: COLORADO

REVISION DATE 2014-12-29

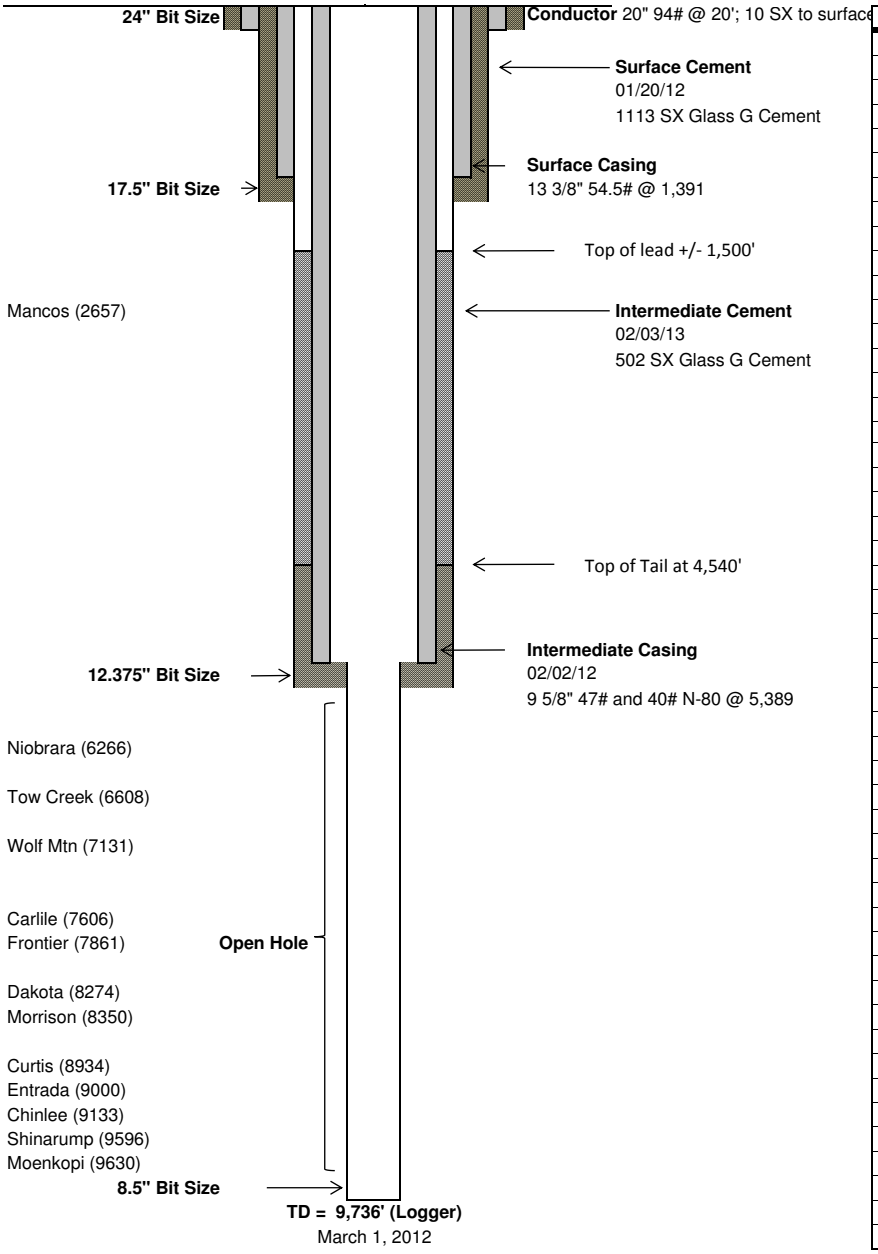

DATE	DESCRIPTION
1/15/12	Spud Patterson 166 @ 05:00
1/19/12	Set Surface Casing X Jts 13 3/8" 54.5#, J-55, 8rd EUE
1/20/12	Surface cement. w/ 575 SX (216 BBL) Lead, 538 SX (112 BBL) Tail
1/20/12	Cement Top Job. 180 SX (38 BBL 15.8#
2/1/12	Wireline Logs. PEX-CMR-ECS-HNGS-MSIP-FMI (5,400' - 1,350')
2/3/12	Ran 9 5/8" 47 Jts 47# N-80, 65 Jts 40# N-80 set at 5,389 (driller)
2/4/12	Int Cement: Lead 252 SX 12 PPG; Tail 250 SX
	PPG 50 BBL
2/12/12	Core Niobrara 6640' - 6673'
2/13/12	Core Niobrara 6673' - 6700'
2/17/12	Core Mowry 8180' - 8206'
2/19/12	Core Mowry 8216' - 8234'
2/20/12	Core Mowry 8216' - 8260'
2/22/12	Core Morrison 8895' - 8898'
2/23/12	Core Morrison 8898' - 8925'
2/25/12	Core Entrada 9012' - 9024'
2/26/21	Core Entrada 9024' - 9047'
3/1/12	Reach total Depth 9,745' (driller) 9,736' (logger)
3/2/12	Wireline Logs. PEX-CMR-ECS-HNGS-MSIP-FMI (9,736' - 5,388') Rotary Cores
3/4/12	Wireline rotary cores, 100 core samples 9,700' to 7,825'
3/5/12	Cement Plug 1 8694-8294 163 SX 33.4 BBL 15.8#
3/5/12	Cement Plug 2 7390-6890239 SX 43 BBL 15.6#
3/5/12	Cement Plug 3 5488-5288 174 SX 32 BBL 15.8#
3/6/12	Peforate surface casing shoe for squeeze @
3/6/12	Cement Plug 4 1333-1183 57 SX 11.7 BBL 15.8#
3/6/12	Cement Plug 5 55-0 17 SX 15.8#
3/10/12	Rig move off

Prepared by : Wayne Rowe
