State M36-09

P&A Procedure

Ben Zapp, PE (303-241-1273)

2 March 2017

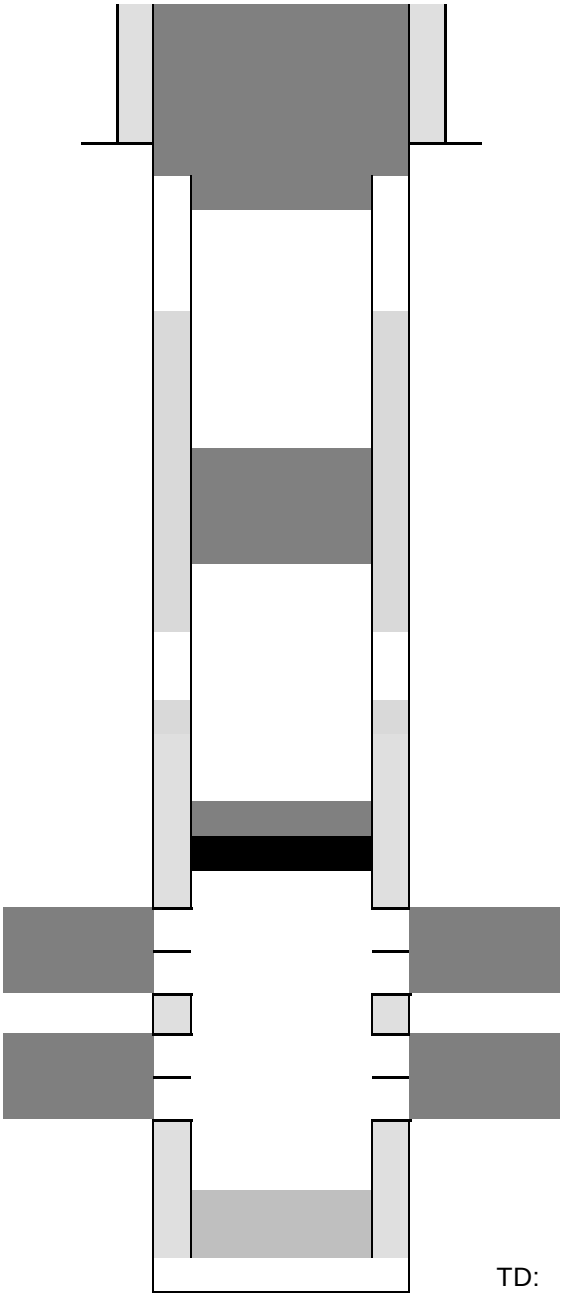

Cut surface casing off 6'-8' below surface.

TOC @ Surface
Cut Casing @ 880'
Pump 345sx @ 930' (15.8 G Neat)

TOC @ 2000'

Pump 40sx @ 2500' (15.8 G Neat)

Existing Annular Cement 1740' – 4840'

Existing TOC 6200'

Set CIBP @ 6698' w/ 2sx cement on top

Niobrara Perforations: 6748' – 6896' KB

Codell Perforations: 7069' – 7087' KB

TD: 7686' KB
