
Main Pass

Repeat Pass

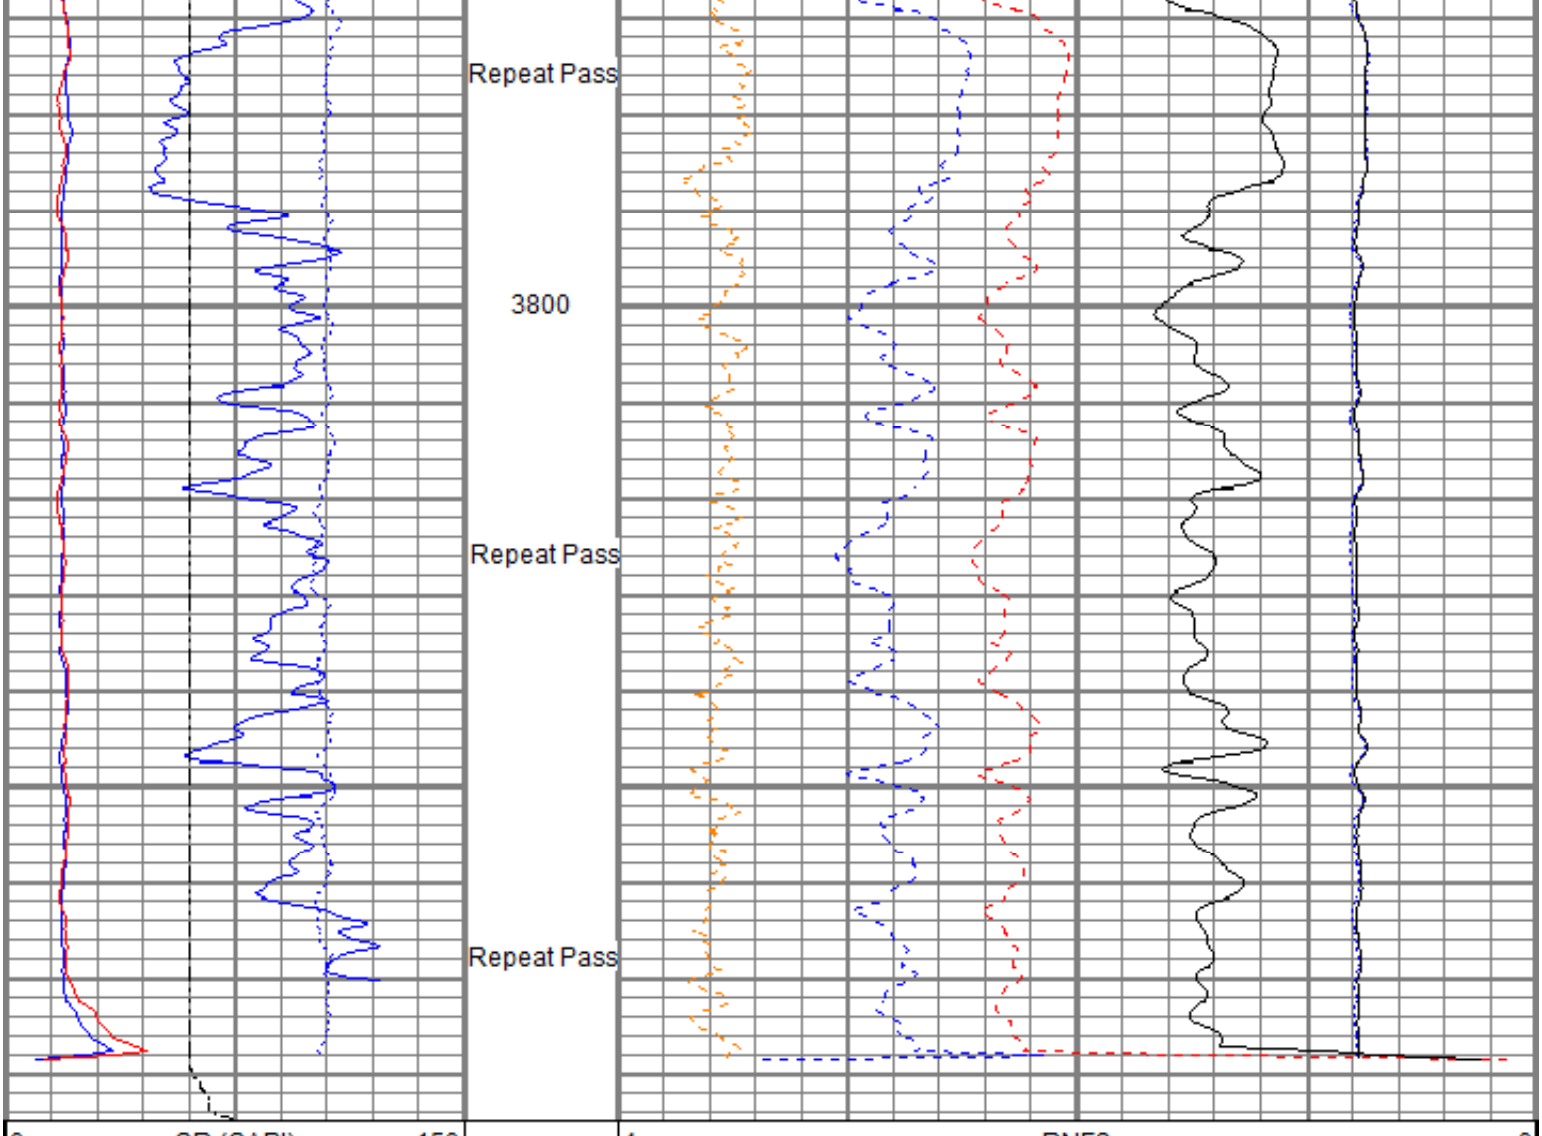

Sensor	Offset (ft)	Schematic	Description	Length (ft)	O.D. (in)	Weight (lb)
			Titan CHD-16875 GO Titan 1-11/16" Assembled Electric Cable Head w/ 1" Fishing Neck	1.03	1.69	5.40
			HWS_TCU-002 (001704) HWS Telemetry Control Unit (TCU002)	2.30	1.69	10.87
TCUTEMP	14.69					
TCUVOLT	14.69					
GCL_CCL	13.97					
			HWS_GCL-001 (001681) HWS Gamma Ray Collar Locator (1.6875")	2.69	1.69	13.40
GCL_GR	12.50					
Long	6.25		HWS_RAS-RAS002 (003040) Hunter Well Science Pulsed Neutron Tool	11.75	1.69	55.82
Far	6.25					
Near	6.25					
Anci	6.25					
LOCTIM	0.00					
UTCTIM	0.00		HWS_TBN-001 (001724) HWS Terminator Bull Nose (1.6875")	0.25	1.69	0.99

Dataset: tep_chevron gm 442-19_pn_02-01-21.db: field/well/run1/main.2
Total length: 18.02 ft
Total weight: 86.48 lb
O.D.: 1.69 in

Calibration Report

Database File f:\data\tep\chevron gm 442-19\pn\tep_chevron gm 442-19_pn_02-01-21.db
Dataset Pathname main.2
Dataset Creation Tue Feb 02 09:06:46 2021

RAS Calibration Report

Calibration Date: Tue Jun 11 14:55 2020 Meas #: 003041

Water Tank

Description	Curve	Standard	Mean	Dev
Sigma Near	SIGN	23.1	24.1	0.23
Sigma Far	SIGF	22.8	23.5	0.27
Ratio Near-Long Capture	RNL2	5.79	6.45	0.04
Ratio Near-Long Burst	RNLB	6.49	6.87	0.04
Ratio Near-Far Capture	RNF2	1.85	2.00	0.01
Ratio Near-Far Burst	RNFB	2.03	2.16	0.01
Spectral Hydrogen Index	HIS2	12.84	12.61	0.16
Carbon-Oxygen Ratio	CORS	1.34	1.30	0.05
Ratio Burst-Capture Near	RNBC	1.46	1.73	0.01
Ratio Burst-Capture Far	RFBC	1.50	1.67	0.01

Hydrocarbon Tank

Description	Curve	Standard	Mean	Dev
Sigma Near	SIGN	25.7	26.8	0.26
Sigma Far	SIGF	25.1	25.5	0.45
Ratio Near-Long Capture	RNL2	1.78	2.98	0.02
Ratio Near-Long Burst	RNLB	2.57	4.38	0.02
Ratio Near-Far Capture	RNF2	0.98	1.30	0.01
Ratio Near-Far Burst	RNFB	1.30	1.64	0.01
Spectral Hydrogen Index	HIS2	16.68	17.41	0.28
Carbon-Oxygen Ratio	CORS	1.51	1.54	0.04
Ratio Burst-Capture Near	RNBC	2.23	2.46	0.02
Ratio Burst-Capture Far	RFBC	2.09	2.18	0.02

Gamma Ray Calibration Report

Serial Number:	001681	
Tool Model:	001	
Performed:	(Not Performed)	
Calibrator Value:	1.0	GAPI
Background Reading:	0.0	
Calibrator Reading:	1.0	
Sensitivity:	1.0000	GAPI/

RELIANCE WELLFIELD SERVICES

Company	TEP Rocky Mountain LLC
Well	Chevron GM 442-19
Field	Grand Valley
County	Garfield
State	Colorado
