J-W WIRELINE COMPANY

CEMENT BOND
GAMMA RAY
COLLAR CORRELATION LOG

Company	CHESAPEAKE ENERGY
Well	WAGNER 11-65 11 1H
Field	DJ BASIN
County	WELD
State	COLORADO

Company CHESAPEAKE ENERGY
Well WAGNER 11-65 11 1H
Field DJ BASIN
County WELD State COLORADO

Location: API # :
600' FSL & 2130' FWL
LAT / LONG: 40.929637 / -104.630528
SEC 11 TWP 11N RGE 65W

Other Services
NONE

Permanent Datum GROUND LEVEL Elevation 5658
Log Measured From KELLY BUSHING (20 FT)
Drilling Measured From KELLY BUSHING

Elevation
K.B. 5678
D.F. 5677
G.L. 5658

Date	15-JUN-2011
Run Number	ONE
Depth Driller	11996
Depth Logger	7550
Bottom Logged Interval	7500
Top Log Interval	342
Open Hole Size	6.250"
Type Fluid	WATER
Density / Viscosity	8.34 #/GAL
Max. Recorded Temp.	216 DEGF
Estimated Cement Top	Not Recorded
Time Well Ready	N/A
Time Logger on Bottom	N/A
Equipment Number	3011
Location	BRIGHTON, CO
Recorded By	SAM HOPPER
Witnessed By	BRIAN BROUSSARD

Borehole Record				Tubing Record			
Run Number	Bit	From	To	Size	Weight	From	To

Casing Record	Size	Wgt/Ft	Top	Bottom
Surface String	9-5/8"	40#	0	1025
Prot. String				
Production String	4-1/2"	11.6#	0	11976
Liner				

<<< Fold Here >>>

All interpretations are opinions based on inferences from electrical or other measurements and we cannot and do not guarantee the accuracy or correctness of any interpretation, and we shall not, except in the case of gross or willful negligence on our part, be liable or responsible for any loss, costs, damages, or expenses incurred or sustained by anyone resulting from any interpretation made by any of our officers, agents or employees. These interpretations are also subject to our general terms and conditions set out in our current Price Schedule.

Comments

RUN CBL FROM 7500' (approx 45deg devation) TO 200' ABOVE TOP OF CEMENT.
CBL RAN AT -0- PSI SURFACE PRESSURE.
FLUID LEVEL FOUND @ 342'.
NO TRUE INDICATION OF FREE PIPE,
RECORDED CEMENT TO CURRENT FLUID LEVEL (342').

THANK YOU FOR USING J-W WIRELINE!!

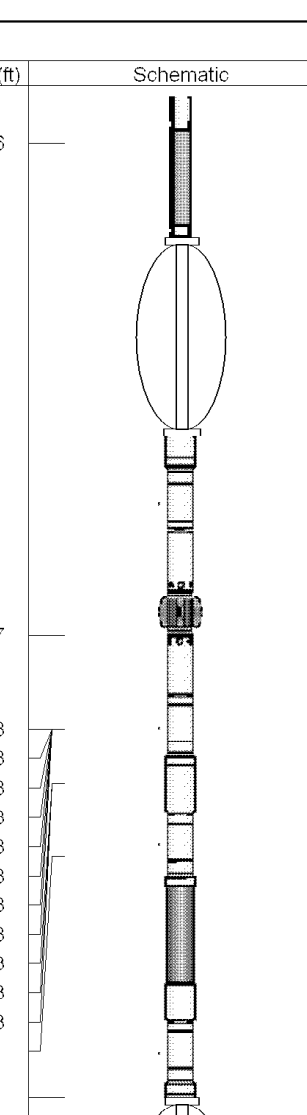

Sensor	Offset (ft)	Description	Len (ft)	OD (in)	Wt (lb)
CCL	19.56	CCL-275tekco (2.75TEKCO) 2.75" TEK CCL Earth Mag	1.96	2.75	20.00
		CENT-TEKCO (101)	2.73	2.75	10.00
TEMP	12.77				
WVFS1	11.48				
WVFS2	11.48	275CTEKSECWTWSLCANS-275RIB (1239.13 2 3/4" (R.I.B.) TOOL 3FT, 5FT and 8EA RIB SIGNALS 400 DEG "F" @20K PSI With Sliding Cans For Pressure Ballance		2.75	102.00
WVFS3	11.48				
WVFS4	11.48				
WVFS5	11.48				
WVFS6	11.48				
WVFS7	11.48				
WVFS8	11.48				
WVF3FT	10.73				
WVFCAL	10.73				
WVFSYNC	10.73				
WVF5FT	9.73				
WVFTEMP	6.40				
		CENT-TEKCO (101)	2.73	2.75	10.00
		GR-TEKCO (101SGR) 2.75 HIGH TEMP LOGGING GR	3.67	2.75	25.00
GR	1.06				

Dataset: chesapeake_wagner_11-65_11_1h.db: field/15jun11/cbl/pass4
Total Length: 20.21 ft
Total Weight: 167.00 lb
O.D. 2.75 in

J-W WIRELINE COMPANY

CBL MAIN PASS

Database File: chesapeake_wagner_11-65_11_1h.db
Dataset Pathname: 15jun11/cbl/pass4
Presentation Format: scbl_dr
Dataset Creation: Wed Jun 15 09:24:11 2011 by Log SCH 110223
Charted by: Depth in Feet scaled 1:240

9 Collar Locator -1	LTEN	0 Amplified Amplitude (mV) 30	200 Variable Density 1200
30 Gamma Ray (GAPI) 150	0 (lb) 2000	0 Amplitude (mV) 100	
300 TT3FT (usec) 200			

J-W WIRELINE COMPANY

Company	CHESAPEAKE ENERGY
Well	WAGNER 11-65 11 1H
Field	DJ BASIN
County	WELD
State	COLORADO
