Final As-Plugged Wellbore Schematic

Well Name:	Yahn 1	Date Prepared:	7/15/2023
Location:	660' FSL, 660' FWL, SWSW Sec 8, T7N, R59W	Last Updated:	1/16/2024
County	Weld	Spud Date:	10/21/1990
API #:	05-123-14798	Completion Start Date:	10/26/1990
Co-ordinates:	40.584156 / -104.009439	Last Workover Date:	10/26/1990
Elevations: GROUND:	4944'	Prepared by:	Jake Van Bramer
KB:	4954'	Updated by:	--
Depths (KB): PBTD:	6950'		
TD:	6950'		

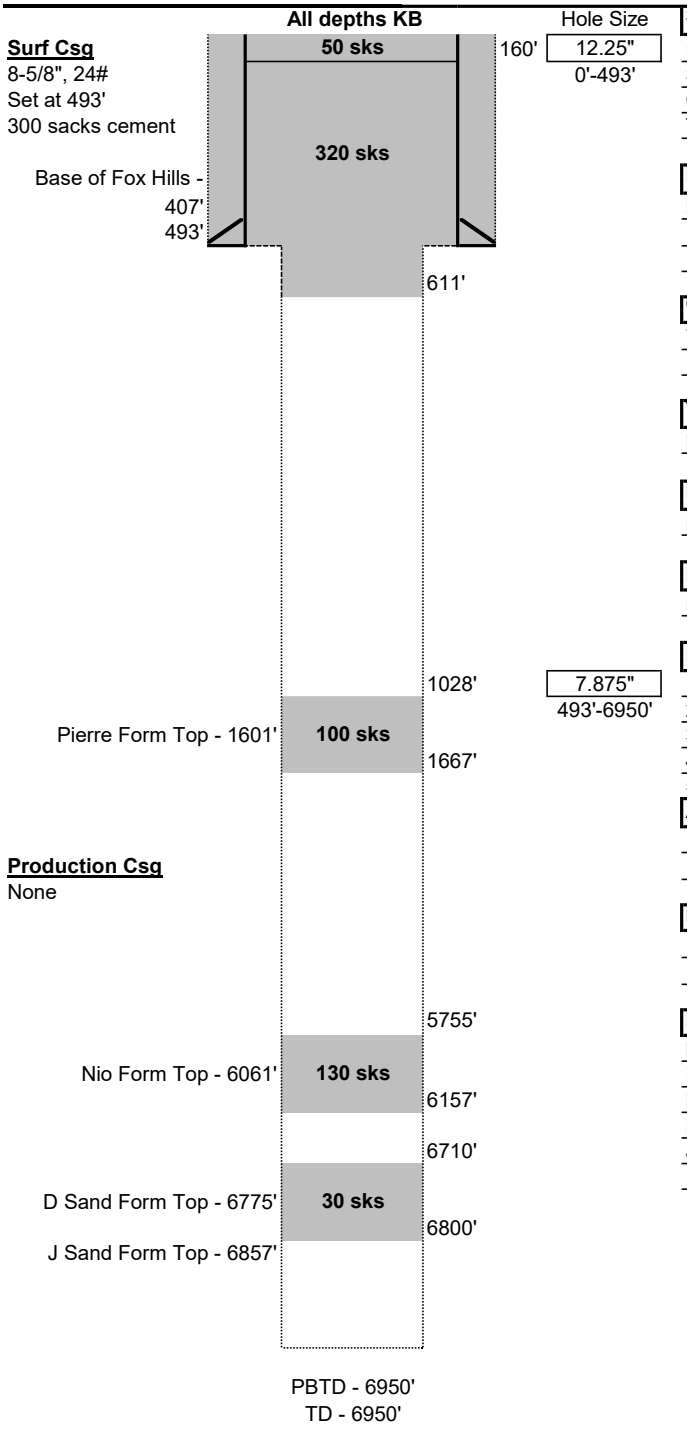

Surface Casing:
- Drilled 12-1/4" surface hole to 493'
- Set 8-5/8", 24# casing at 493'
- Cemented with 300 sks
- TOC at surface

Production Casing:
- None

Open Hole:
- 7-7/8" Open Hole drilled from 493'-6,950', expected to be washed out

Tubing:
- None

Rods:
- None

Perforations:
- None

P&A Plugs:
1. 30 sks from 6,710'-6,800' (existing)
2. 130 sks Class G (1.15 cuft/sk) from 5,755'-6,157' (new, tagged)
3. 100 sks Class G (1.15 cuft/sk) from 1,028'-1,667' (new, tagged)
4. 320 sks Class G (1.15 cuft/sk) from 611' to surface (new)
5. 50 sks Class G (1.15 cuft/sk) from 160' to surface to top off well

Additional Notes:

Initial Potential Test:

Formation Tops:

Base of the Fox Hills	407'
Pierre	1601'
Niobrara	6061'
D Sand	6775'
J Sand	6857'
