Final As-Plugged Wellbore Schematic

Well Name:	UPRR 1	Date Prepared:	10/3/2024
Location:	660' FNL, 660' FEL, NENE Sec 7, T3S, R65W	Last Updated:	5/8/2025
County:	Adams	Spud Date:	10/29/1956
API #:	05-001-05084	Completion Start Date:	11/21/1956
Co-ordinates:	39.810972 / -104.699244	Last Workover Date:	11/21/1956
Elevations:	GROUND: --	Prepared by:	Jake Van Bramer
	KB: 5393'	Updated by:	--
Depths (KB):	PBTD: --		
	TD: 8404'		

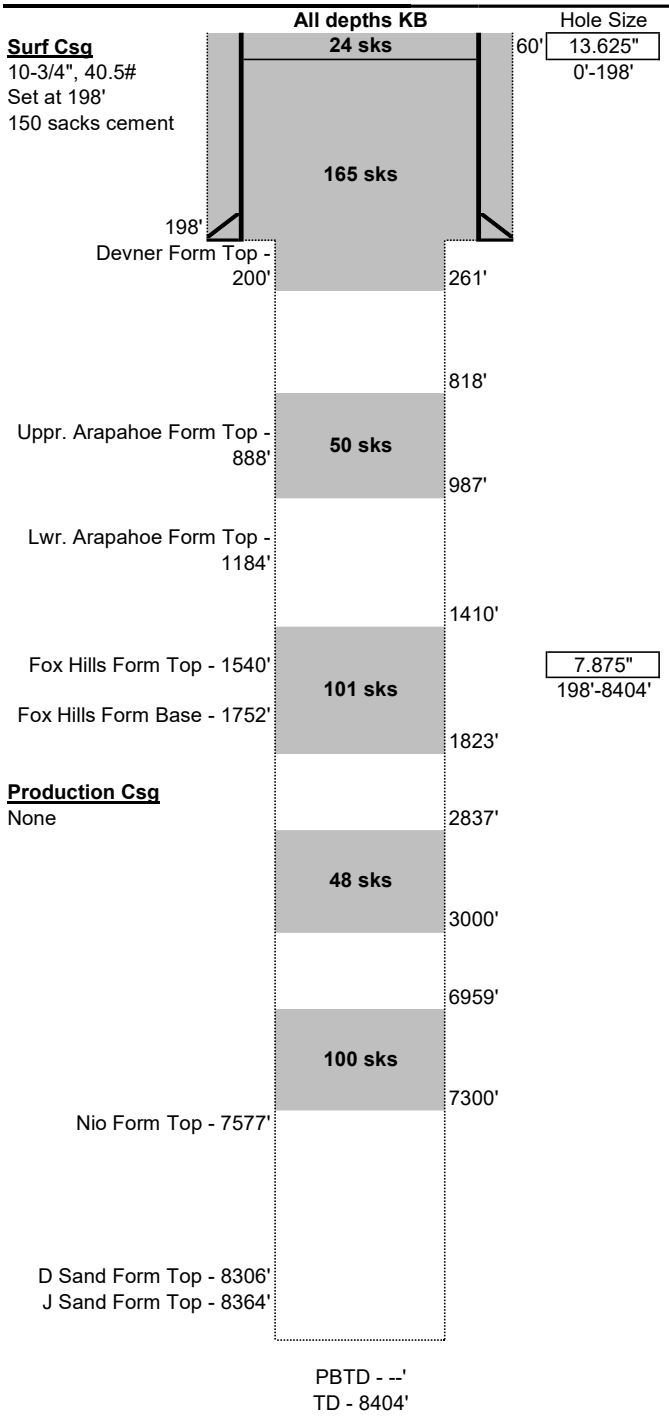

Surface Casing:
Drilled surface hole of unknown size (assumed to be 13-5/8") to 198'
Set 10-3/4", 40.5# H-40 casing at 198'
Cemented with 150 sks
TOC at surface

Production Casing:
None

Open Hole:
Assumed 7-7/8" Open Hole from 198'-8,404', expected to be washed out

Rods & Tubing:
None

Perforations:
None

P&A Plugs:
1. 100 sks Class G (1.15 cuft/sk) from 6,959'-7,300' (new)
2. 48 sks Class G (1.15 cuft/sk) from 2,837'-3,000' (new)
3. 101 sks Class G (1.15 cuft/sk) from 1,410'-1,823' (new, tagged)
4. 50 sks Class G (1.15 cuft/sk) from 818'-987' (new)
5. 165 sks Class G (1.15 cuft/sk) from 60'-261' (new, tagged)
6. Topped off with 24 sks Class G (1.15 cuft/sk) from 60' to surface (new)

Additional Notes:
Received approval from ECMC engineer on 3/18/25 to adjust original plugging procedure due to difficulty getting deeper than 7300'

Initial Potential Test:

Formation Tops:

Denver	200'
Upper Arapahoe (Base)	888'
Lower Arapahoe (Base)	1184'
Fox Hills	1540'
Fox Hills (Base)	1752'
Niobrara	7577'
D Sand	8306'
J Sand	8364'
