Final As-Plugged Wellbore Schematic

Well Name:	Rocchio 19-1	Date Prepared:	12/16/2025
Location:	1500' FSL, 2250' FWL, NESW Sec 19, T5N, R60W	Last Updated:	3/25/2026
County	Morgan	Spud Date:	10/19/1989
API #:	05-087-07989	Completion Start Date:	10/24/1989
Co-ordinates:	40.383558 / -104.139192	Last Workover Date:	2/26/2026
Elevations:	GROUND: 4956'		
	KB: 4606'		
Depths (KB):	PBTD: --		
	TD: 6880'		

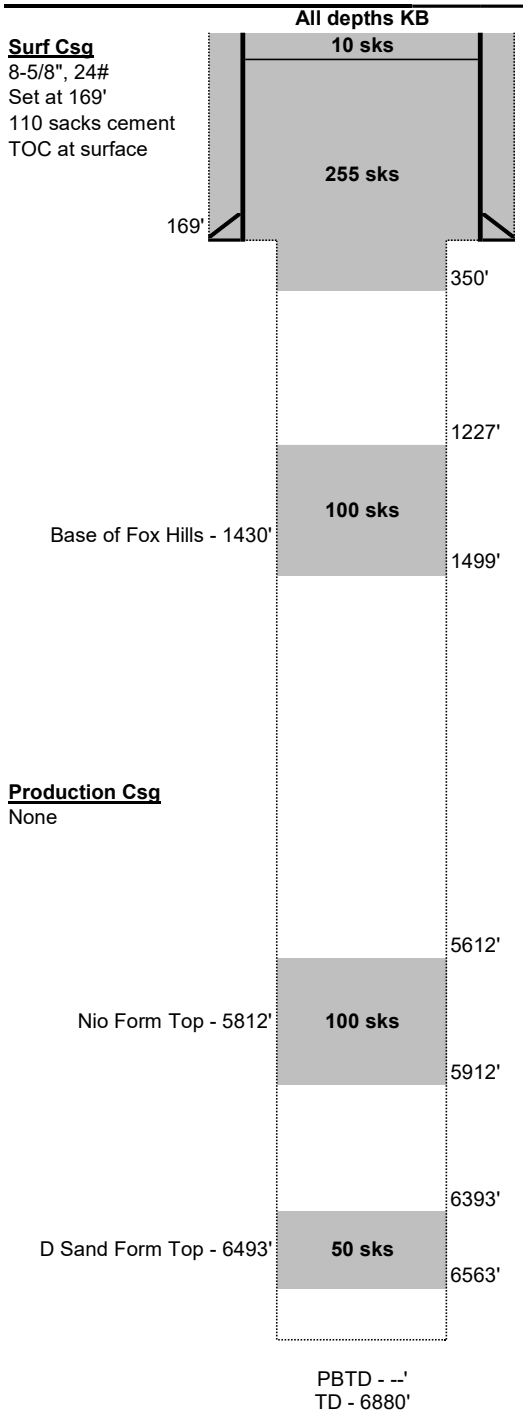

Surface Casing:
- Drilled 12-1/4" surface hole to 323'
- Set 8-5/8", 24# casing at 169'
- Cemented with 110 sks
- TOC at surface

Production Casing:
- None

Open Hole:
- 7-7/8" Open Hole from 169'-6,880', expected to be washed out

Rods & Tubing:
- None

Perforations:
- None

P&A Plugs:
1. 50 sks Class G (1.15 cuft/sk) from 6,393'-6,563' (new)
2. 100 sks Class G (1.15 cuft/sk) from 5,612'-5,912' (new)
3. 100 sks Class G w/ 2% CaCl2 (1.15 cuft/sk) from 1,227'-1,499' (new, tagged)
4. 255 sks Class G w/ 3% CaCl2 (1.15 cuft/sk) from 350' to surface (new)
5. 10 sks Class G (1.15 cuft/sk) topped off at surface (new)

Additional Notes:

Initial Potential Test:
- None

Formation Tops:

Base of the Fox Hills	1430'
Niobrara	5812'
D Sand	6493'
