AXIS ENERGY SERVICES CEMENT

PO Box 329
Ft. Lupton, CO 80621
(303) 654-9202

"Here Safety Meets Quality at the Axis of Efficency"

Date of Service	Job Type	Customer	Consultant	Well Name	Last Tckt	Ticket #
3/6/2026	Surface	MDS Energy	Matt Morgan	Castor #1	Yes	6254

State	County	API	Rig	Operator
Colorado	Weld	05-123-05488	Axis 3011	

Well Information

	Work String	Prod CSG	Surface	OH (I.D.)	Annular
OD & Weight	2 7/8" 6.5#		10 3/4	9	
Factor	0.00579	0	0.1009	0.0787	
Length	554		223	331	
Capacity	3.21	0.00	22.50	26.05	0.00
OD & Weight					
Factor	0	0	0	0.0000	
Length					
Capacity	0.00	0.00	0.00	0.00	0.00
OD & Weight					
bbl/ft	0	0	0	0.0000	
Length					
Capacity	0.00	0.00	0.00	0.00	0.00
Buoyancy	**0.87**	Buoyancy	**0.76**	Buoyancy	**0.76**
Lift Pressure	PRV	Lift Pressure	PRV	Lift Pressure	PRV
483	***250***				

Water

Temp	60 °F
PH	7
Chloride	2

Well Description	Depth in Ft
TOC	0
Shoe	223
EOT	554

Drivers, Crew and Equipment Allocation

Driver and Heavy Duty Equipment				Crew and Light Duty Equipment			Misc. Tools or Equipment
Driver	Tractor	Trailer	Mileage	Crew	Equipment	MIleage	Required or Requested
	8461	CP2900			7475		
	1435	CB2321					
Total Heavy Duty Mileage			0	Total Light Duty Mileage		0	
G Neat	**176**	**G Neat**	**5**	**Blend**	**0**		

Desc	Qty	Rate	Total	Desc	Qty	Rate	Total
G Neat	176.00	$0.00	$0.00	Sugar	50.00	$0.00	$0.00
G Neat	5.00	$0.00	$0.00	Defoamer	3.00	$0.00	$0.00
Blend	0.00	$0.00	$0.00			$0.00	$0.00
Pump & Bulk Per Hour	3.00	$0.00	$0.00			$0.00	$0.00
Data Recording	1.00	$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00
		$0.00	$0.00			$0.00	$0.00

Ticket total $0.00

Print *Sign* *Date*

See page 2 for job log and any necessary remarks

AXIS ENERGY SERVICES CEMENT
PO Box 329
Ft. Lupton, CO 80621
(303) 654-9202

"Here Safety meets Quality at the Axis of Efficency"

Date of Service	Customer	Consultant	Well Name	Last Tckt	Ticket #
3/6/2026	MDS Energy	Matt Morgan	Castor #1	Yes	6254

State	County	API	Rig	Mileage	Operator
Colorado	Weld	05-123-05488	Axis 3011	0	0

Job Specific Remarks

Time	Injection Rate	Injection BBL	Pressure PSI	Slurry Weight	Slurry Yield	Job Log
9:00						Arrived on location
9:10						JSA Spot and rig up
9:15						JSA Pump schedule w Rig Crew
9:22	0.5	2	1500	8.34		Pressure test
9:26	2.5	10	700	8.34		Break Circulation Fresh water
9:30	2.5	36	700	15.8	1.15	Mix and pump Cement
9:45						Shutdown and release pressure
9:47						Standby for rig crew
11:38	0.5	1	0	15.8	1.15	Top off well
11:40						Wash Pumps & Lines
11:50						Blow down pump and lines
12:00						JSA Rig down Cement equipment
12:10						Leave location

Customer Name (print) (sign) (Date)

Date of Service	3/6/2026
Ticket total	$0.00

CASTOR 1
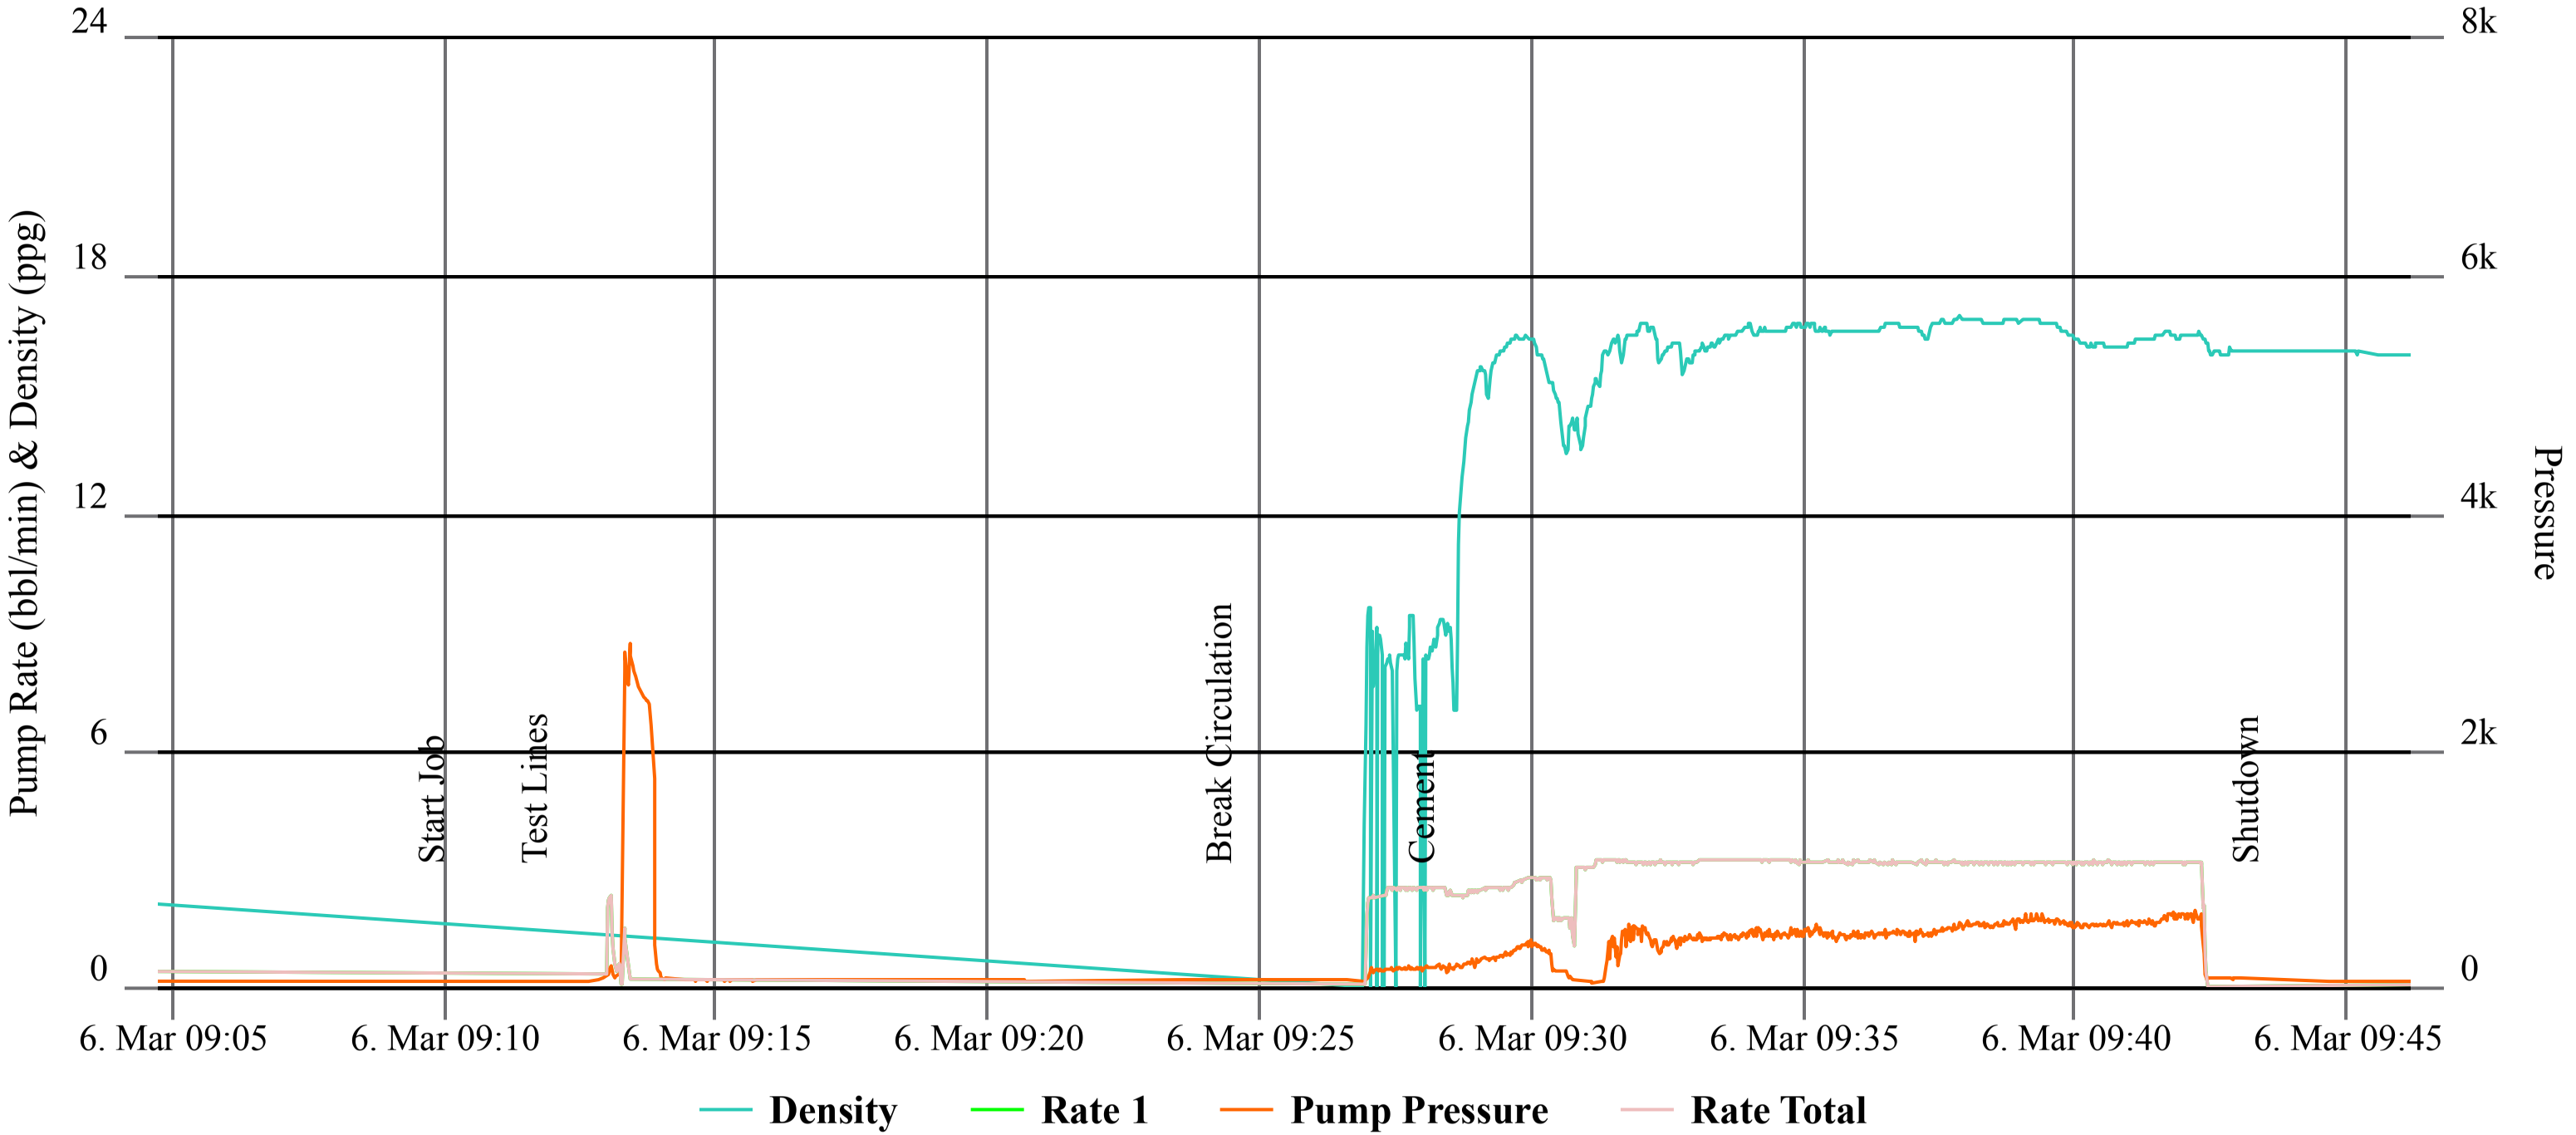
CEMENTING
