PIONEER NATURAL RESOURCES

Downhole Well Profile

Well Name: Colton 32-1

API/UWI	Surface Legal Location	License/Lease Number	Field Name	State
05-071-08924-0000			RATON-SPANISH PEAKS	COLORADO

Well Profile	Original KB Elevation (ft)	KB-Ground Distance (ft)	KB-Casing Flange Distance (ft)	KB-Tubing Head Distance (ft)
VERTICAL	7,106.00	4.00		

Type

Des	Make	Model	WP (psi)	Service	WP Top (psi)	Top Ring Gasket	Bore Min (in)

VERTICAL - Original, 7/1/2015 7:15:04 AM

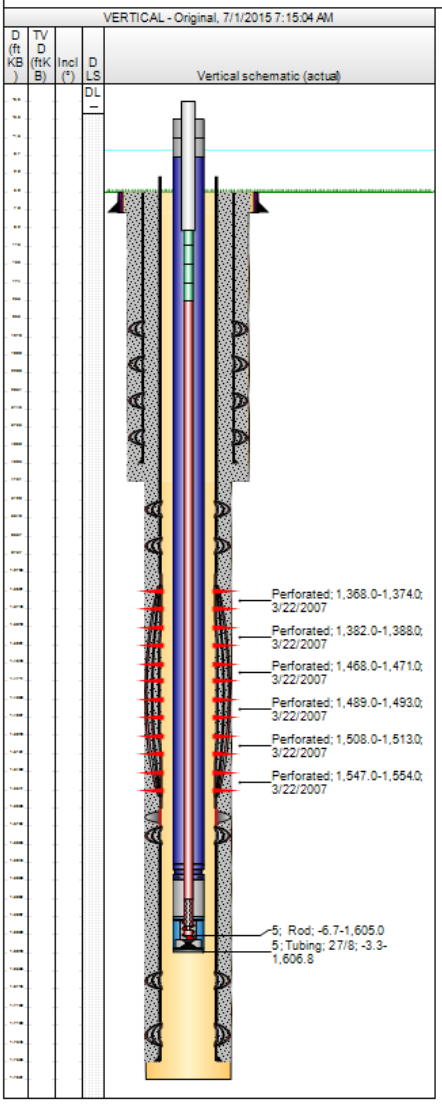

Casing Strings

Description	OD (in)	Wt/Len (lb/ft)	Grade	Top Thread	Set Depth (ftKB)
Conductor	12 3/4				8.0
Surface	8 5/8	23.00	X-42	ST&C	469.5
Production	5 1/2	17.00	J-55	LT&C	1,735.7

Perforations

Date	Top (ftKB)	Btm (ftKB)	Zone
3/22/2007	1,368.0	1,374.0	Vermejo, Original
3/22/2007	1,382.0	1,388.0	Vermejo, Original
3/22/2007	1,468.0	1,471.0	Vermejo, Original
3/22/2007	1,489.0	1,493.0	Vermejo, Original
3/22/2007	1,508.0	1,513.0	Vermejo, Original
3/22/2007	1,547.0	1,554.0	Vermejo, Original

Tubing set at 1,606.8ftKB on 6/6/2013 00:00

Tubing Description	Run Date	String Length (ft)	Set Depth (ftKB)
Tubing	6/6/2013	1,610.09	1,606.8

Item Des	Jts	Make	Model	OD (in)	Wt (lb/ft)	Grade	Len (ft)
Tubing Pup Joint	1			2 7/8			2.00
Tubing Pup Joint	1			2 7/8			2.00
Tubing	49		T&C Upset	2 7/8	6.50	J-55	1,593.92
Pump Seating Nipple	1			2 7/8			1.10
Tubing Pup Joint	1			2 7/8			4.00
PC Pump	1	Wilson		2 7/8			7.07

Rod on 6/6/2013 00:00

Rod Description	Run Date	String Length (ft)	Set Depth (ftKB)
Rod	6/6/2013	1,611.67	1,605.0

Item Des	Jts	Make	Model	OD (in)	Wt (lb/ft)	Grade	Len (ft)
Polished Rod	1	Norris	Norloy Steel	1 1/4			16.00
Pony Rod	1			7/8			2.00
Pony Rod	1			7/8			2.00
Pony Rod	1			7/8			4.00
Pony Rod	1			7/8			6.00
Sucker Rod	63	Norris	Grade 78	7/8	2.22	D	1,575.00
Progressing Cavity Pump	1			7/8			6.67

Page 1/1 Report Printed: 7/1/2015
